

Renaissance at Antiquity

PROJECT DASHBOARD


12/19/2014

| Time Metrics | | 12/19/14 |
|----------------------------------|-------------|----------|
| Project Start Date | 6/12/14 | |
| Original Contract Days | 365 | |
| Approved contract Extension Days | 0 | |
| Revised Contract Days | 365 | |
| Revised Contract Completion Date | 6/11/15 | |
| Projected Completion Date | 4/30/15 | |
| Days on Project | 187 | |
| % Time Elapse | 51% | |
| Days Remaining | 178 | |
| Schedule Status | On Schedule | |
| Pending Extension Days | 0 | |

| Document Metrics | |
|---------------------------------|---|
| Open PCO's | 1 |
| Open RFI's | 0 |
| Open Submittals | 6 |
| Issued ASI's | 0 |
| Daily Reports Completed | ✓ |
| Weekly Safety Meeting | ✓ |

| \$ Metrics | | |
|---|----|-----------|
| Original Contract Amount | \$ | 6,675,500 |
| Approved Changed Orders | \$ | 38,488 |
| Revised Contract Amount | \$ | 6,713,988 |
| # of Open Owner PCO's | \$ | 2 |
| Projected \$ Amount OCO (PCO's Pending) | \$ | 15,570 |
| Projected Contract Amount | \$ | 6,729,558 |
| Completed to Date (thru draw # 5) | \$ | 2,219,320 |
| % Completed | | 33% |

Work In Place (\$ Value)

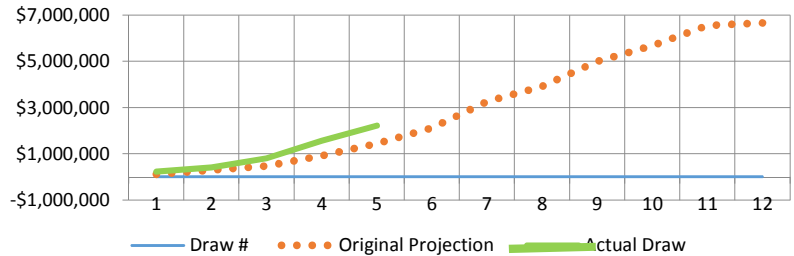

Work Area / % Complete

Legend

Change From Previous Week

25% Complete

50% Complete

75% Complete

100% Complete

| | West Wing | East Wing | Notes |
|-------------------------|-----------|-----------|--------------------------------------|
| Fire Alarm Rough | | | |
| Electrical Rough | | | |
| Sprinkler Rough | | | |
| HVAC Rough | | | |
| Plumbing Rough | 35% | | |
| Windows | | | |
| Roofing | 8% | 15% | |
| Roof Trusses | | | |
| 4th Floor Framing | | | |
| 4th Floor Trusses | | | |
| 3rd Floor Framing | | | |
| 3rd Floor Trusses | | | |
| 2nd Floor Framing | | | |
| 2nd Floor Trusses | | | |
| 1st Floor Framing | | | |
| Slab Pour | | | |
| Slab Prep | | | |
| Underslab Plumbing | | | |
| Stem Wall | | | |
| Segmental Wall | | | |
| Elevator Pits | | | |
| Water Lines | | | |
| Sanitary Sewer | | | |
| Storm Sewer | | | |
| Wall Excavation | | | |
| Rough Grading | | | |
| Demolition | | | |
| Temporary Skimmer Basin | | | Waiting on cable co. to relocate box |
| Silt Fence | | | |

CRITICAL ACTION ITEMS NEXT TWO WEEKS

| Item # | Brief Description | Who | When |
|--------|------------------------|---------------|-------|
| 1 | Start HVAC Rough | Mega Plumbing | 12/29 |
| 2 | Start Electrical Rough | Toler | 12/22 |
| 3 | Start Roofing | Roof Depot | 12/22 |
| 4 | Start Fire Alarm | Central | |
| 5 | | | |
| 6 | | | |
| 7 | | | |
| 8 | | | |

WORK PLANNED FOR NEXT TWO WEEKS

| | 22 | | | | | | 29 | | | | | | |
|-------------------------------|---|---|---|---|---|---|----|---|---|---|---|---|--|
| Work Description/Sub/Location | M | T | W | T | F | S | M | T | W | T | F | S | |
| West Wing | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| Plumbing Rough | | | | | | | | | | | | | |
| Sprinkler Rough | | | | | | | | | | | | | |
| Electrical Rough | | | | | | | | | | | | | |
| Roofing | | | | | | | | | | | | | |
| East Wing | | | | | | | | | | | | | |
| Plumbing Rough | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| Electrical Rough | | | | | | | | | | | | | |
| Roofing | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| Site | | | | | | | | | | | | | |
| Demo Lovers Lawn | Waiting on cable company to relocate line | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |
| | | | | | | | | | | | | | |

Media



Appendix 1



Appendix 2



Appendix 3



Appendix 4



Appendix 5
