


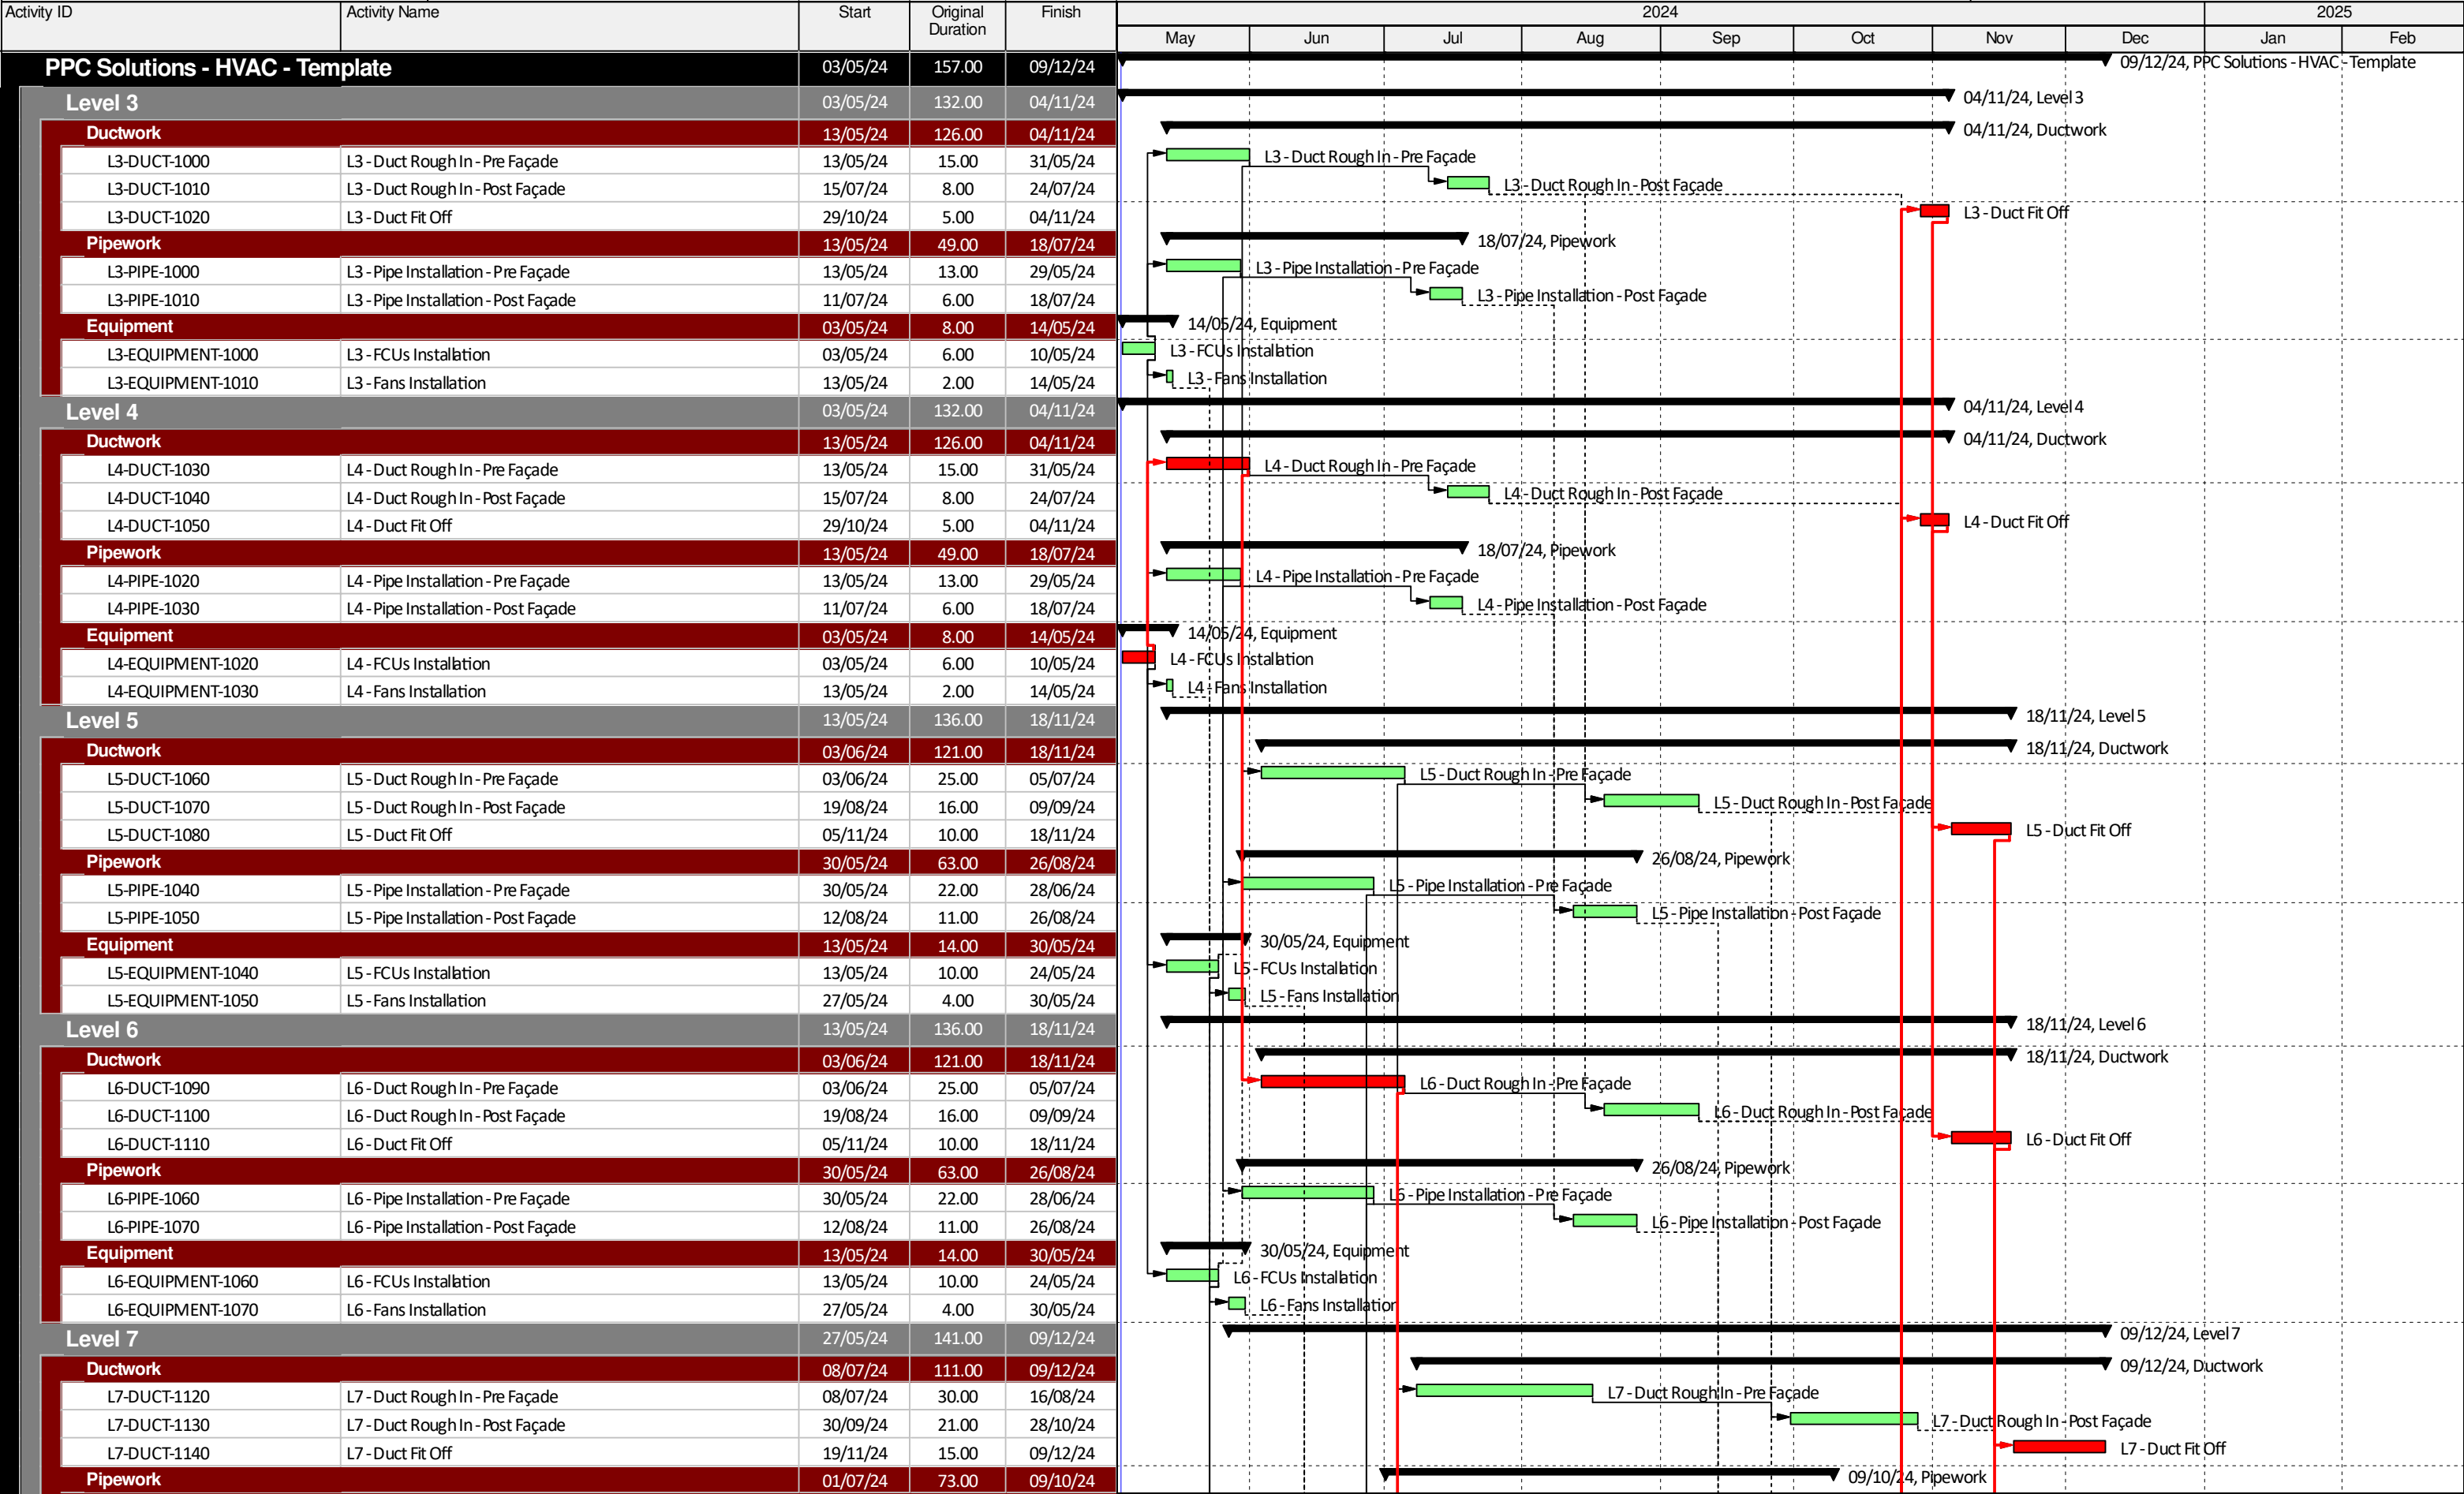

Activity ID	Activity Name	Start	Original Duration	Finish	2024								2025	
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
L7-PIPE-1080	L7 - Pipe Installation - Pre Façade	01/07/24	27.00	06/08/24										
L7-PIPE-1090	L7 - Pipe Installation - Post Façade	18/09/24	16.00	09/10/24										
Equipment		27/05/24	24.00	27/06/24										
L7-EQUIPMENT-1080	L7 - FCUs Instalation	27/05/24	15.00	14/06/24										
L7-EQUIPMENT-1090	L7 - Fans Installation	17/06/24	9.00	27/06/24										
Level 8		27/05/24	141.00	09/12/24										
Ductwork		08/07/24	111.00	09/12/24										
L8-DUCT-1150	L8 - Duct Rough In - Pre Façade	08/07/24	30.00	16/08/24										
L8-DUCT-1160	L8 - Duct Rough In - Post Façade	30/09/24	21.00	28/10/24										
L8-DUCT-1170	L8 - Duct Fit Off	19/11/24	15.00	09/12/24										
Pipework		01/07/24	73.00	09/10/24										
L8-PIPE-1100	L8 - Pipe Installation - Pre Façade	01/07/24	27.00	06/08/24										
L8-PIPE-1110	L8 - Pipe Installation - Post Façade	18/09/24	16.00	09/10/24										
Equipment		27/05/24	24.00	27/06/24										
L8-EQUIPMENT-1100	L8 - FCUs Installation	27/05/24	15.00	14/06/24										
L8-EQUIPMENT-1110	L8 - Fans Installation	17/06/24	9.00	27/06/24										
