

Project Status Update

The Division of Transportation Engineering
One-Cent Surtax Capital Projects

Vanderbilt Beach Road Extension Project # 60168


Prepared By: *Mario A. Puente, PE-CGC.*
Senior Project Manager

October 30th, 2020

Project Summary

- 7-mile extension of existing roadway.
- Six-lane divided urban roadway from east of Collier Blvd to the Curry Canal.
- Four lanes to east of Wilson Blvd
- Two lanes to 16th Str. NE
- Major improvements to Massey St
- Minor improvements to existing intersecting streets including Weber Boulevard, Danbury Blvd and Douglas Rd
- New roadway intersections at Wilson Blvd, 8th St NE and 16th St NE
- A new traffic signal at the Vanderbilt Beach Rd/Wilson Blvd intersection
- Canal relocation to south of the roadway from 31st St NW to 15th St NW

Project Site Location

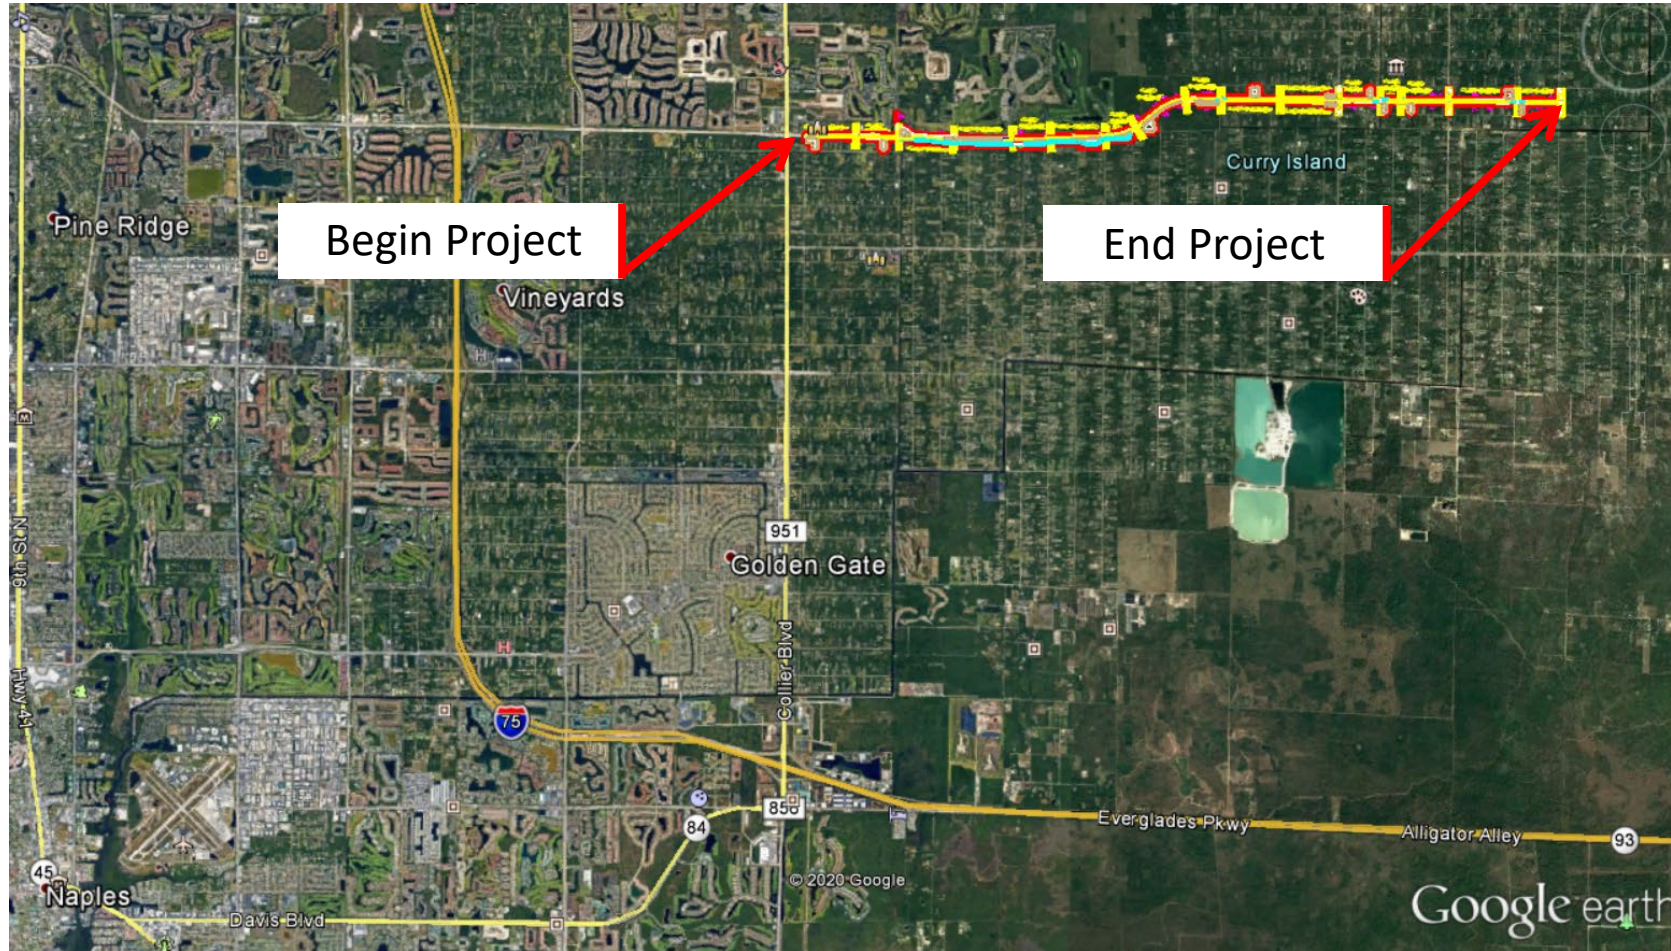


Project Schedule / Status

- Design NTP: 01/22/2018
- 60% Plans: 10/23/2020
- 100% Plans due by: 08/2021
- Target construction start: 12/2021
- Target construction completion: 07/2024

Project Status: Timeline and Budget

- 60% Plans under review – on schedule.
- Right of Way Condemnation Process started.
- Public Meeting scheduled for November 17th ,2020.
- SFWMD weir relocation regular coordination – ongoing.
- School District and Parks & Rec. developments regular coordination – ongoing.

Project Expenditures

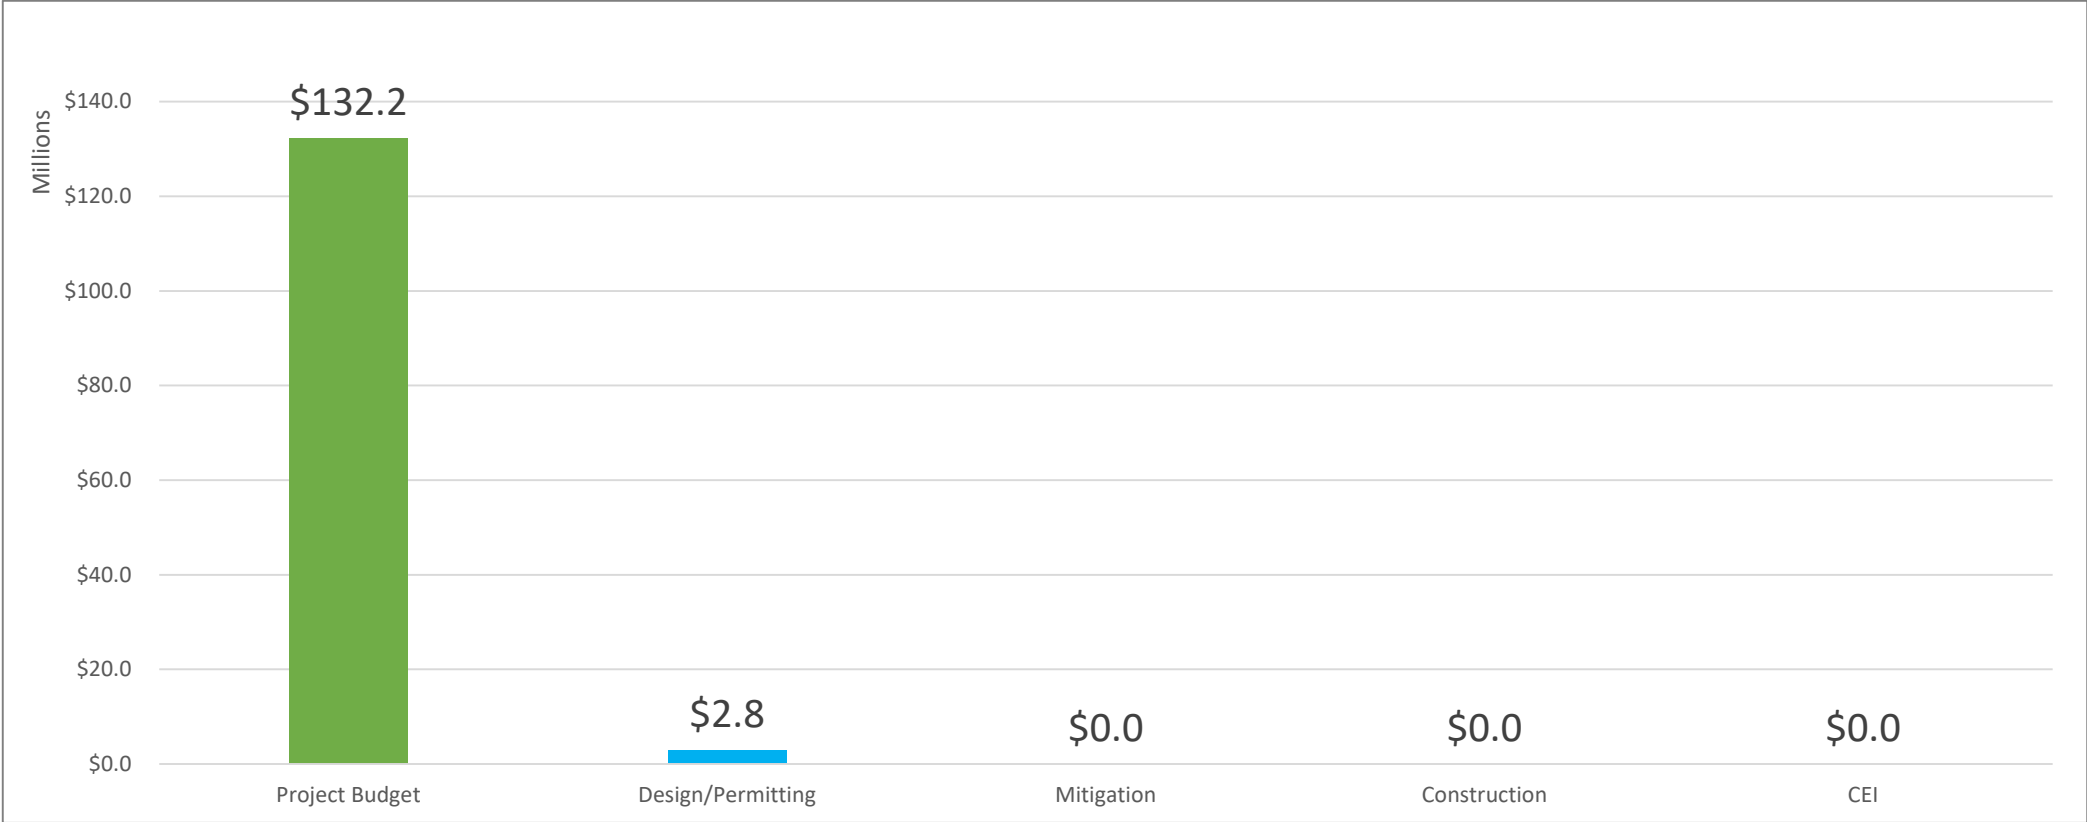

Sales Tax Funded: ≈\$74M

Gas Tax and Impact Fees Funded: ≈\$58.2M
