




CONSTRUCTION DELAYS IN THE O'CONNOR DISPOSAL AREA (OCDA)

- Construction activities in the OCDA have been delayed to modify the design of the soil cap and the Borough Recycling Center that will be constructed on the soil cap.
- During construction activities, it was determined that the elevation of Peter's Mine Road near the OCDA was one to four feet higher than displayed on the EPA-approved Final Design Drawings.
- It was also determined during construction that additional clean fill will be needed to be imported to complete the OCDA cap and construct entrance and exit ramps to the Recycling Center.
- Modifications to the Borough Recycling Center design are in progress, including the redesign of the entrance and exit ramps. The EPA-approved OCDA Final Design Drawings will be updated to address completion of the OCDA landfill soil cap.
- Construction activities are anticipated to resume in 2023. A more specific timeframe will be provided to the public as soon as it is available.

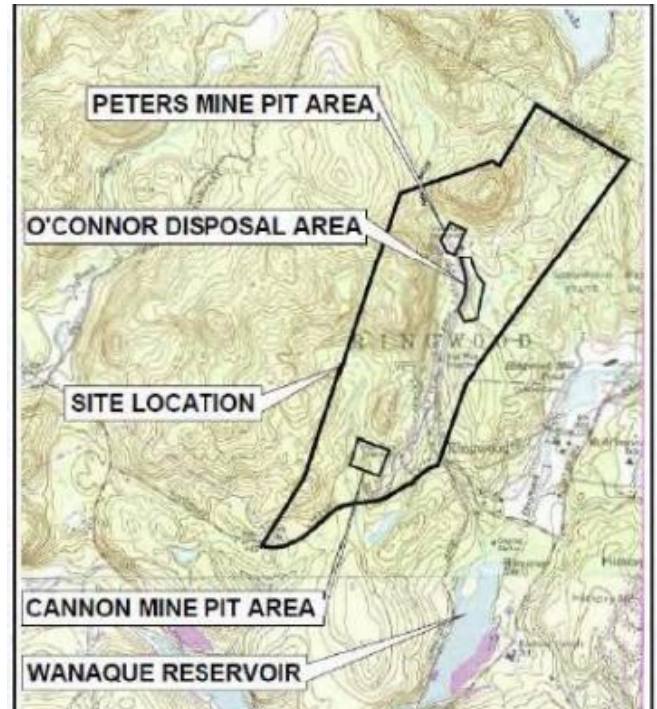

Contact Information:

Joe Gowers
EPA Remedial Project Manager
(212) 637-4413
gowers.joe@epa.gov

Pat Seppi
EPA Community Involvement Coordinator
(646) 369-0068
seppi.pat@epa.gov

Immediate concerns regarding construction can also be referred to:

de maximis, inc.
(610) 435-1151 ext. 2
