

Marrowstone Island Fire Station Crew Quarters Progress Report




November 2022



Crew Quarters Progress Timeline - 1

- August 24 – concrete foundation slab poured
- September 20 – the two building modules arrived and were placed on the foundation slab

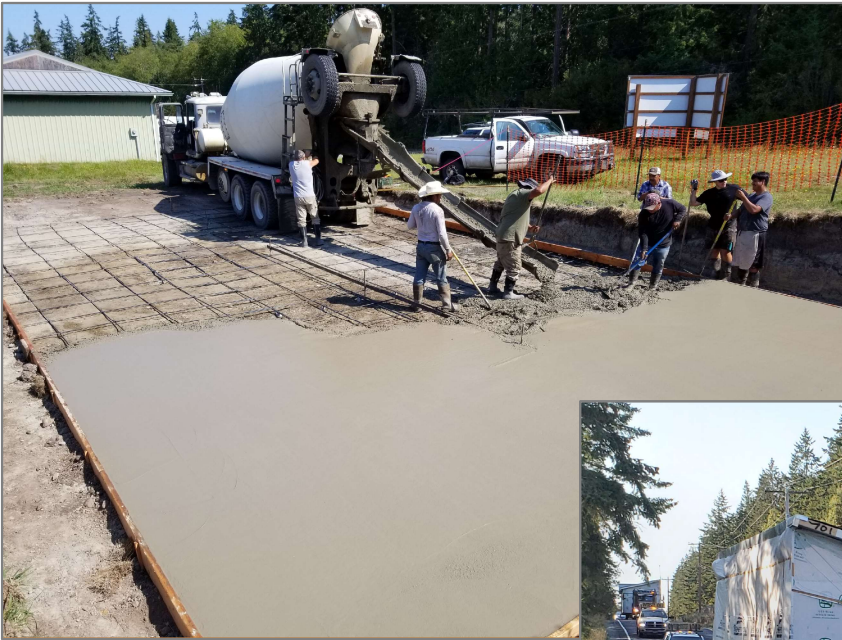

Crew Quarters Progress Timeline - 2

- September 28 – the two modules are joined, made weather tight, and tied down to foundation slab
- September 30 – exterior finish work underway
- November 1 – utility connections underway



Crew Quarters Progress Timeline - 3

- October/November – interior finish work underway
- November 14 thru 16 – site grading done and parking lot gravel put down and rolled



Crew Quarters Progress Timeline - 5

- Interior Photographs


Dining/Meeting Area
Office Beyond



Day Room



Kitchen
Utility Room Beyond

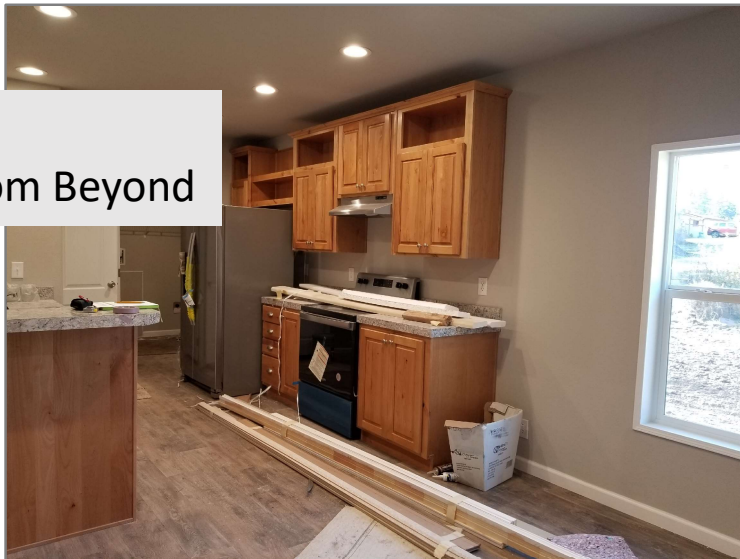

Restroom (1 of 2)

