



## July 9, 2020: General Users Meeting #10

### TAXIWAY A-D1-E

Construction Administration & Inspection

## July 9, 2020: General Users Meeting #10 Meeting Summary

### Project Update:

- Final work on subphase S3/4/5 will continue through at least Monday, July 13

### Continued User Impacts / NOTAMS:


- The week of July 13, expect conversion to subphase S6
  - Weather required for paving and marking may delay the start date
- Closures of TWY C1 and TWY A between TWYs C and F will continue
  - Aircraft near the work area will use TWY C to access TWY A
  - No terminal ramp space reductions or expected impacts to large aircraft pushbacks from the gate
- Taxilane H1 now in use with nonstandard signage
- Runway backtaxi and alternate routes continue for many users

### Closures:

- TWY C1, D, D1, D2, E, E1
- TWY A between TWY C and TWY F

### Next phase:

- Beginning next week, estimated to be July 13th:
  - Taxilane H will be controlled by ATC between TWYs B2 and D1. Look for non-movement area boundary markings. **ATC contact required!**
  - Vehicle service road (VSR) revisions on the apron near the passenger terminal
  - Closures: TWYs B, B1, B2, C and TWY A between TWYs B and C1
  - See attached subphase S6 flyer for details and maps or [visit the Links & Docs](#) page on the project website
  - Below is a clip of subphase S6 map

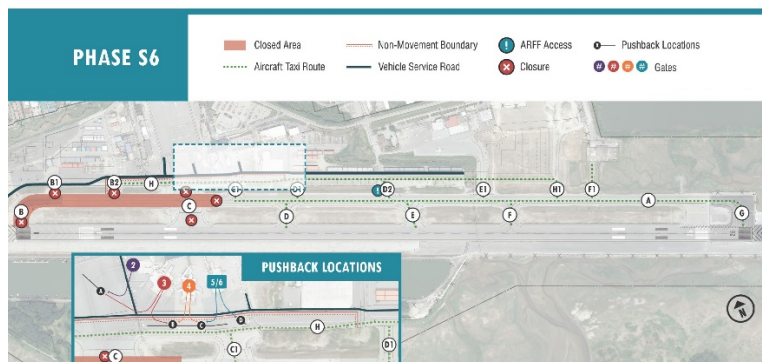

### Important Information:

- JNU-DOWL will continue to provide project update notifications via email and announcements on the website ([www.JNUTaxiways.com](http://www.JNUTaxiways.com))
