



HUNNELL RD: LOCO RD TO TUMALO RD

PRELIMINARY SCHEDULE




Project: Hunnell Road
Date: Fri 1/6/23

Legend: Task (blue bar), Milestone (black diamond), Summary (black line), Progress (blue line)



HUNNELL RD: LOCO RD TO TUMALO RD

PRELIMINARY SCHEDULE

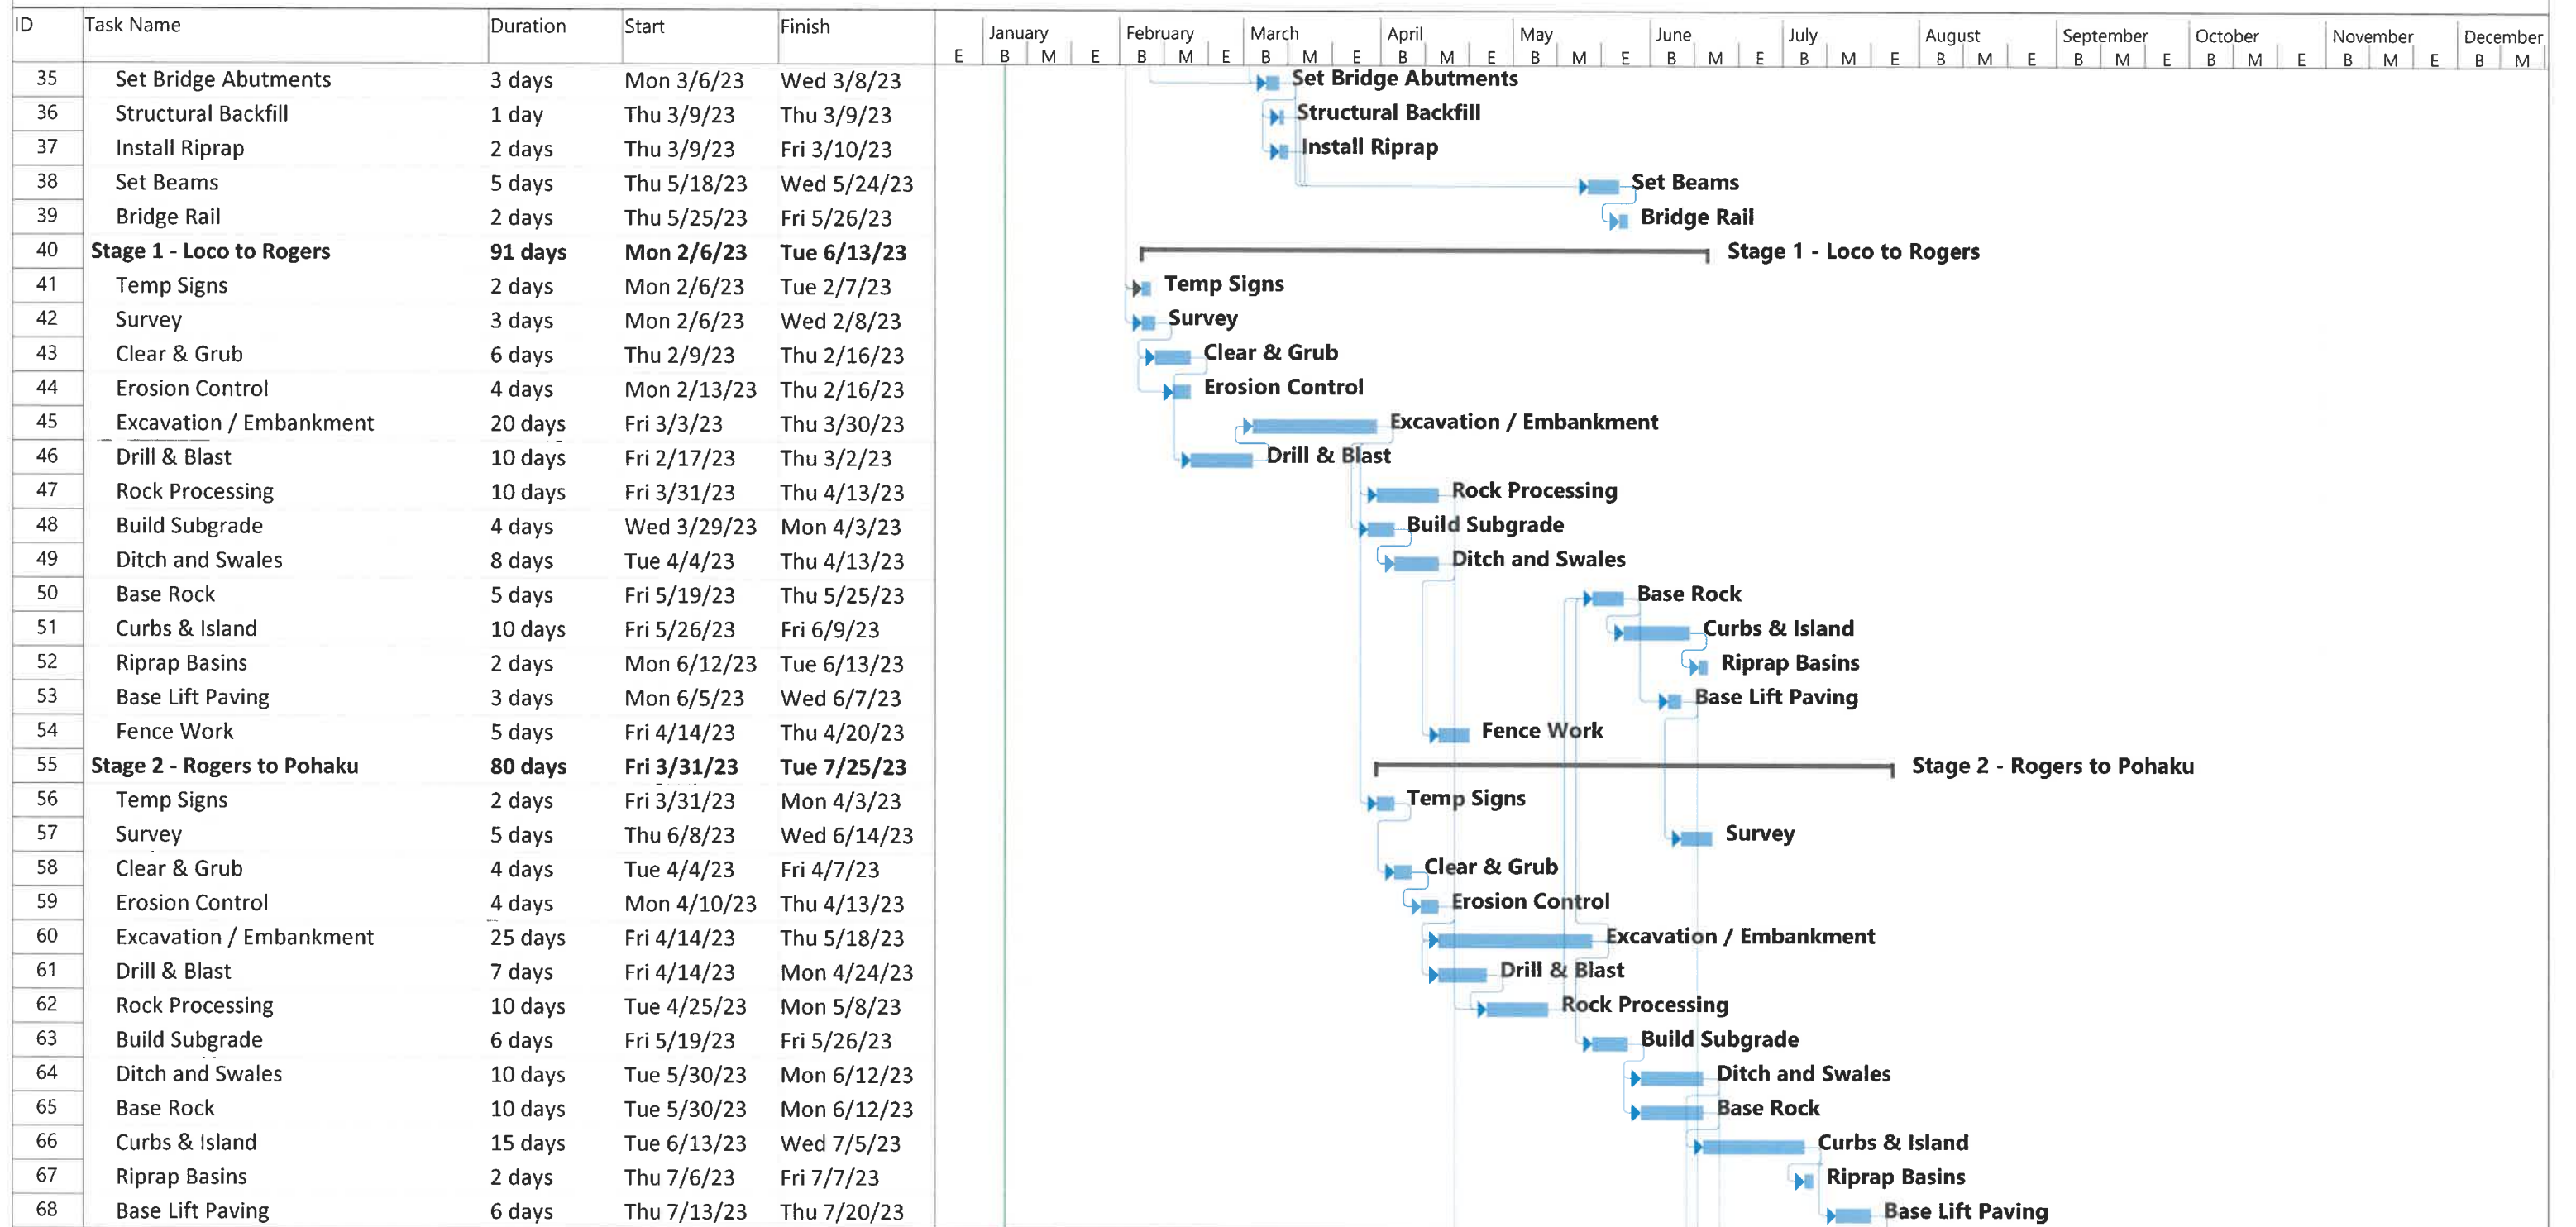

Project: Hunnell Road
Date: Fri 1/6/23

Task Milestone Summary Progress



HUNNELL RD: LOCO RD TO TUMALO RD

PRELIMINARY SCHEDULE

ID	Task Name	Duration	Start	Finish	Calendar Months																																										
					January				February				March				April				May				June				July				August				September				October				November		
69	Fence Work	5 days	Tue 6/13/23	Mon 6/19/23																																											
70	Guardrail	3 days	Fri 7/21/23	Tue 7/25/23																																											
71	Stage 3 - Pohaku - Tumalo	55 days	Fri 7/21/23	Fri 10/6/23																																											
72	Temp Signs	2 days	Fri 7/21/23	Mon 7/24/23																																											
73	Survey	5 days	Fri 7/21/23	Thu 7/27/23																																											
74	Clear & Grub	2 days	Fri 7/28/23	Mon 7/31/23																																											
75	Erosion Control	2 days	Tue 8/1/23	Wed 8/2/23																																											
76	Excavation / Embankment	15 days	Thu 8/3/23	Wed 8/23/23																																											
77	Build Subgrade	4 days	Thu 8/24/23	Tue 8/29/23																																											
78	Ditch and Swales	6 days	Wed 8/30/23	Thu 9/7/23																																											
79	Base Rock	8 days	Wed 8/30/23	Mon 9/11/23																																											
80	Curbs & Island	10 days	Tue 9/12/23	Mon 9/25/23																																											
81	Riprap Basins	2 days	Tue 9/26/23	Wed 9/27/23																																											
82	Base Lift Paving	4 days	Tue 10/3/23	Fri 10/6/23																																											
83	Fence Work	4 days	Fri 9/8/23	Wed 9/13/23																																											
84	Top Lift Paving	6 days	Mon 10/9/23	Mon 10/16/23																																											
85	Shoulder Rock	4 days	Tue 10/17/23	Fri 10/20/23																																											
86	Pavement Marking	3 days	Mon 10/23/23	Wed 10/25/23																																											
87	Recessed Markers	3 days	Thu 10/26/23	Mon 10/30/23																																											
88	Seeding	2 days	Fri 9/8/23	Mon 9/11/23																																											
89	Mailboxes	4 days	Thu 10/26/23	Tue 10/31/23																																											
90	Speed Feedback System	15 days	Mon 10/9/23	Fri 10/27/23																																											

Project: Hunnell Road
Date: Fri 1/6/23

Task Milestone Summary Progress
