

SOUTHEAST AREA COMBINED SEWER IMPROVEMENTS PHASE 2 CONSTRUCTION STATUS REPORT

Status Report 14 – May 10, 2024



Standpipes, as shown above, have been installed in various locations to assist with the testing of the water main prior to it being placed into service

Work Completed from May 6th to May 10th


- Water main installation on North Downer Avenue between East Beverly Road and East Shorewood Boulevard
- Water main installation across the intersections of East Newton Avenue, East Beverly Road, and East Shorewood Boulevard

Work Scheduled for the Week of May 13th

- Combined sewer and storm sewer installation on North Downer Avenue between East Stratford Court and East Beverly Road
- Water main testing
- Water main connections at East Newton Avenue, East Beverly Road, and East Shorewood Boulevard

Access Notes:

- For properties on North Downer Avenue, please use the side street intersection for access. **Some side street access may be blocked depending on when water main connections are occurring throughout the week.**
- For properties on East Newton Avenue, please use the North Lake Drive intersection for access
- For properties on North Ridgefield Circle, please use the East Capitol Drive intersection for access

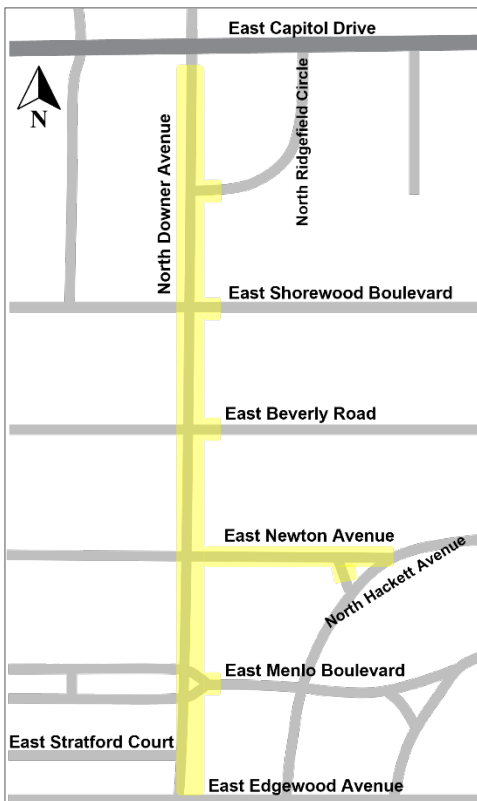

Important Note:

Construction sequencing for this project requires the Contractor to complete different improvements at different times, meaning they will be working in front of each residence more than once.

Example construction sequencing can be viewed here:

<https://www.villageofshorewood.org/DocumentCenter/View/11144/SEACSI-Phase-2-construction-sequencing>

2024 Project Timeline

February-July: North Downer Avenue utility installation

May-July: East Newton Avenue utility installation

July-September: North Downer Avenue and East Newton Avenue road reconstruction

September: North Downer Avenue and East Newton Avenue are open to the public

QR Code to Website



Project Contact Information:

Konrad Temnitz, Onsite Representative: (414) 982-2300, ext. 1524

Shorewood DPW: (414) 847-2650

Emily Rowntree, P.E., Project Manager: (414) 271-0771, ext. 1525

