

Broadband Project Update: 1/30/2021

Hello again all! Here is the latest on the Broadband front:

- Great news! 3 of the 6 sections in town have completed the Fiber Build out and Splicing phases, and all are currently in testing! The remaining 3 phases are closing in on completion as well, so CCI is making good progress.
- While the overall schedule seems to have slipped a bit, the most recent word from CCI is that they plan on beginning to take orders for install this coming Monday, 2/1. It is unclear to me at this point what this looks like, but based on the information provided to date, I would expect CCI to begin making these calls to folks who pre-registered. I am working to get in touch with CCI to get these questions answered as well as questions about bundling. I appreciate the patience and will pass along these details as soon as I can.
- As a reminder, if you pre-registered and have not been able to get back in touch with CCI after an initial call, go ahead and give them a call at **1-888-604-3050**. Please note that this number should only be used if you have pre-registered and CCI has initially tried to contact you with no success. **If you have pre-registered and have yet to received an initial call from CCI, do not call this number. Let them try at least once first.**


As always, if you have not done so already, do not forget to fill out the pre-registration information and form on the Westmoreland Broadband Website. The link is below. Pre-registration will help ensure you get hooked up faster than those who do not.

[www.consolidated.com/westmoreland](http://www.consolidated.com/westmoreland)

Take care. See you in two weeks!

Job	Fiber Built % (Previous)	Fiber Built % (Current)	Splicing % (Previous)	Splicing % (Current)	Testing Complete (Previous)	Testing Complete (Current)	Ready for Install (Previous)	Ready for Install (Current)
Orange	100%	100%	90%	100%	In Progress	In Progress	0%	0%
Purple	100%	100%	80%	100%	In Progress	In Progress	0%	0%
Light Blue	100%	100%	75%	75%	In Progress	In Progress	0%	0%
Yellow	100%	100%	75%	75%	In Progress	In Progress	0%	0%
Red	100%	100%	50%	100%	In Progress	In Progress	0%	0%
Green	99%	99%	85%	85%	In Progress	In Progress	0%	0%

**WESTMORELAND NH FTTP PROJECT**

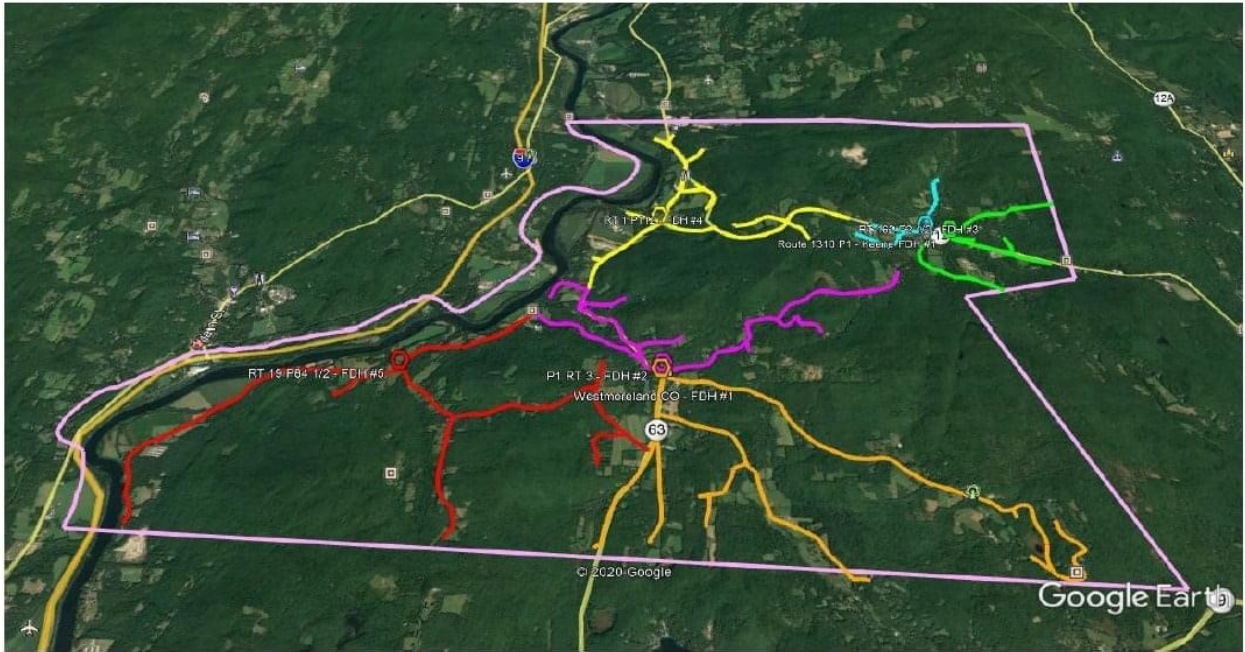

- Pink – Westmoreland Town Boundary
- Orange – Westmoreland Exchange FDH #1 Fiber Path
- Purple – Westmoreland Exchange FDH #2 Fiber Path
- Light Blue – Westmoreland Exchange FDH #3 Fiber Path
- Yellow – Westmoreland Exchange FDH #4 Fiber Path
- Red – Westmoreland Exchange FDH #5 Fiber Path
- Green – Keene Exchange FDH #1 Fiber Path
