

Seacove Place – Week 3 – Antis Reroof Report

Friday Aug 22, 2025

Seacove Place HOA – Project Progress Update

Recent Completions:

Bldg. #2 (48–62 Waxwing Lane) – Finished as of Thursday August 21, 2025

Current Status:

The project is officially underway and progressing steadily.

- **Bldg. #3 (64–78 Night Heron Lane)** – In progress
 - Tear-off took place August 12, 2025
 - Sheathing inspection took place August 13, 2025
- **Bldg. #4 (18-32 Fulmar Lane)** – In progress
 - Tear-off took place August 19, 2025
 - Sheathing inspection took place August 20, 2025
- **Bldg. #5 (95-109 Night Heron Lane)** – In progress
 - Tear-off took place August 20, 2025
 - Sheathing inspection took place August 21, 2025

Change Orders:

- **Bldg. #3 (64–78 Night Heron Lane)** – Submitted on August 21, 2025
- **Bldg. #4 (18-32 Fulmar Lane)** – Submitted on August 21, 2025

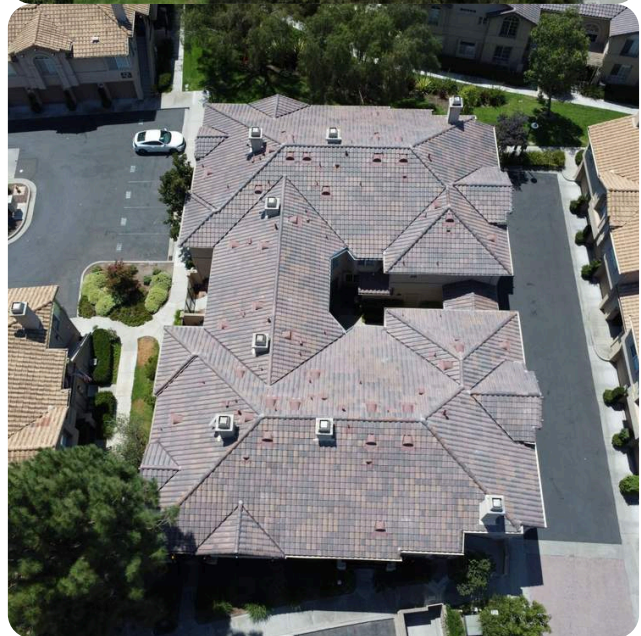
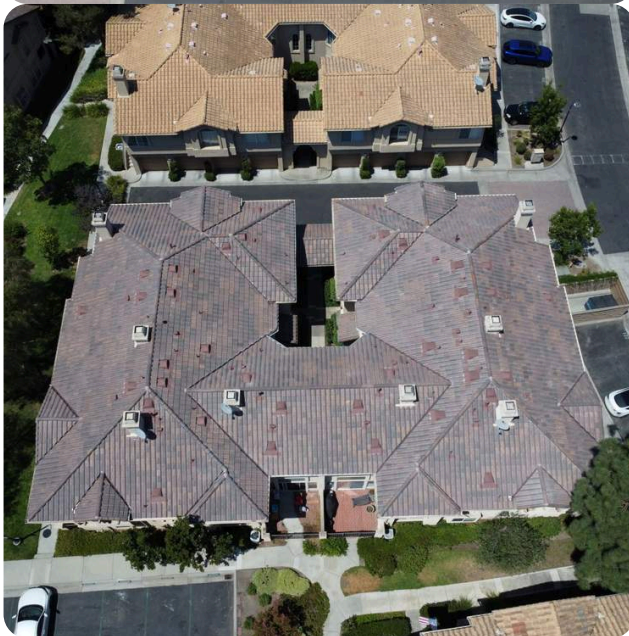
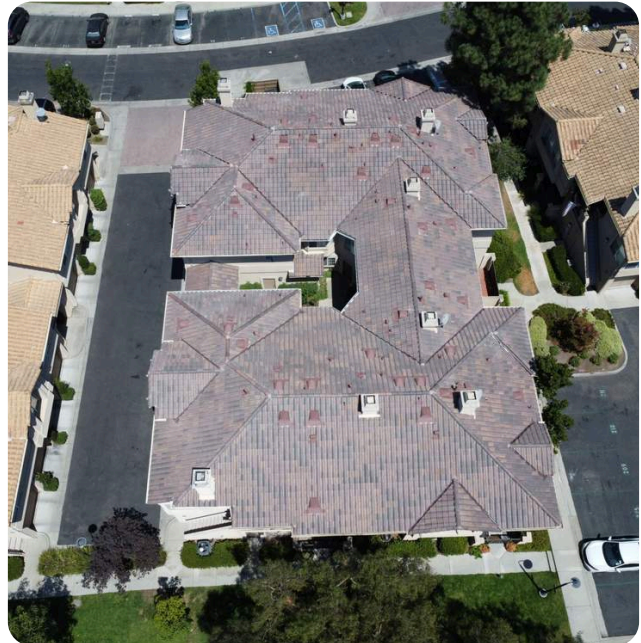
Upcoming:

Next Week (Aug 25–29):

- **Bldg. #6** scheduled to start August 26, 2025

Total Project Percent Completed: 9%

We will continue to monitor progress closely and provide updates as the project advances.

Bldg. #2 (48–62 Waxwing Lane) – Finished August 21, 2025

Bldg. #3 (64-78 Night Heron Lane)



Bldg. #4 (18-32 Fulmar Lane)



Bldg. #5 (95-109 Night Heron Lane)

