




SEAL REPORT

Envelope sealing performed for:

Austin, TX 78723

Date: 10/2/2025
Floor Area: 1508.00 ft²
Structure Volume: 16930.00 ft³
Operational Leakage: 169.3 CFM@50Pa

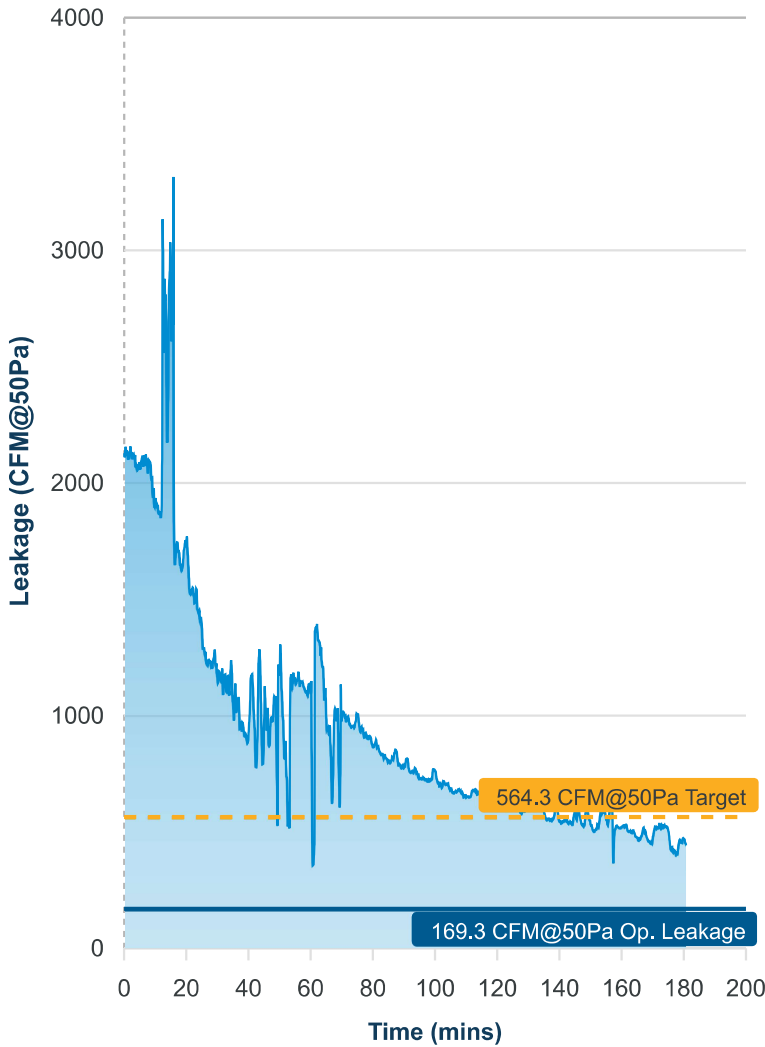

Note: Envelope leakage and air-change results are calculated at a STANDARD OPERATING PRESSURE of 50 Pa.

Envelope sealing performed by:

Kevin Holder

Phone:

Aeroseal Case ID: 8340

Hardware: AeroBarrier Connect

ACH@50Pa

8.08 ACH@50Pa	1.51 ACH@50Pa
-------------------------	-------------------------

Leakage equivalent to

274.3 Sq.In	51.4 Sq.In
--------------------	-------------------

● Before ● After

87.8%

Reduction in
Envelope
Leakage

03:00

hh:mm
Seal Time
