



CERTIFIED LEAKAGE REPORT

Duct sealing performed for:

Austin, TX 78739

Square Footage: 4500

Technician Name: 6058

Date: 6/23/2025


Aeroseal Case ID: 6058

System Description: Attic Supply/Return

Seal Description: Supply/Return


Hardware: Homeseal Connect

Leakage (CFM₂₅)

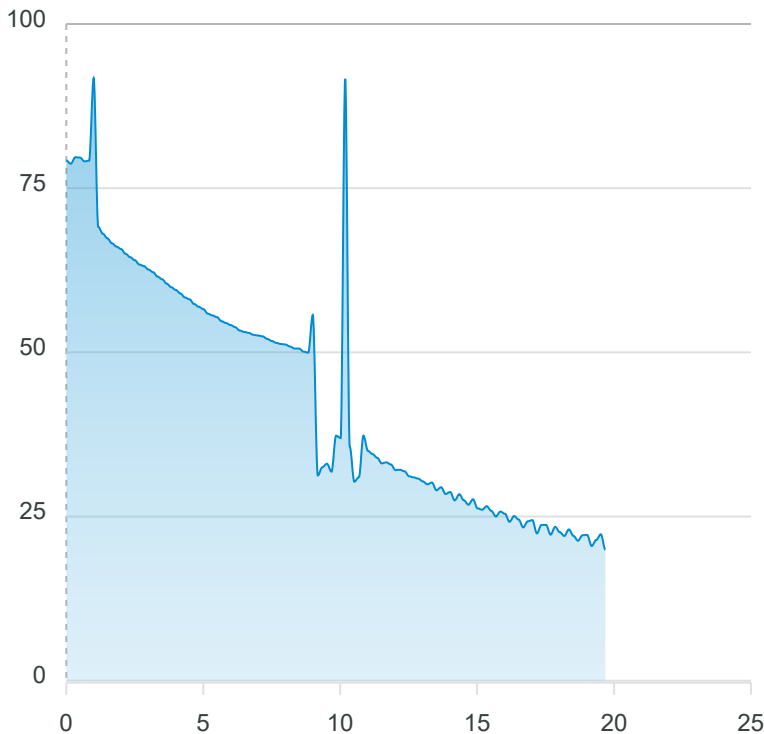

Duct leakage results are calculated in Cubic Feet per Minute (CFM) calculated at a STANDARD OPERATING PRESSURE of 25 Pa.

	Initial	Final
CFM ₂₅	81	20
CFM ₂₅ /100 ft ²	1.8	.4
Equivalent Hole Size	15.2 in ²	3.7 in ²
% System Capacity	5.0%	1.2%



Going Beyond Any Other Energy Reduction Service



Improved Indoor Air Quality



Improved Efficiency



Increased Home Comfort

Scan for more details



Aeroseal
aeroseal.com
877-FIX-DUCT
info@aeroseal.com

Duct sealing performed by:

787 development

