

CERTIFIED LEAKAGE REPORT


Duct sealing performed for:

Austin, TX 78739

Square Footage: 4500 **Technician Name:**6058

Date:6/23/2025

Leakage (CFM 25)

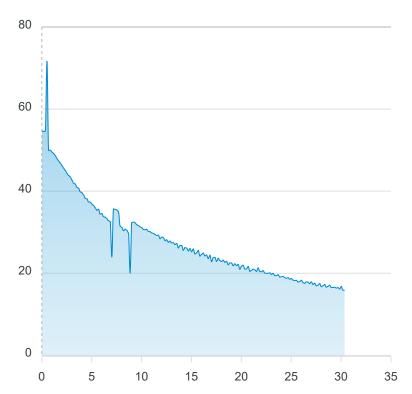

Duct leakage results are calculated in Cubic Feet per Minute (CFM) calculated at a STANDARD OPERATING PRESSURE of 25 Pa.

Going Beyond Any Other Energy Reduction Service







Aeroseal Case ID:6058
System Description:Attic Supply & Return
Seal Description:Upstairs Unit
Hardware:Homeseal Connect

	Initial	Final
CFM ₂₅	51	12
CFM ₂₅ /100 ft ²	1.1	.3
Equivalent Hole Size	9.5 in ²	2.2 in ²
% System Capacity	4.2%	1.0%



Scan for more details

Aeroseal aeroseal.com 877-FIX-DUCT info@aeroseal.com



Duct sealing performed by:

787 development



Aeroseal process uses DuctSeal sealant that is certified to meet requirements listed in UL 1381 standard - "Outline of investigation for Aerosol Duct Sealant"
