

ENVELOPE SEALING REPORT

Envelope Sealing Performed For:

██████████
██████████
██████████

AEROBARRIER CASE ID: 8340

SEAL DESCRIPTION: ██████████

HARDWARE: AeroBarrier Connect

TECHNICIAN: Kevin

DATE:
1/18/2024

BUILDING TYPE:
Single Family Detached

Envelope Sealing Results:

BEFORE SERVICE

1253.9 CFM of Leakage, equivalent to a
151.0 Square Inch Hole, or
2.15 Air Changes per Hour

(for your 2692-ft² structure
enclosing a volume of 35000 cubic feet)


AFTER SERVICE

722.4 CFM of Leakage, equivalent to a
87.0 Square Inch Hole, or
1.24 Air Changes per Hour

This corresponds to a
42.4% Reduction
in Envelope Leakage

NOTE: Envelope leakage and air-change results are
calculated at a standard pressure of 50 Pa.
Sealing time elapsed: 3:07:27

Envelope Sealing Progress:

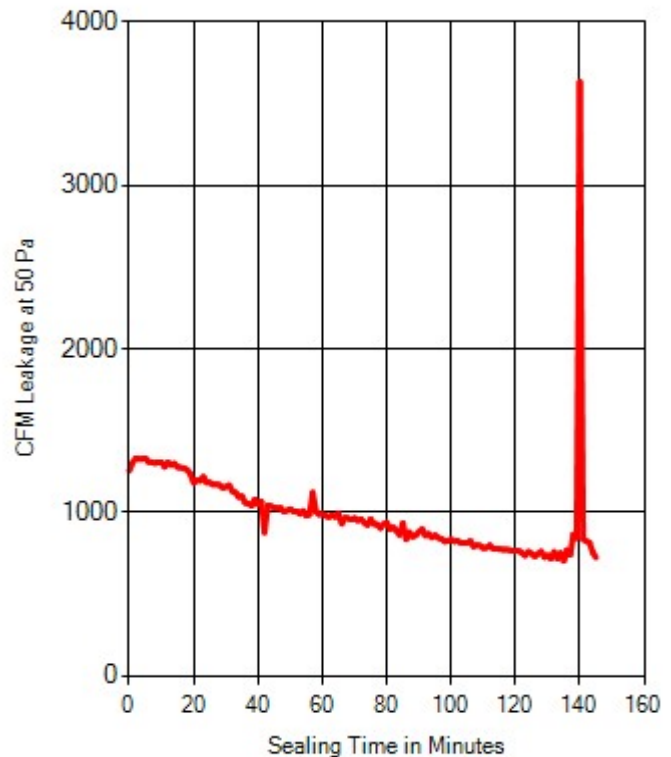

Envelope Sealing Performed By:



787 Development

NOTES: a) A certified HVAC contractor or rater should be used to assess the need for enhanced/balanced mechanical equipment as the desired leakage is reduced. b) This certificate provides results based on an enclosure test, using positive pressure. A final blower door test may still be required.
