



CERTIFIED LEAKAGE REPORT

Duct sealing performed for:


Austin, TX 78759

Square Footage: 1500

Technician Name: 6058

Date: 6/2/2025

Leakage (CFM₂₅)

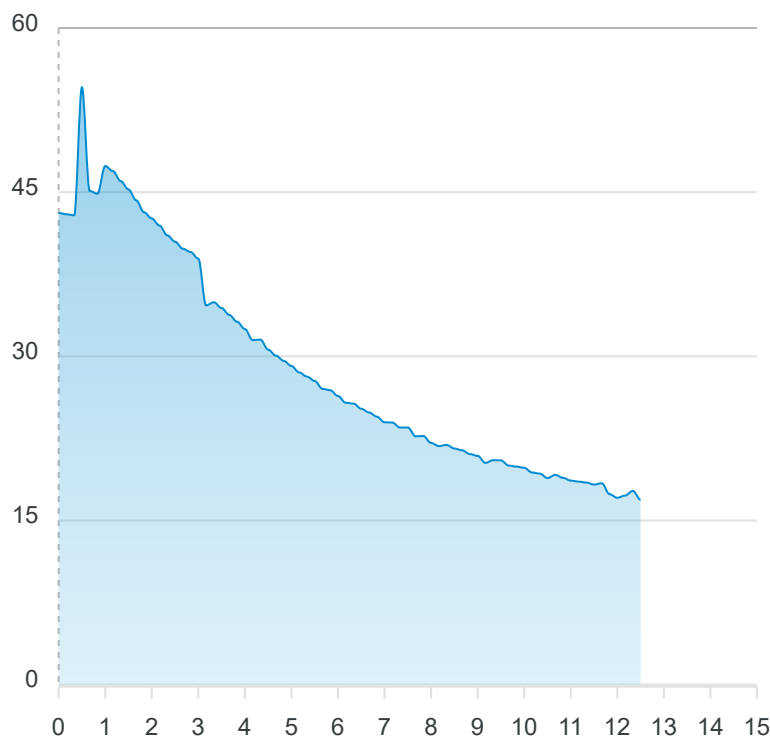

Duct leakage results are calculated in Cubic Feet per Minute (CFM) calculated at a STANDARD OPERATING PRESSURE of 25 Pa.

Going Beyond Any Other Energy Reduction Service



Improved Indoor Air Quality



Improved Efficiency



Increased Home Comfort

Aeroseal Case ID: 6058

System Description: Closet Upright

Seal Description: Supply Only

Hardware: Homeseal Connect

	Initial	Final
CFM ₂₅	33	11
CFM ₂₅ /100 ft ²	2.2	.7
Equivalent Hole Size	6.2 in ²	2.0 in ²
% System Capacity	2.7%	.9%



Scan for more details



Aeroseal
aeroseal.com
877-FIX-DUCT
info@aeroseal.com

Duct sealing performed by:

787 development

