

Project Status Update

The Division of Transportation Engineering

One-Cent Surtax Capital Projects

11 Bridge Replacements Project


Prepared By: *Marlene Messam*, Principal Project Manager

October 30th, 2020

Project Summary

- To design and replace 11 existing bridges due to the deficient structural condition ratings received from the Florida Department of Transportation.
- The 11 existing bridges are located in rural Collier County east of SR29. There are six (6) bridges on Immokalee Road, one (1) bridge on Countyline Road, and four (4) bridges on Oilwell Road.
- The bridges will have a standard typical cross-section consisting of two lanes (one in each direction), wider shoulders, and animal crossing shelves at six (6) locations.

Project Site Location

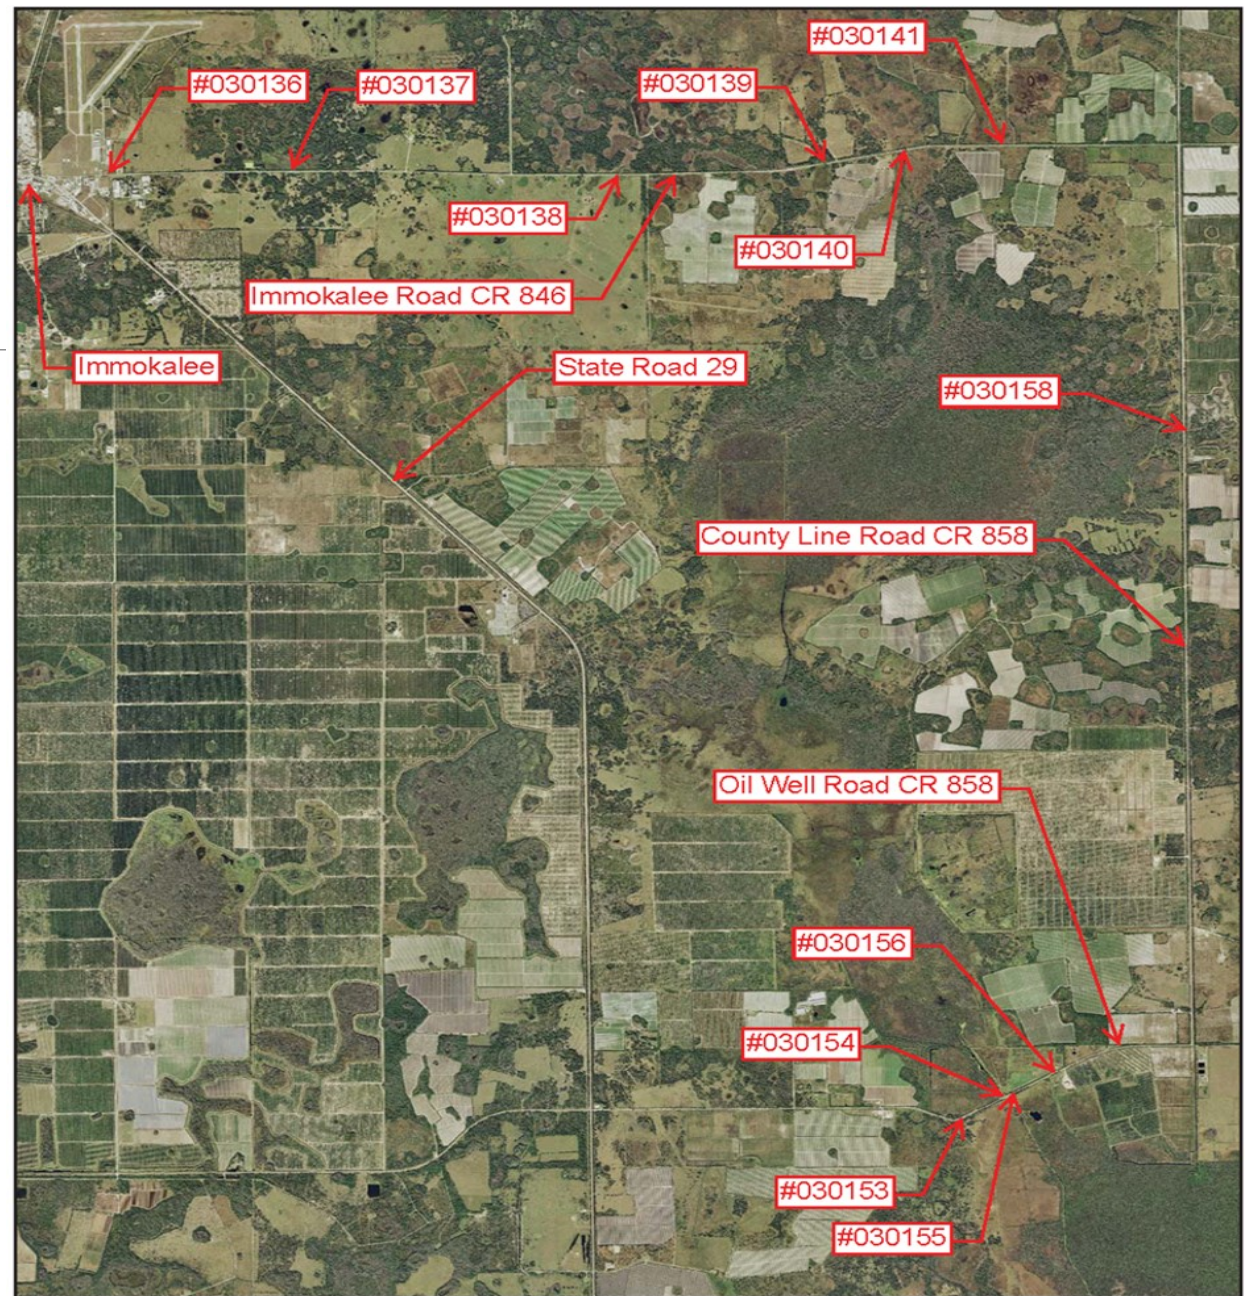

Project Schedule / Status

ACTIVITY	START	FINISH	2020				2021				2022				2023				2024	
			Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
US Army Corps Permitting*	Jun-19	Dec-20	█	█	█	█														
Procurement (incl. BCC approvals)	Jan-21	Jun-21					█	█												
Construction Starts (Estm.)	Jul-21								█	█	█	█	█	█	█	█	█	█	█	
Construction End (Estm)		Jan-24																		

* US Army Corps has issued permits for eight(8) of the Eleven (11) bridges as of 10/31/2020.

Project Status: Timeline and Budget

- On April 3, 2019, Surtax Committee validated expenditures in the amount of \$35,434,846 of which \$7,000,000 were earmarked as Surtax Funding.
- The design production is currently at the final phase, and all permits except for the USACE are in hand.
- On September 2, 2020, Surtax Committee validated a reallocation of Infrastructure Sales Surtax Funding from New Bridges Golden Gate Estates to the Bridge Replacement Project, in the amount of \$26,000,000.

Project Expenditures

