

SAGUACHE CREEK DIVERSION INFRASTRUCTURE INVENTORY

Structure Name: JEEP SCANDRETT D

Reported By: Daniel Boyes

Date: July 3, 2019

Headgate	Latitude	Longitude
Location:	38.066693	-106.083656

Headgate Type: Manually operated 2' wide screw gate

Headgate Condition:	A <input type="checkbox"/>	Diversion and Other Condition:	A <input type="checkbox"/>	Stream Miles from Saguache Creek Terminus (Point of Diversion):	Structure Submerged: Yes <input checked="" type="checkbox"/>
	B <input checked="" type="checkbox"/>		B <input type="checkbox"/>	24.4 mi	No <input type="checkbox"/>
	C <input type="checkbox"/>		C <input checked="" type="checkbox"/>		
	D <input type="checkbox"/>		D <input type="checkbox"/>		
	F <input type="checkbox"/>		F <input type="checkbox"/>		

Structure Description: A diversion dam of boulders and woody debris directs water to the headgate, located on the north bank of the stream. The diversion is located on the outside of a tight meander. The diversion dam functions poorly during low flow, collects debris, and does not have adequate sediment transport capacity.

Repair(s) or Improvement(s) Currently Needed: The SMP Technical Advisory Team (TAT) recommends improving the diversion to more effectively divert water and to improve sediment transport. Alternatively, combining the diversion dam with that of the Slane Scandrett may improve this ditch's function and reduce maintenance.

Comments: This ditch is a priority 25.

Notes:

Estimated Range of Cost: Low

Headgate looking downstream



Headgate outlet



Headgate and diversion dam




Diversion dam



Stream channel upstream of diversion



Flume looking downstream

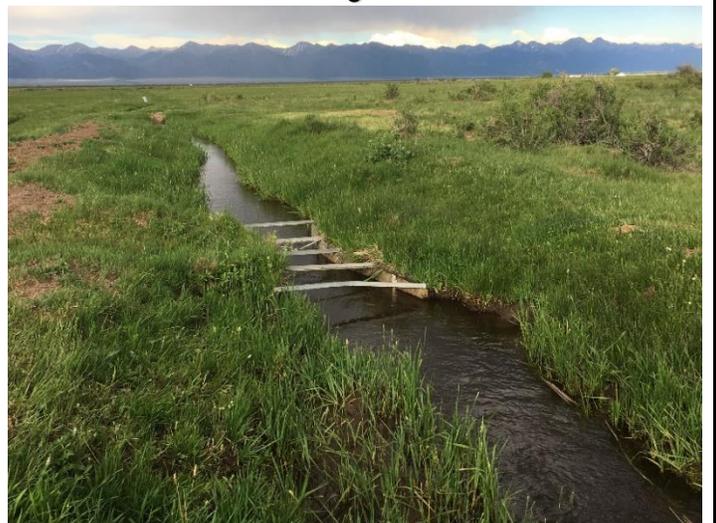

SAGUACHE CREEK DIVERSION INFRASTRUCTURE INVENTORY

JEEP SCANDRETT DITCH

PHOTO LOG

Saguache Creek Stream
Management Plan
