

PROJECT

TJ MAXX - PENDLETON, OR
1900 SOUTHWEST COURT AVENUE
PENDLETON, OR 97801

CONTRACTOR / OWNER

DICKERHOOF CONSTRUCTION LLC
P.O. BOX 1583
CORVALLIS, OR
US

BRANCH (INSTALLATION AND SERVICE)

QUALITY DOOR SERVICE
434 SE 5TH AVE HILLSBORO, OR 97123

Construction Manager :

Installation Coordinator :

Installation Phone Number :

Installation Fax Number :

Service Phone Number : 000-000-0000

TERRITORY MANAGER (SALES)

Territory Manager : Bill Gerardin

Sales Phone Number :

Sales Fax Number :

Sales Email Address : william.gerardin@allegion.com

SHOP DRAWING / SUBMITTAL REVIEW

☒ NO EXCEPTIONS TAKEN ☐ APPROVE WITH CHANGES NOTED

☐ REVISE & RESUBMIT ☐ REJECTED _____





SUBMITTAL WAS REVIEWED FOR DESIGN CONFORMITY AND GENERAL CONFORMANCE TO CONTRACT DOCUMENTS ONLY. THE SUBCONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION PROCESSES AND TECHNIQUES OF CONSTRUCTION, COORDINATION OF HIS WORK WITH OTHER TRADES AND FULL COMPLIANCE WITH CONTRACT DOCUMENTS

By: Connor Hoke Date: 07/23/26

STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801
Door Location: Exterior Door




Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP ✓

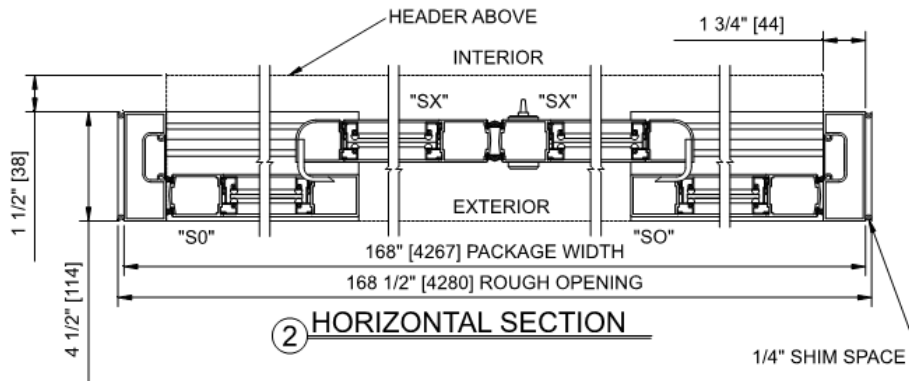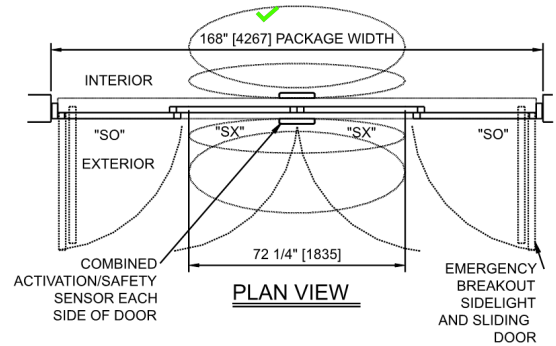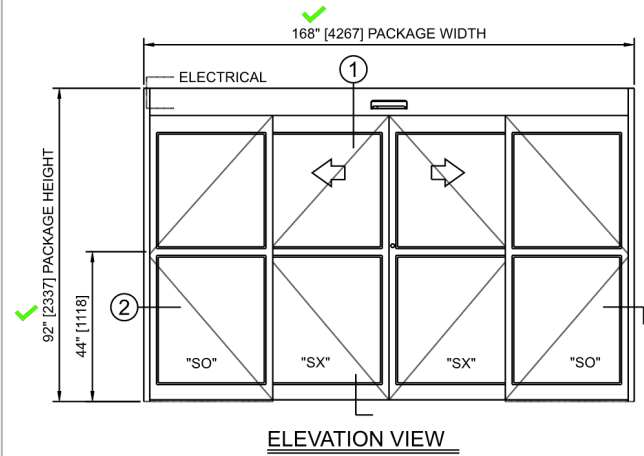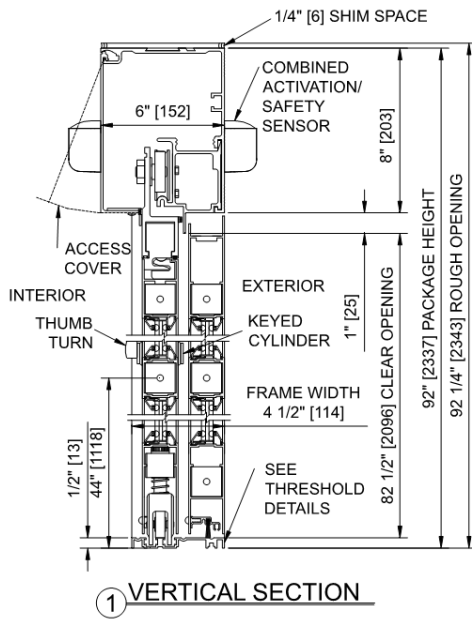




STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801, {1} {2}
Door Location: Exterior Door

Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP

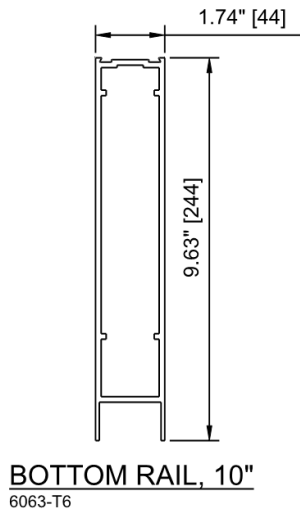

Detail-Transom not Selected in the Package

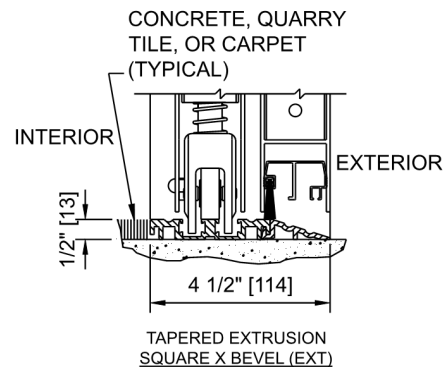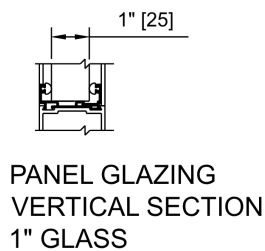

STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801
Door Location: Exterior Door

Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP

Door Details

Package Width	Masonry/Rough Opening Width	Clear Door Opening Width	Emergency Breakout	Package Height	Rough Opening Height
168.00	168.50	72.31	153.50	92.00	92.25

Options

Inclusions/Exclusions

Finish

COLOR OF DOOR PACKAGE CLEAR ANODIZED

Locking / Access Control

Lock Configuration Description CYLINDER/THUMBTURN
REQUIRED

Options and Accessories

Hardware Color CLEAR
BEST LOCK CYL W/CORE &
KEY,EXIT
Hardware Options INDICATOR,BOTTOM BALL
DETENT,TWO POINT LOCK
ROTARY SWITCH - 6
Switch and Control Options POSITION,DOOR POSITION
SWITCH,ALARM CONTACTS
Threshold Color CLEAR ANODIZED
THRESHOLD
Threshold Option SQUARE BEVEL 4.5
(CONTINUOUS)

Glass Specifications

SO Glass Thickness 1.000 "
SX Glass Thickness 1.000 "

Inclusions

Door package installation.
Glass & Glazing
Caulking

Exclusions

Delegated Design
120 volts AC to inside auto door header 5 amp min.
Cleaning and protection of installed material.
Permits & Inspections.
Prevailing Wage and/or Certified Payroll.
Structural Review (no seismic review)
Cleaning of installed materials.
Protection of installed materials.
Break metal
After hours premium labor
Union Labor

Exclusion Note

Transoms

Shop Drawing / Submittal Review

Date: _____

☐ No Exceptions Taken ☐ Furnish With Changes Noted ☐ Review and Resubmit ☐ Rejected

SUBMITTAL WAS REVIEWED FOR GENERAL CONFORMANCE TO THE CONTRACT DOCUMENTS. THE GENERAL CONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION, TECHNIQUES OF CONTRUCTION, COORDINATION OF THIS WORK WITH THE WORK OF OTHER TRADES, AND FULL COMPLIANCE WITH THE CONTRACT DOCUMENTS.





By: _____

Company: _____

STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801
Door Location: Interior Door


Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP

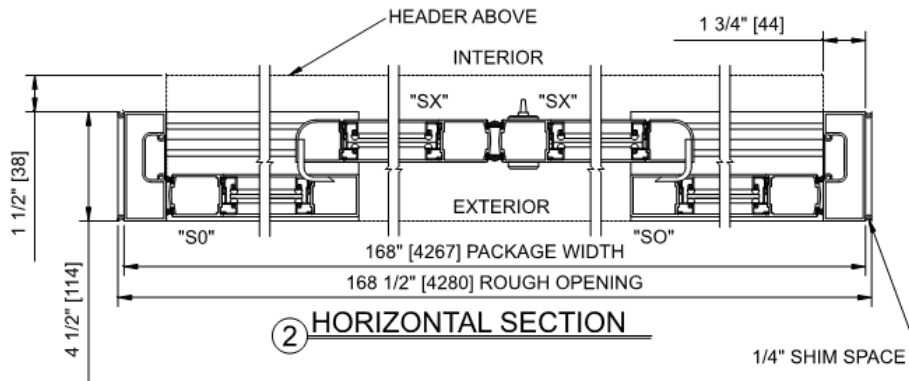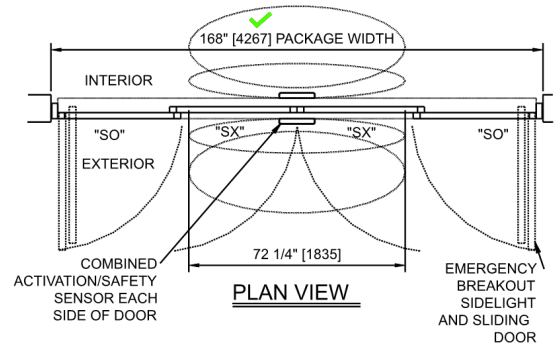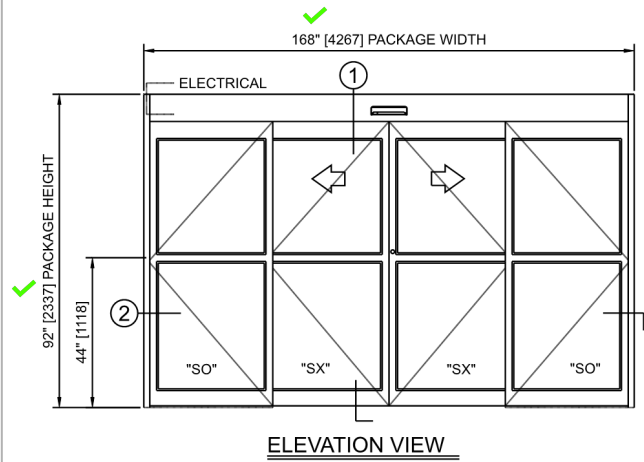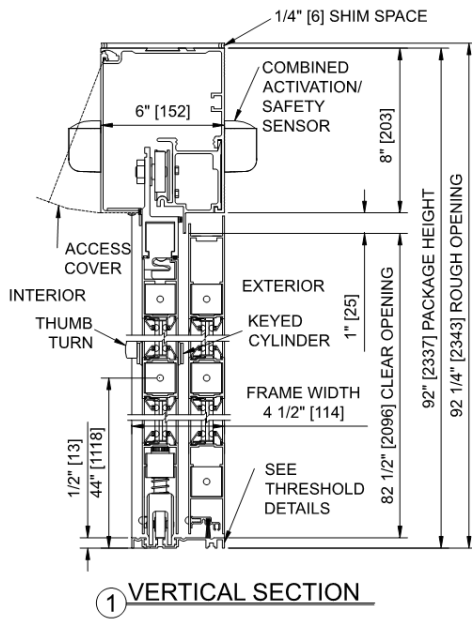


STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801, {1} {2}
Door Location: Interior Door


Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP



BOTTOM RAIL, 10"
6063-T6




MUNTIN BAR, 2"
6063-T6




STILE, NARROW
6063-T6


Detail-Transom not Selected in the Package



**PANEL GLAZING
SECTIONS**
1/4" GLASS

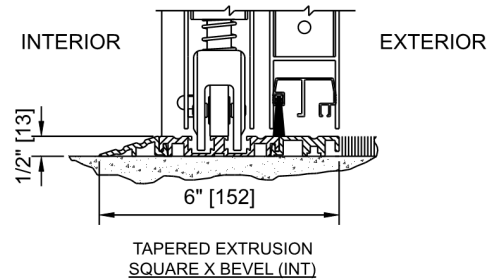

**THRESHOLD -ONE SIDE TAPERED
4 1/2" FRAME**



JAMB, 4 1/2"
6063-T6

STANLEY

Job Name: TJ Maxx - Pendleton, OR
Location: 1900 Southwest Court Avenue
Pendleton, OR 97801
Door Location: Interior Door

Job#: Q-279645 **Date:** Jul 22 2026
Product Qty: 1.00
Product: D/G3000 BP

Door Details

Package Width	Masonry/Rough Opening Width	Clear Door Opening Width	Emergency Breakout	Package Height	Rough Opening Height
168.00	168.50	72.31	153.50	92.00	92.25

Options

Inclusions/Exclusions

Finish

COLOR OF DOOR PACKAGE CLEAR ANODIZED

Locking / Access Control

Lock Configuration Description CYLINDER/THUMBTURN
REQUIRED

Options and Accessories

Hardware Color CLEAR
BEST LOCK CYL W/CORE &
Hardware Options KEY,EXIT
INDICATOR,BOTTOM BALL
DETENT,TWO POINT LOCK
Switch and Control Options ROTARY SWITCH - 6
POSITION,DOOR POSITION
SWITCH,ALARM CONTACTS
Threshold Color CLEAR ANODIZED
THRESHOLD
Threshold Option SQUARE BEVEL 6
(CONTINUOUS)

Glass Specifications

SO Glass Thickness 0.250 "
SX Glass Thickness 0.250 "

Inclusions

Door package installation.
Glass & Glazing
Caulking

Exclusions

Delegated Design
120 volts AC to inside auto door header 5 amp min.
Cleaning and protection of installed material.
Permits & Inspections.
Prevailing Wage and/or Certified Payroll.
Structural Review (no seismic review)
Cleaning of installed materials.
Protection of installed materials.
Break metal
After hours premium labor
Union Labor

Exclusion Note

Transoms

Shop Drawing / Submittal Review

Date: _____

☐ No Exceptions Taken ☐ Furnish With Changes Noted ☐ Review and Resubmit ☐ Rejected

SUBMITTAL WAS REVIEWED FOR GENERAL CONFORMANCE TO THE CONTRACT DOCUMENTS. THE GENERAL CONTRACTOR IS RESPONSIBLE FOR CONFIRMING AND CORRELATING DIMENSIONS AT JOBSITE FOR TOLERANCE, CLEARANCE, QUANTITIES, FABRICATION, TECHNIQUES OF CONTRUCTION, COORDINATION OF THIS WORK WITH THE WORK OF OTHER TRADES, AND FULL COMPLIANCE WITH THE CONTRACT DOCUMENTS.

By: _____

Company: _____
