


innovative turf solutions

Hydroseeding Demo Shallenberger Construction-New Mix #2 Commodore, PA 15729 August 15, 2013

100 lbs. seed
20 lbs. lime
12.5 lbs. 20-20-20 fertilizer
25 lbs. Tacking Agent 3 tackifier
2.5 gal. Hydro-Ultra Plus
750 lbs. 70/30 blend hydromulch
(Tank loaded per ITS' loading instructions)

Site was sprayed with New Mix #2 on August 16th (surrounding dirt areas were also sprayed with regular company blend on August 16th). Site as of August 26th sprayed with New Mix #2 (surrounding dirt area in picture was sprayed the same day with the regular company hydroseeding blend).

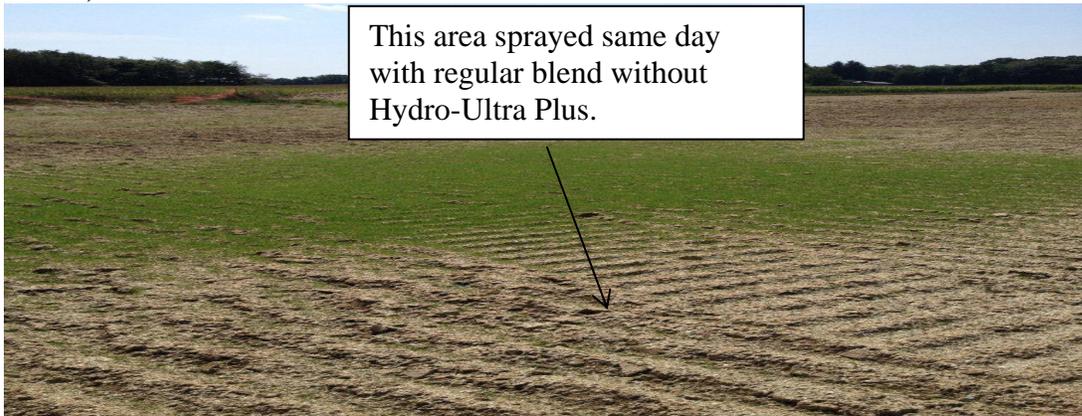

Germination began around 5 days after application on site sprayed with Hydro-Ultra Plus. Site sprayed on following day is just beginning to germinate at 1.5 weeks.
