
Melvich Hall Demolition

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		Set Up Site Welfare & Temp Heras	1 day	06/09/2021	06/09/2021	
2		Disconnet Water & Sewage after flushing	1 day	07/09/2021	07/09/2021	1
3		Erect Scaffold	2 days	07/09/2021	08/09/2021	1
4		Chimney Removal	1 day	09/09/2021	09/09/2021	3
5		Sinks & Fittings Removal - Plumber	1 day	10/09/2021	10/09/2021	4
6		Windows & Door Removal	1 day	10/09/2021	10/09/2021	4
7		Floor Removal (for safekeeping)	2 days	10/09/2021	13/09/2021	4
8		Asbestos Removal - Roof & Water Heater	3 days	14/09/2021	16/09/2021	7
9		Remove External Cladding	2 days	17/09/2021	20/09/2021	8
10		Remove Scaffold	1 day	21/09/2021	21/09/2021	9
11		Demolish Timber Structure & Remove from Site	2 days	22/09/2021	23/09/2021	10
12		Demolish Blockwork & Remove from Site	2 days	23/09/2021	24/09/2021	11FS-1 day
13		Break out Concrete Floor & Stonework	1 day	27/09/2021	27/09/2021	12
14		Landscape, lay Hard Core	2 days	28/09/2021	29/09/2021	13
15		Erect Stob & Wire Fence	2 days	30/09/2021	01/10/2021	14
16		Clear Site	2 days	30/09/2021	01/10/2021	14

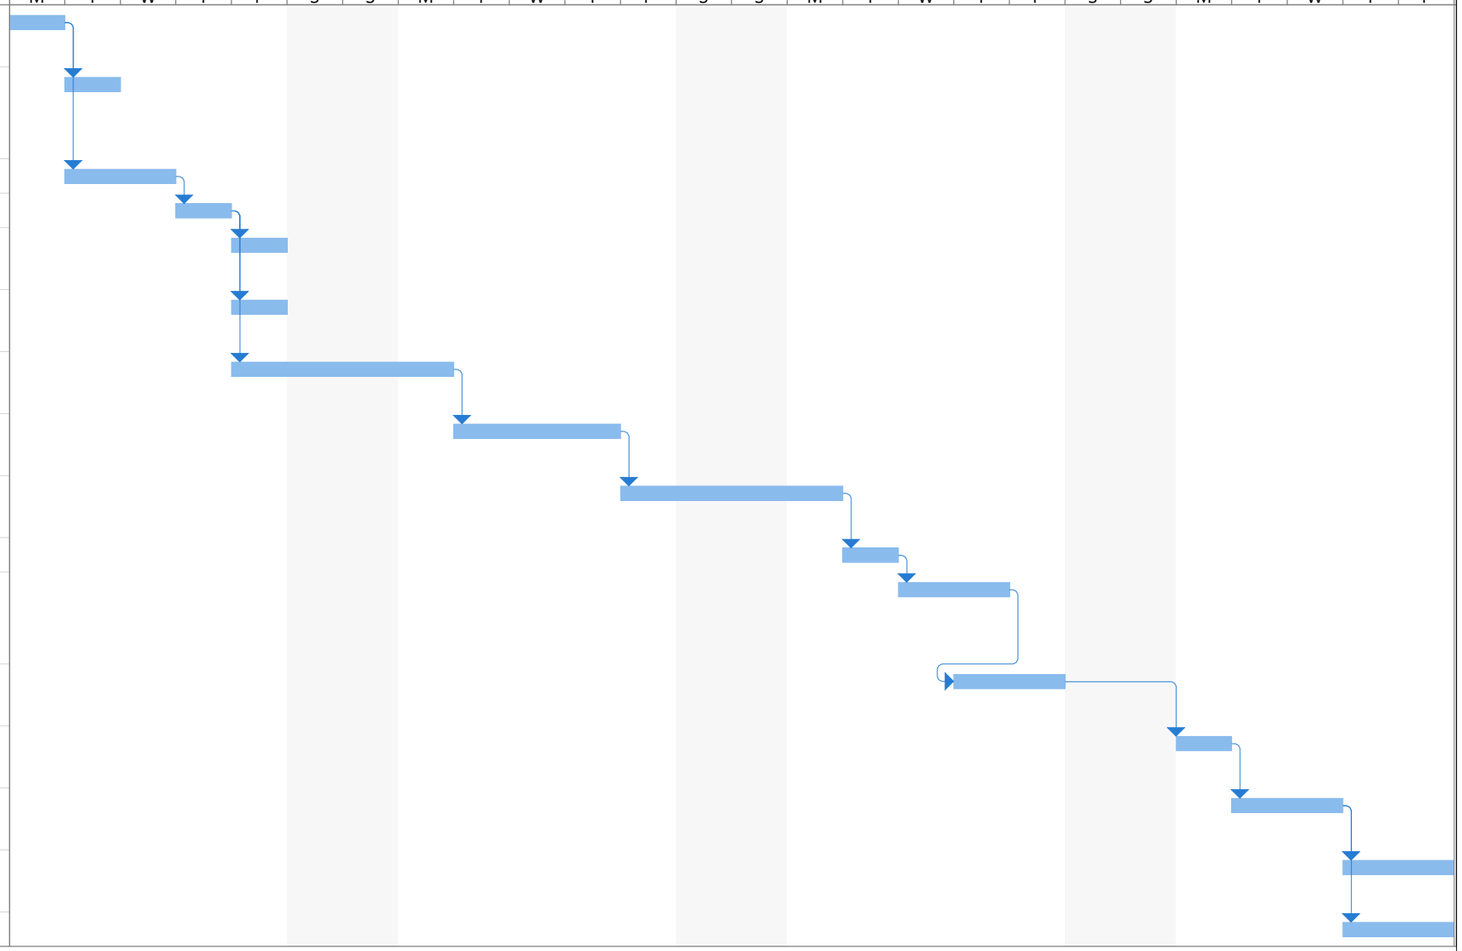

Project: Programme
Date: 28/06/2021

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone
