OPPORTUNITY #3 - WESTERN AVE. MEDIAN TREE PLANTING

Construction was completed for this Opportunity Summer 2017. The images on this page are taken from the Construction Documents that that were used to guide the installation of 43—24 inch box size trees in raised medians between 1st Street in the north to 19th Street in the south along Western Ave.

The project was funded by Council District 15 at approximately $150,000 to remove 10 ft. x 10 ft. sections of asphalt paving within these raised median areas. Two (2) species of small stature trees were selected in coordination with CD 15, and planted in an alternating pattern approximately 30 ft. apart. The planting area was then covered with 3 inches of shredded cedar mulch to conserve moisture within the soil.

Each tree will be watered from a water truck by Clean San Pedro 33 times per year for the first 3 years of establishment.

The two (2) species are:

1.Chinese Fringe tree

2.Crape Myrtle

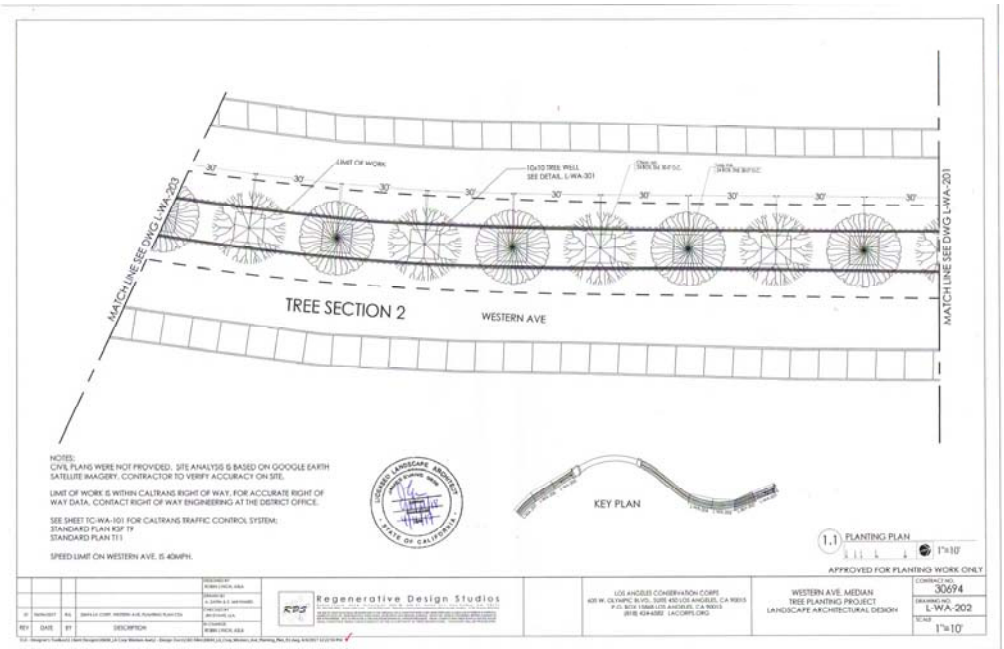

Chinese Fringe Tree

Crape Myrtle

SAN PEDRO GREEN OUTLETS & PATHWAYS
