

## REVISED PLAN TO COMPLETE LITTLE PARK + RESERVOIR PARK

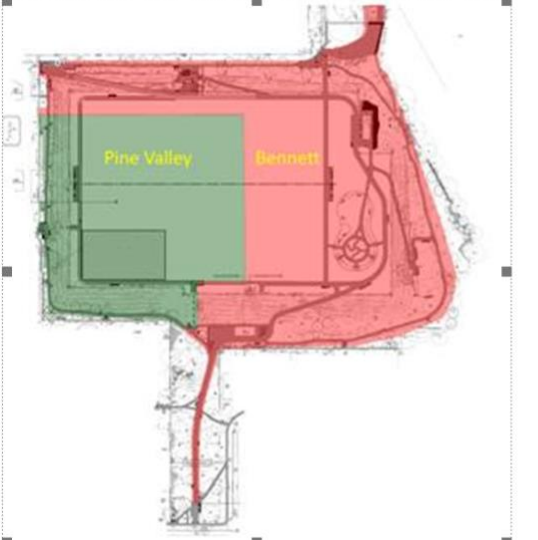
Proposal to the City for the following consideration to edit the Staging Plan that has already been proposed by the City. A redefined Staging Process with the objective of removing all hoardings, and opening each of three distinct stages of work for public use once construction is complete, as follows:

**Little Park:** complete and Opened on or before Labour Day, 2021 (18 weeks)

**West Reservoir Park** – complete and Opened by March, 2022 (29 weeks)

**East Reservoir Park** – complete and Opened by July 1, 2022 (19 weeks)

### STAGE 1: April 28 to Mid-May, 2021: ( 90% COMPLETE)

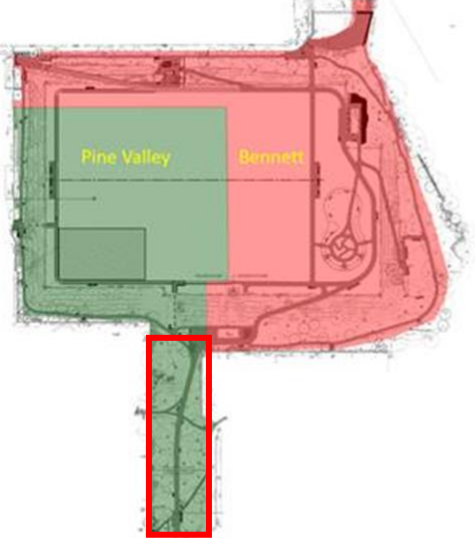
	<p><b>Stage 1: April 28 to mid-May, 2021</b></p> <ul style="list-style-type: none"><li>• Pine Valley to work in west side of park</li><li>• Fast fencing around Pine Valley (within existing hoarding)</li><li>• Pine Valley to receive deliveries via Jackes Ave</li><li>• Email Update to Community</li></ul> <p>From April to late July, Bennet will complete the washroom, ramps from Rosehill to Upper Path, Memorial Garden structures.</p>
--	---

**Pine Valley** completes Stage 1 by mid-May, 2021

**Bennett** completes its work by end of July, 2021

**Note:** All deliveries to and from Site are now limited to **Jackes** and **Rosehill/Avoca** and **NOT Summerhill** so Central Temporary Wood Fence is demolished. **Interim Summerhill Fair** to be held in late June in cordoned off area of Little Park and/or adjacent Streets.

## STAGE 2: Mid May – Labour Day:

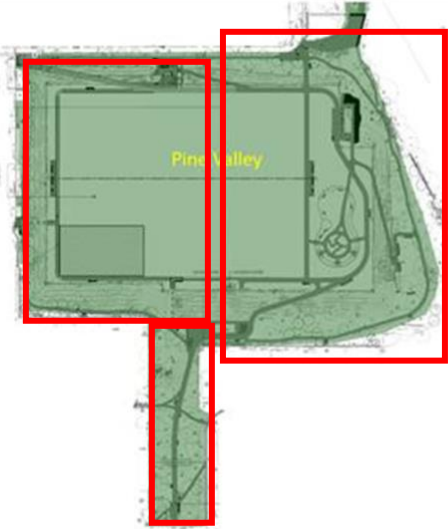
	<p><b>Stage 2: Mid-May to late July, 2021</b></p> <ul style="list-style-type: none"><li>• Pine Valley to move into Little Park &amp; continue working in west side</li><li>• Fast fencing will enclose Little Park</li><li>• Pine Valley trailer located in south-west corner of park (shaded rectangle to be confirmed) via Summerhill</li><li>• Construction Notice will be provided in early May (ASAP) &amp; Email Update</li><li>• Woodlawn Property Owner letter (for east-west secondary path)</li><li>• Pine Valley deliveries via Jackes and Summerhill (parking flyer will be provided for the on-street parking spots)</li><li>• Bennet deliveries via Rosehill/Avoca</li></ul>
---	--

**Pine Valley** starts and completes work on **Little Park only** (including Central Walkway, Woodlawn-to-Summerhill-Gardens path, Sodding, benches, waste bins, etc.) by **Labour Day, 2021**. **Little Park** to be fenced off at its North End from Rosehill Reservoir Park

**Bennett** completes its work by end-July, 2021

**Note:** All deliveries to and from Site are now limited to Jackes and Rosehill/Avoca and NOT Summerhill so the Central Temporary Wood Fence can be demolished. Interim Version of **Summerhill Fair** to be held in late June in cordoned off area of Little Park and/or adjacent Streets.

## STAGE 3: Labour Day 2021 – July 1, 2022:

STAGE 3.1	STAGE 3.2
	<p><b>Stage 3: August 2021 to Summer 2022</b></p> <ul style="list-style-type: none"><li>• No changes to hoarding</li><li>• Pine Valley deliveries via Jackes, Rosehill/Avoca, Summerhill</li><li>• There will be a slow-down in work over the winter</li></ul>

### STAGE 2: LITTLE PARK

**Pine Valley** completes work on **Rosehill Reservoir Park** in two Stages – **Stage 3-1 Western Res Park (opens March 2022)** and **Stage 3-2: Eastern Res Park (Opens July 1, 2022)**

This all predicated on the City's and the Contractors likely requirement to maintain peripheral but fencing around each stage of the work
