JOBDRIVER

Font : Haettenschweiler

Font ratio: Letters J and D are size 48 and all other letters are size 36

Colors: Black and orange letters only

Author: (Trip) Syd W. Smith III

Date: 9/16/19

JobDriver / CONSTRUCTION PRODUCTIVITY SOFTWARE APPLICATION NARRATIVE DESCRIPTION
DATE 8/19/19 – Author – (Trip) Syd W. Smith III - CONFIDENTIAL

Introduction

The names "JobDriver" and "software" are used interchangeably to describe the product throughout. JobDriver is a construction productivity matrix. Construction is very limited when it comes to technical tools in the industry. Data is collected at a selected interval and displayed over time to provide a visual dashboard of jobsite or project production. JobDriver makes it easy to see a wide array of valuable productivity information and importantly JobDriver highlights areas of inefficiency where work could be happening, but is not.

How it works – ATTACHED EXHIBIT A

A basic template allows for information on an x, y and/or z axis to display production information in 2D, 3D or as a model. Area information at a minimum is populated on an x and y axis to provide coordinates or detail for a location, or percent complete on y axis and plan numbers with activities for a trade on the x axis. The display can mimic actual project shape, plan grid, thermometer style, or custom. Second tier or additional location details are provided on an axis to help drill down specific locations. However the template is set the productivity matrix is by trade and trade specific activities are populated along a chosen axis to track for that trade. Field personnel verify the certain activities are complete for a trade. By populating complete items over a selected time period represents production or measures productivity for that trade. The trades are linked so that completion of one activity by a trade highlights that work is available for another following trade. The software synchronizes trades and the flow of work to produce a live productivity matrix. Parties can be notified that work is available. The software tracks and creates a history of how long work is available. Notification can be shared over a project group for accountability to the project. Few markets or industries lend themselves to such valuable, actual measurable productivity as the construction industry.

Results

Productivity information in construction is paramount. The JobDriver dashboard allows management to see an enormous amount of vital information all on one dashboard. All trades and their activities are included for the entire project. Production rates are key to managing manpower at a cost-effective level. An all to common problem in construction projects are the items and areas of work that remain stagnant or areas of work that could be completed and no one is working there. There is always an area management walks by and thinks "why is this or that item not done", or "why isn't anyone working here". JobDriver creates a real productivity dashboard of what is happening and highlights what is not happening. There is enormous value in the number of work areas that sit inactive for great lengths of time. JobDriver can identify a problem area and provide a reason something has stopped. Moreover, most importantly JobDriver highlights areas of work that could be progressing and are not.

Conclusion

JobDriver increases production exponentially. JobDriver is a unique tool in the construction industry, which currently has limited technical tools. It can identify and highlight unproductive areas and activities and cut them multifold. JobDriver provides a visual dashboard of the most vital project information related to productivity in construction projects. JobDriver optimizes productivity and indisputably increases profitability.

BAY PAINTING PROGRESS CHART

FLOOR	26 Unit	28 Unit	24 Unit	27 Unit	25 Unit	22 Unit	23 Unit	21 Unit	20 Unit
18	N/A								
17									
16									
15									
14									
13									
12									
11									
10									
9									
8									
7									
6									
5									
4									
3								N/A	
2			N/A						
	Prep / Point -Agent WC DBL Vanity Bath WC Single Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath WC Single Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath WC Single Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath WC Single Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath WC Single Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated	Prep / Point -Agent WC DBL Vanity Bath Accent wall painting Doors and Frames Prime Paint Walls Base Coat Walls Finish Coat Walls Misc Trim and Valence Caulking Popcorn Balcony Finish Coated

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12
AREAS AVAILABLE FOR YOU TO WORK
* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

BAY PAINTING PROGRESS CHART

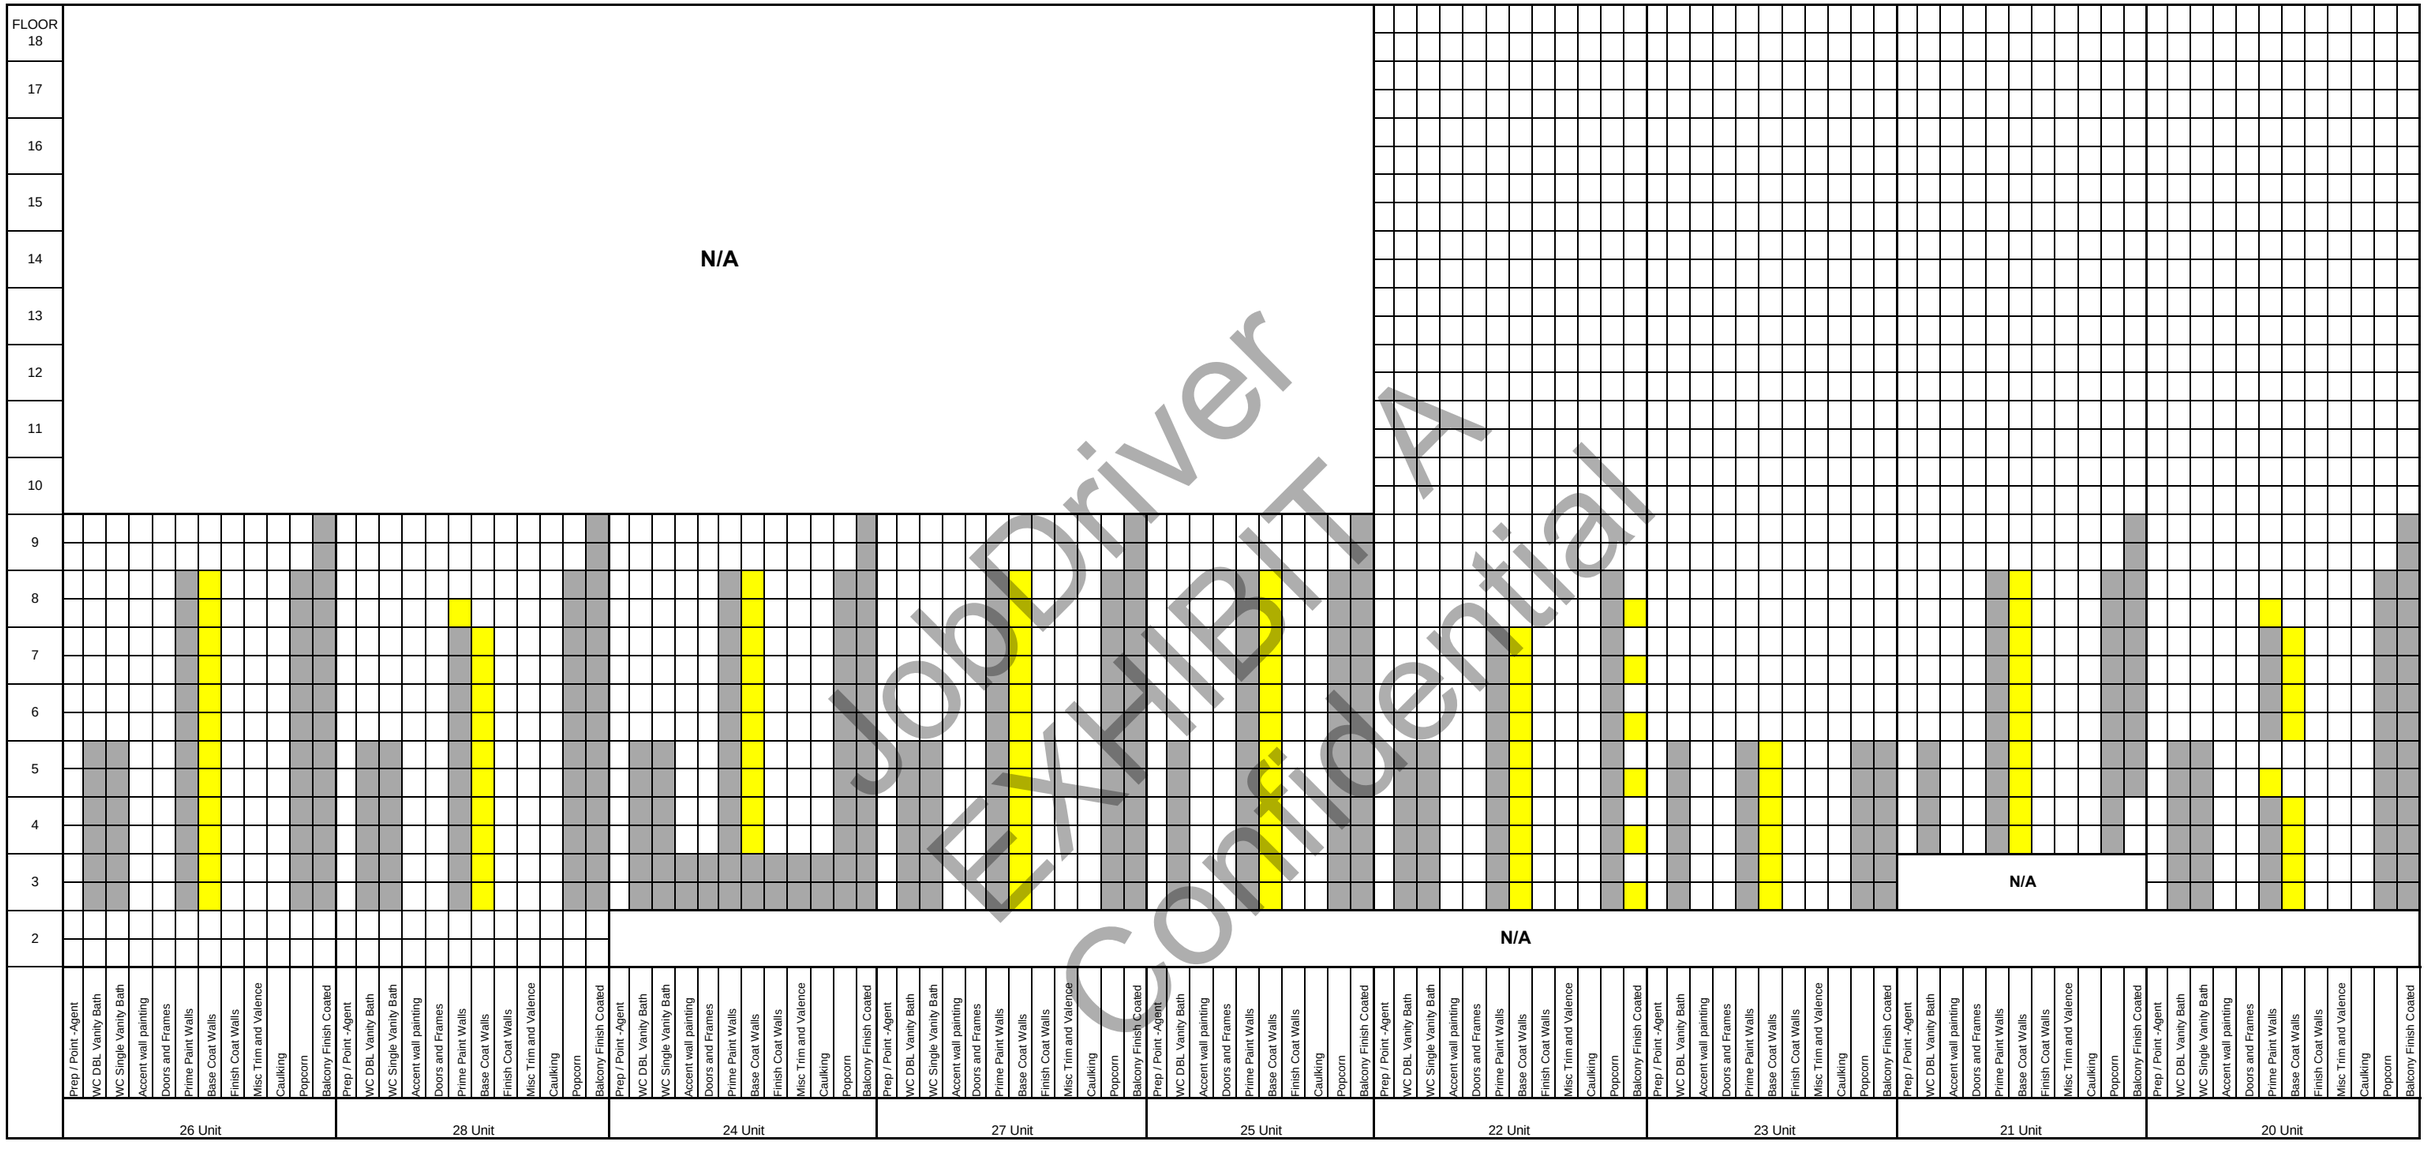

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12

AREAS AVAILABLE FOR YOU TO WORK

* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

BAY PAINTING PROGRESS CHART

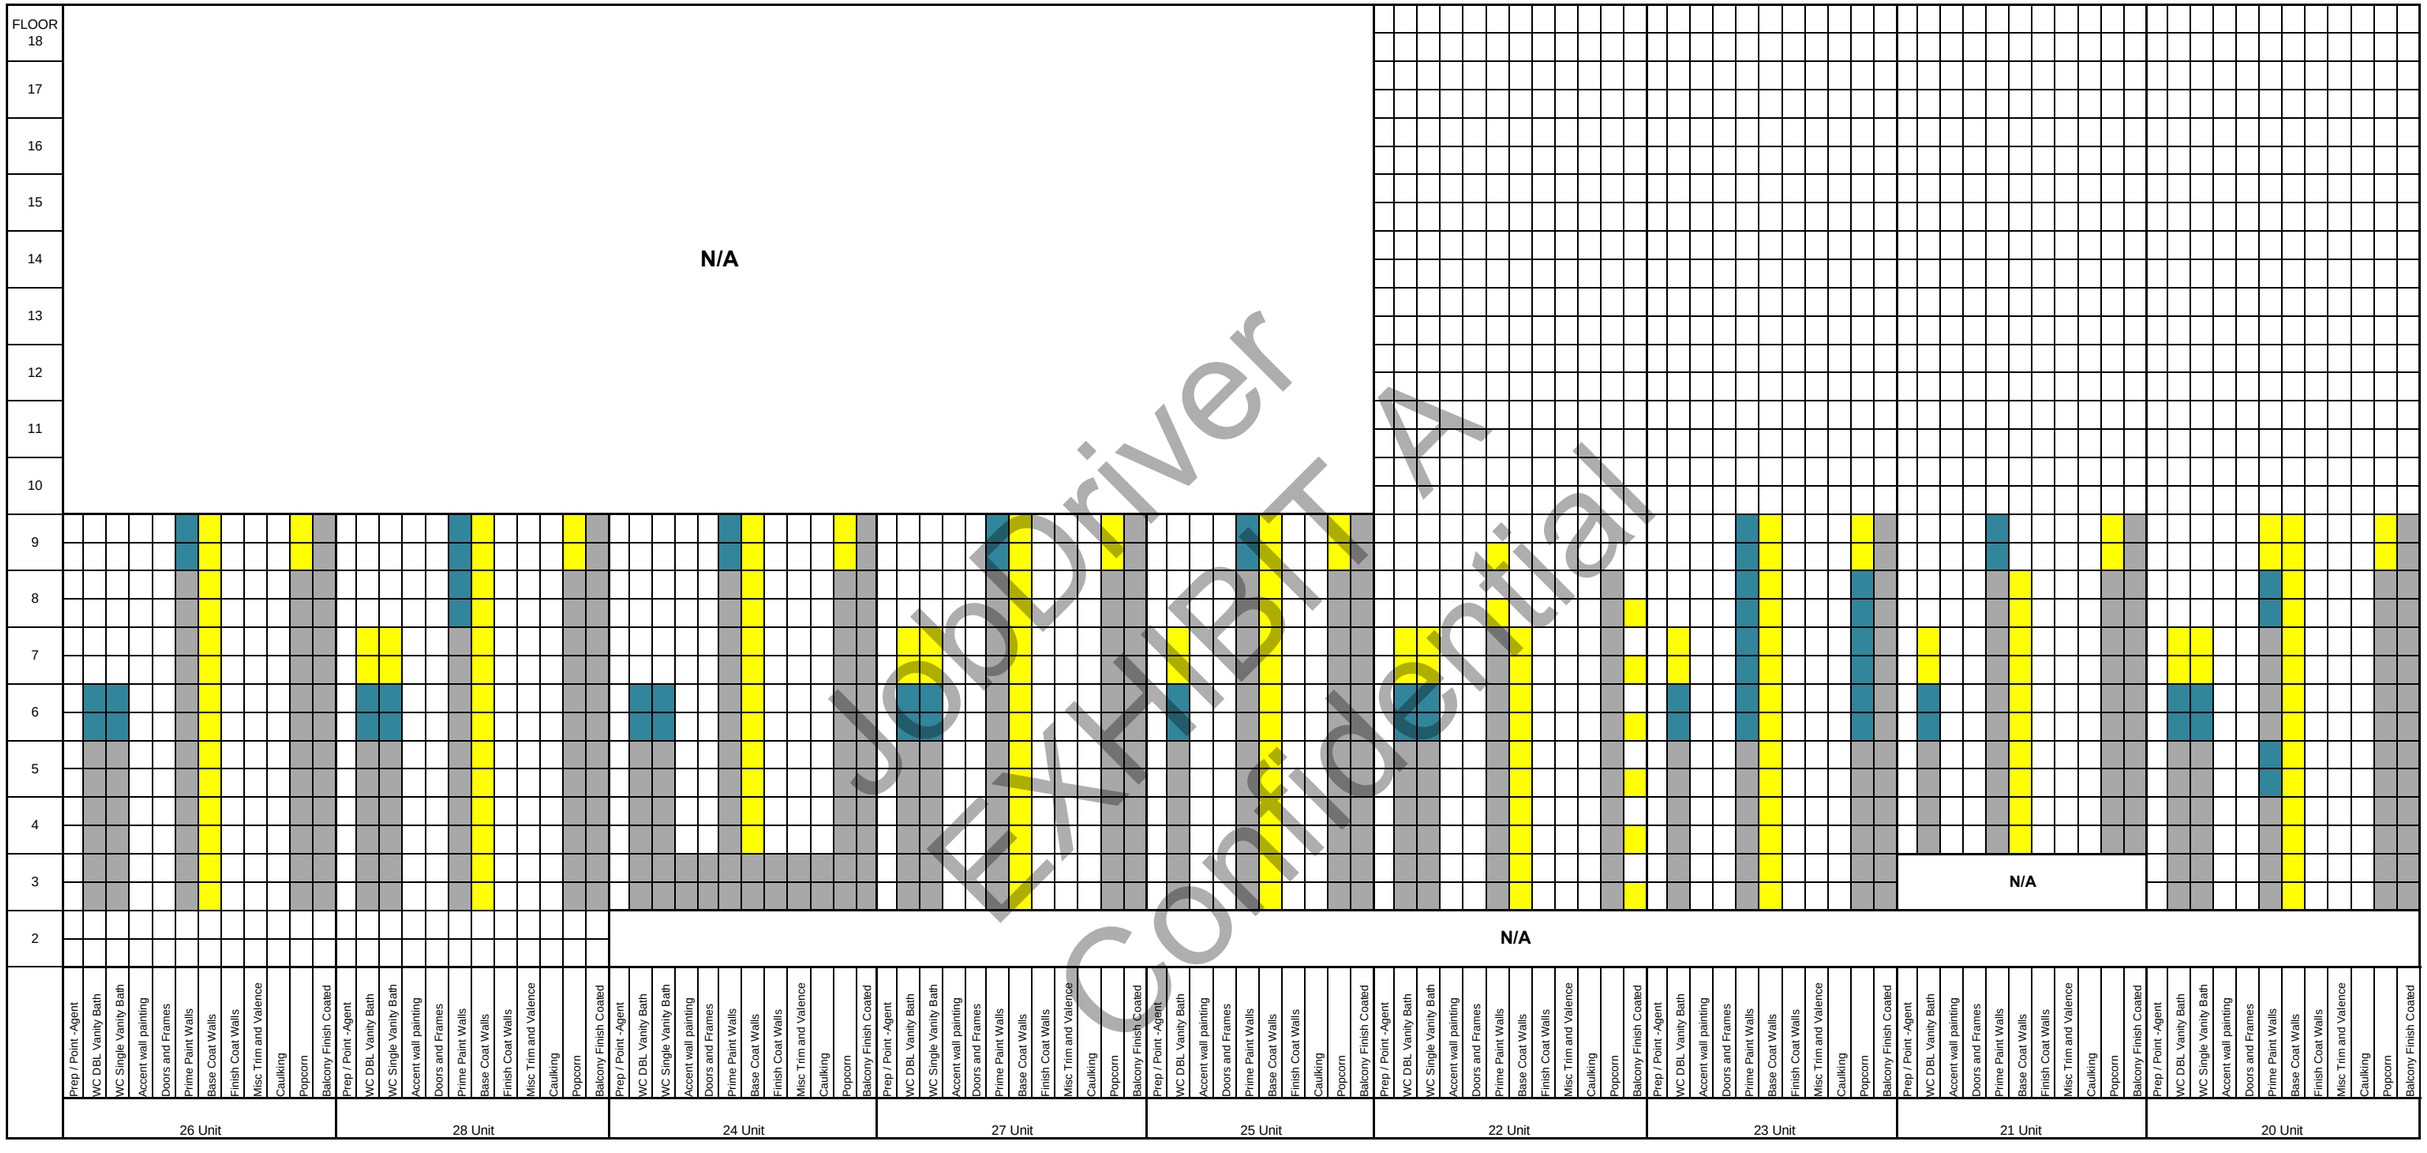

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12

BAY PAINTING PROGRESS CHART

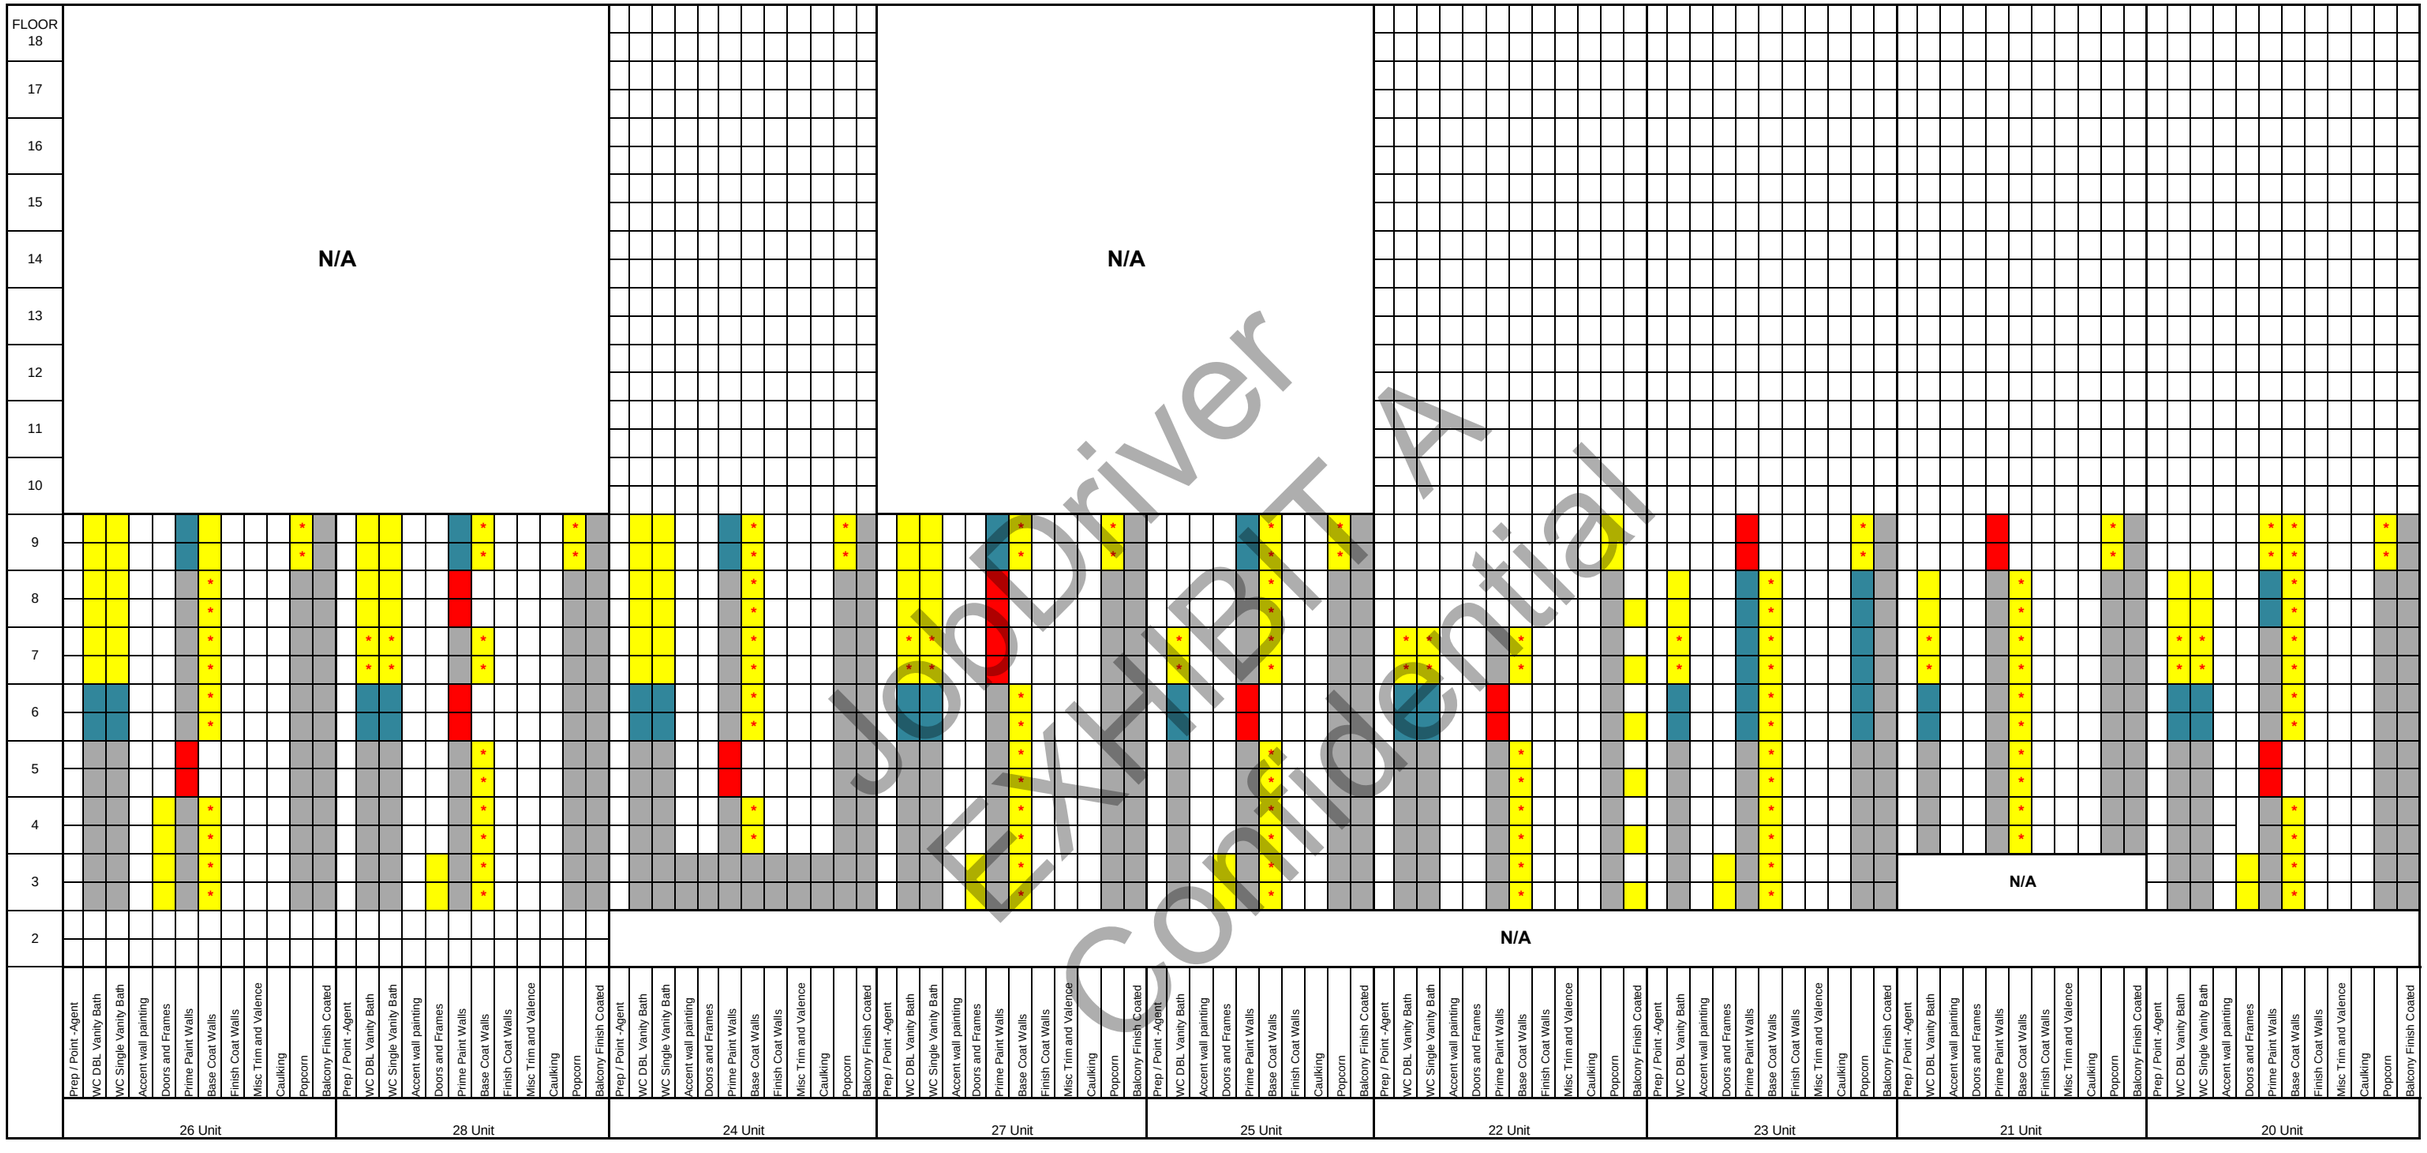

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING

BAY PAINTING PROGRESS CHART

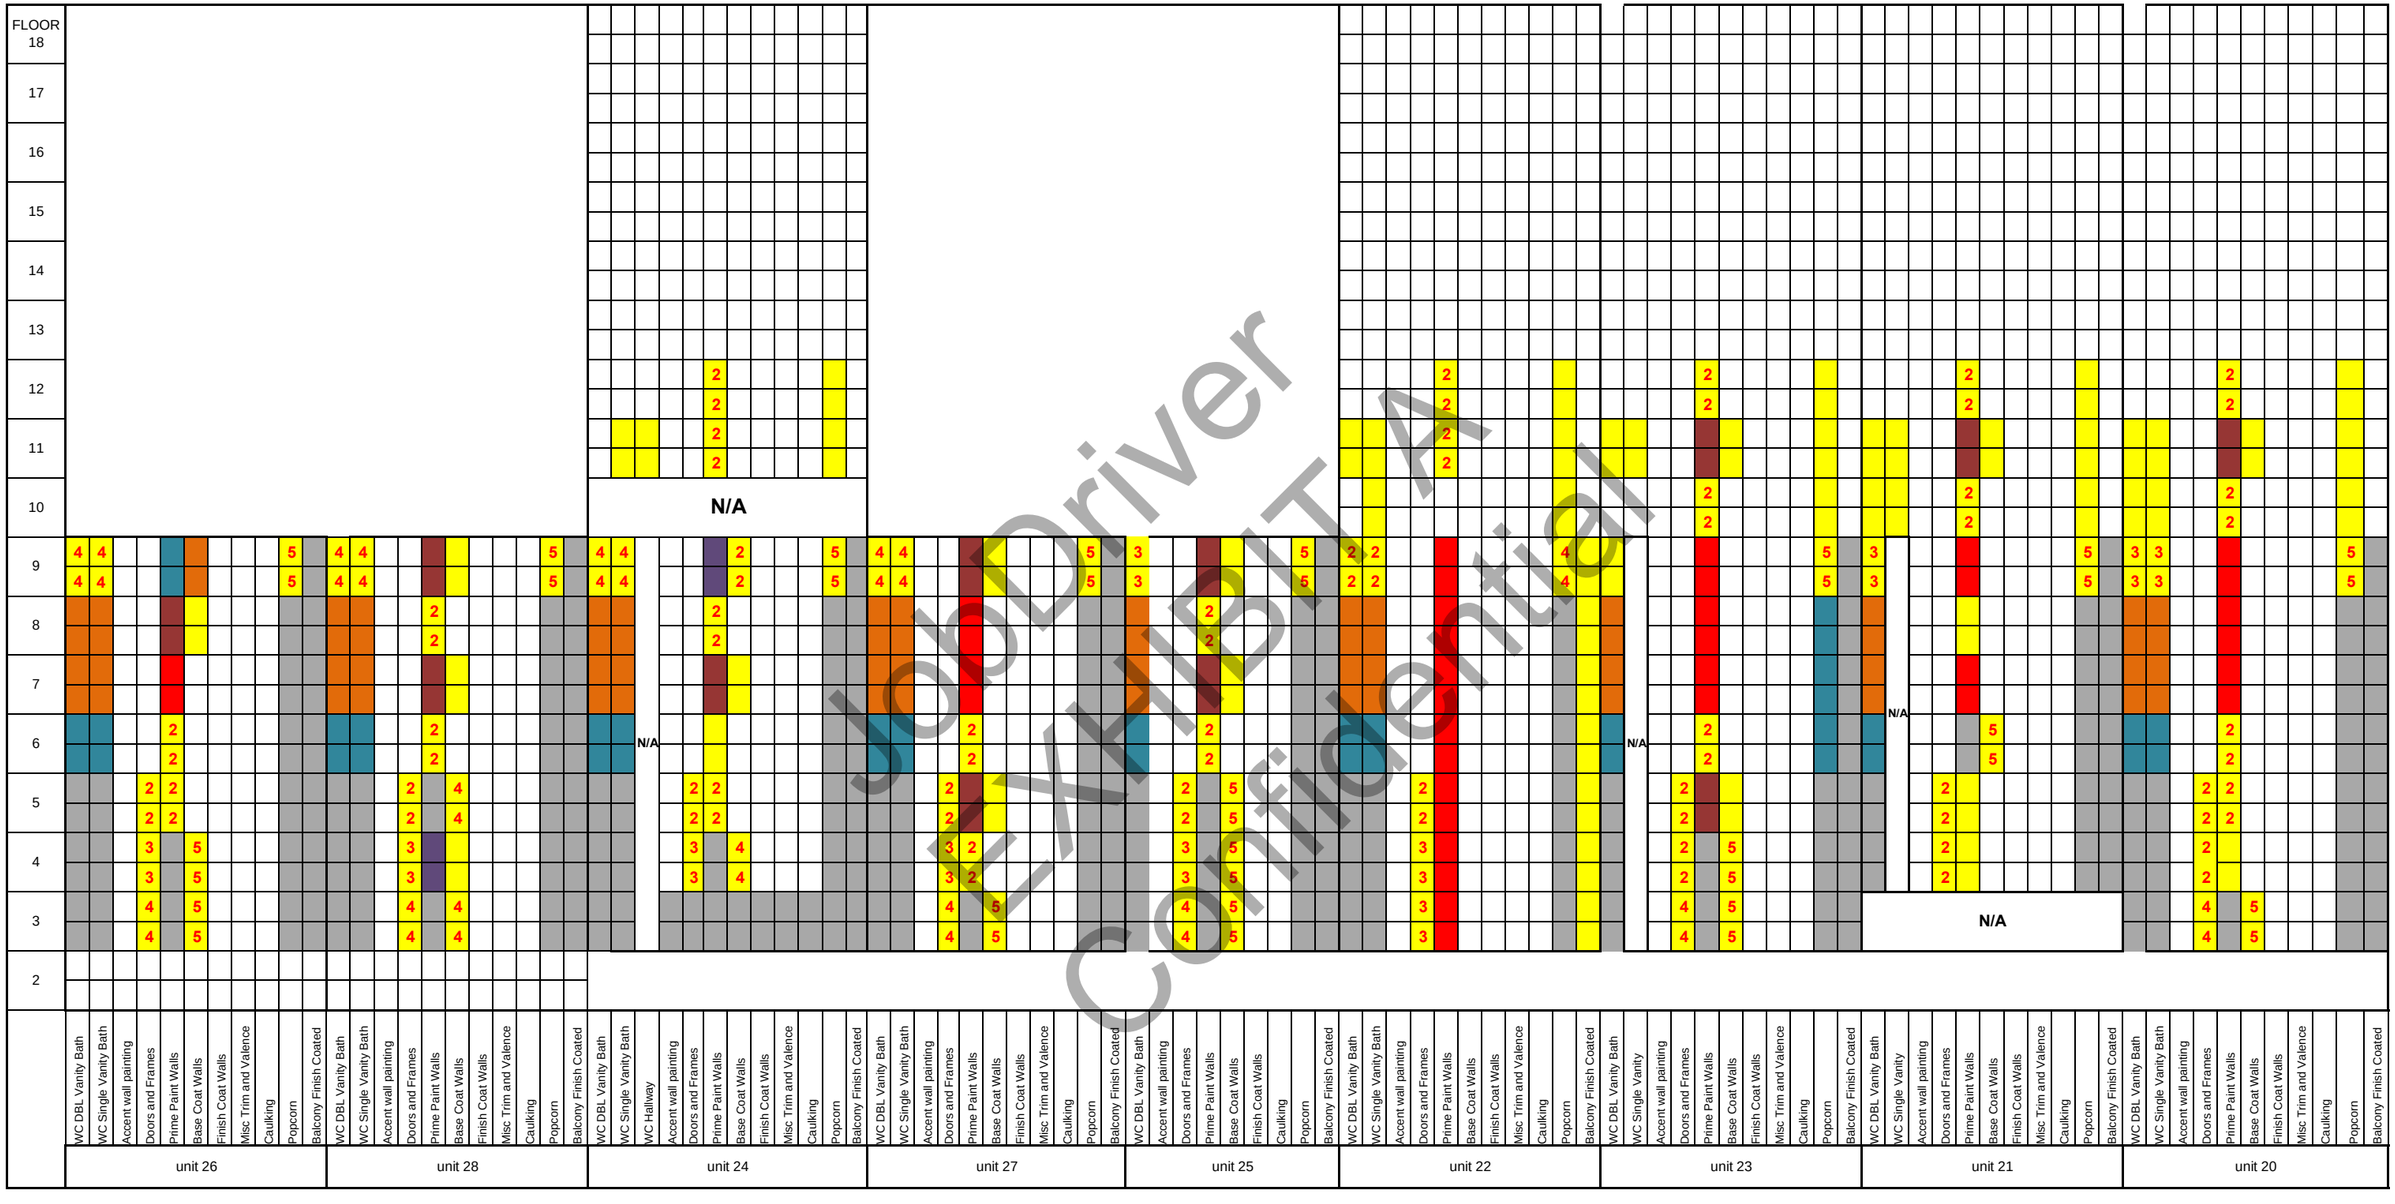

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2011
- WORK COMPLETE TO DATE 2/20/2011

BAY PAINTING PROGRESS CHART

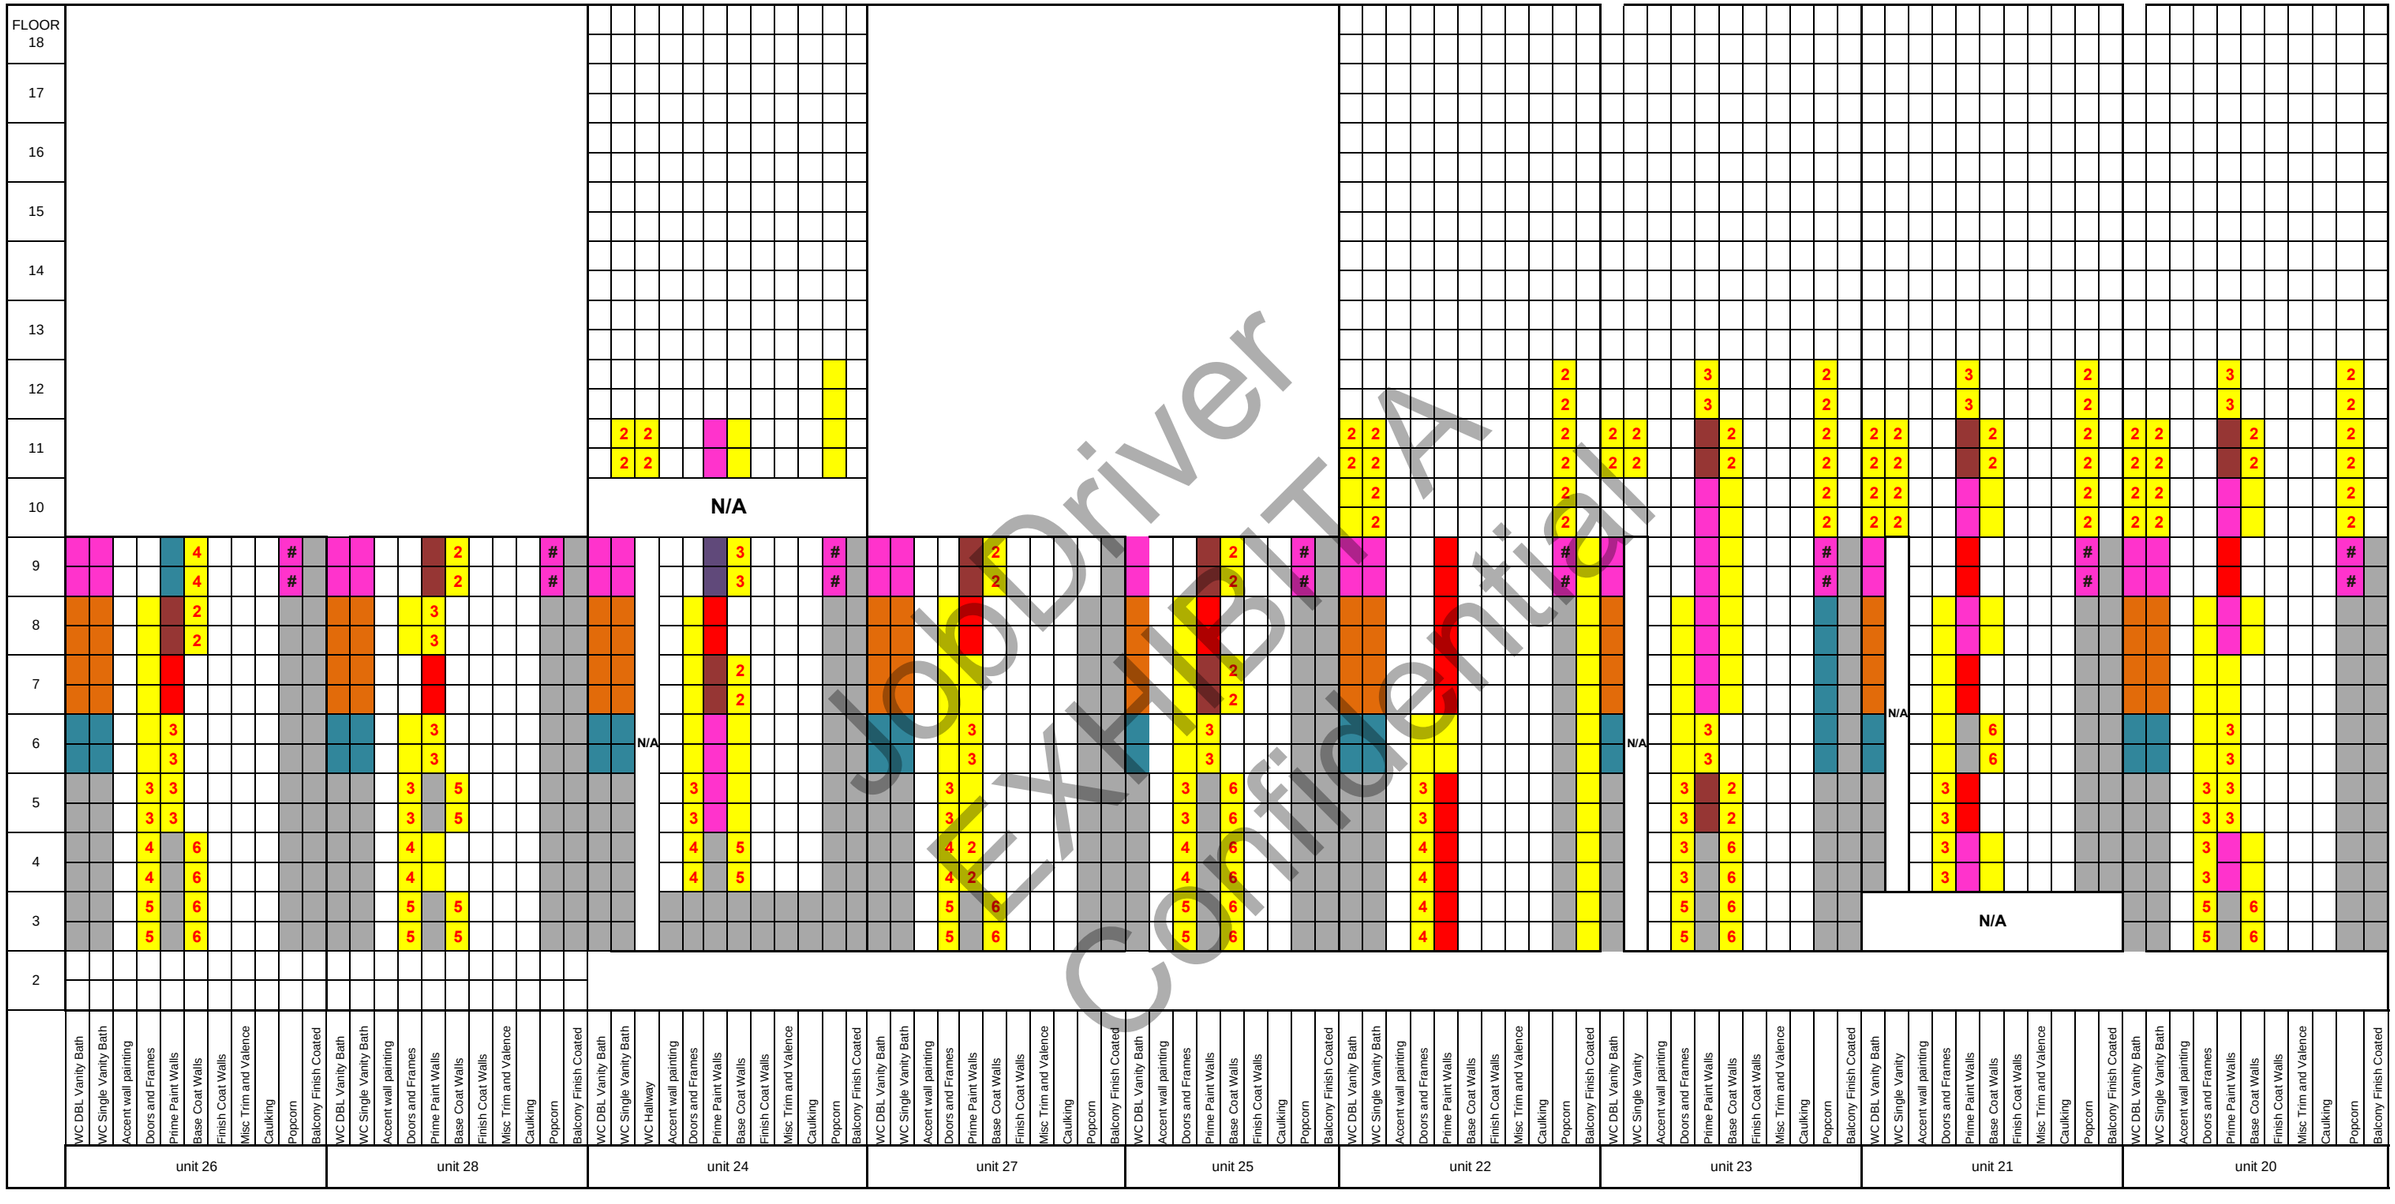

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012

BAY PAINTING PROGRESS CHART

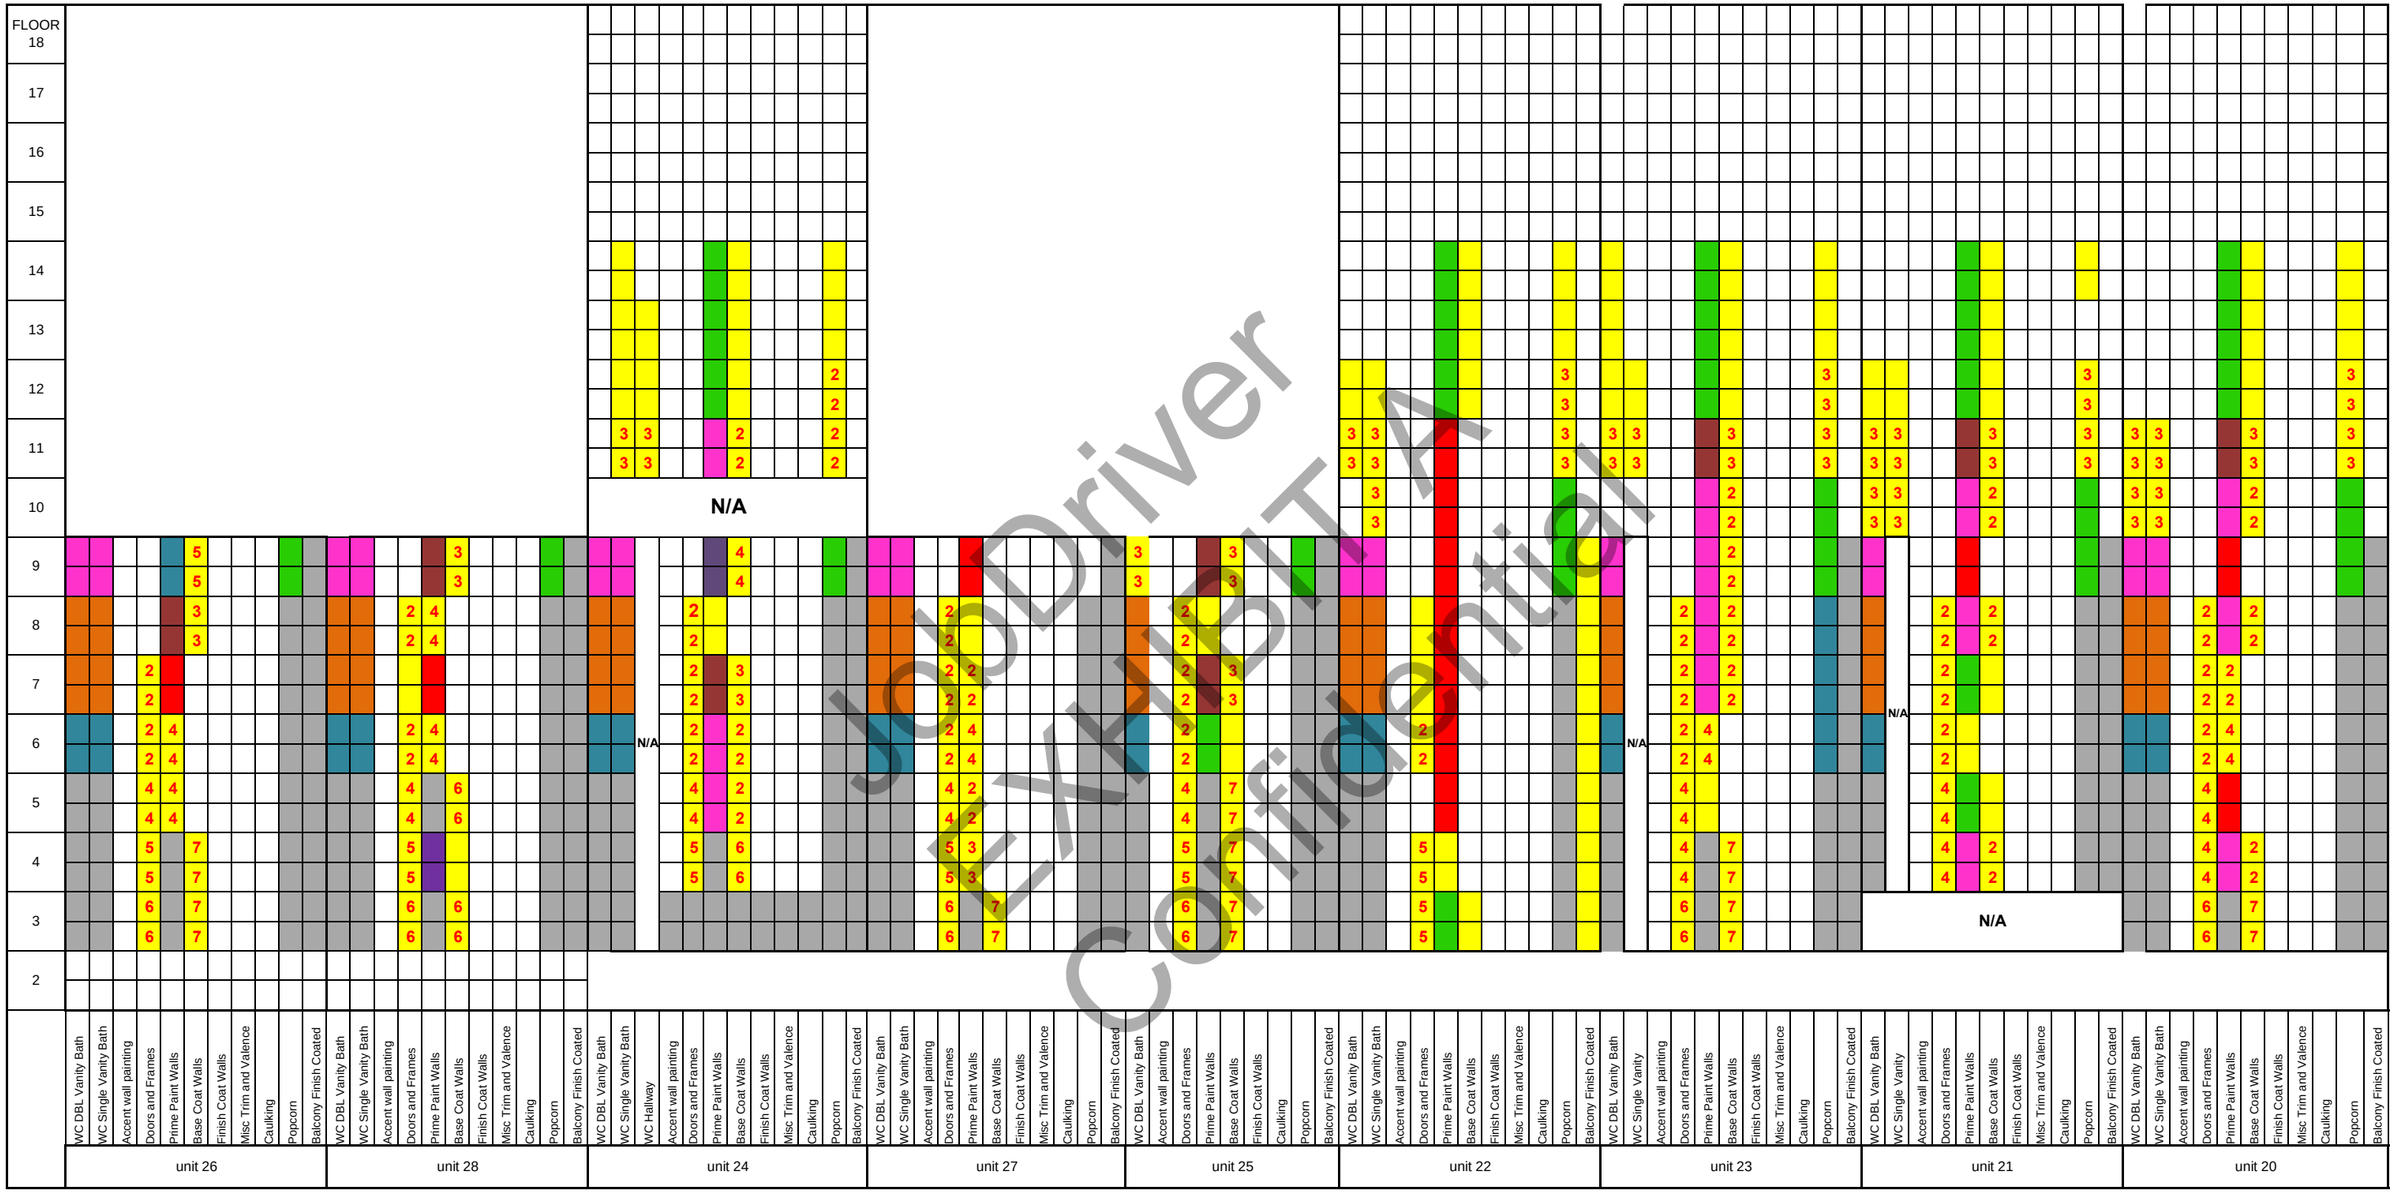

JobDriver EXHIBIT A Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012

BAY PAINTING PROGRESS CHART

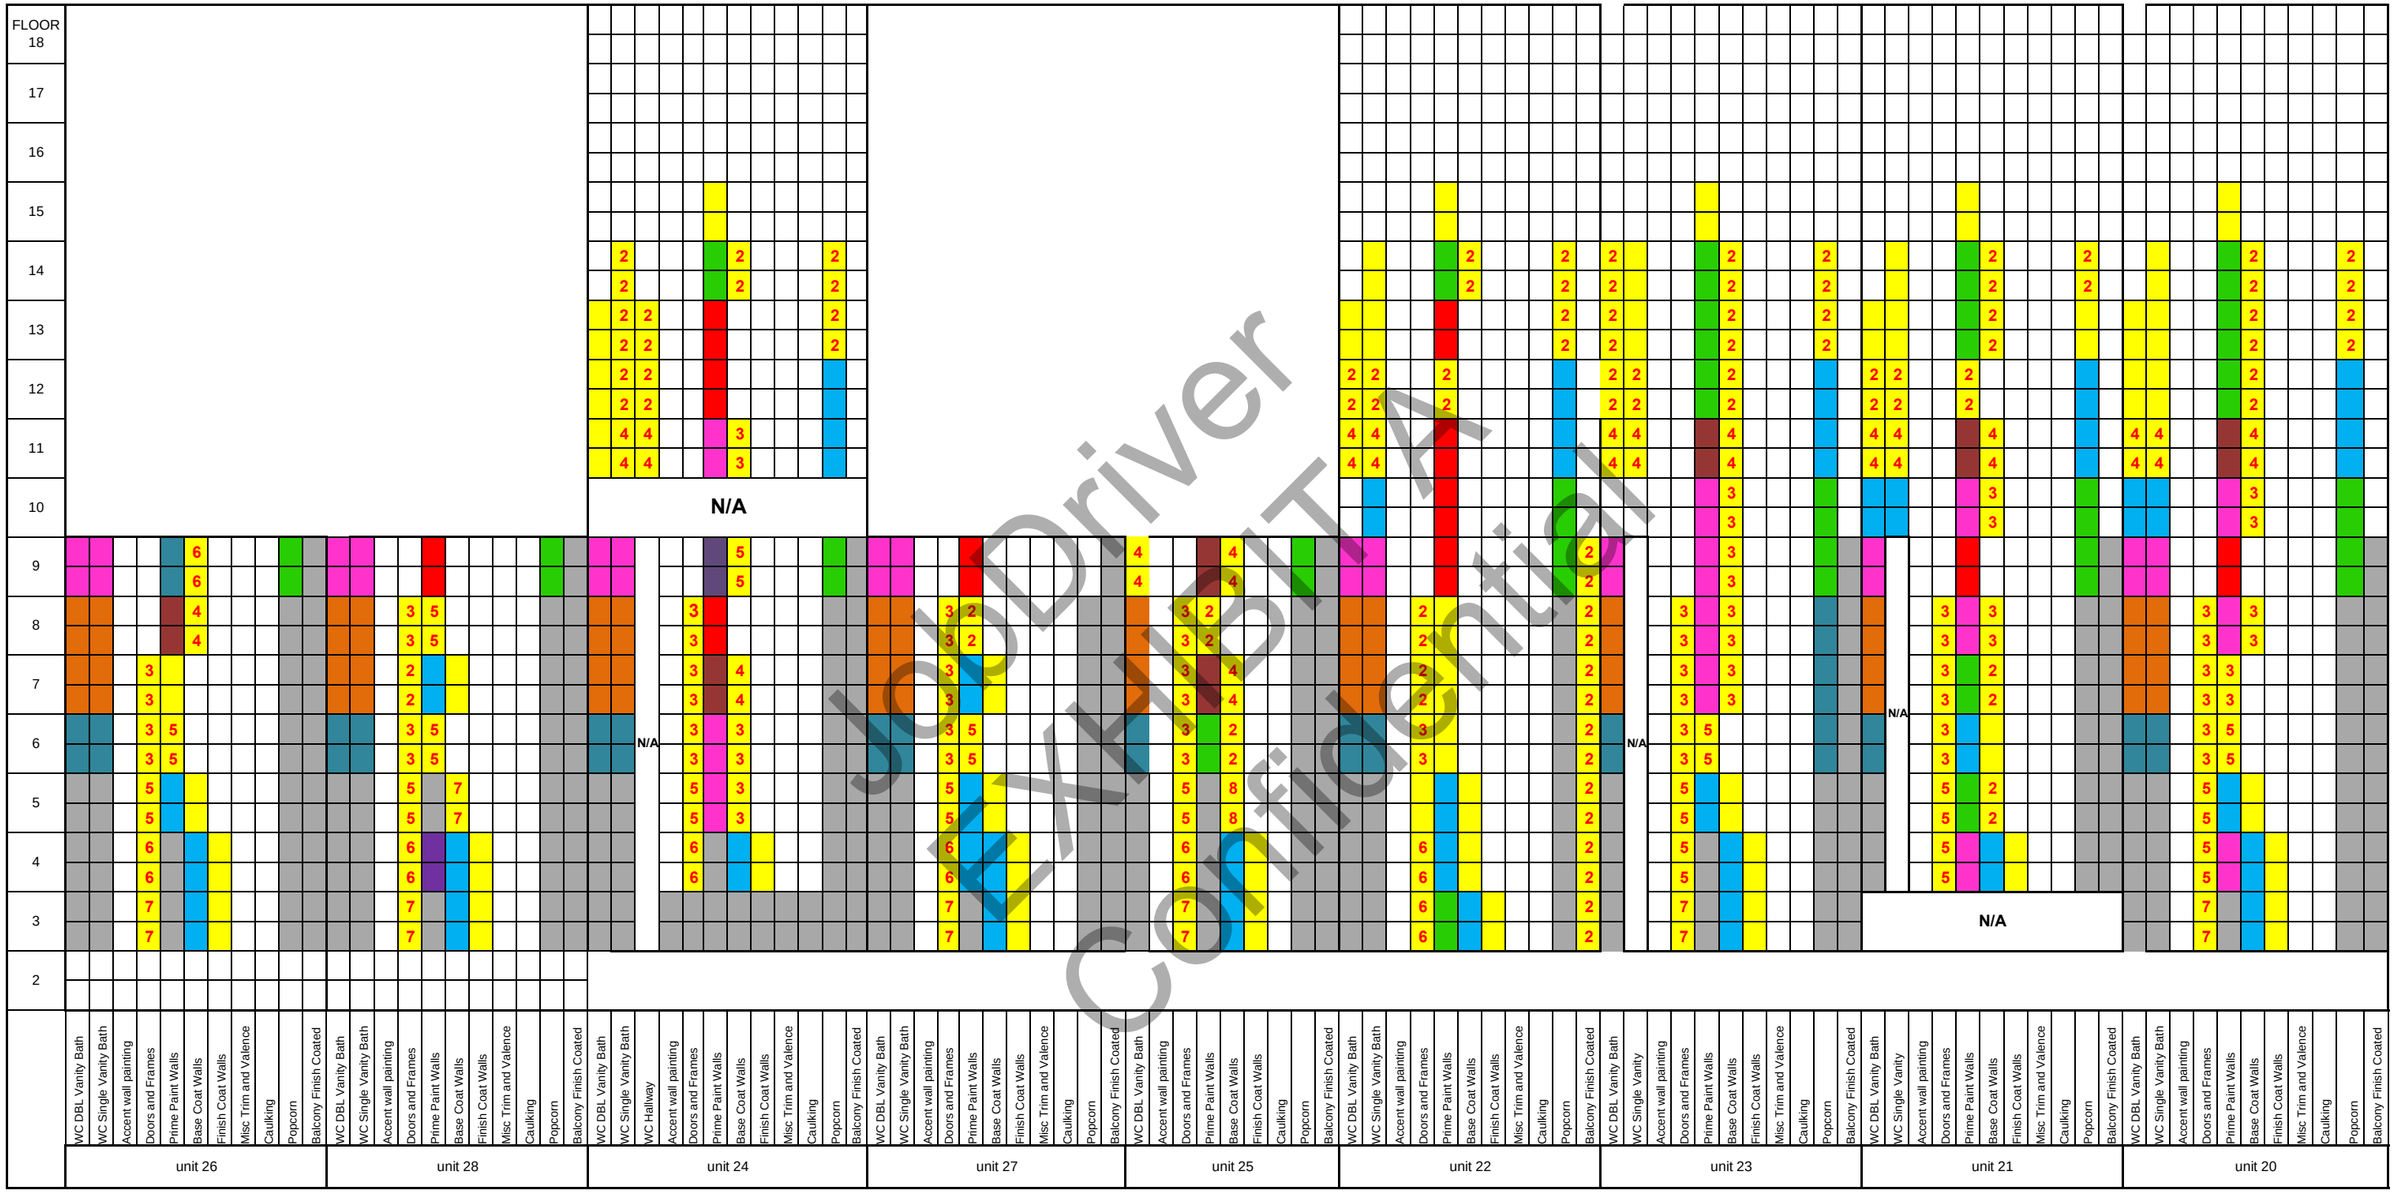

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012

BAY PAINTING PROGRESS CHART

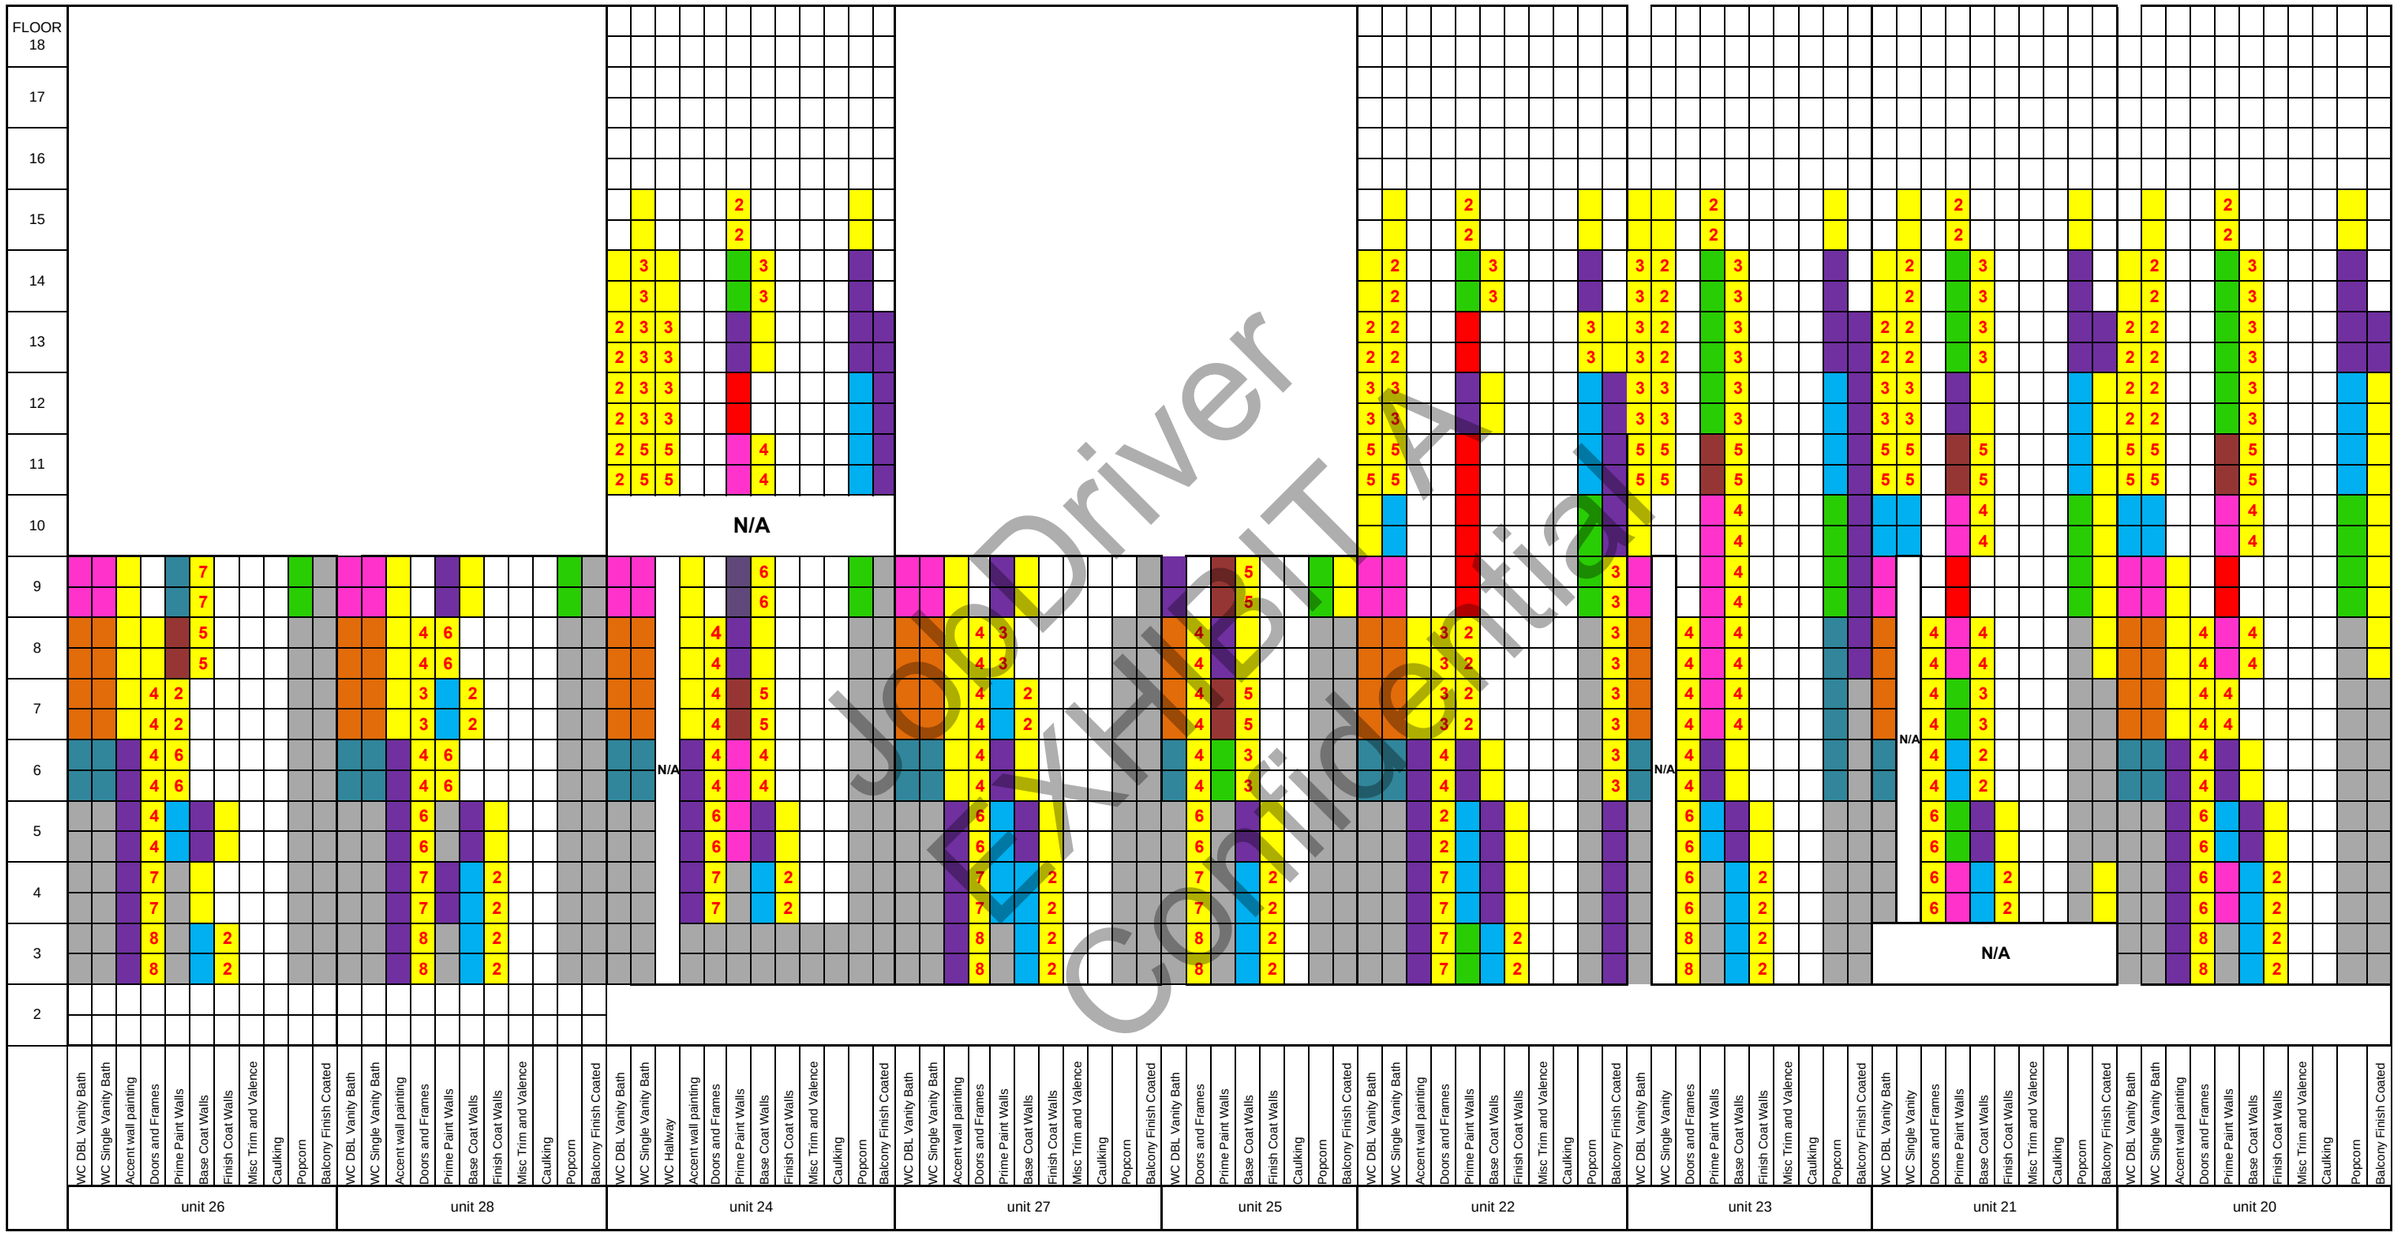

logDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012

BAY PAINTING PROGRESS CHART

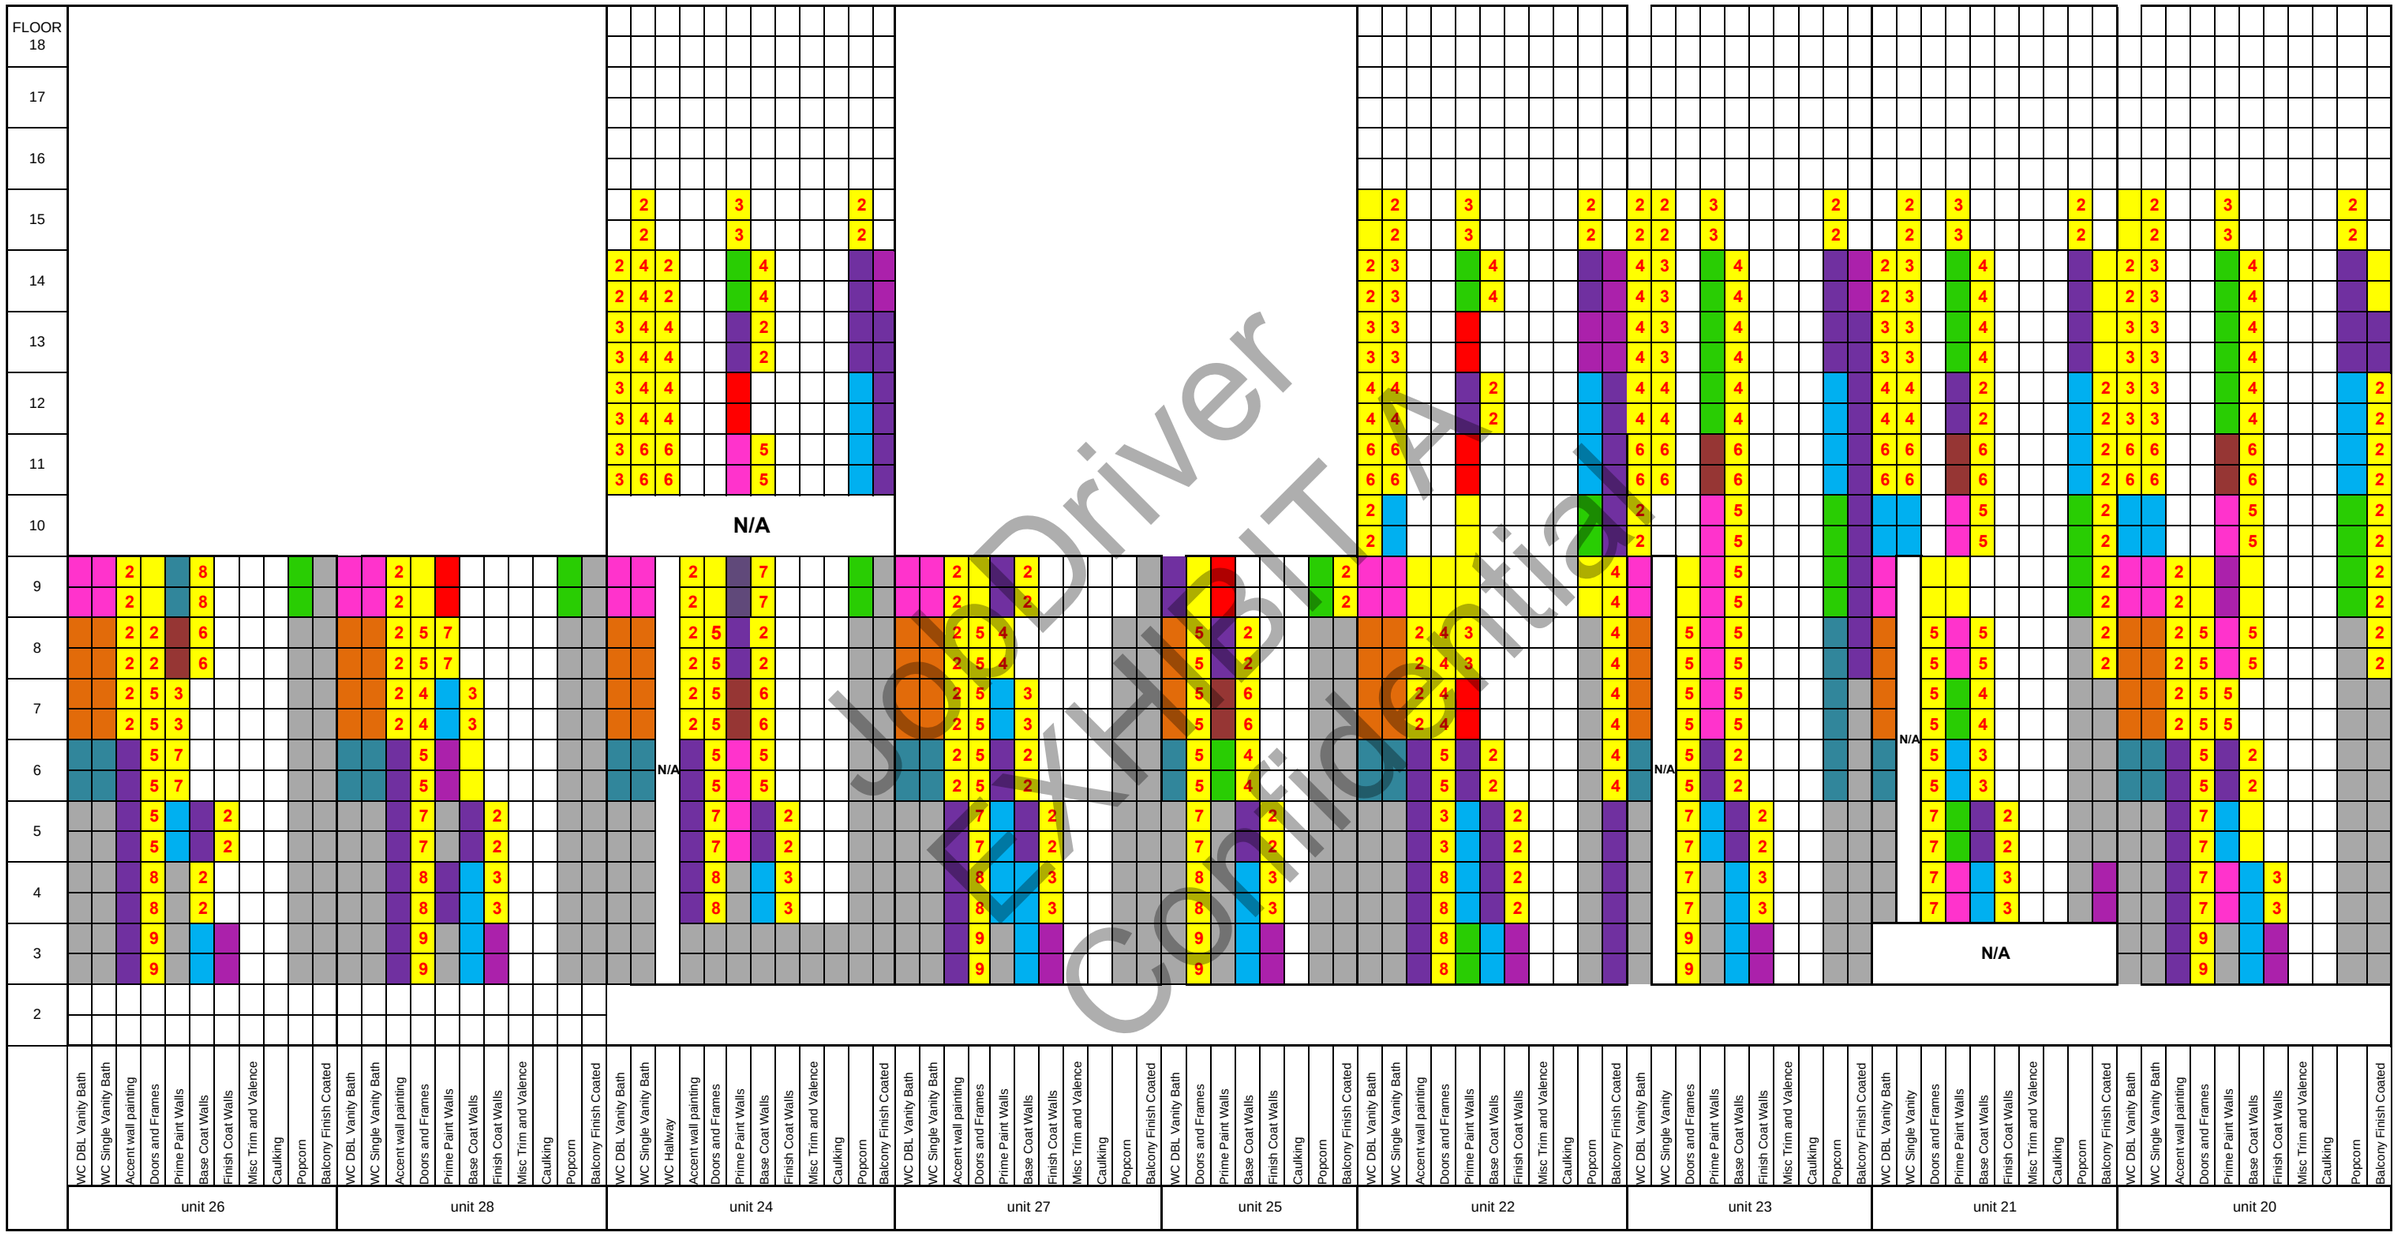

logDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012

BAY PAINTING PROGRESS CHART

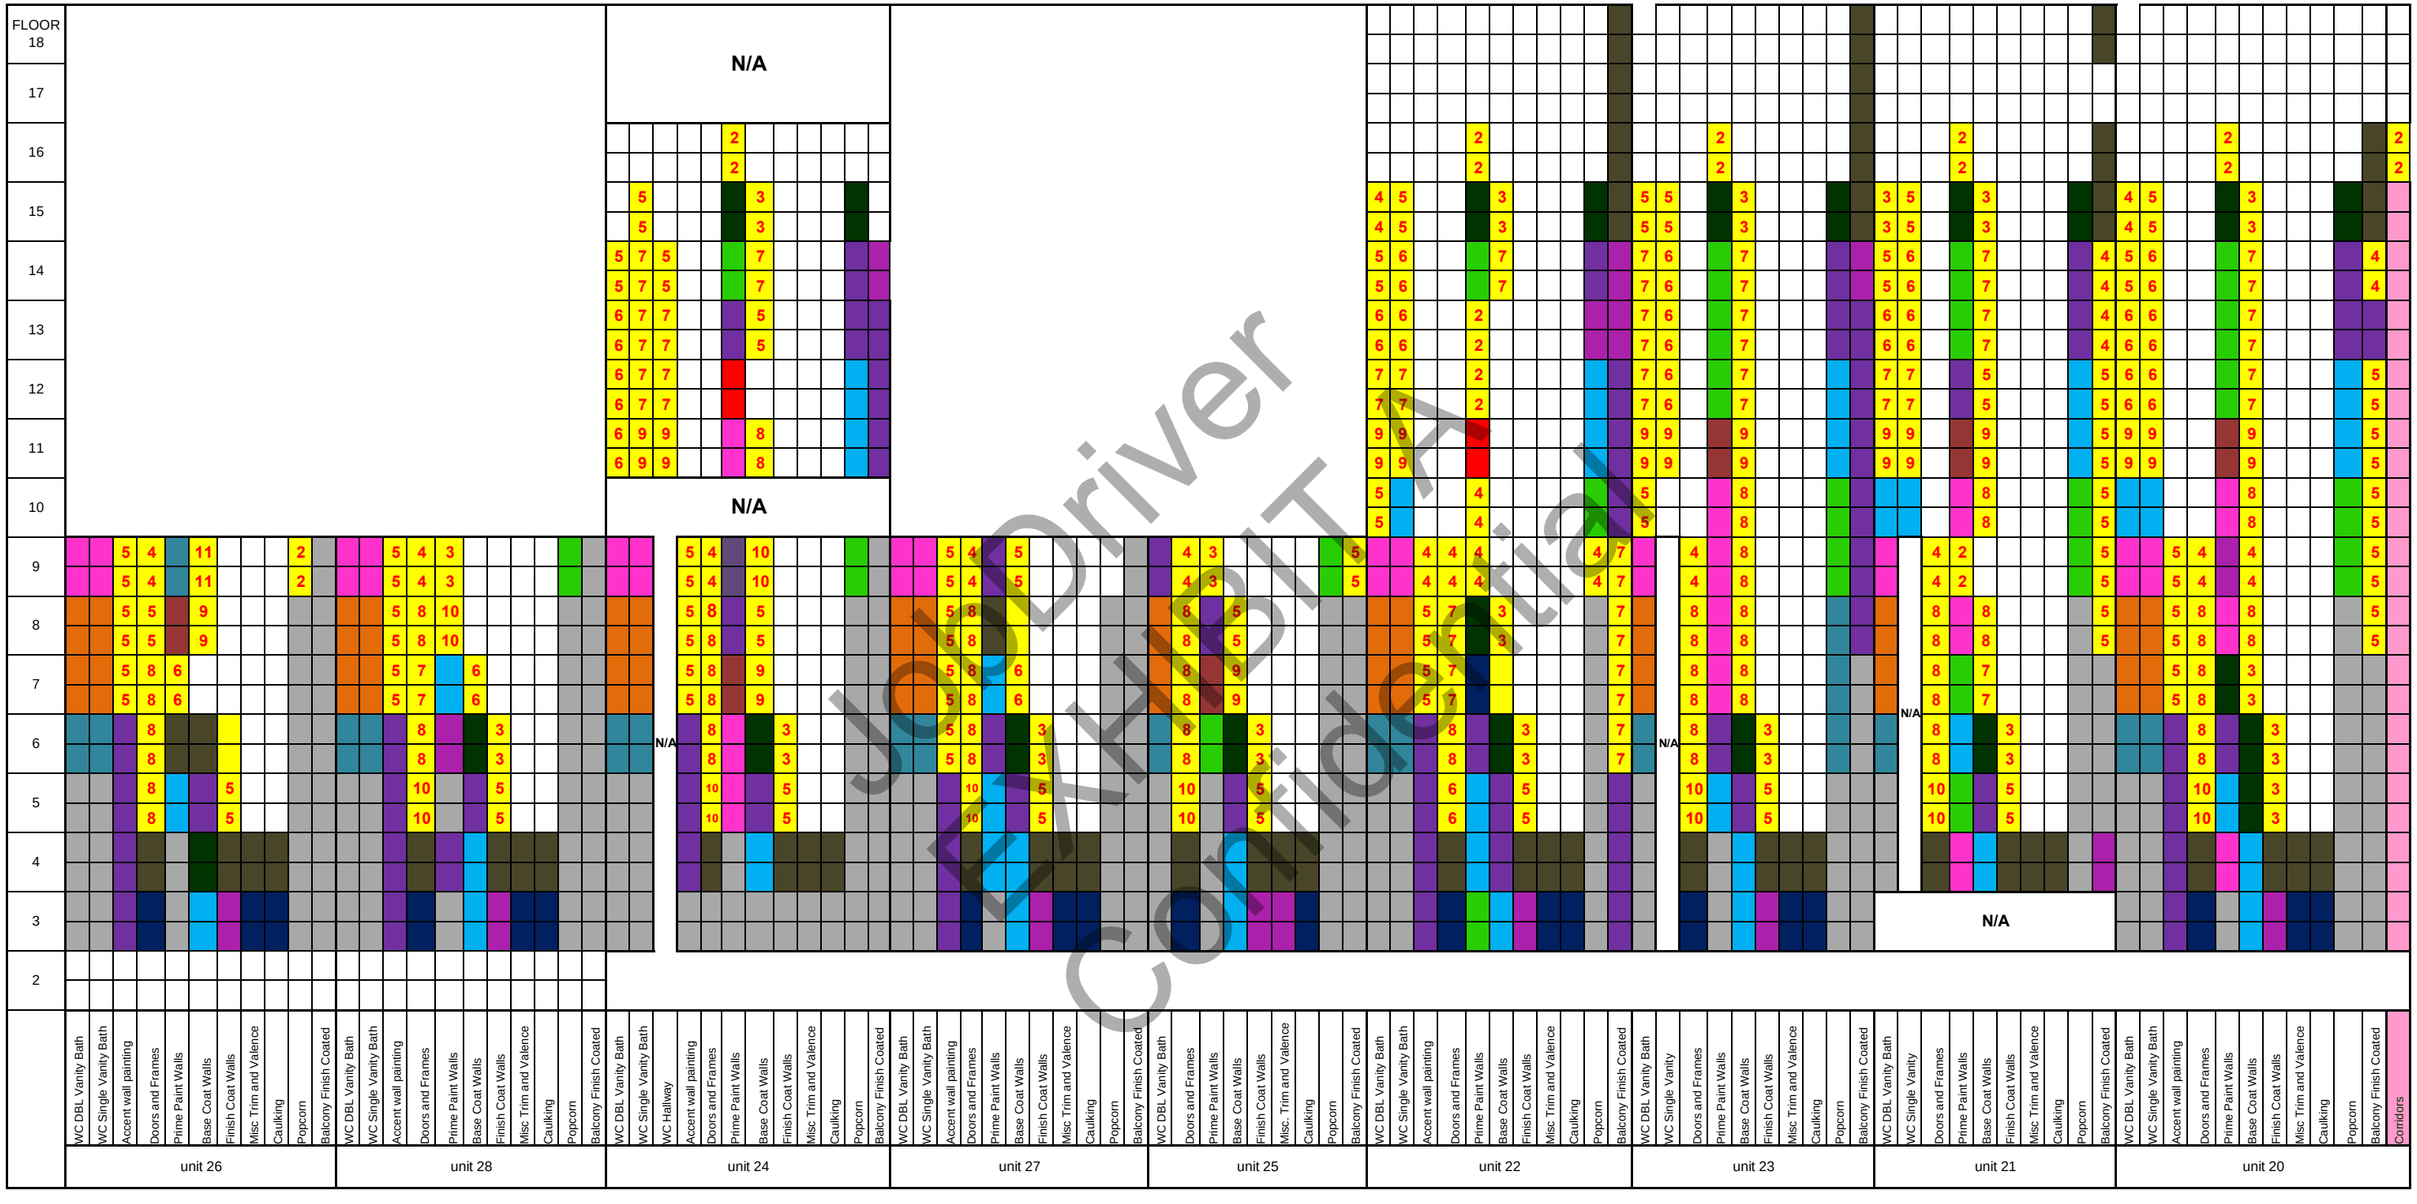

Job Driver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012

BAY PAINTING PROGRESS CHART

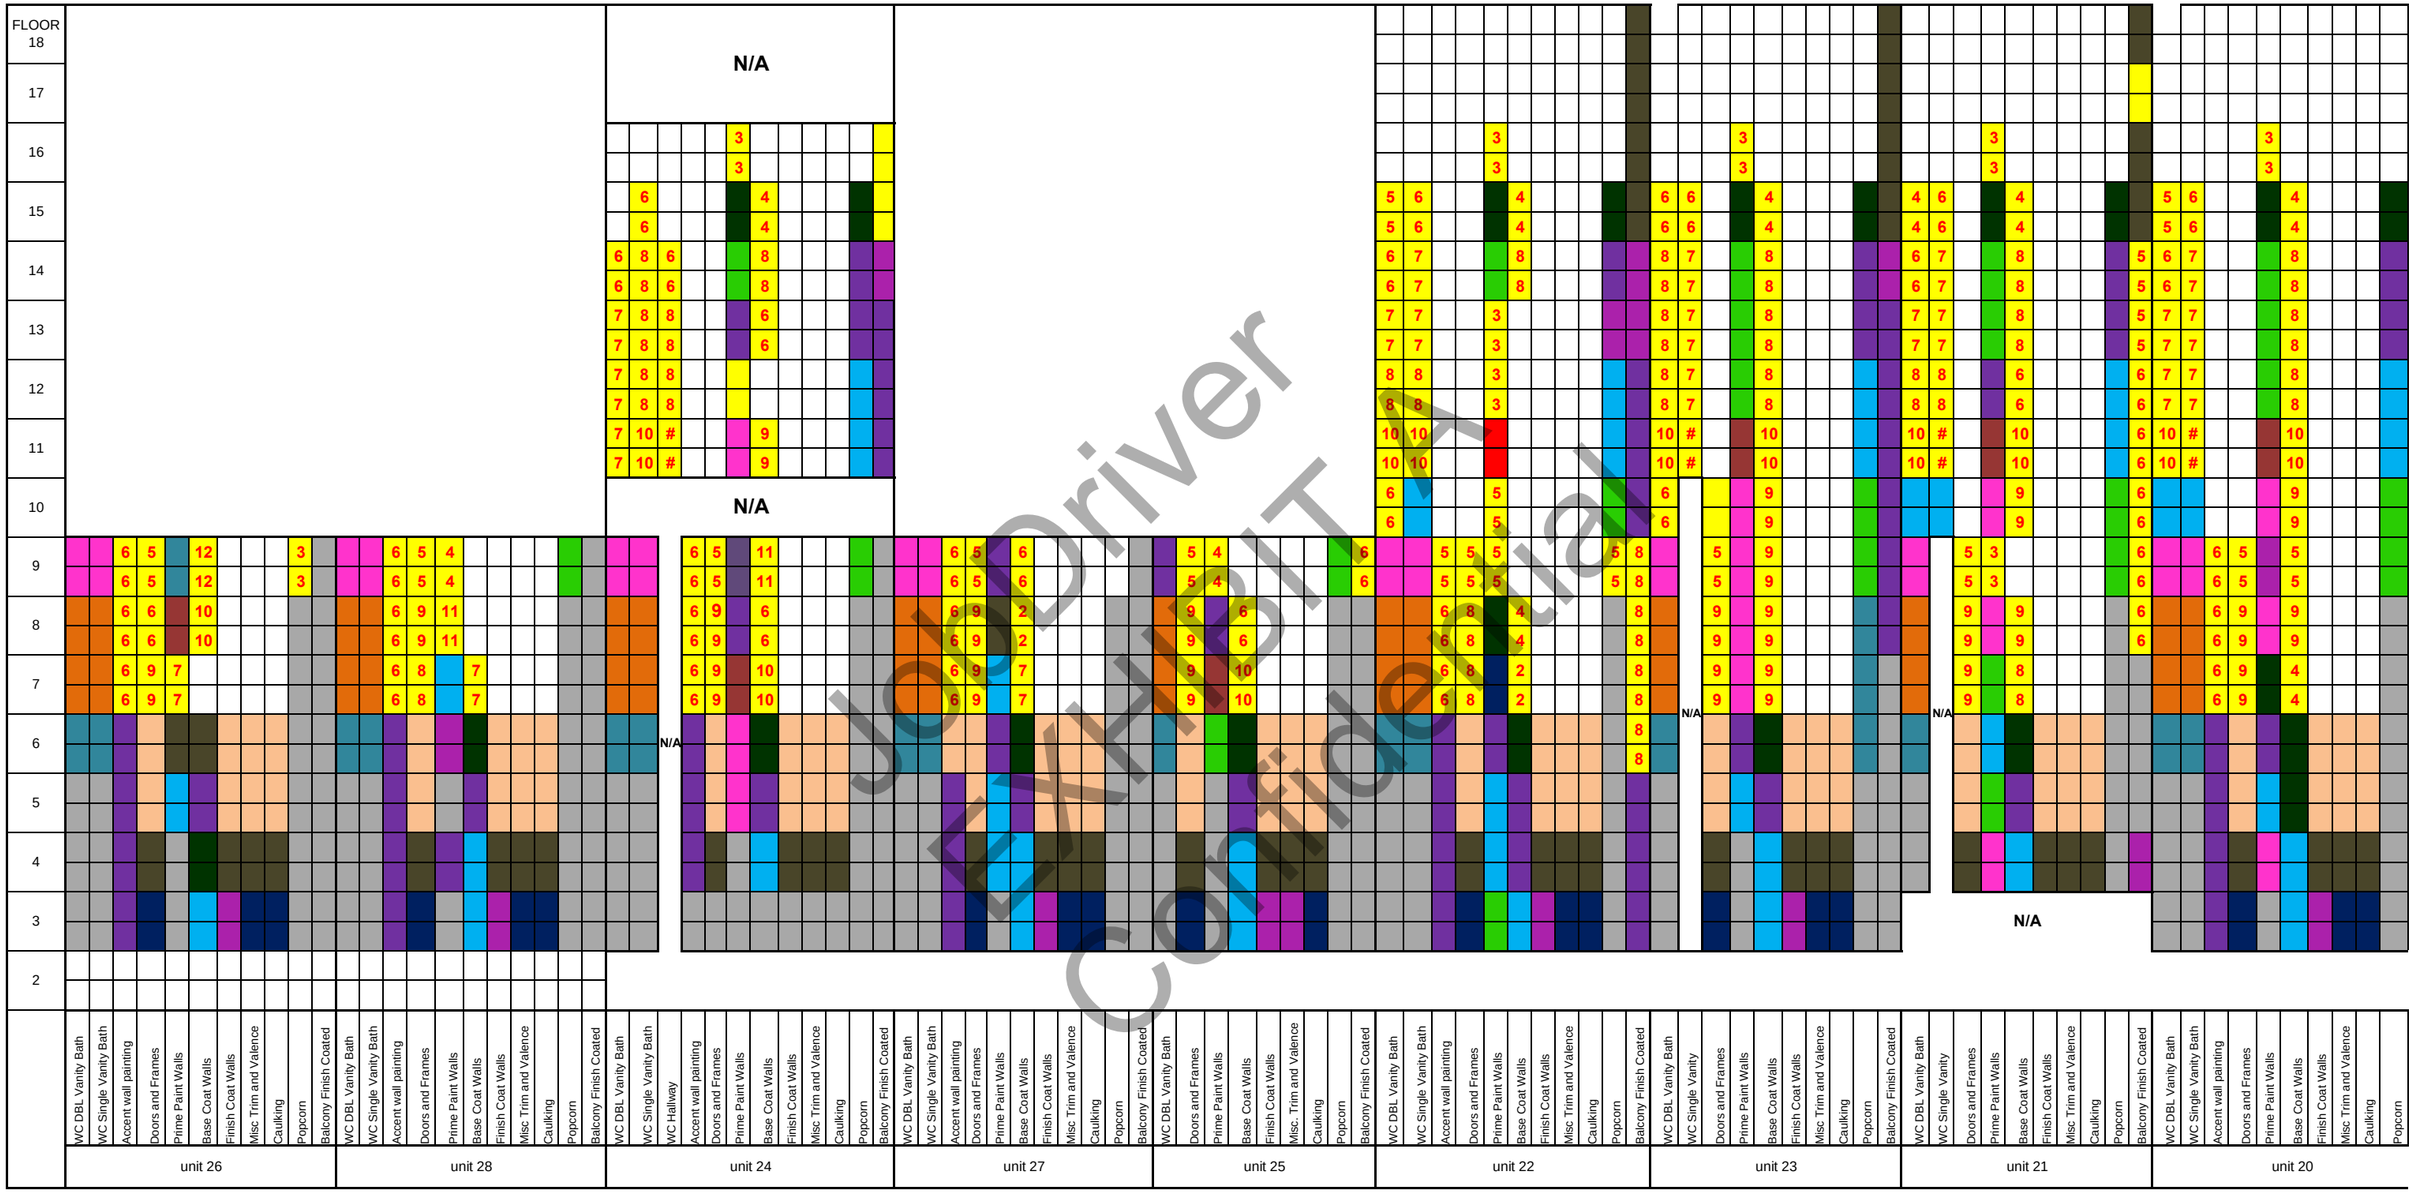

JobDriver EXHIBIT A Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012

BAY PAINTING PROGRESS CHART

5
5
6
6
6
6
6
6
6
6
6
6

Balcony Finish Coated

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

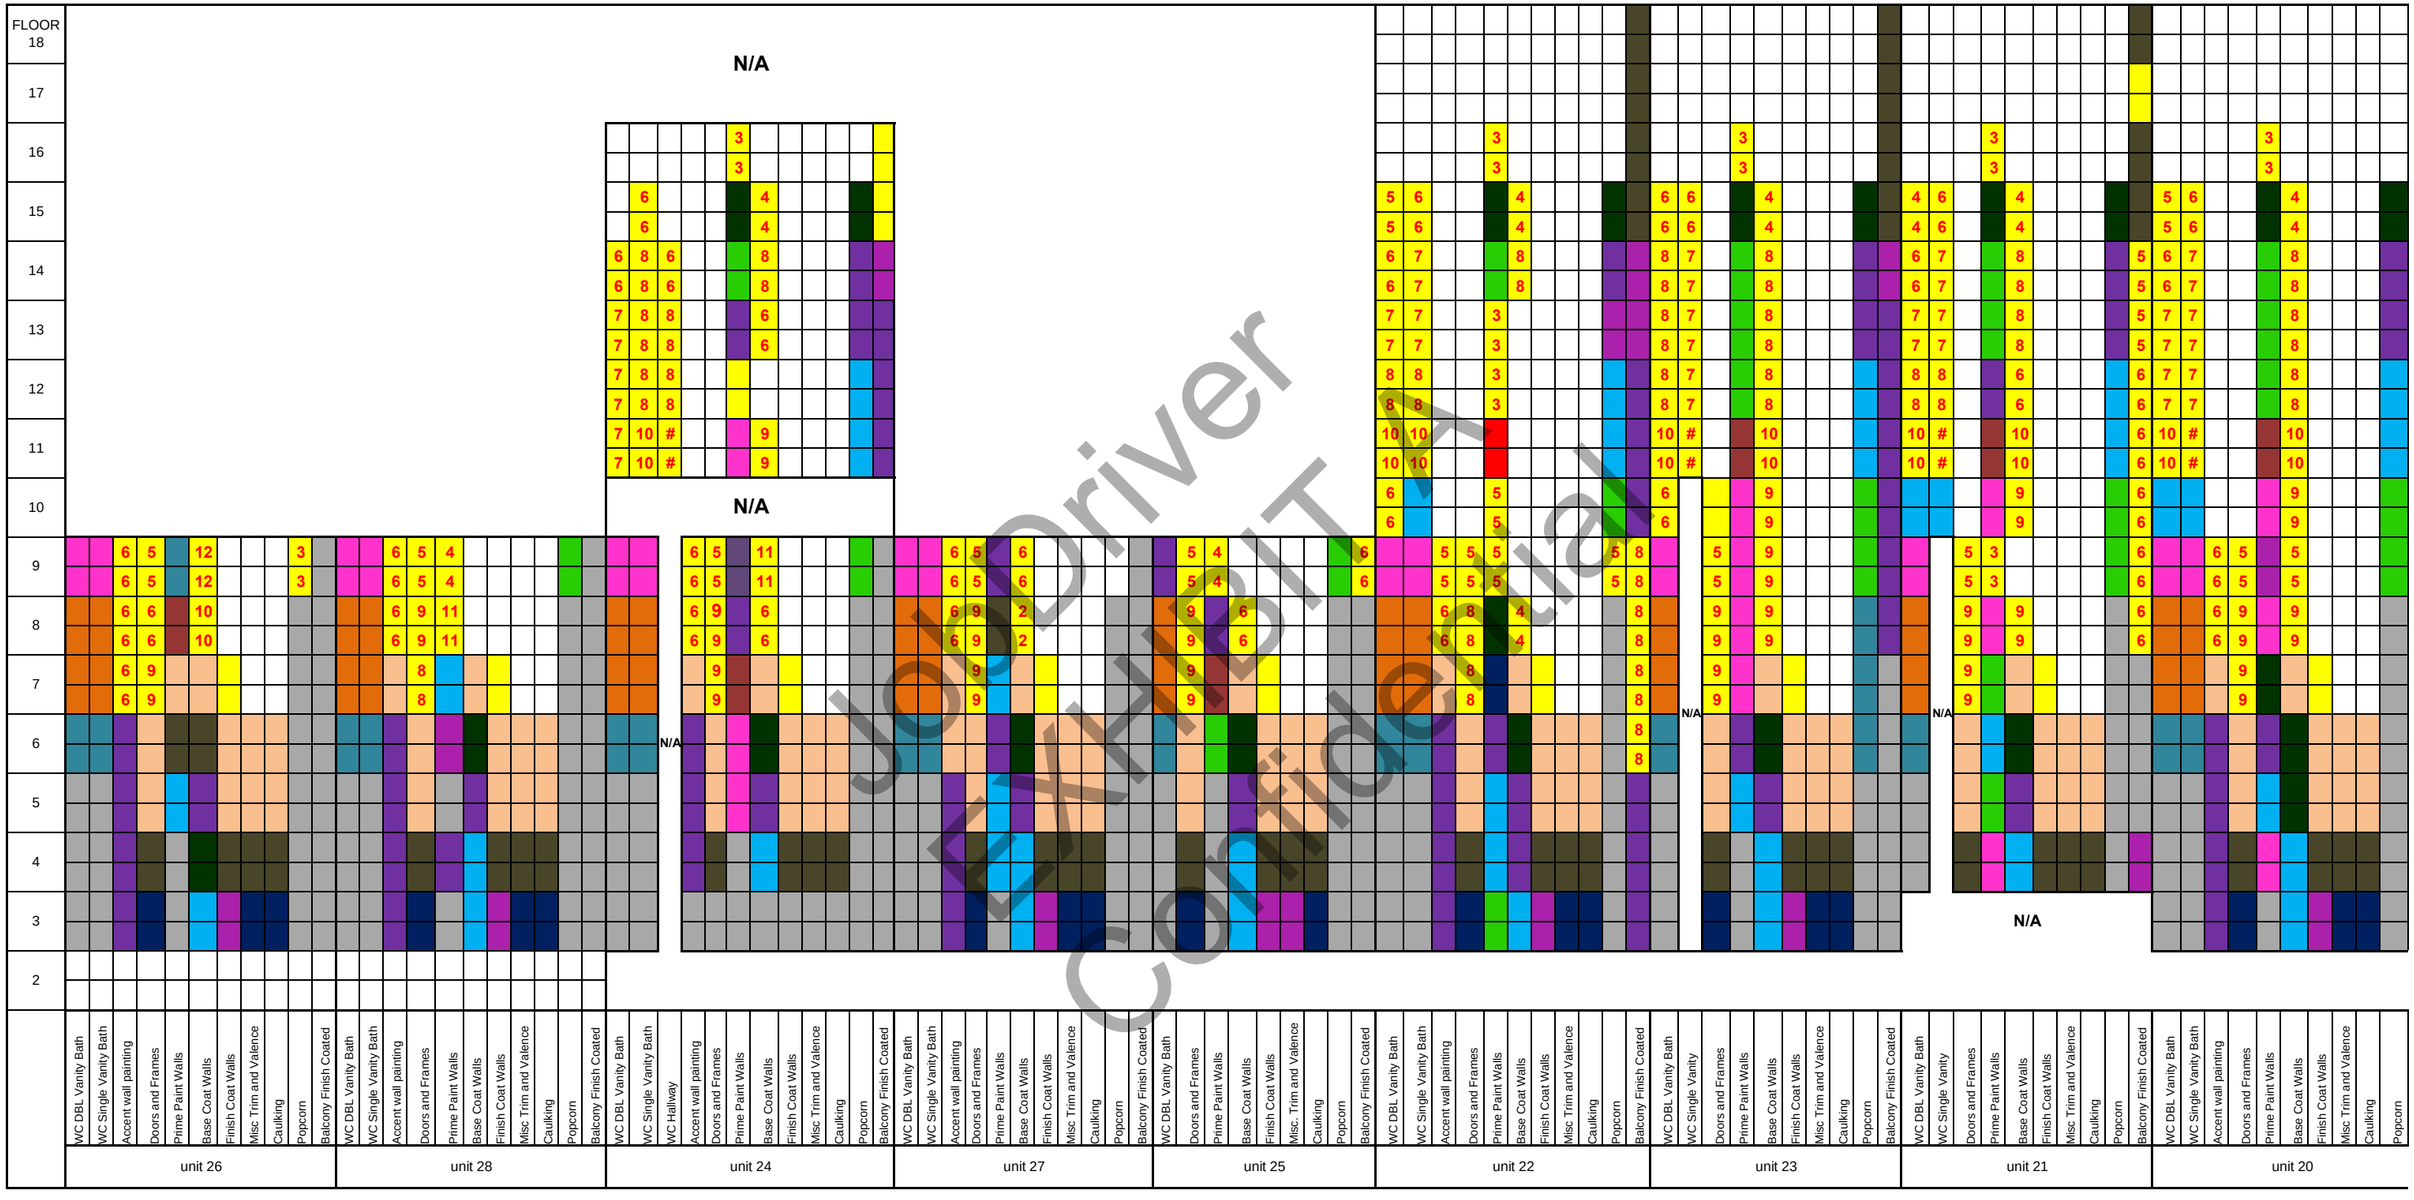

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012

BAY PAINTING PROGRESS CHART

5
5
6
6
6
6
6
6
6
6
6
6

Balcony Finish Coated

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

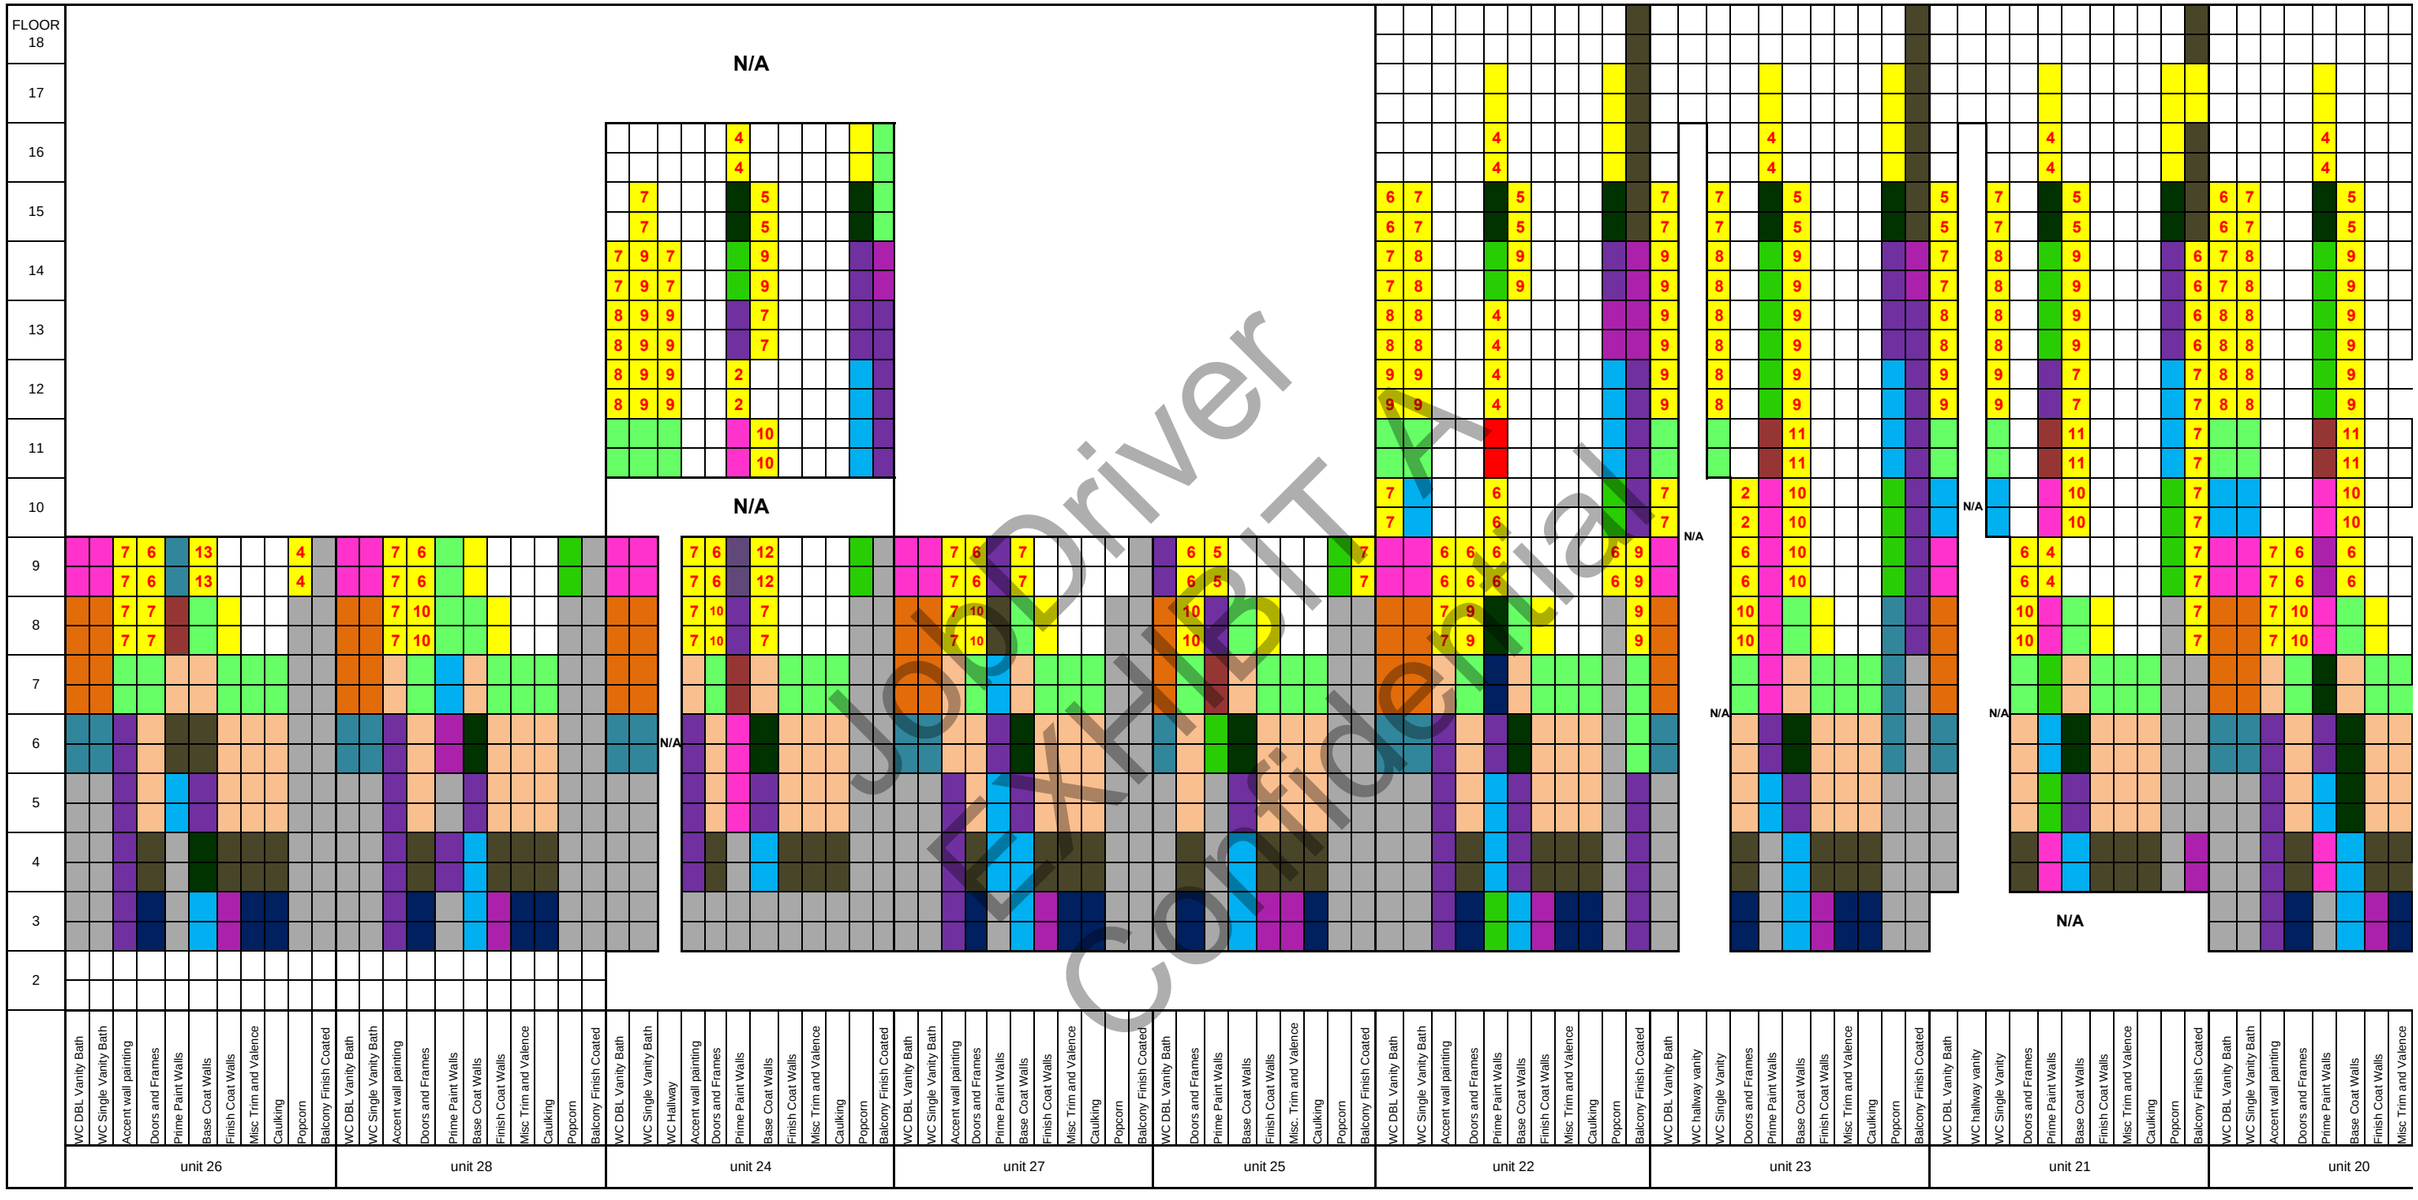

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012

BAY PAINTING PROGRESS CHART



JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

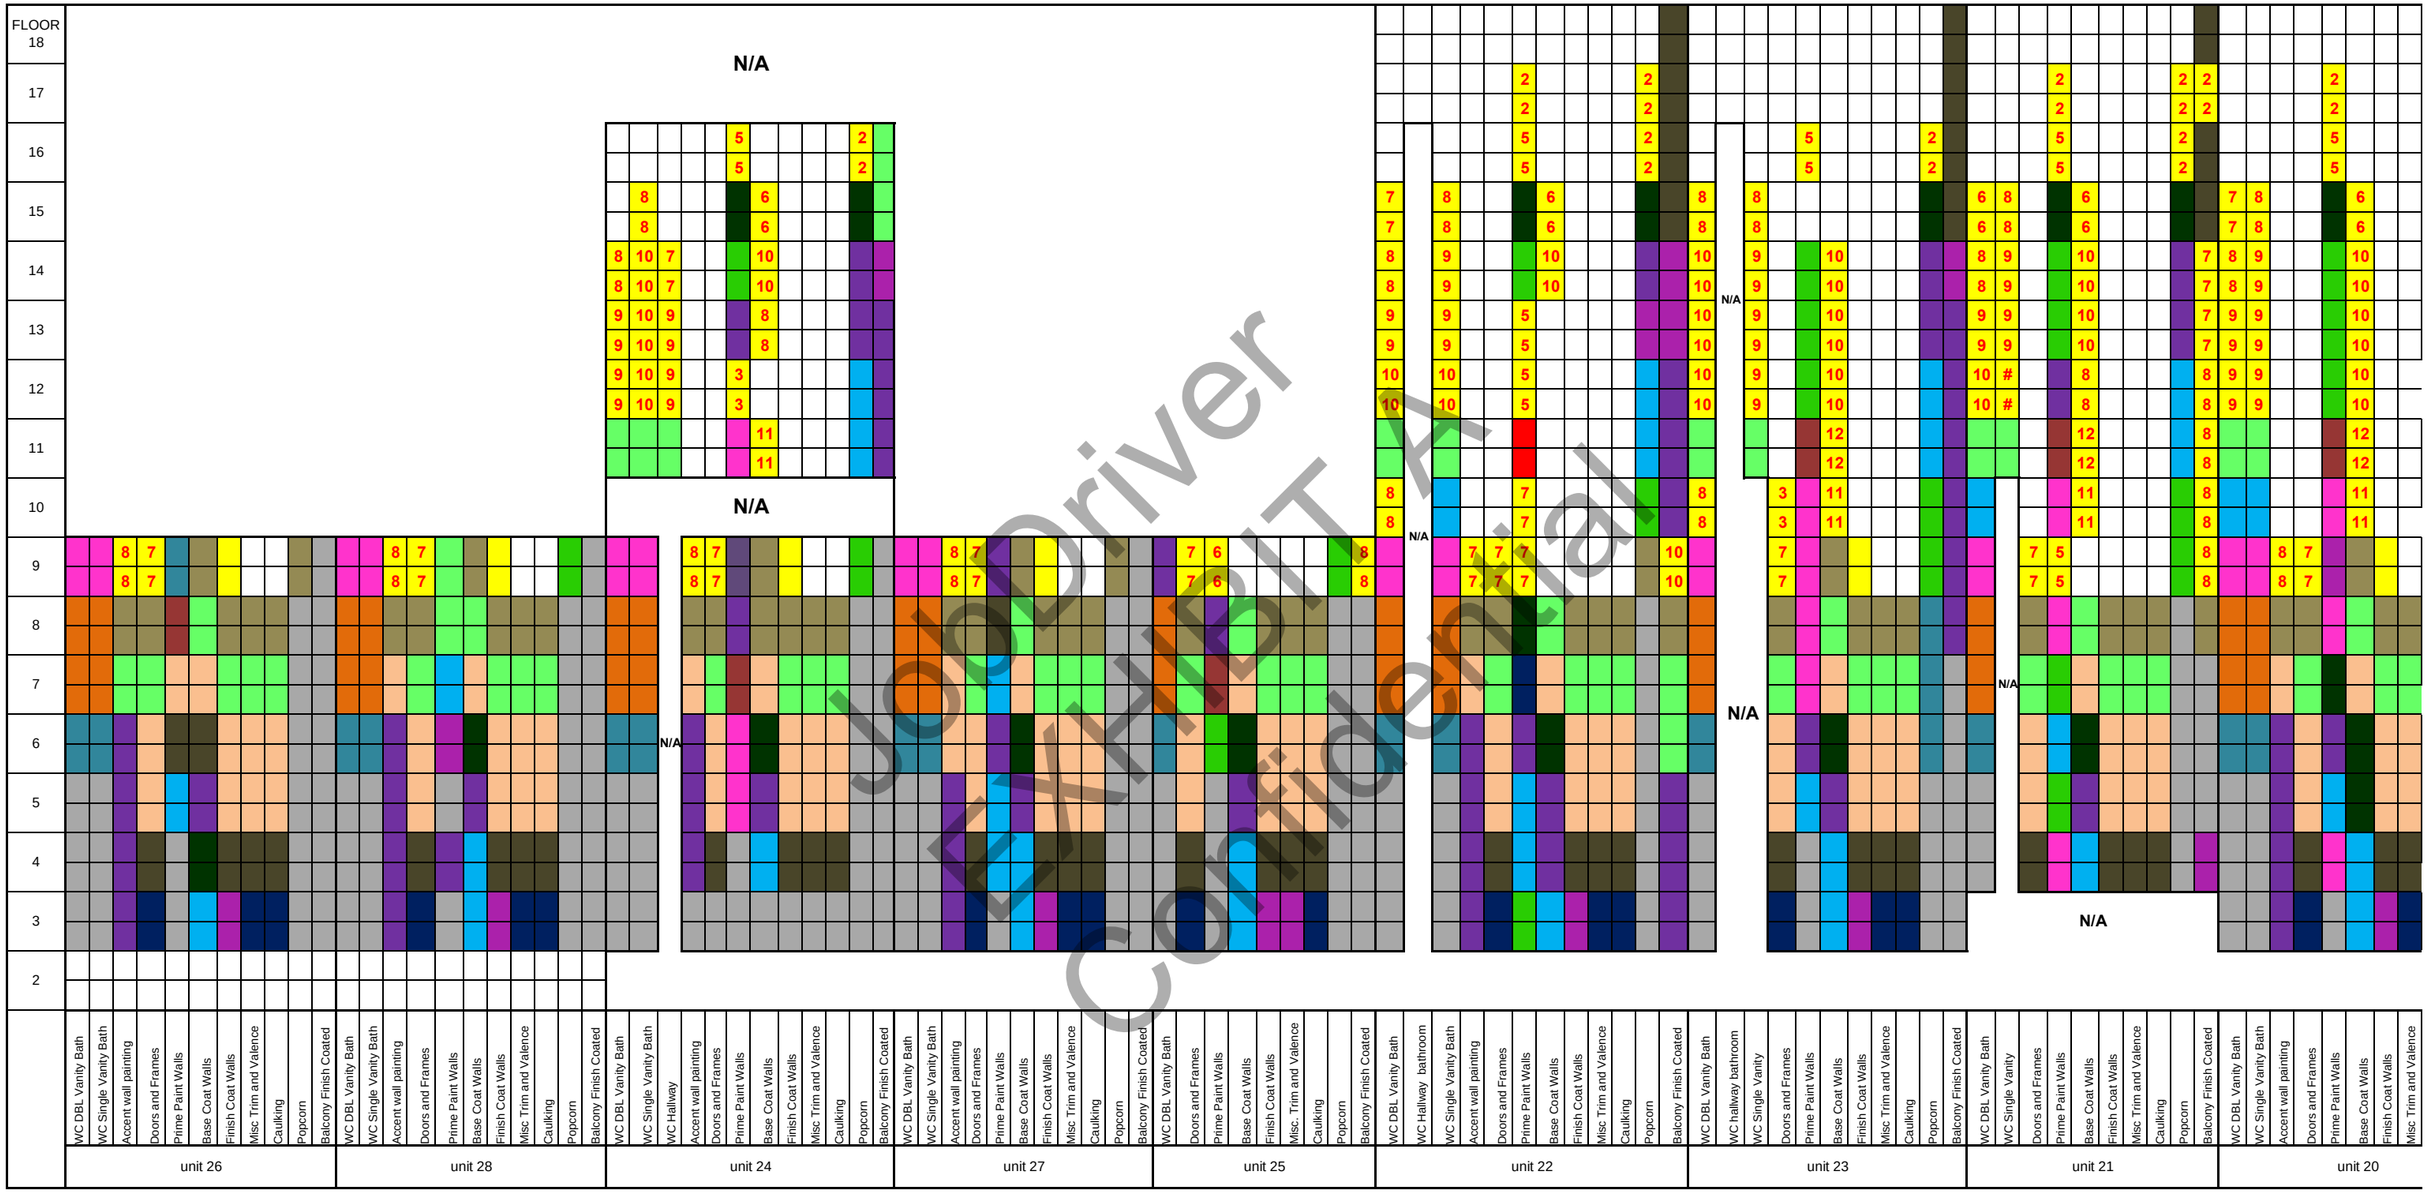

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- SHEET ROCK REWORK/NEEDS PRIMING
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012

BAY PAINTING PROGRESS CHART



JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

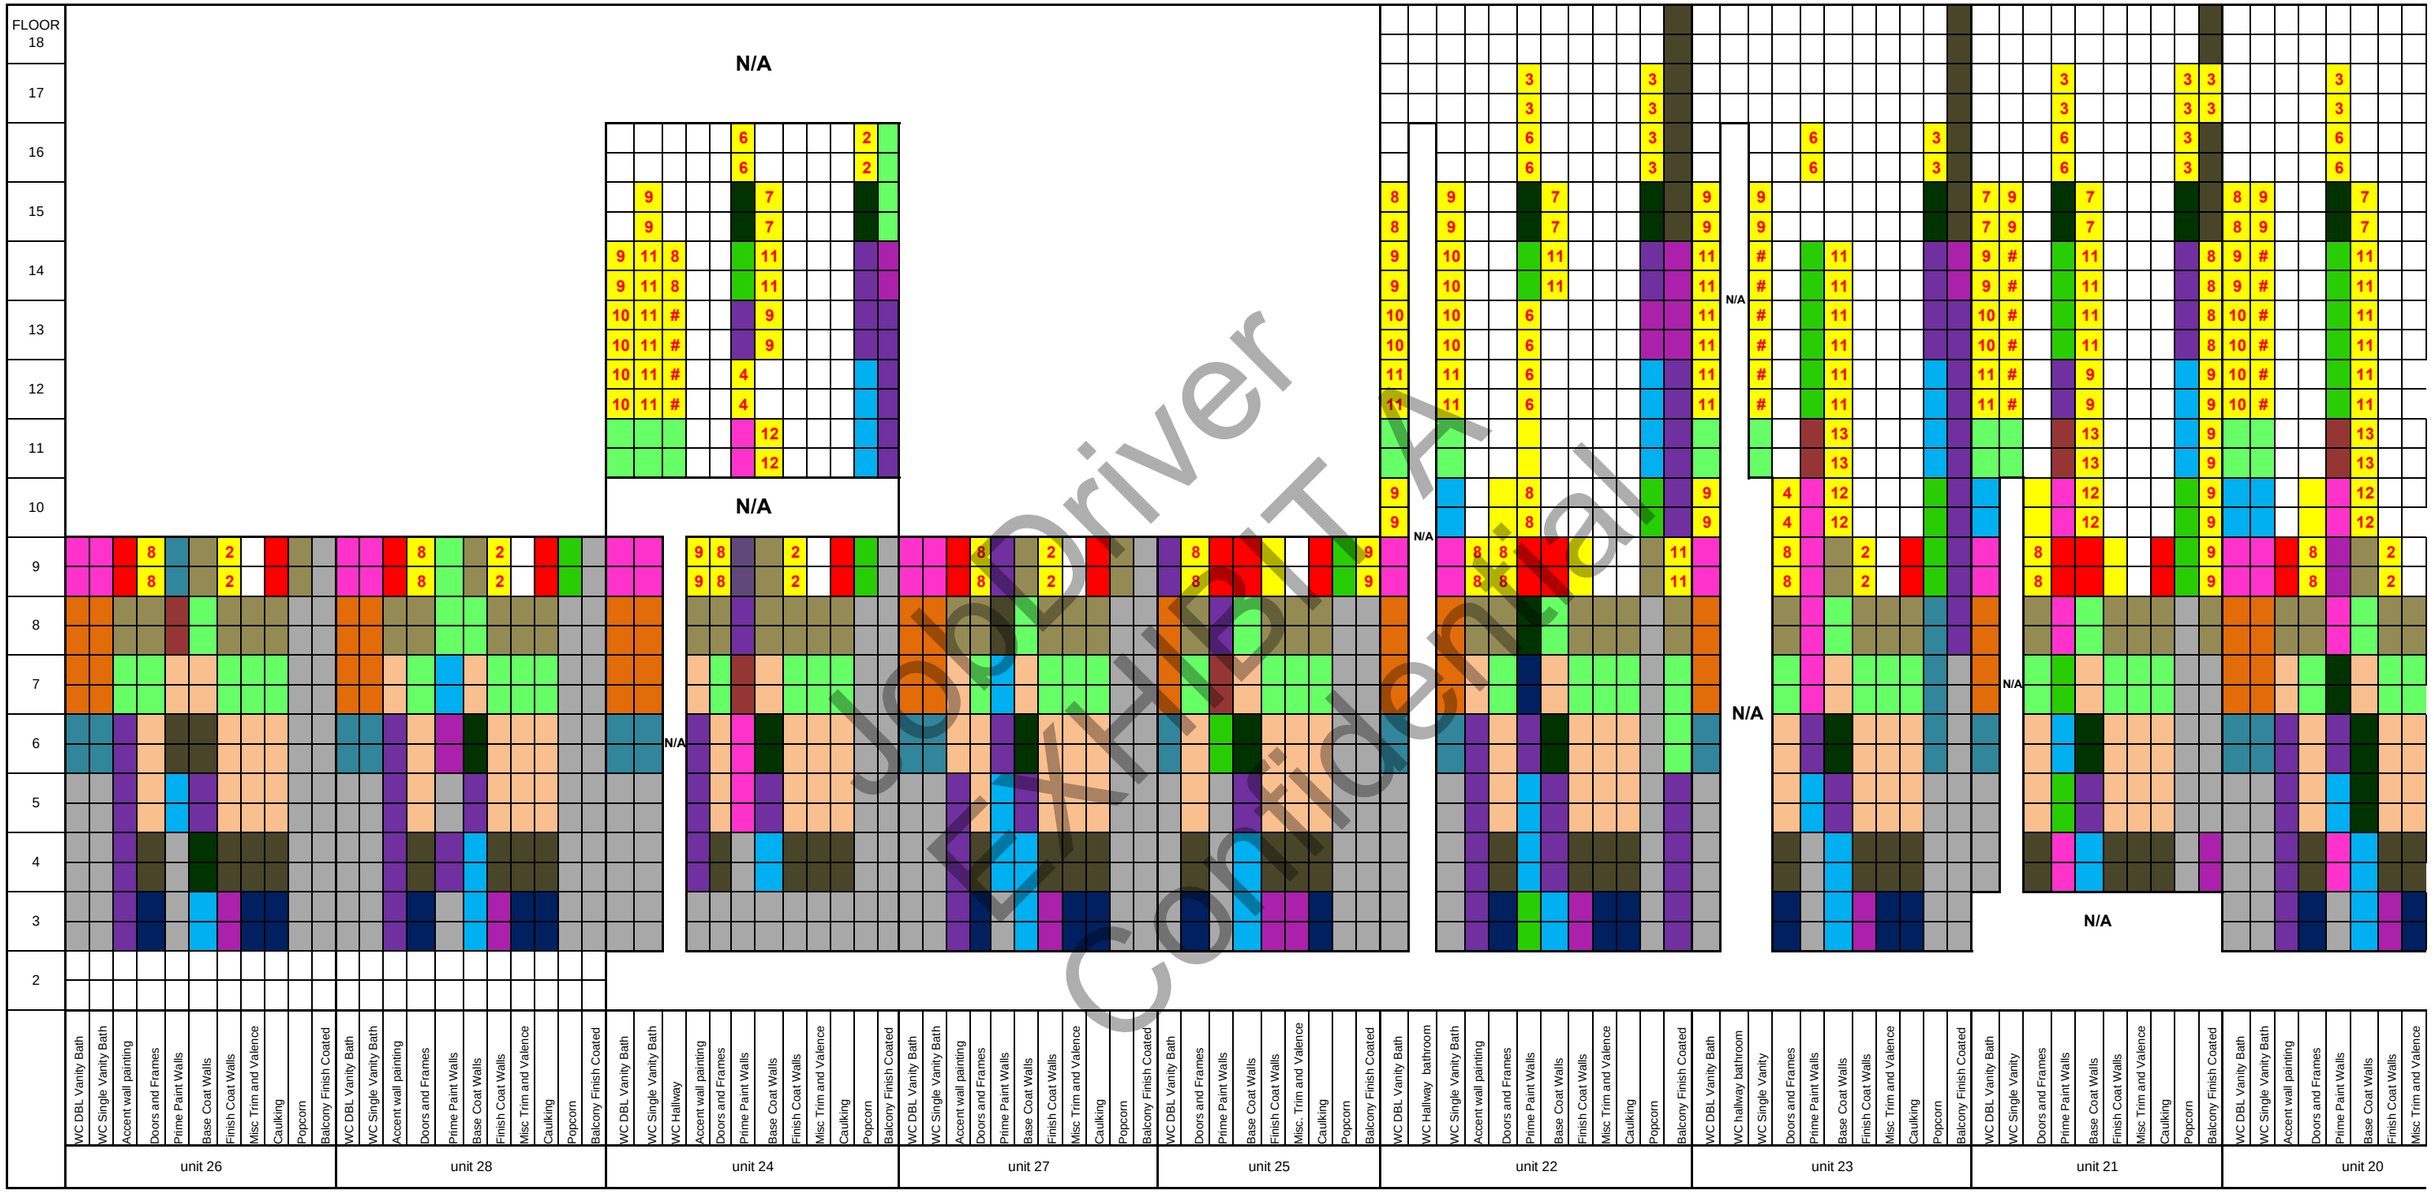

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012

BAY PAINTING PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

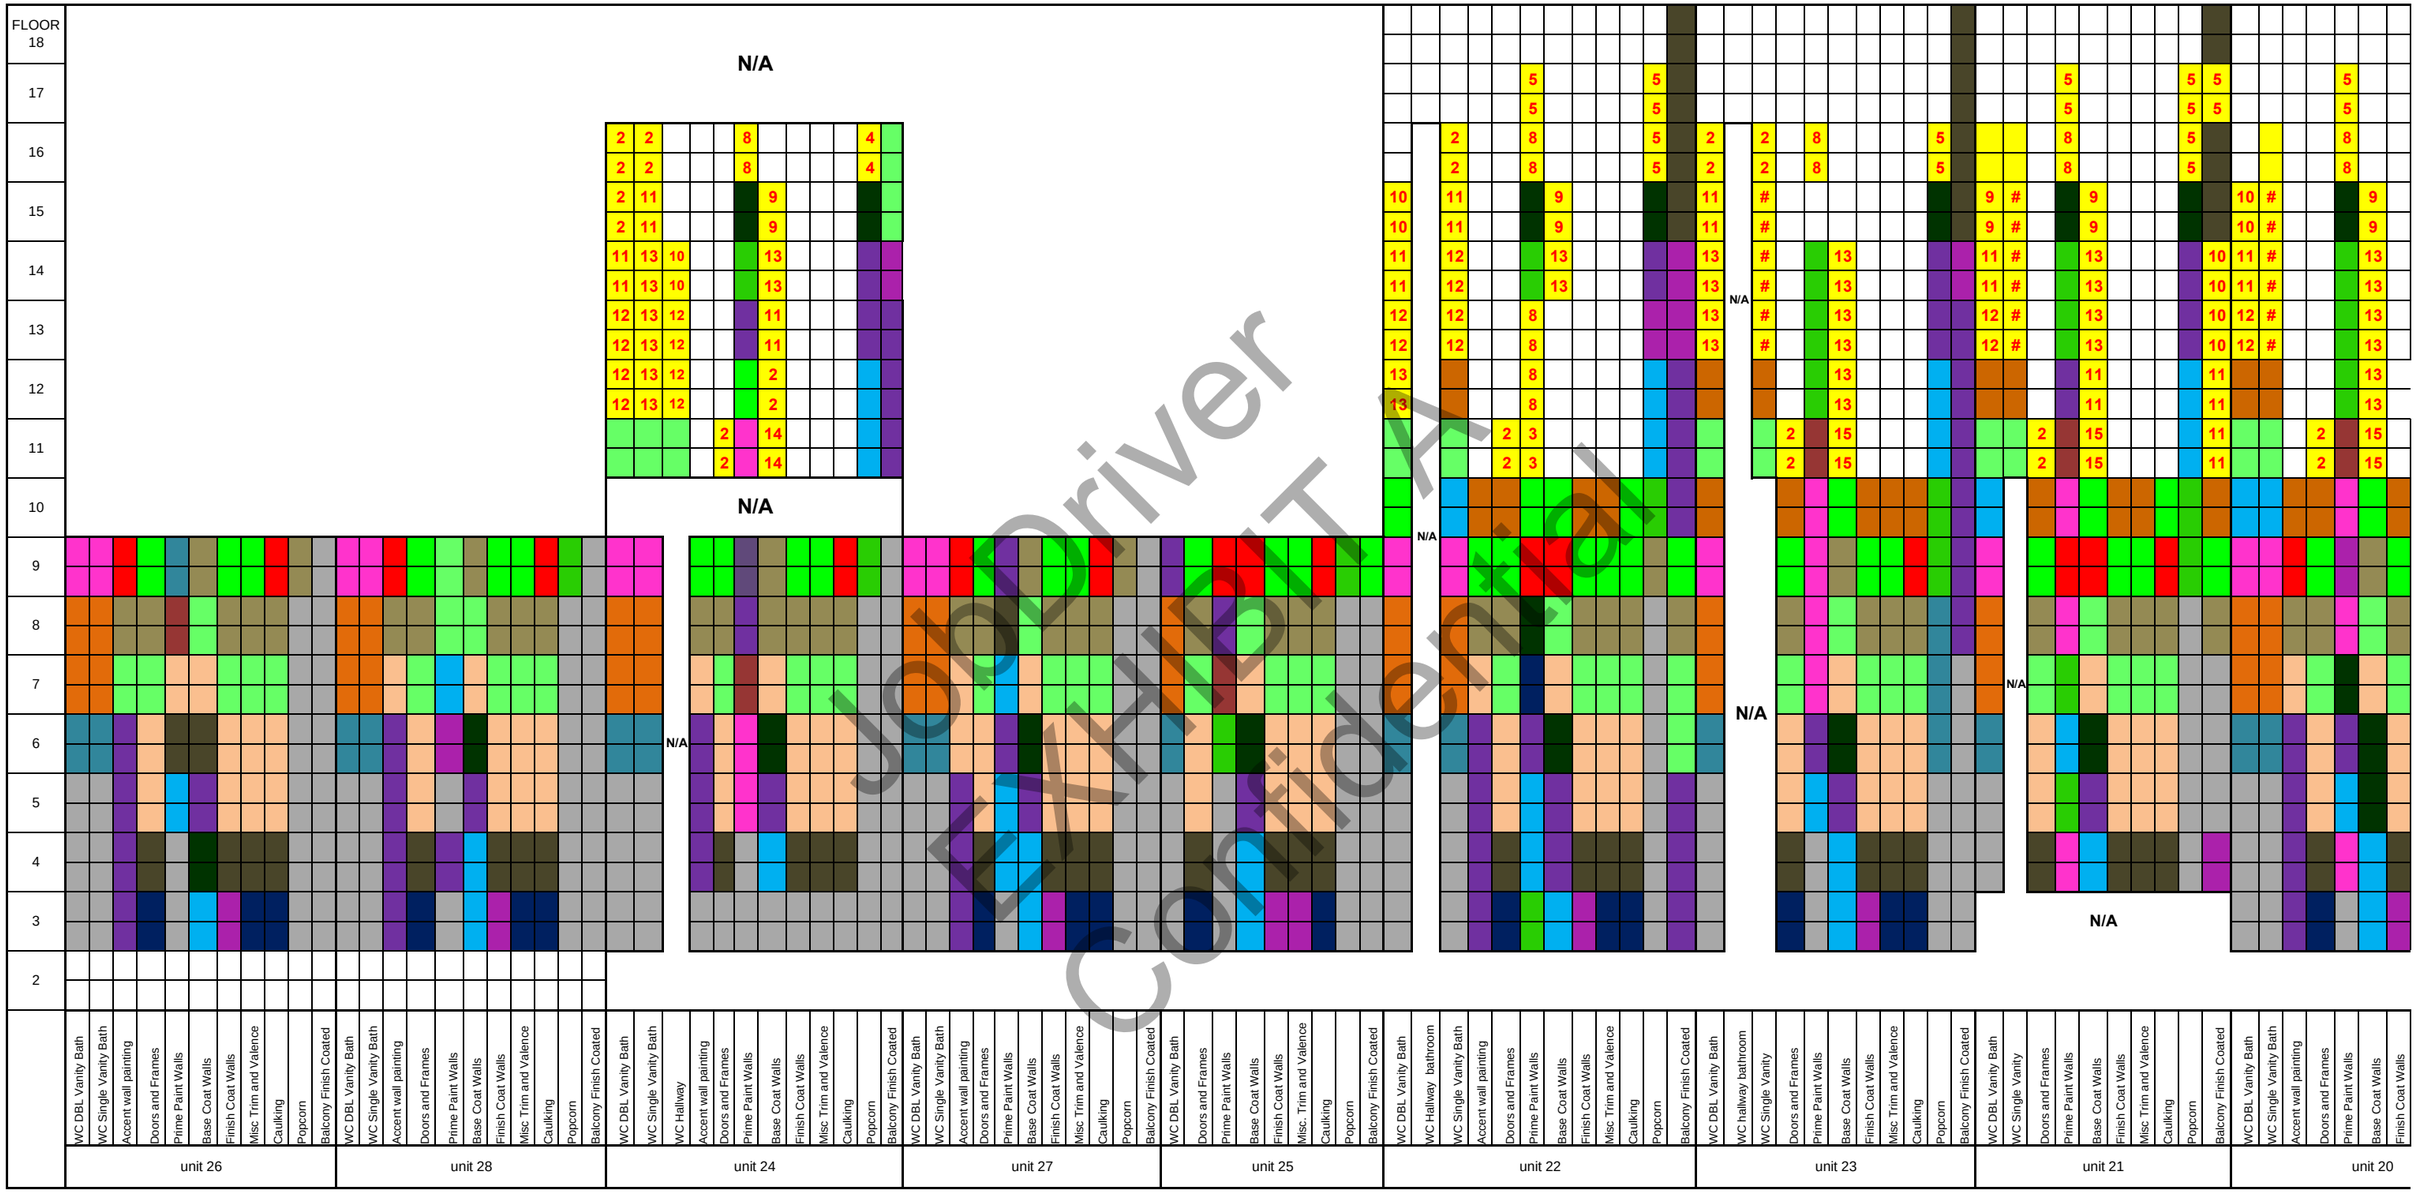

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012

BAY PAINTING PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

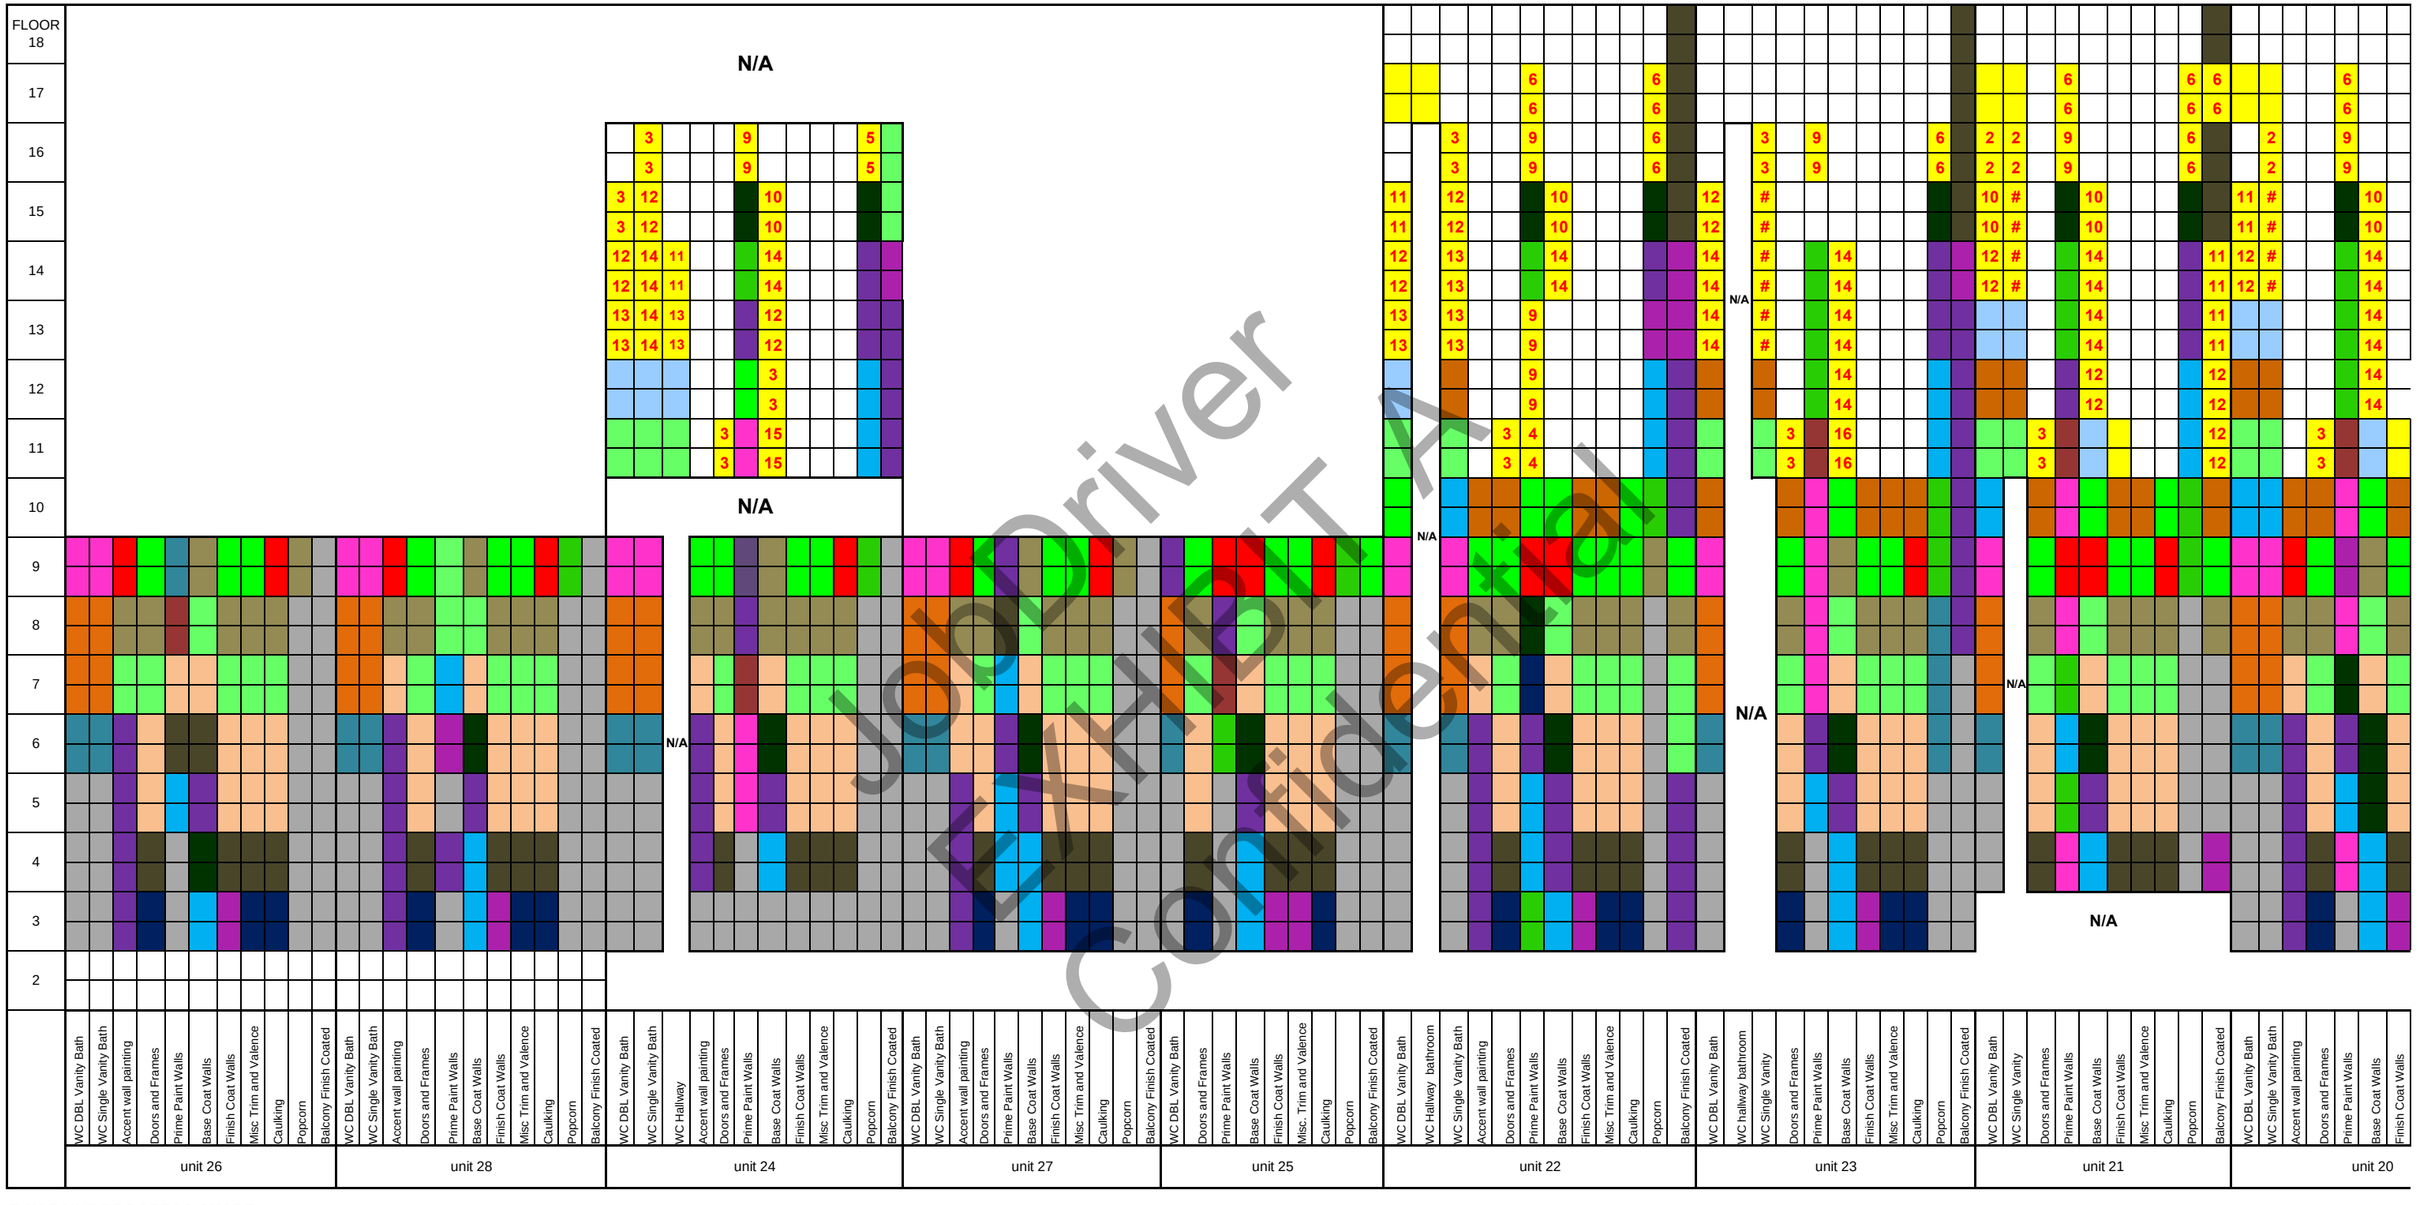

JobDriver EXHIBIT A Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012

BAY PAINTING PROGRESS CHART



JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

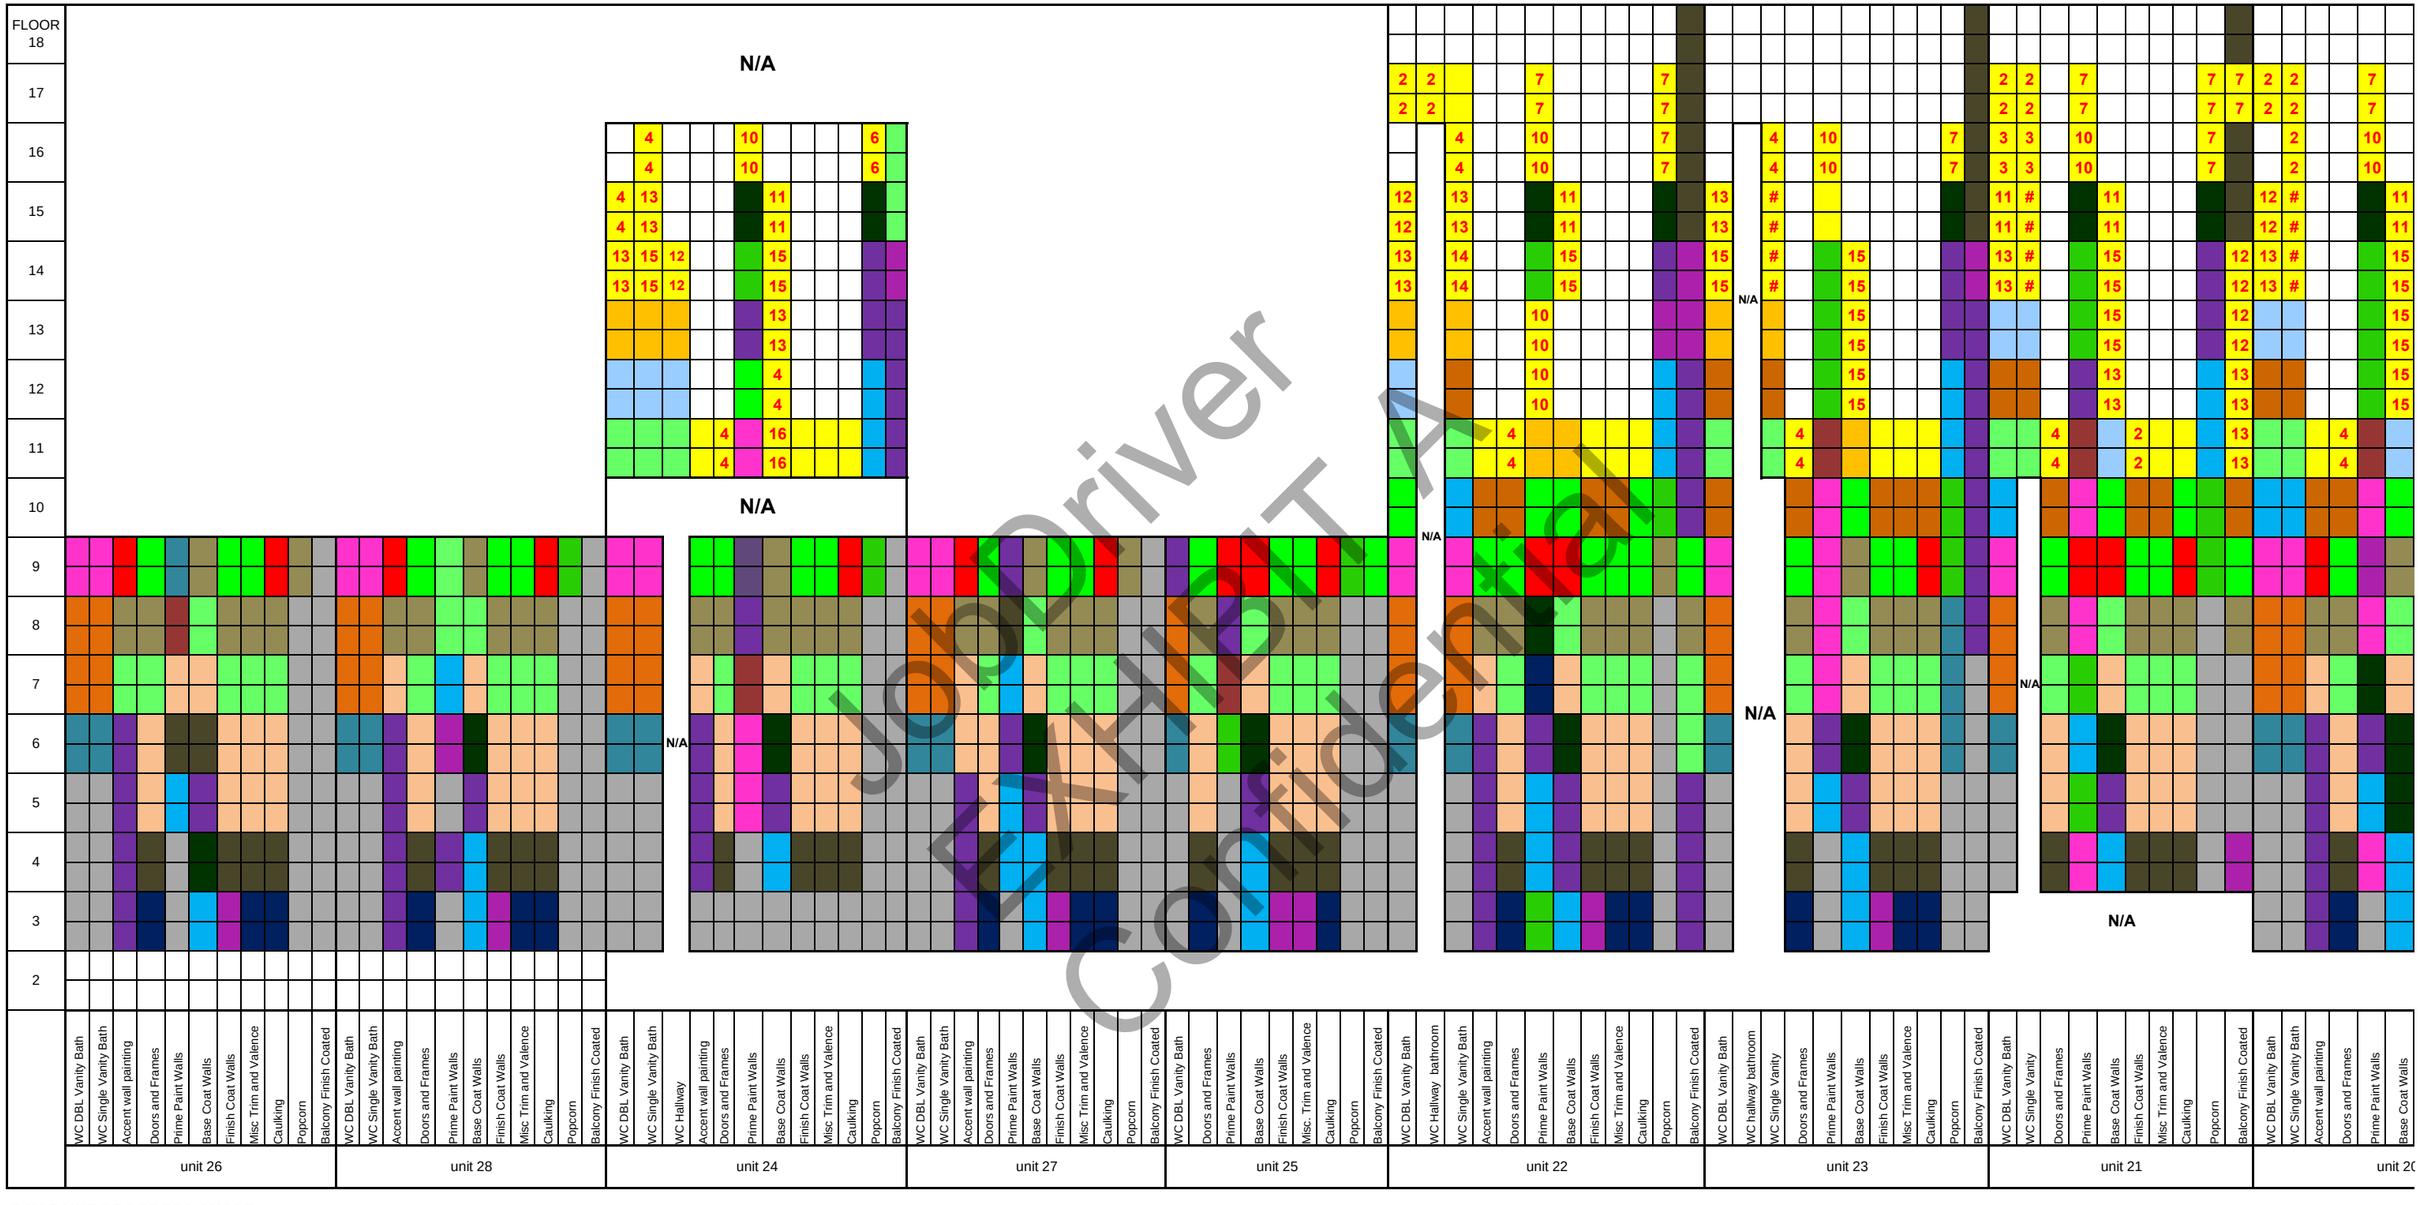

Job Driver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012

BAY PAINTING PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

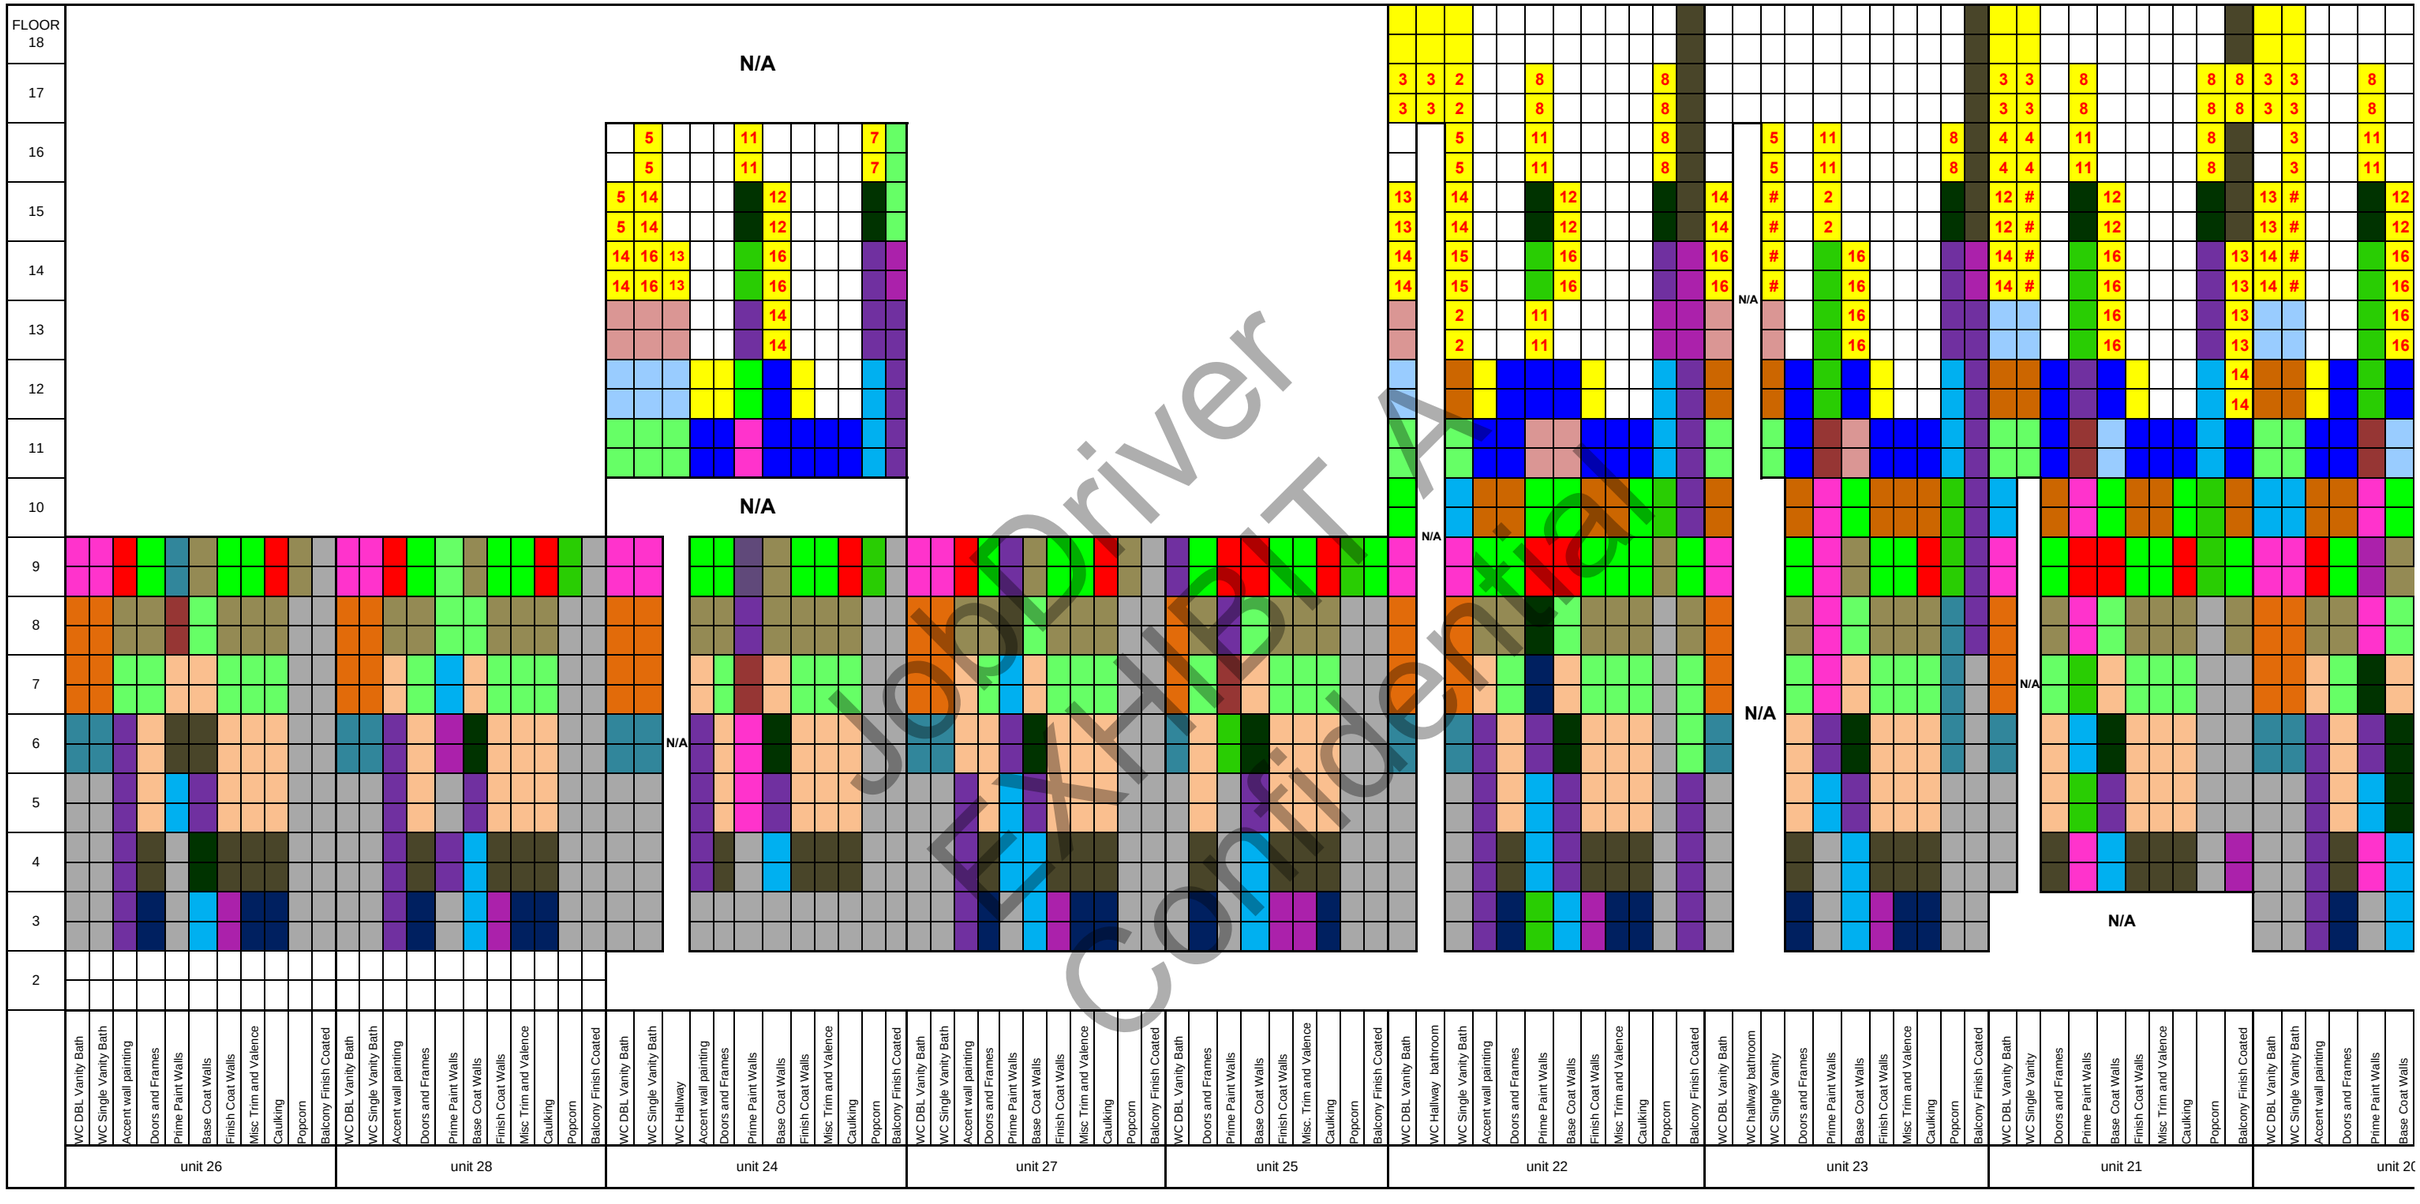

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART



JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

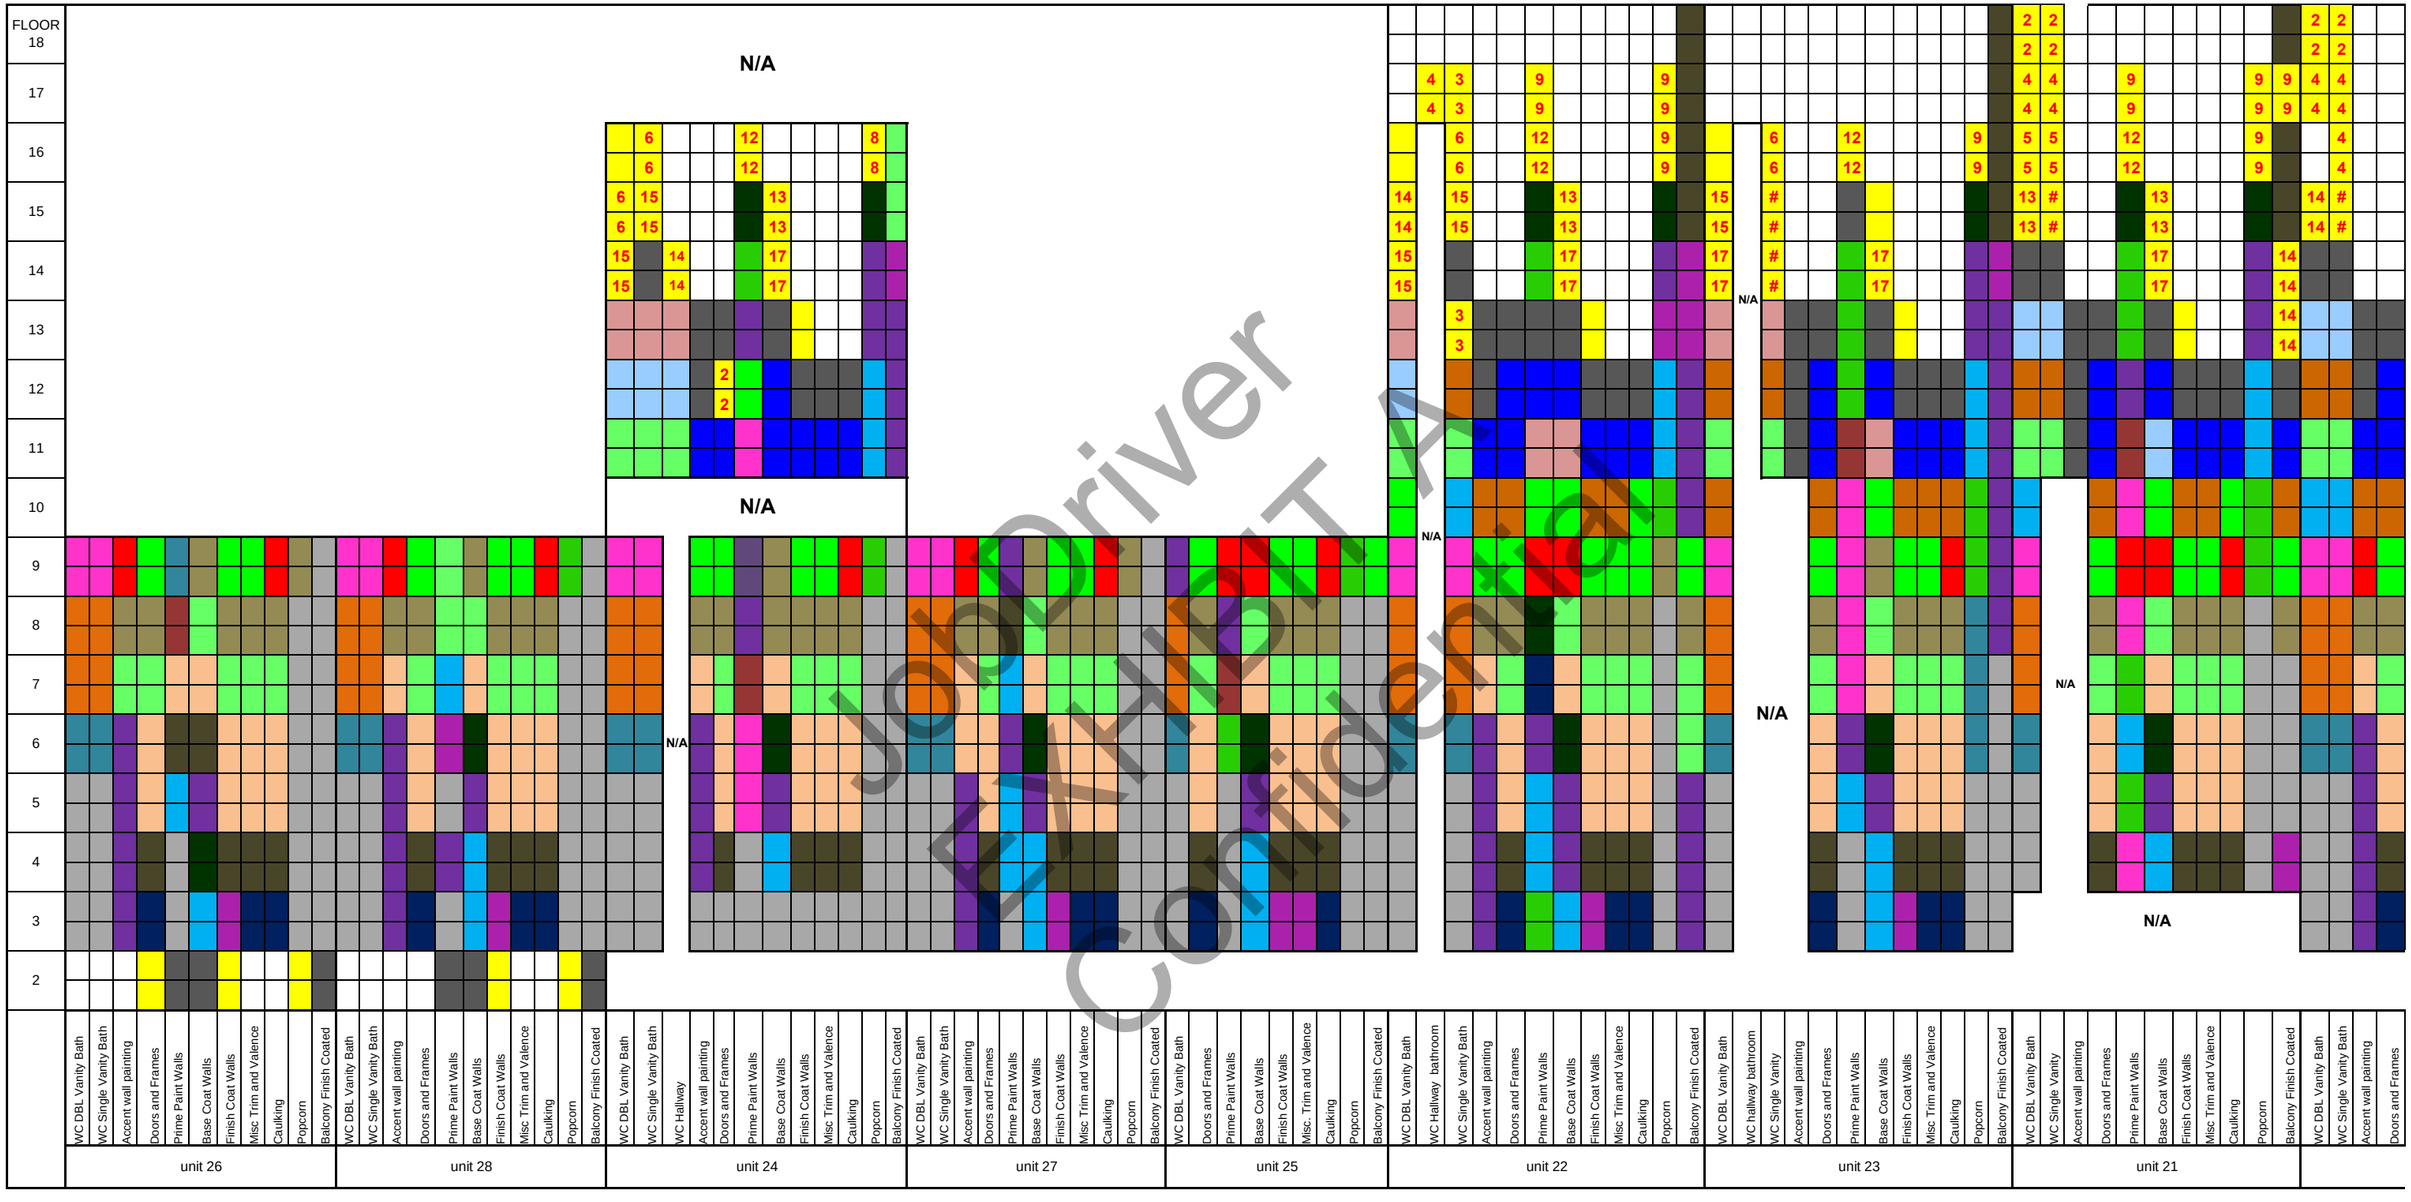

JobDriver
EXTRA
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/2/2012

BAY PAINTING PROGRESS CHART



Prime Paint Walls	
Base Coat Walls	
Finish Coat Walls	
Misc Trim and Valence	
Caulking	
Popcorn	
Balcony Finish Coated	

unit 20

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

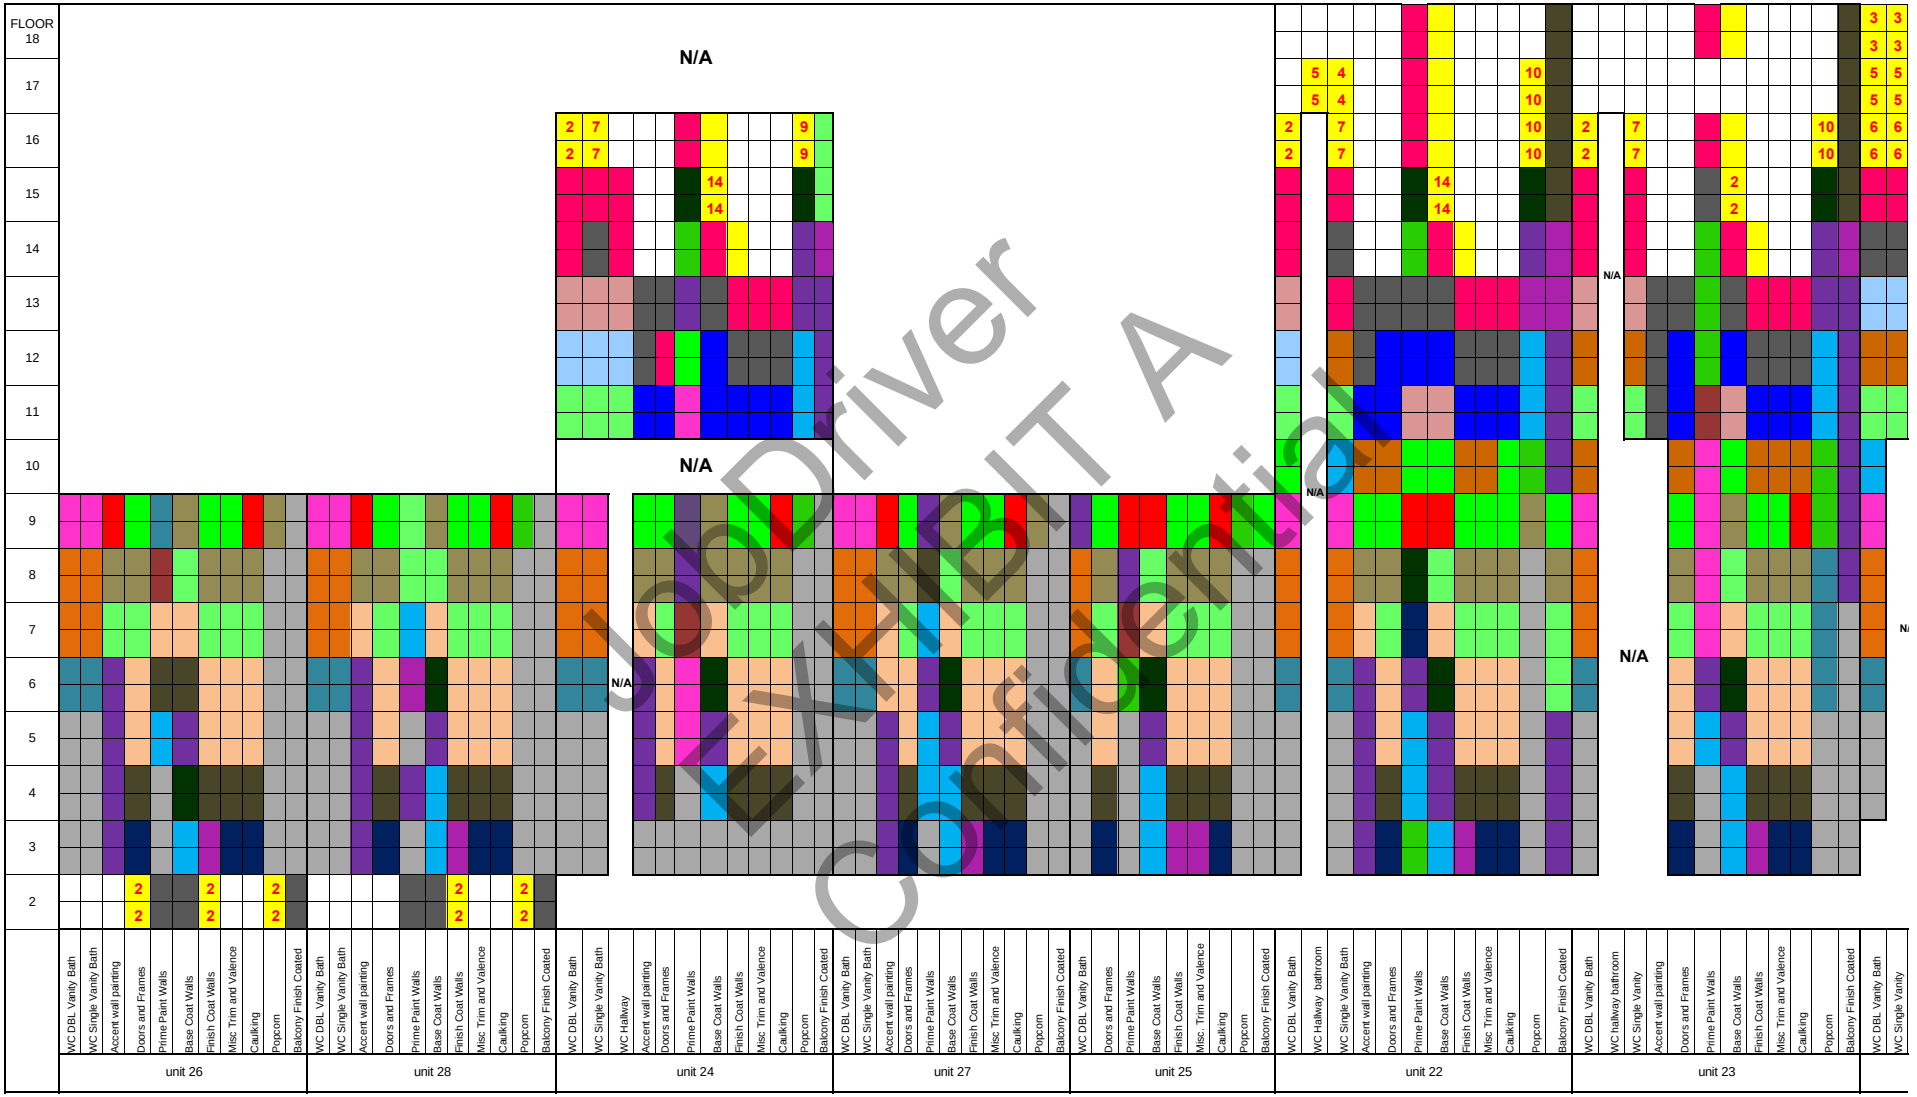

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART

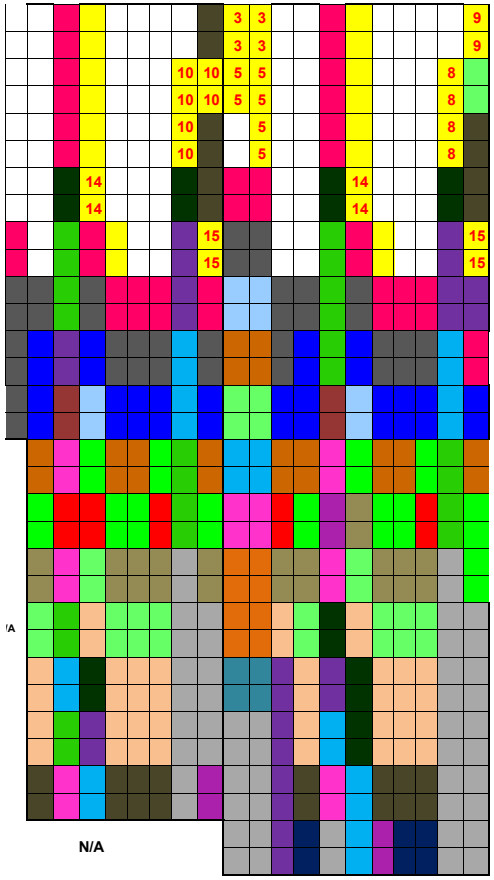

	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									

	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 20											

WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

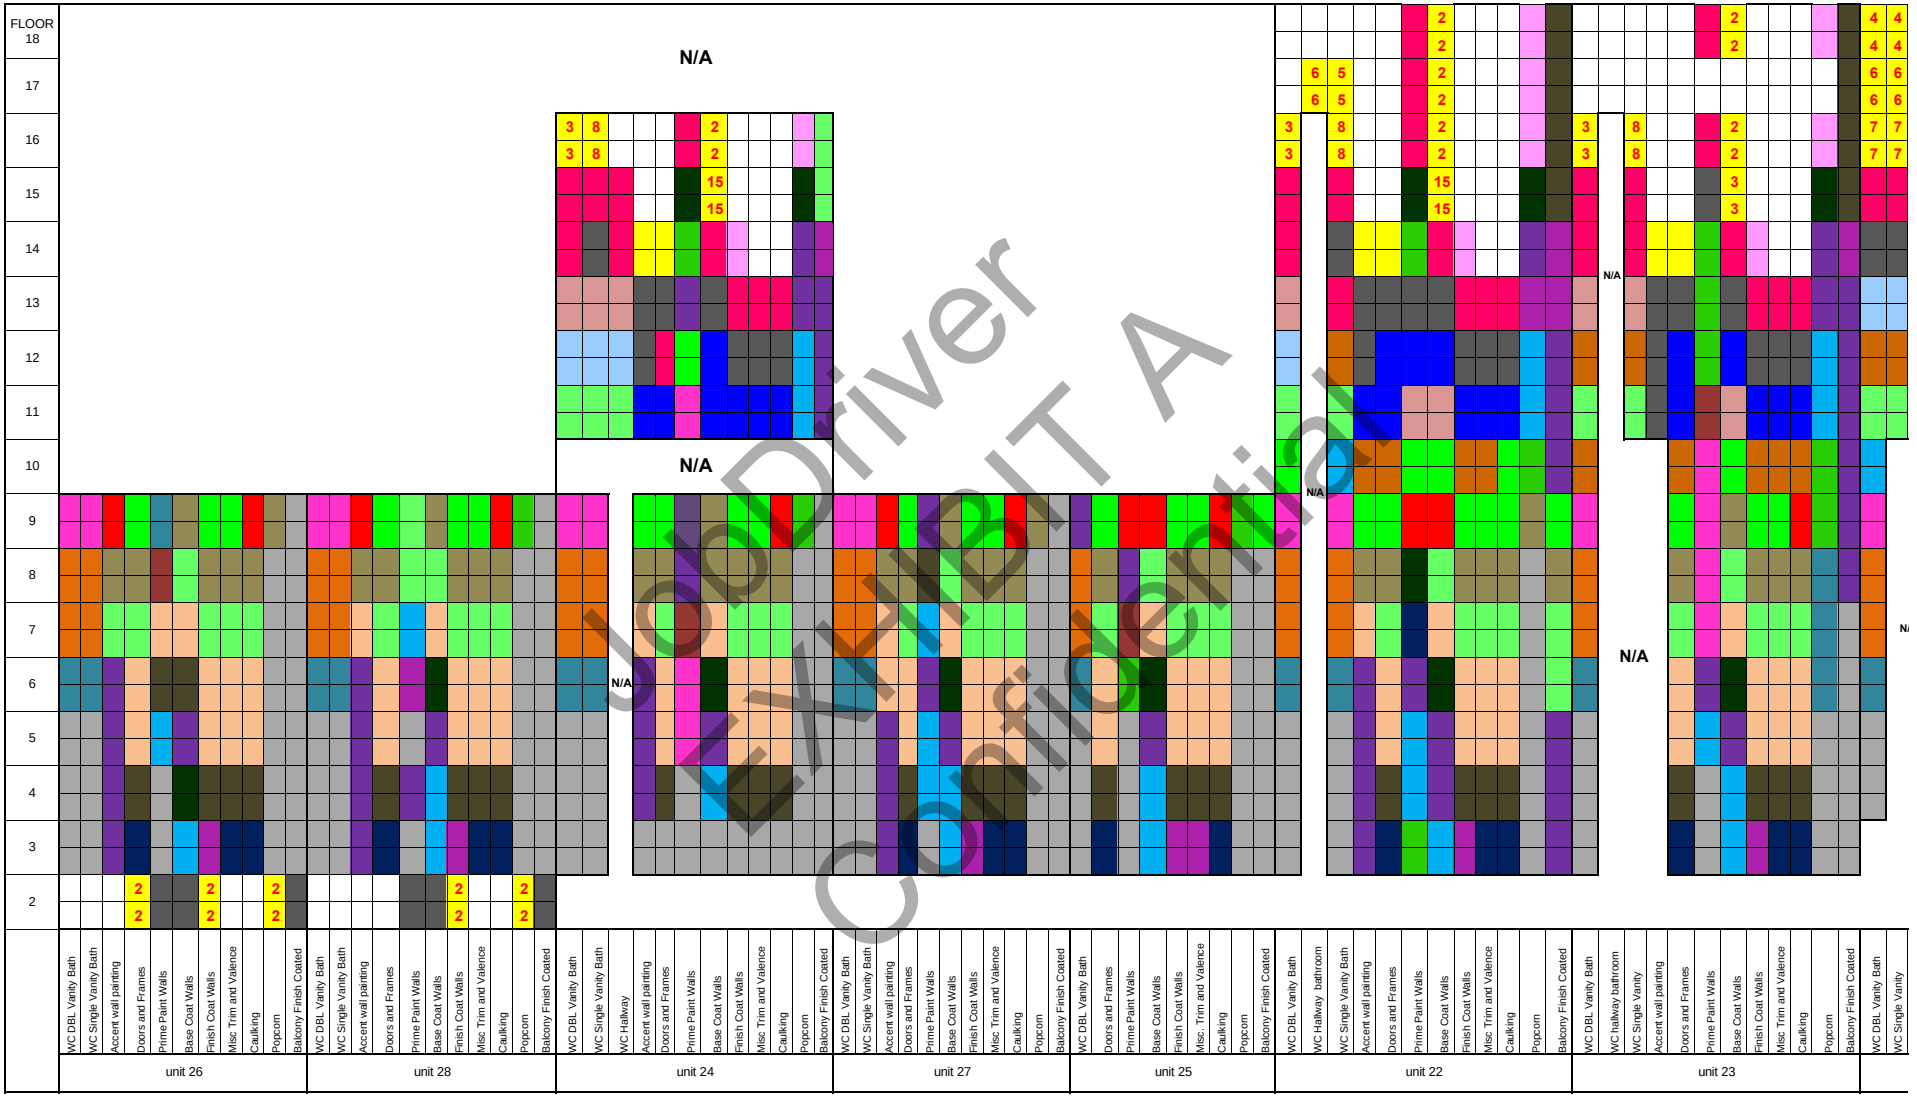

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART

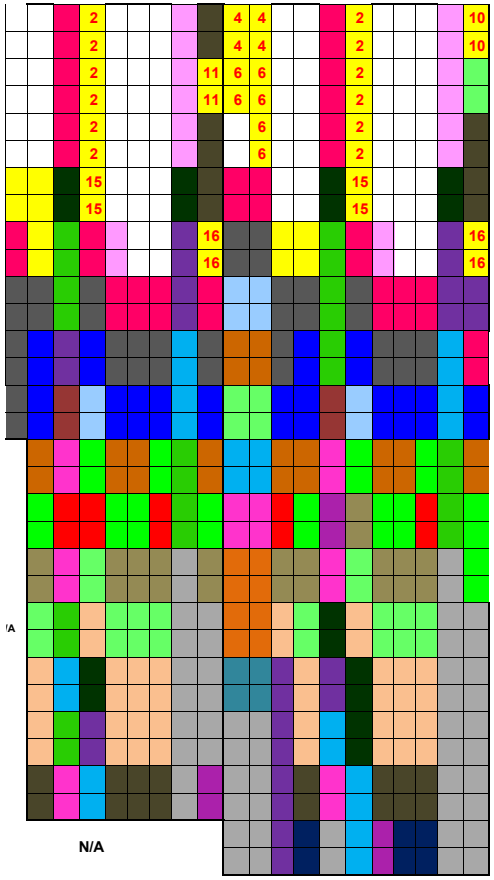

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

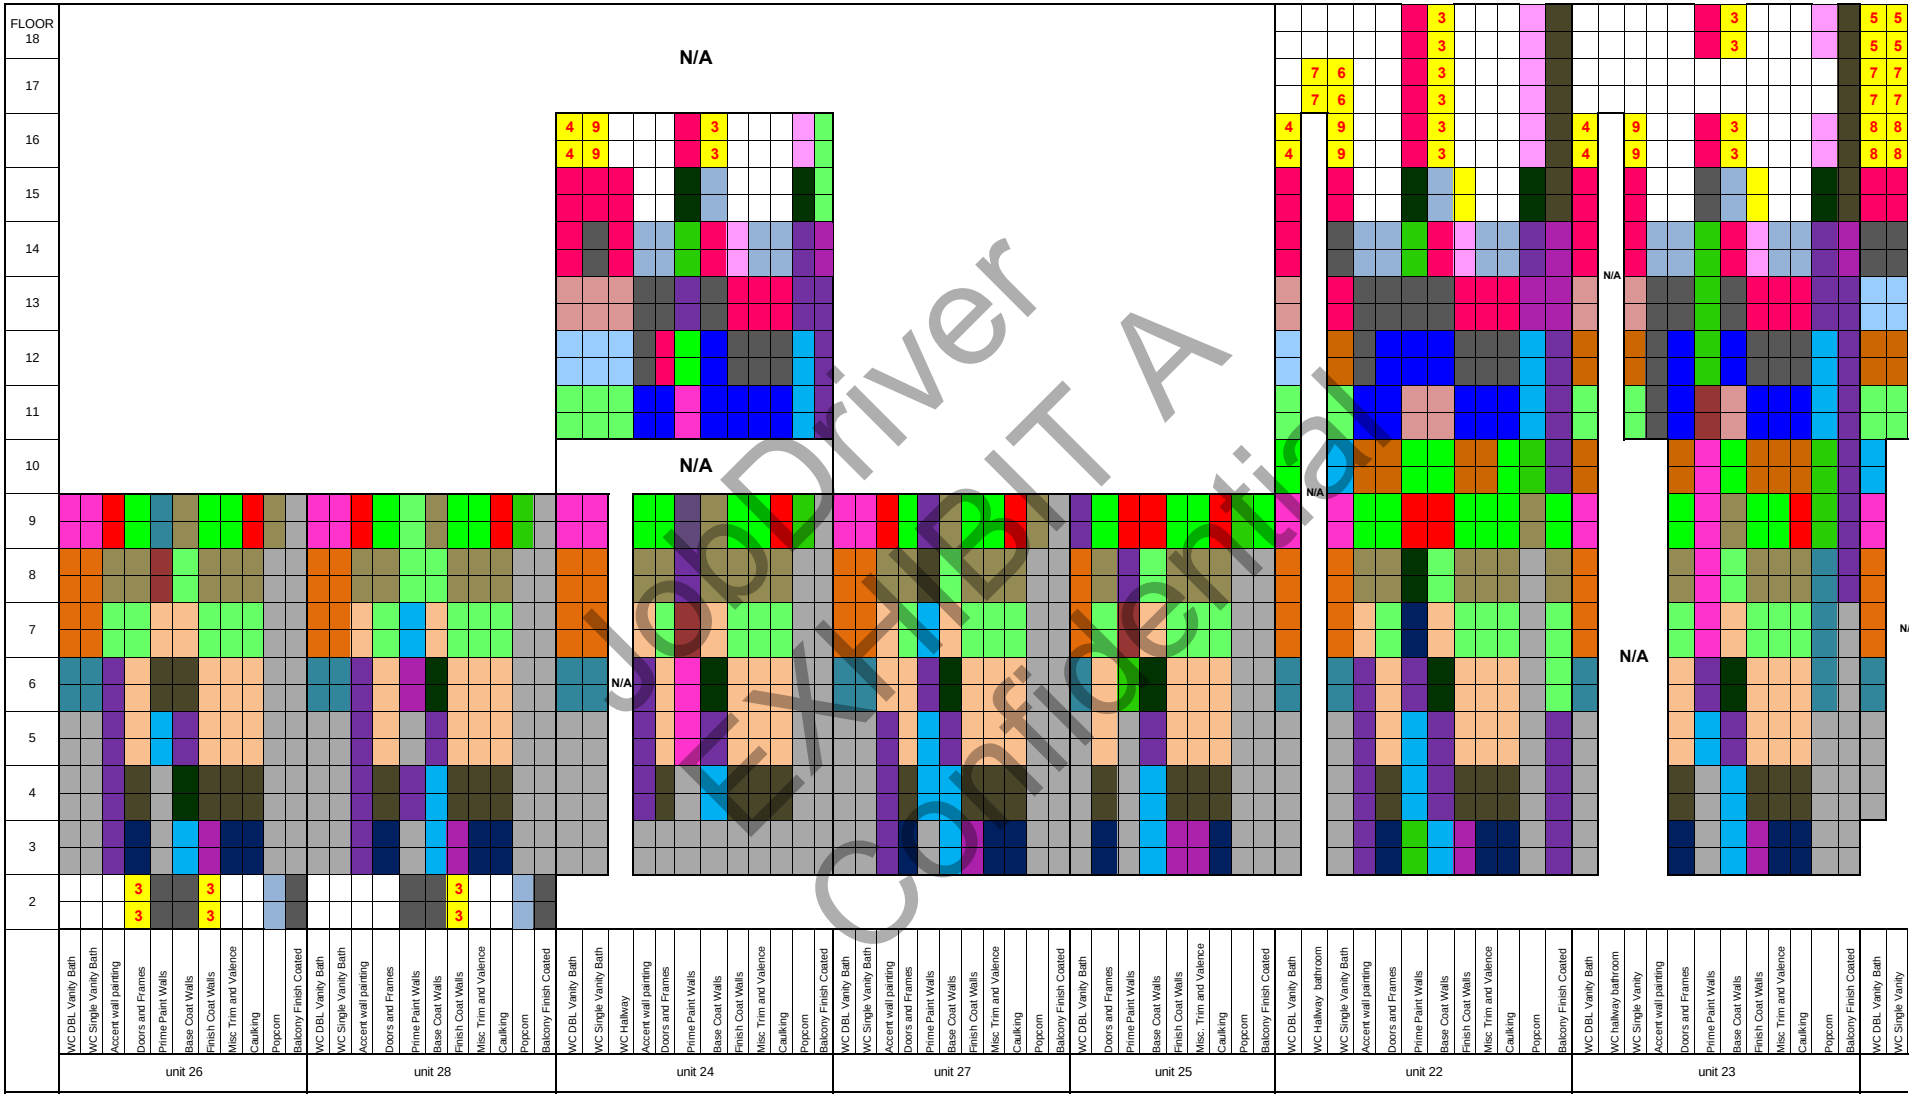

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART

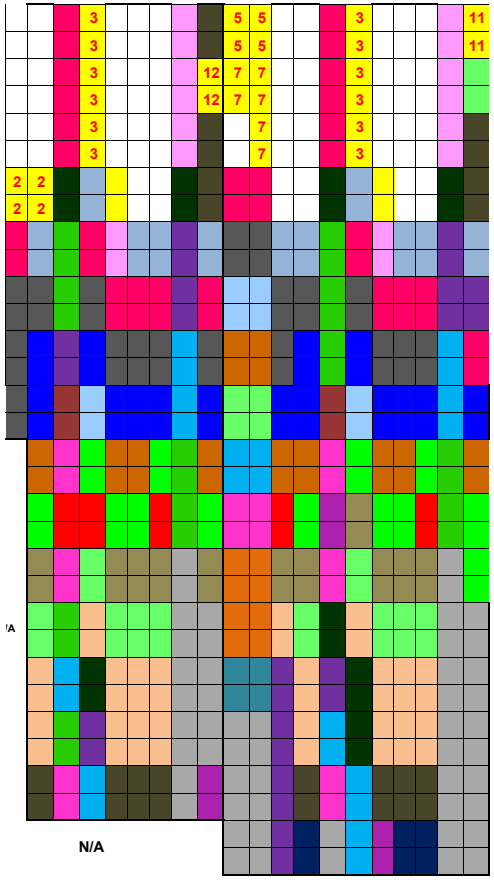

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012
WORK COMPELTED TO DATE 7/16/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

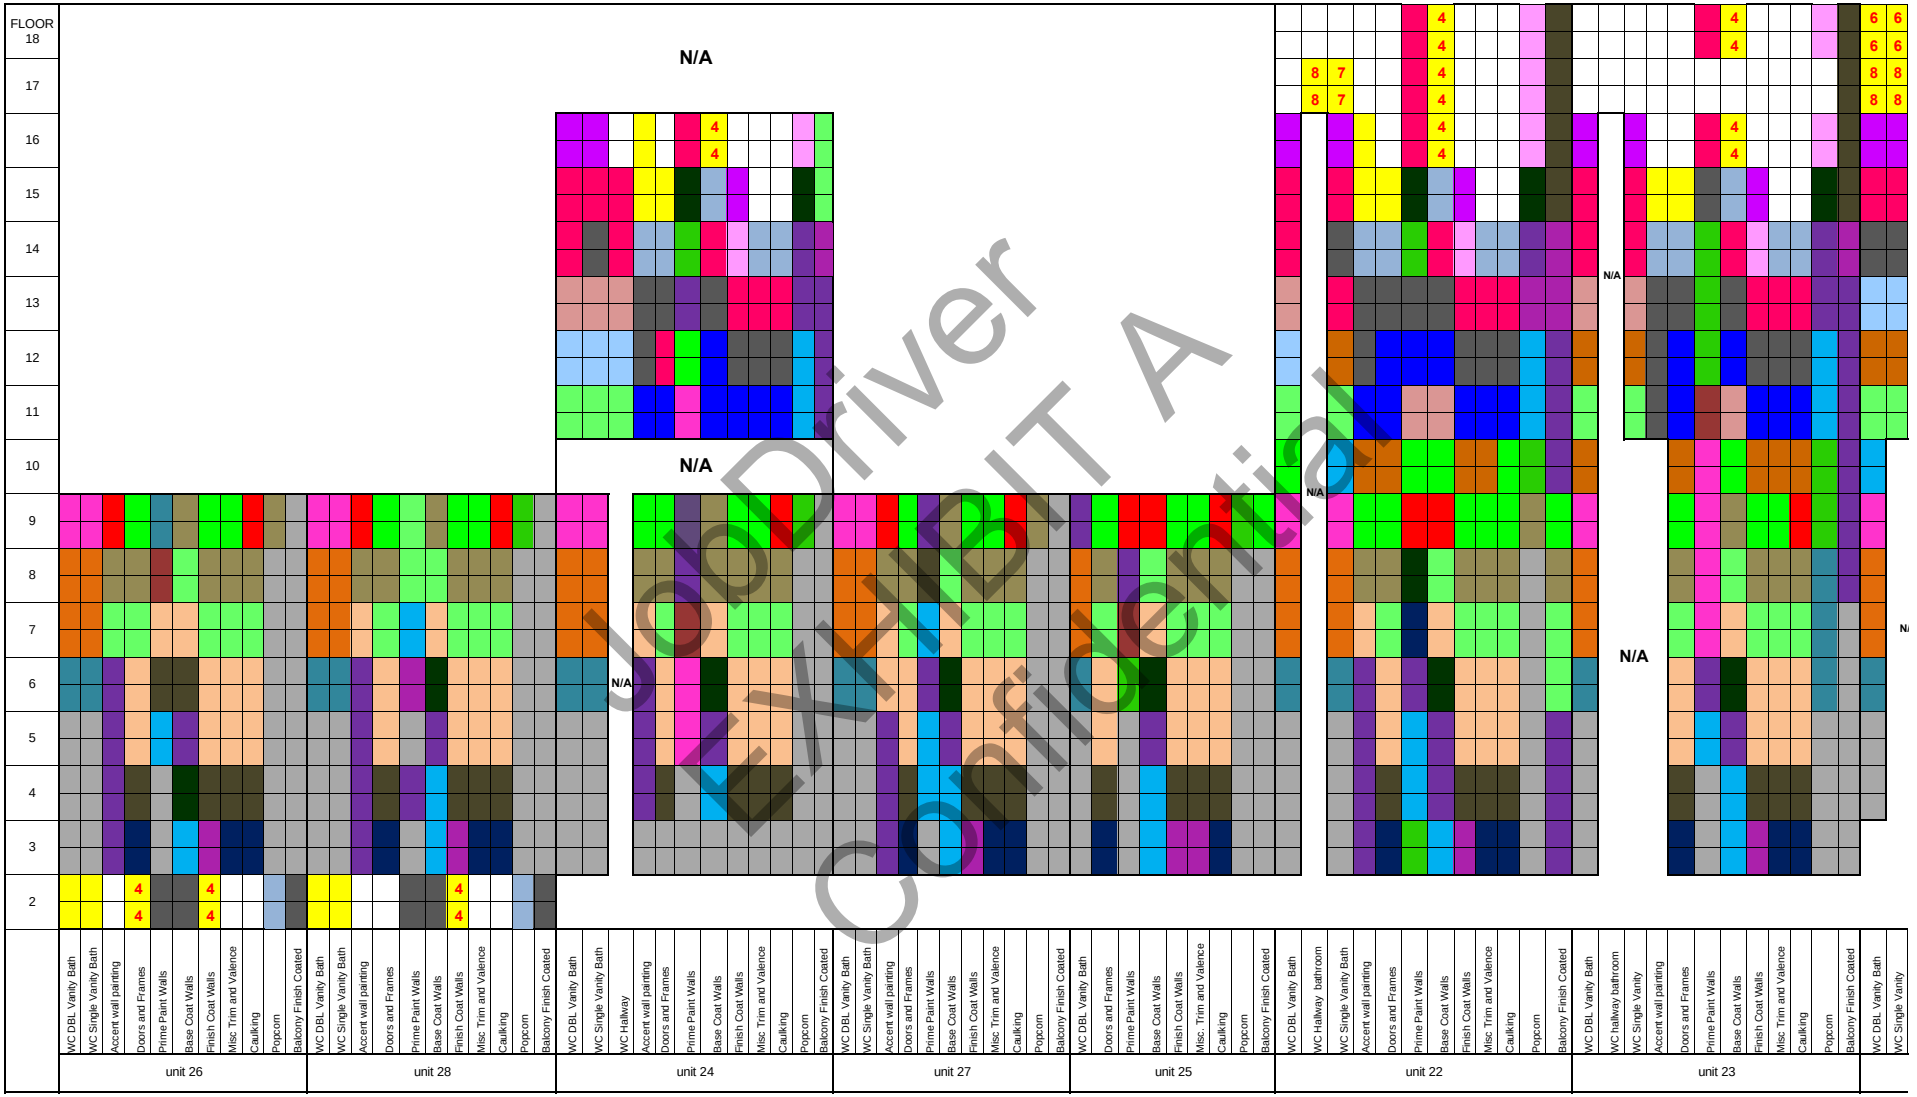

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART

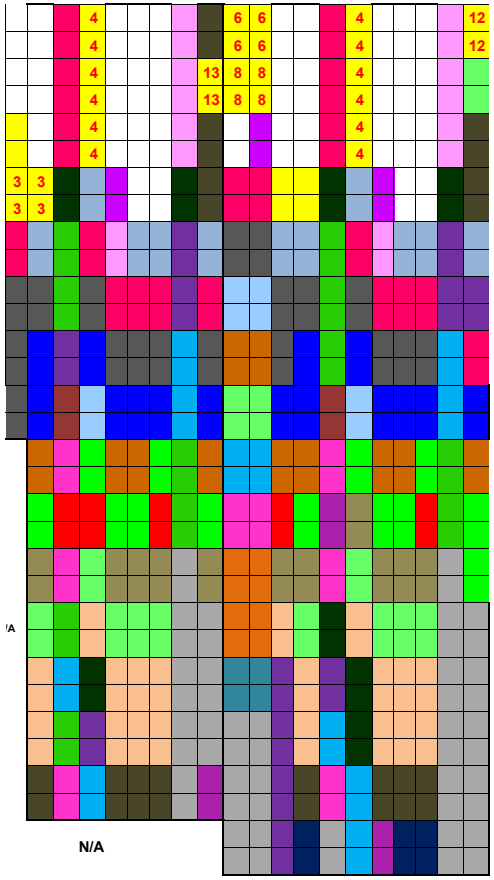

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012
WORK COMPELTED TO DATE 7/16/2012
WORK COMPLETED TO DATE 7/23/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

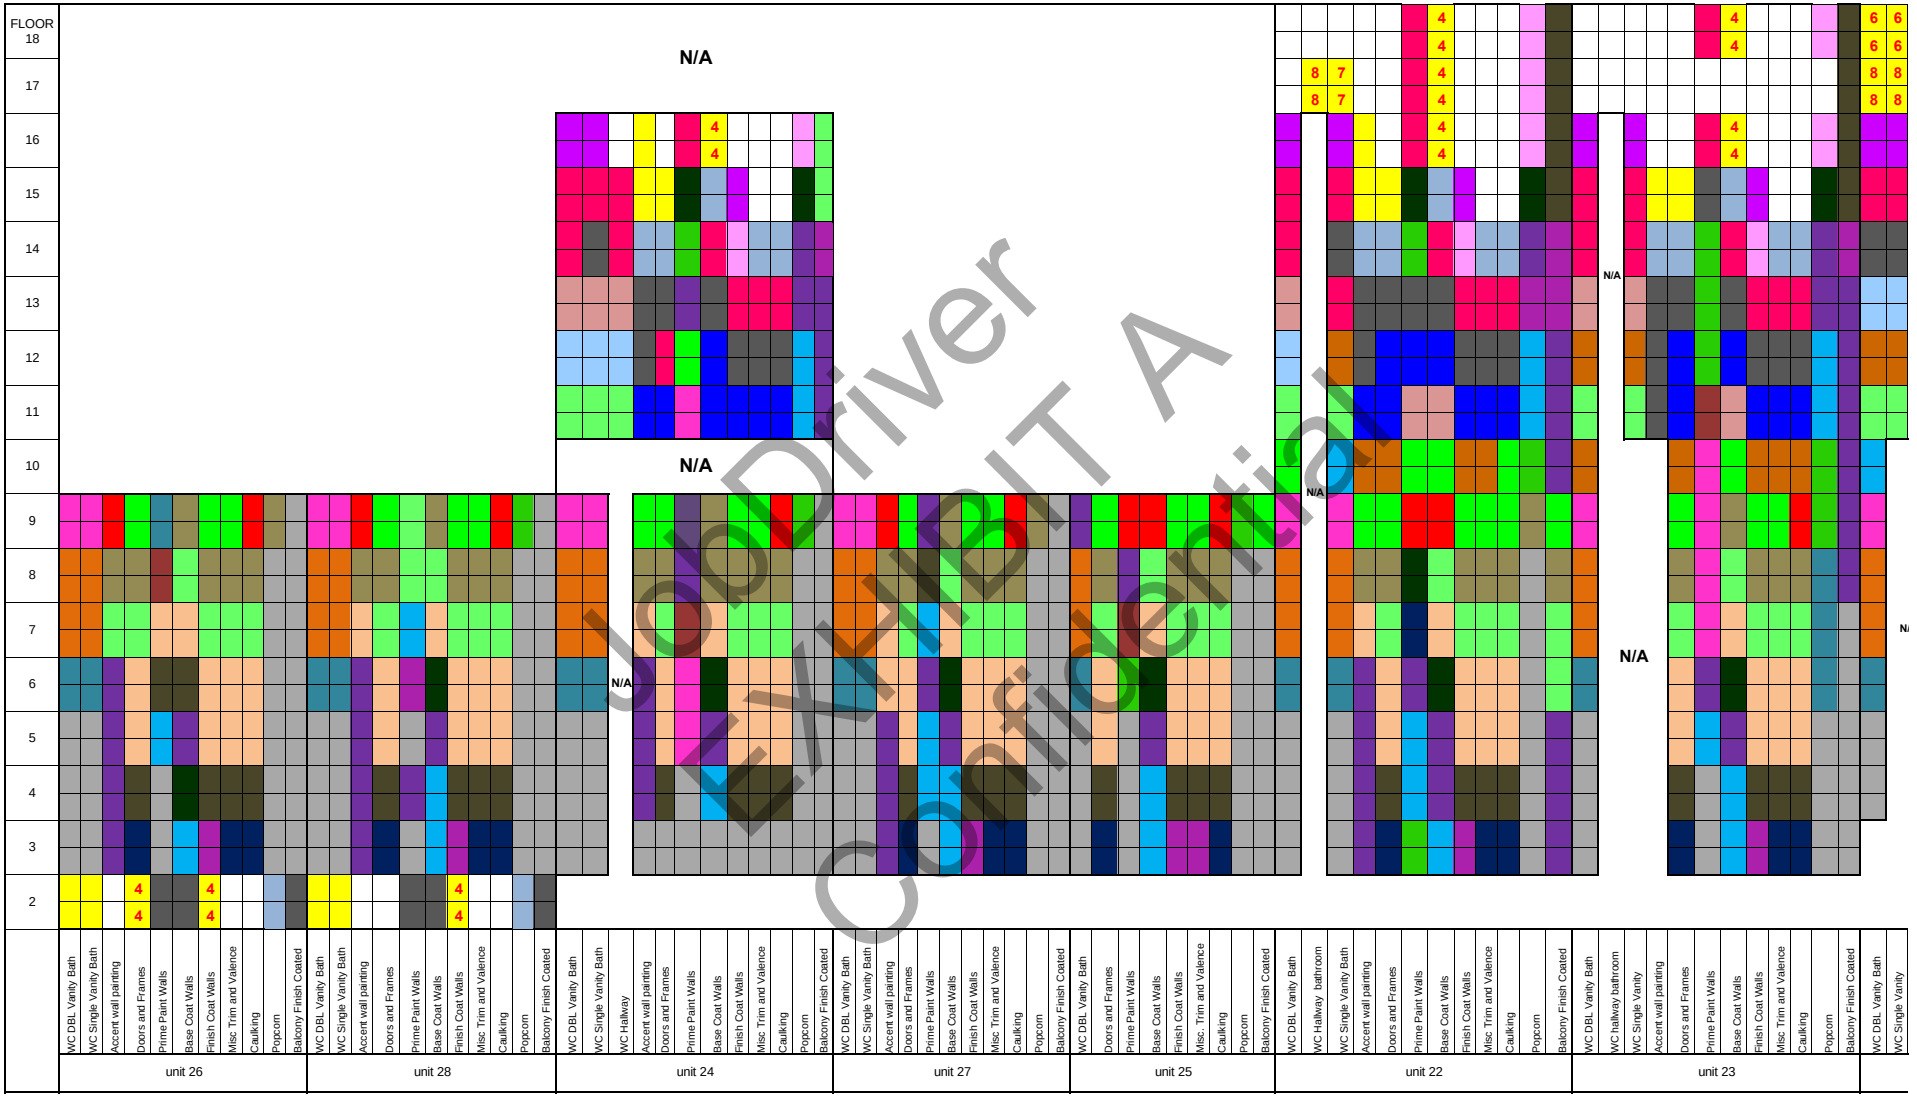

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012

BAY PAINTING PROGRESS CHART

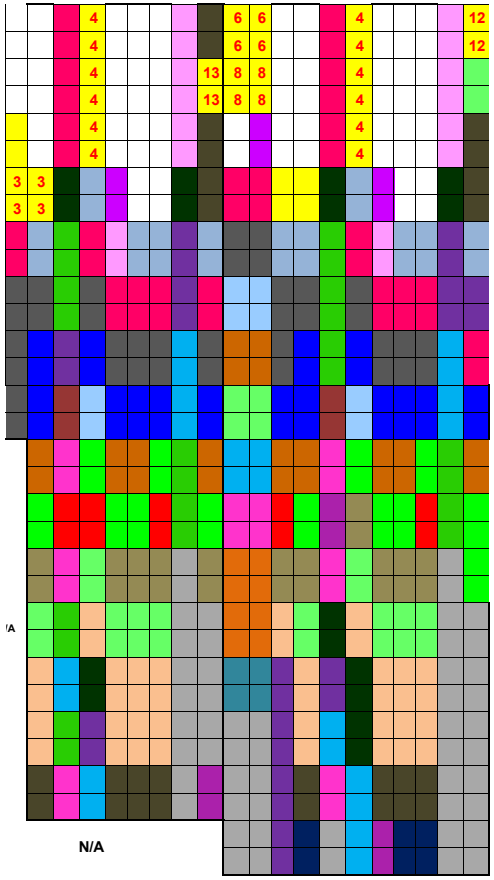

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012
WORK COMPELTED TO DATE 7/16/2012
WORK COMPLETED TO DATE 7/23/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

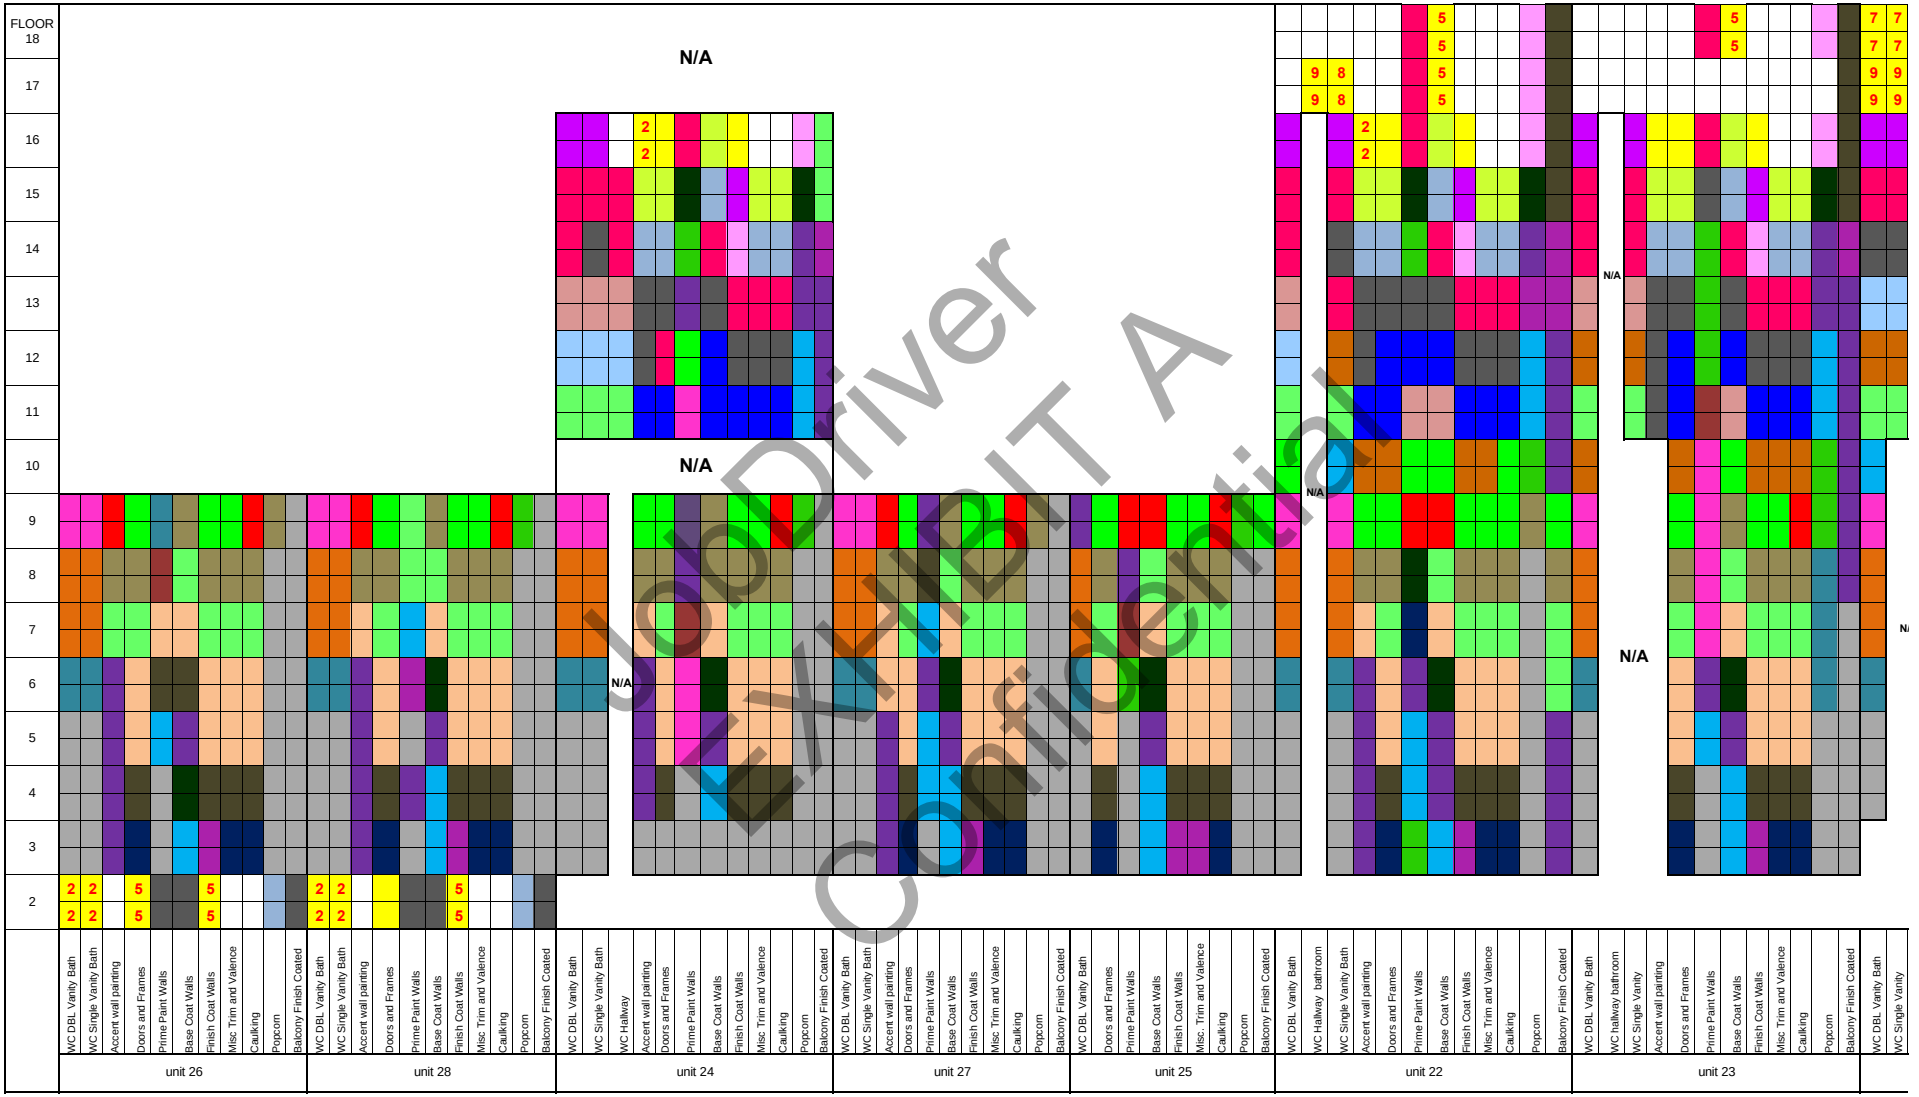

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPELTED TO DATE 7/16/2012
- WORK COMPLETED TO DATE 7/23/2012
- WORK COMP
- WORK COMP

BAY PAINTING PROGRESS CHART

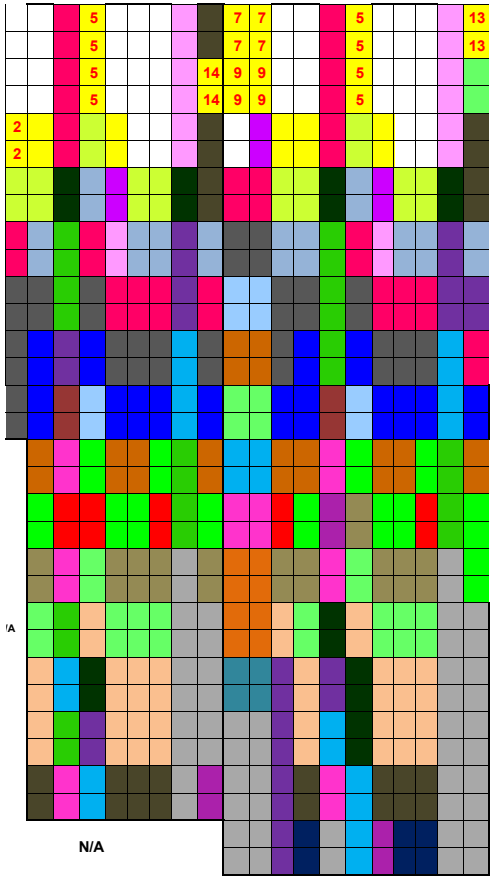

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

LETED TO DATE 7/30/2012
LETED TO DATE 8/6/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

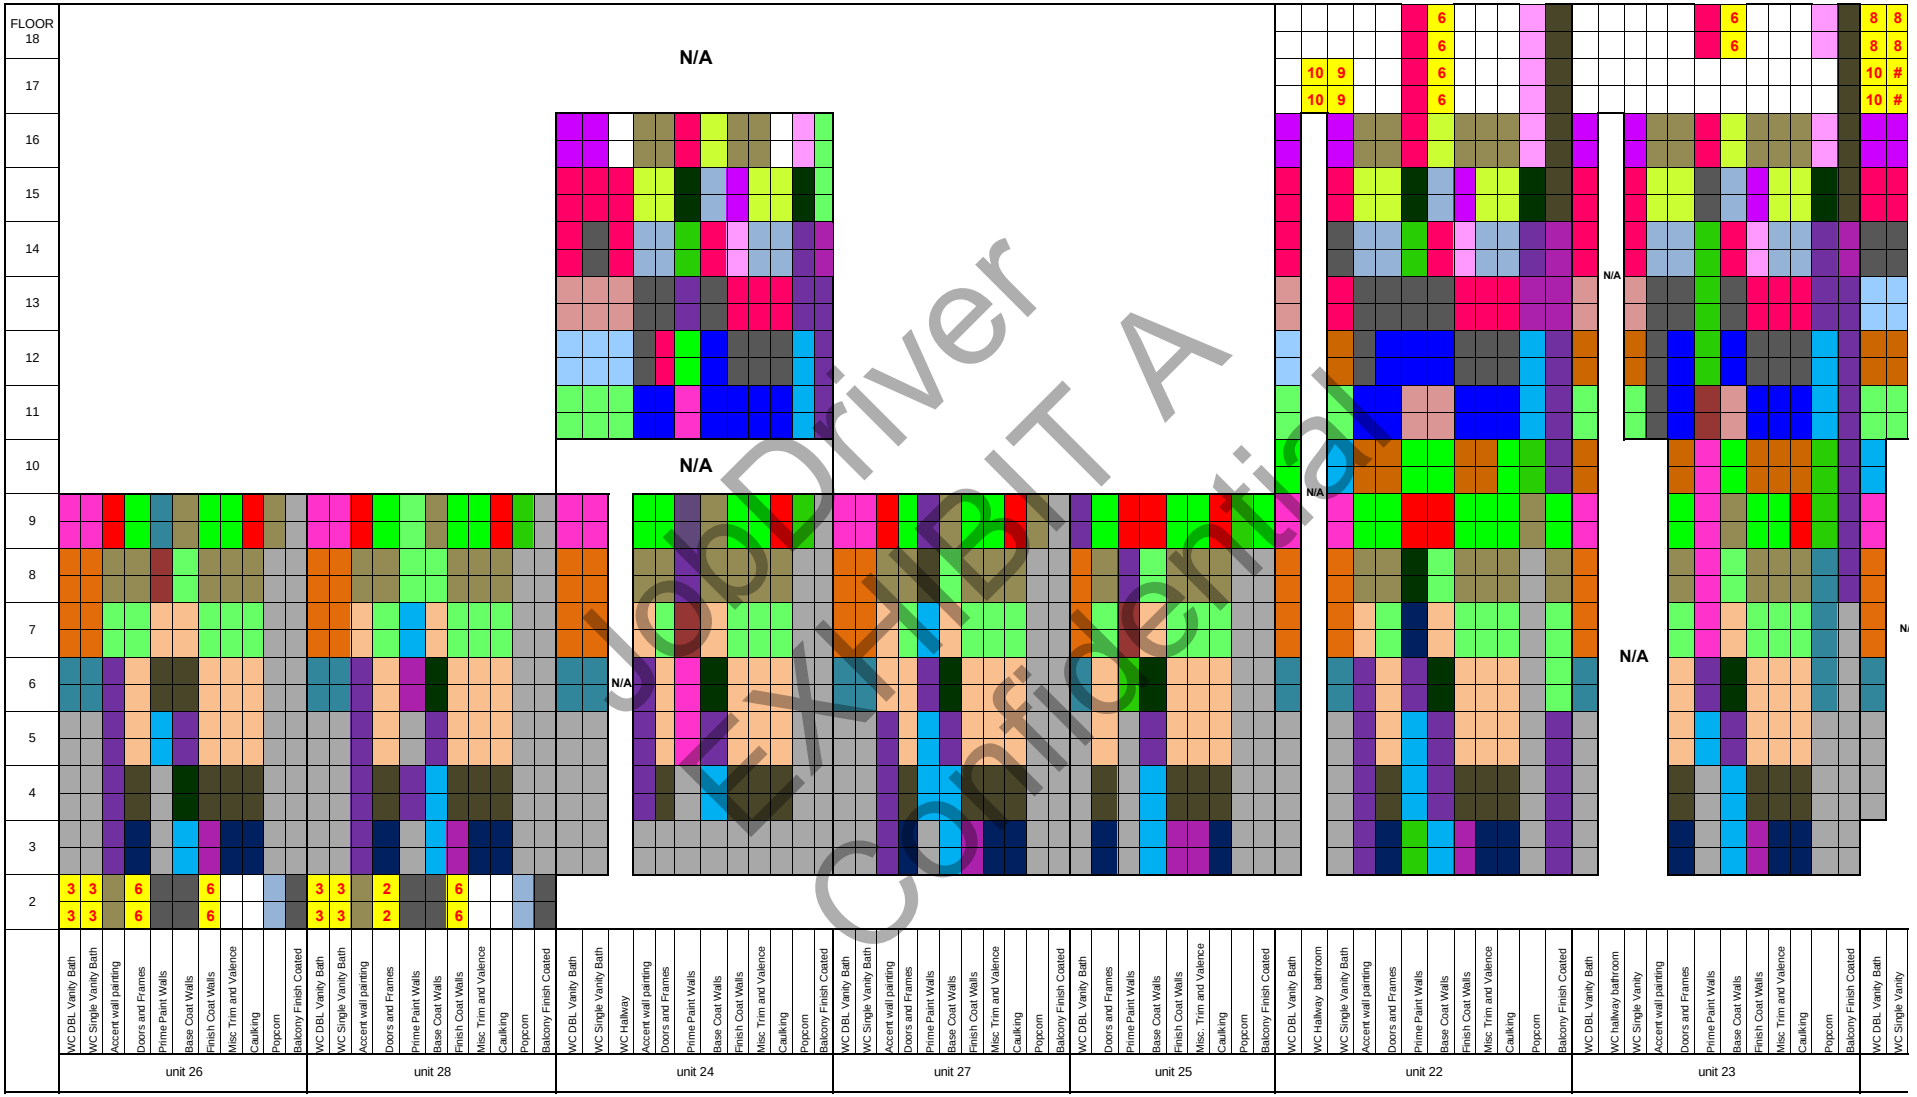

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPELTED TO DATE 7/16/2012
- WORK COMPLETED TO DATE 7/23/2012
- WORK COMP
- WORK COMP
- WORK COMP

BAY PAINTING PROGRESS CHART

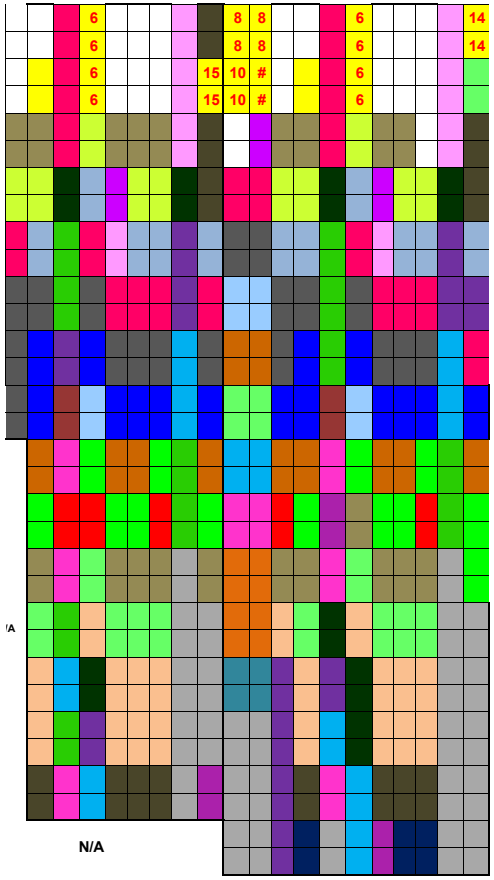

Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulking	Popcorn	Balcony Finish Coated
unit 21									unit 20										

LETED TO DATE 7/30/2012
LETED TO DATE 8/6/2012
LETED TO DATE 8/13/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

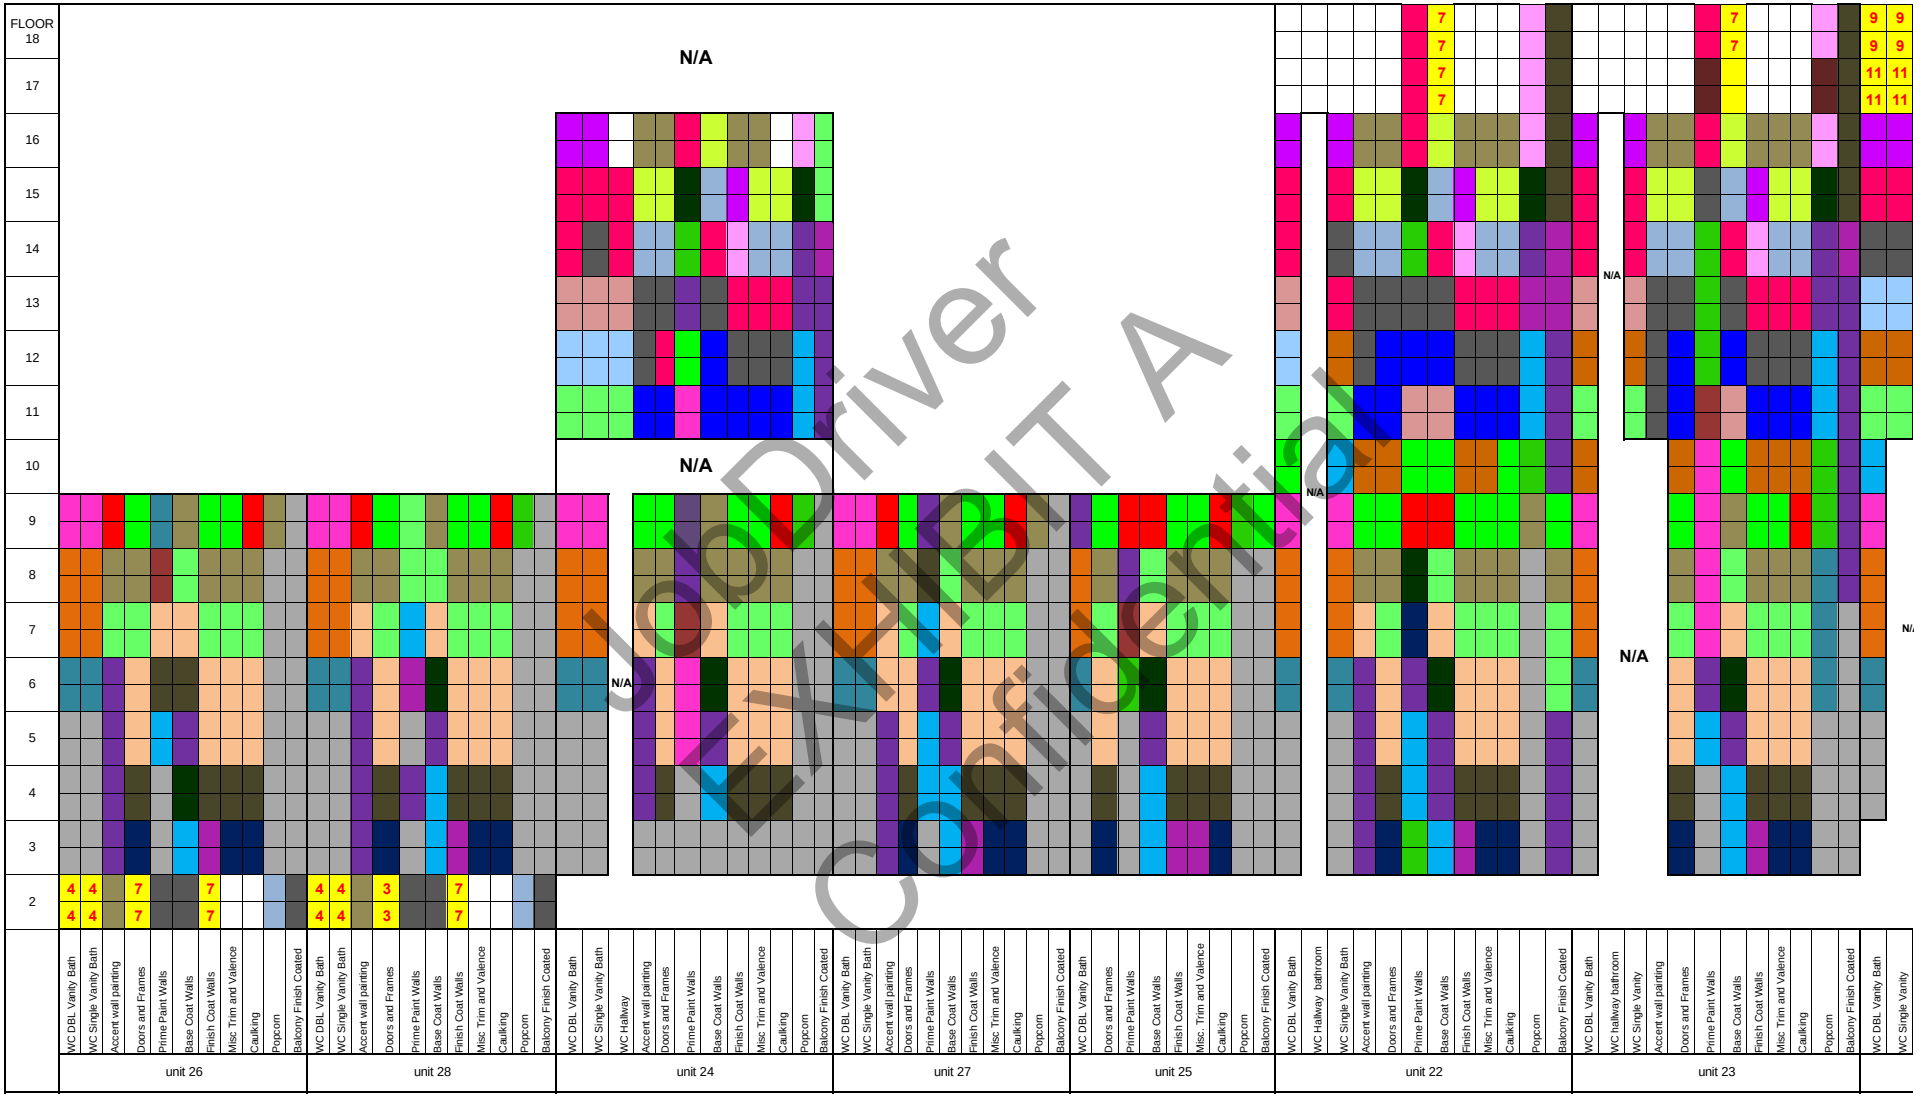

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/2012
- WORK COMPLETED TO DATE 7/23/2012
- WORK COMPL
- WORK COMPL
- WORK COMPL

BAY PAINTING PROGRESS CHART

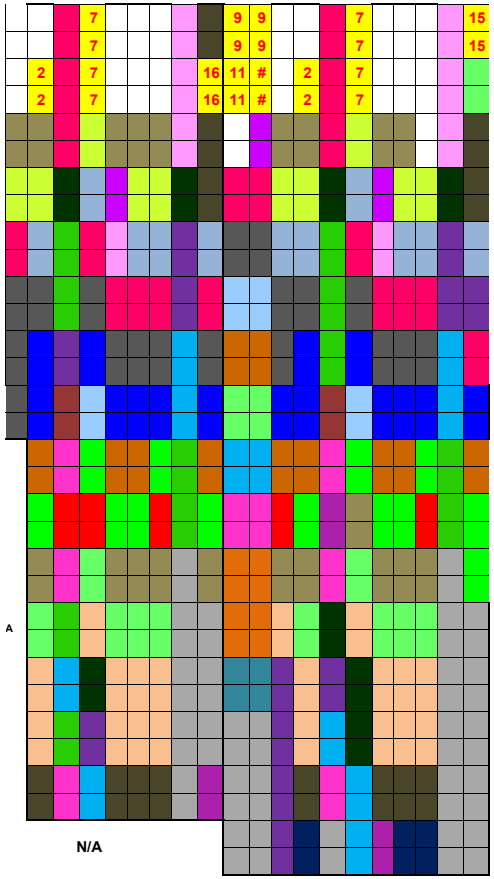

	unit 21	unit 20
Accent wall painting		WC DBL Vanity Bath
Doors and Frames		WC Single Vanity Bath
Prime Paint Walls		Accent wall painting
Base Coat Walls		Doors and Frames
Finish Coat Walls		Prime Paint Walls
Misc Trim and Valence		Base Coat Walls
Caulking		Finish Coat Walls
Popcorn		Misc Trim and Valence
Balcony Finish Coated		Caulking
		Popcorn
		Balcony Finish Coated

.ETED TO DATE 7/30/2012
.ETED TO DATE 8/6/2012
.ETED TO DATE 8/13/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

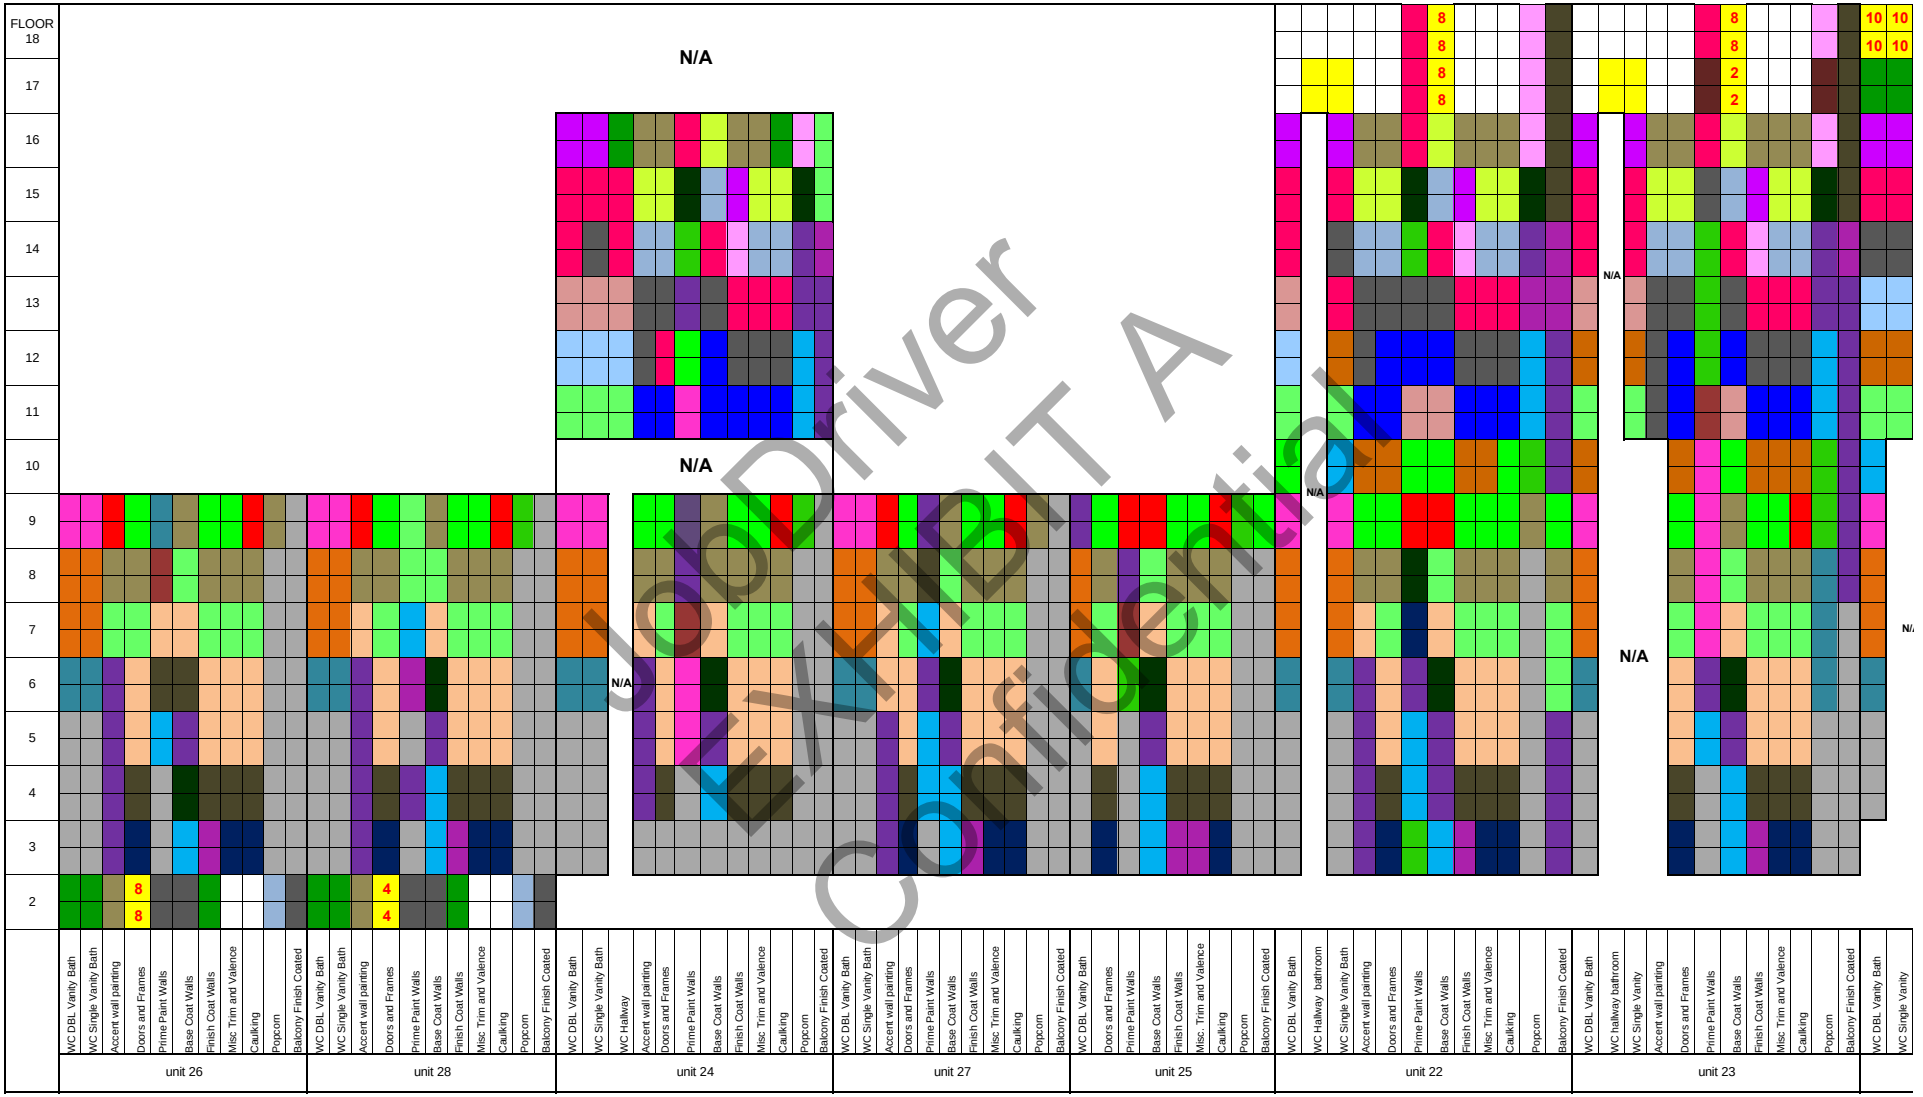

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/2012
- WORK COMPLETED TO DATE 7/23/2012
- WORK COMPL
- WORK COMPL
- WORK COMPL
- WORK COMPL

BAY PAINTING PROGRESS CHART

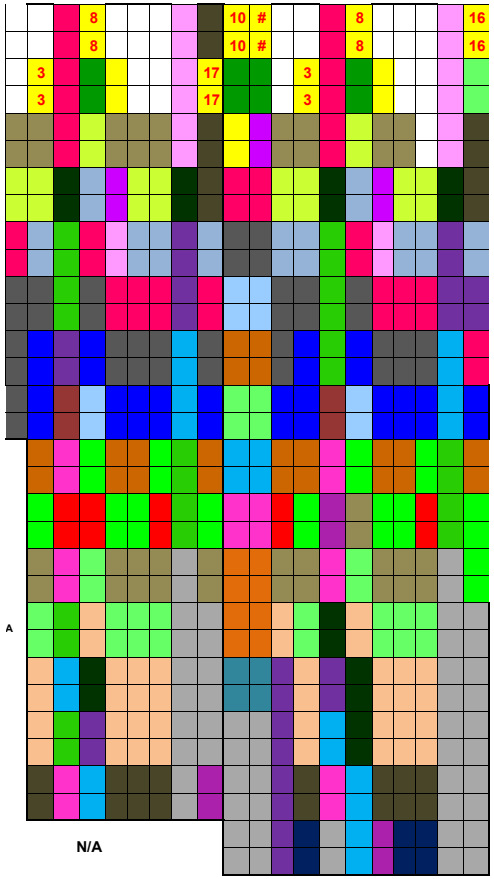

	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulk'ing	Popcorn	Balcony Finish Coated
unit 21									

	WC DBL Vanity Bath	WC Single Vanity Bath	Accent wall painting	Doors and Frames	Prime Paint Walls	Base Coat Walls	Finish Coat Walls	Misc Trim and Valence	Caulk'ing	Popcorn	Balcony Finish Coated
unit 20											

.ETED TO DATE 7/30/2012
.ETED TO DATE 8/6/2012
.ETED TO DATE 8/13/2012
.ETED TO DATE 8/20/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

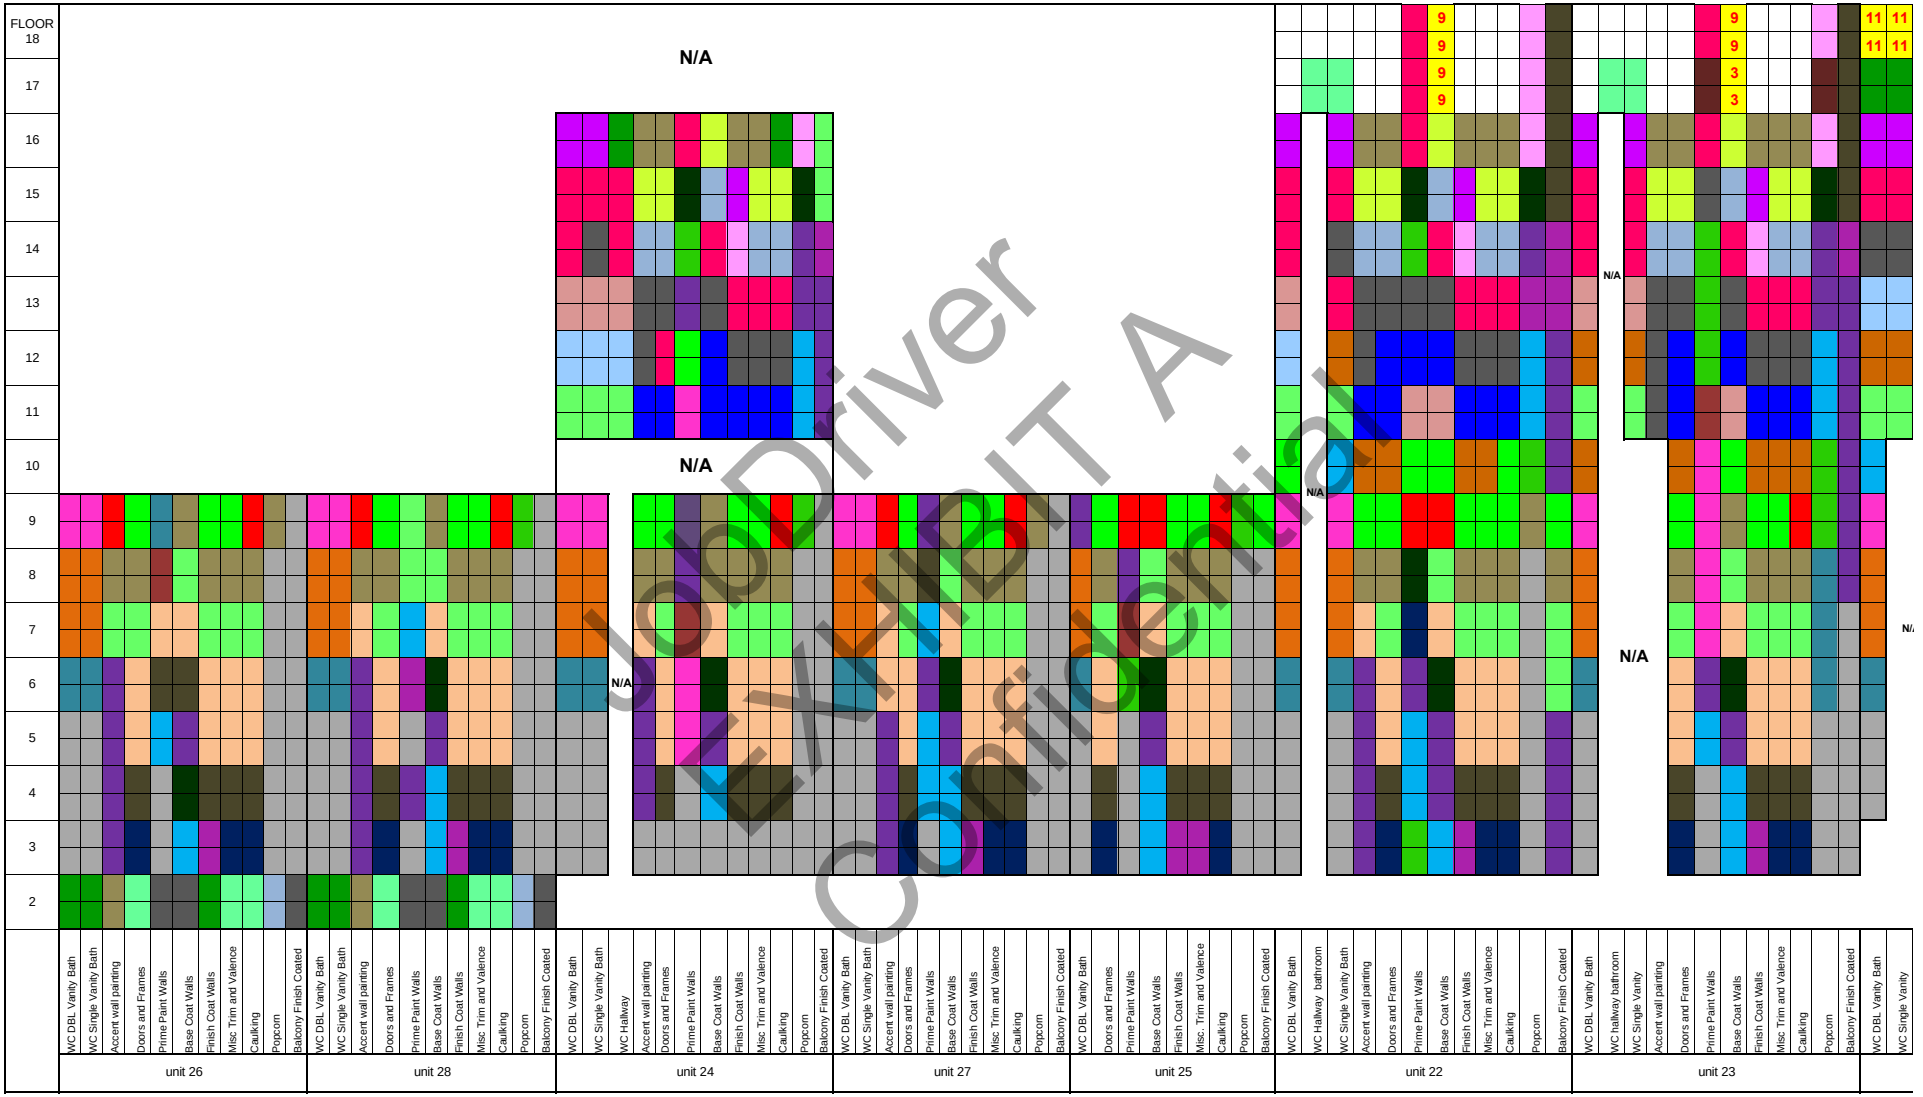

JobDriver
EXHIBIT A
Confidential

BAY PAINT PROGRESS CHART

RUN DATE : 1/30/2012

- WORK COMPLETE TO DATE 1/16/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETE TO DATE 1/23/12
- WORK COMPLETE TO DATE 1/30/12
- No items were completed this week
- WORK COMPLETE TO DATE 2/6/2012
- WORK COMPLETE TO DATE 2/13/2012
- WORK COMPLETE TO DATE 2/20/2012
- WORK COMPLETE TO DATE 2/27/2012
- WORK COMPLETE TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/2012
- WORK COMPLETED TO DATE 7/23/2012
- WORK COMPL
- WORK COMPL
- WORK COMPL
- WORK COMPL
- WORK COMPL

BAY PAINTING PROGRESS CHART

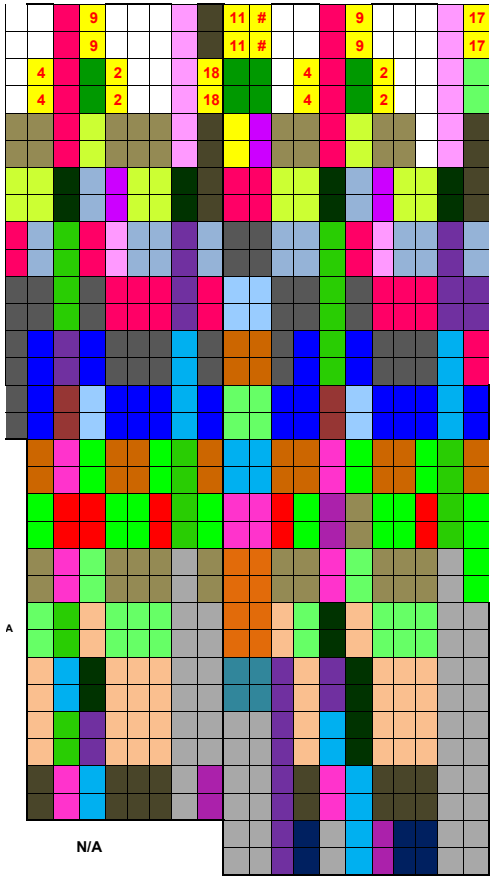

unit 21	unit 20
Accent wall painting	WC DBL Vanity Bath
Doors and Frames	WC Single Vanity Bath
Prime Paint Walls	Accent wall painting
Base Coat Walls	Doors and Frames
Finish Coat Walls	Prime Paint Walls
Misc Trim and Valence	Base Coat Walls
Caulking	Finish Coat Walls
Popcorn	Misc Trim and Valence
Balcony Finish Coated	Caulking
	Popcorn
	Balcony Finish Coated

.ETED TO DATE 7/30/2012
.ETED TO DATE 8/6/2012
.ETED TO DATE 8/13/2012
.ETED TO DATE 8/20/2012
.ETED TO DATE 8/27/2012

JobDriver
EXHIBIT A
Confidential

BAY PAINTING PROGRESS CHART

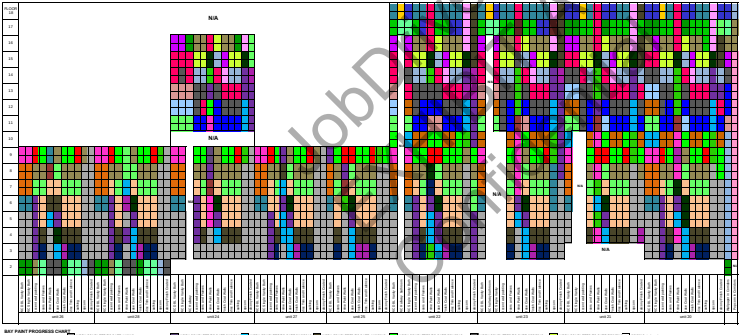

NobDover
Copyright
Confidential

PLEASANTS HARDWARE PROGRESS CHART

FLOOR	26 Unit	28 Unit	24 Unit	27 Unit	25 Unit	22 Unit	23 Unit	21 Unit	20 Unit
18	N/A								
17									
16									
15									
14									
13									
12									
11									
10									
9									
8									
7									
6									
5									
4									
3								N/A	
2			N/A						
	Main&Lockout Entry Door	Main&Lockout Entry Door	Main&Lockout Entry Door	Main&Lockout Entry Door	Entry Door	Entry Door hardware	Entry door hardware	Entry Door hardware	Entry Door
	Entry door hardware	Entry door hardware	Entry door hardware	Entry door hardware	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door	Entry Door hardware
	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware	Living Rm Closet door
	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware	Bathroom Pocket door	Communicating doors	Communicating doors	Bathroom Pocket door	L. Rm Closet Hardware
	Communicating doors	Communicating doors	Communicating doors	Communicating doors	Pocket door hardware	Comm. door hardware	Comm. door hardware	Pocket door hardware	Bathroom Pocket door
	Comm. door hardware	Comm. door hardware	Comm. door hardware	Comm. door hardware	Master Bath Swing Door	Lockout Bath swing door	Lockout Bath swing door	Master Bath Swing Door	Pocket door hardware
	Lockout Bath swing door	Lockout Bath swing door	Lockout Bath swing door	Lockout Bath swing door	M.B. Swing Dr. Hardware	L.O. Bath Hardware	L.O. Bath Hardware	M.B. Swing Dr. Hardware	Master Bath Swing Door
	L.O. Bath Hardware	L.O. Bath Hardware	L.O. Bath Hardware	L.O. Bath Hardware	M.Bed Closet Doors	L.O. Closet Door	L.O. Closet Door	M.Bed Closet Doors	M.B. Swing Dr. Hardware
	L.O. Closet Door	L.O. Closet Door	L.O. Closet Door	L.O. Closet Door	M. Bed Closet Hardware	L.O. Closet hardware	L.O. Closet hardware	M. Bed Closet Hardware	M.Bed Closet Doors
	L.O. Closet hardware	L.O. Closet hardware	L.O. Closet hardware	L.O. Closet hardware		Bathroom Pocket door	Bathroom Pocket door		M. Bed Closet Hardware
	Bathroom Pocket door	Bathroom Pocket door	Bathroom Pocket door	Bathroom Pocket door		Pocket door hardware	Pocket door hardware		
	Pocket door hardware	Pocket door hardware	Pocket door hardware	Pocket door hardware		Master Bath Swing Door	Master Bath Swing Door		
	Master Bath Swing Door	Master Bath Swing Door	Master Bath Swing Door	Master Bath Swing Door		M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware		
	M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware		M.Bed Closet Doors	M.Bed Closet Doors		
	M.Bed Closet Doors	M.Bed Closet Doors	M.Bed Closet Doors	M.Bed Closet Doors		M. Bed Closet Hardware	M. Bed Closet Hardware		
	M. Bed Closet Hardware	M. Bed Closet Hardware	M. Bed Closet Hardware	M. Bed Closet Hardware					

JobDriver
EXHIBIT A
Confidential

PLEASANTS HARDWARE PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/27/12

AREAS AVAILABLE FOR YOU TO WORK

* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

INCOMPLETE ITEMS

PLEASANTON-HARDWARE PROGRESS CHART

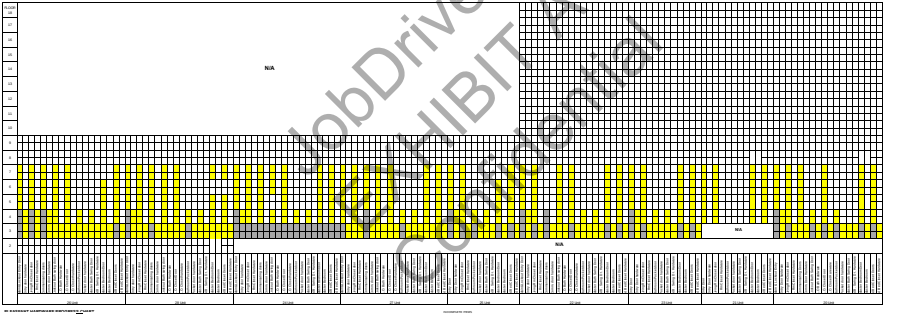

JobDriver
EXHIBIT A
Confidential

M. KARNOVAT HARDWARE IMPLEMENTS CHART

PLAN DATE: 6/14/2019

- DESIGN COMPLETE TO SUPPLY SERVICE
- DESIGN COMPLETE AND SUPPLY SERVICE COMPLETE
- DESIGN AND SERVICE INCLUDED IN FIRM SERVICE AFFIDAVITS

CONSIDERATION PROVIDED

Pleasants Hardware

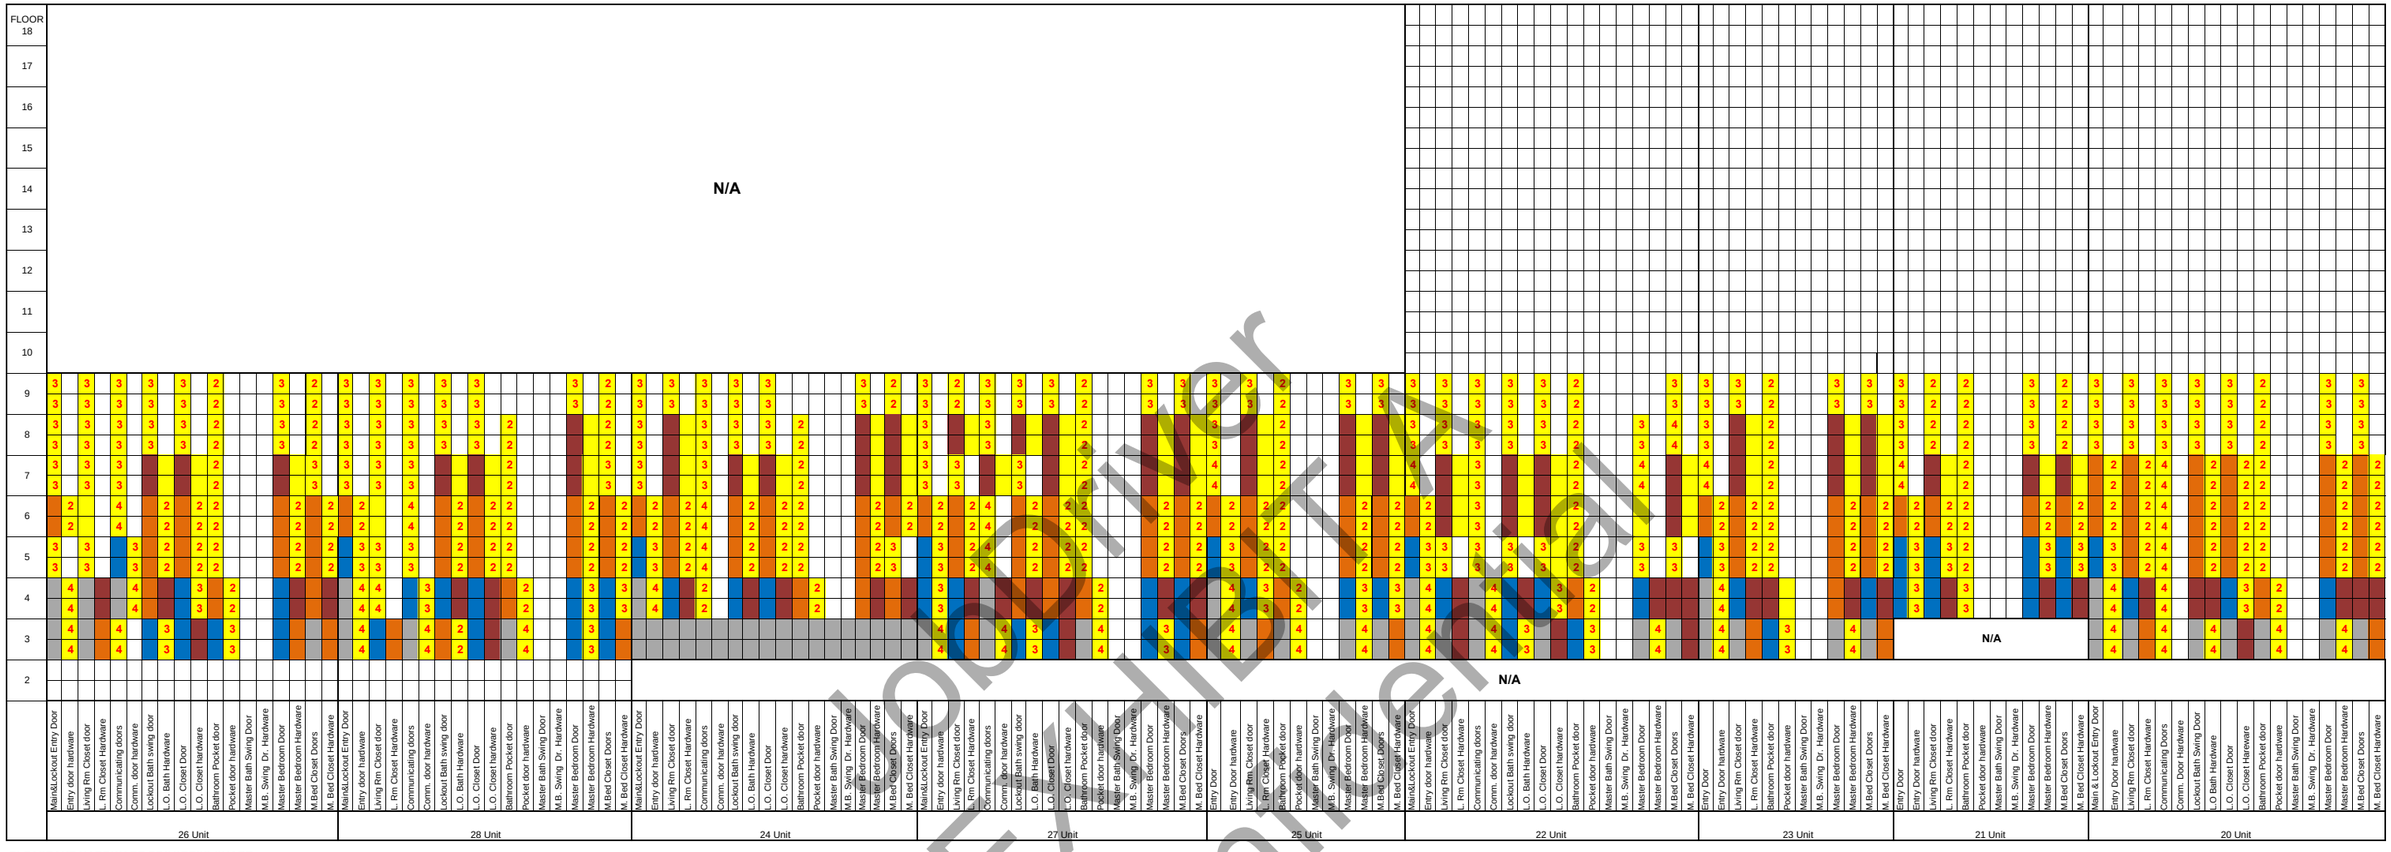

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

INCOMPLETE ITEMS

! 5TH FLOOR COULD NOT BE WALKED DUE TO PAINTING 2/15/2012

Property of
Exhibit M
Confidential

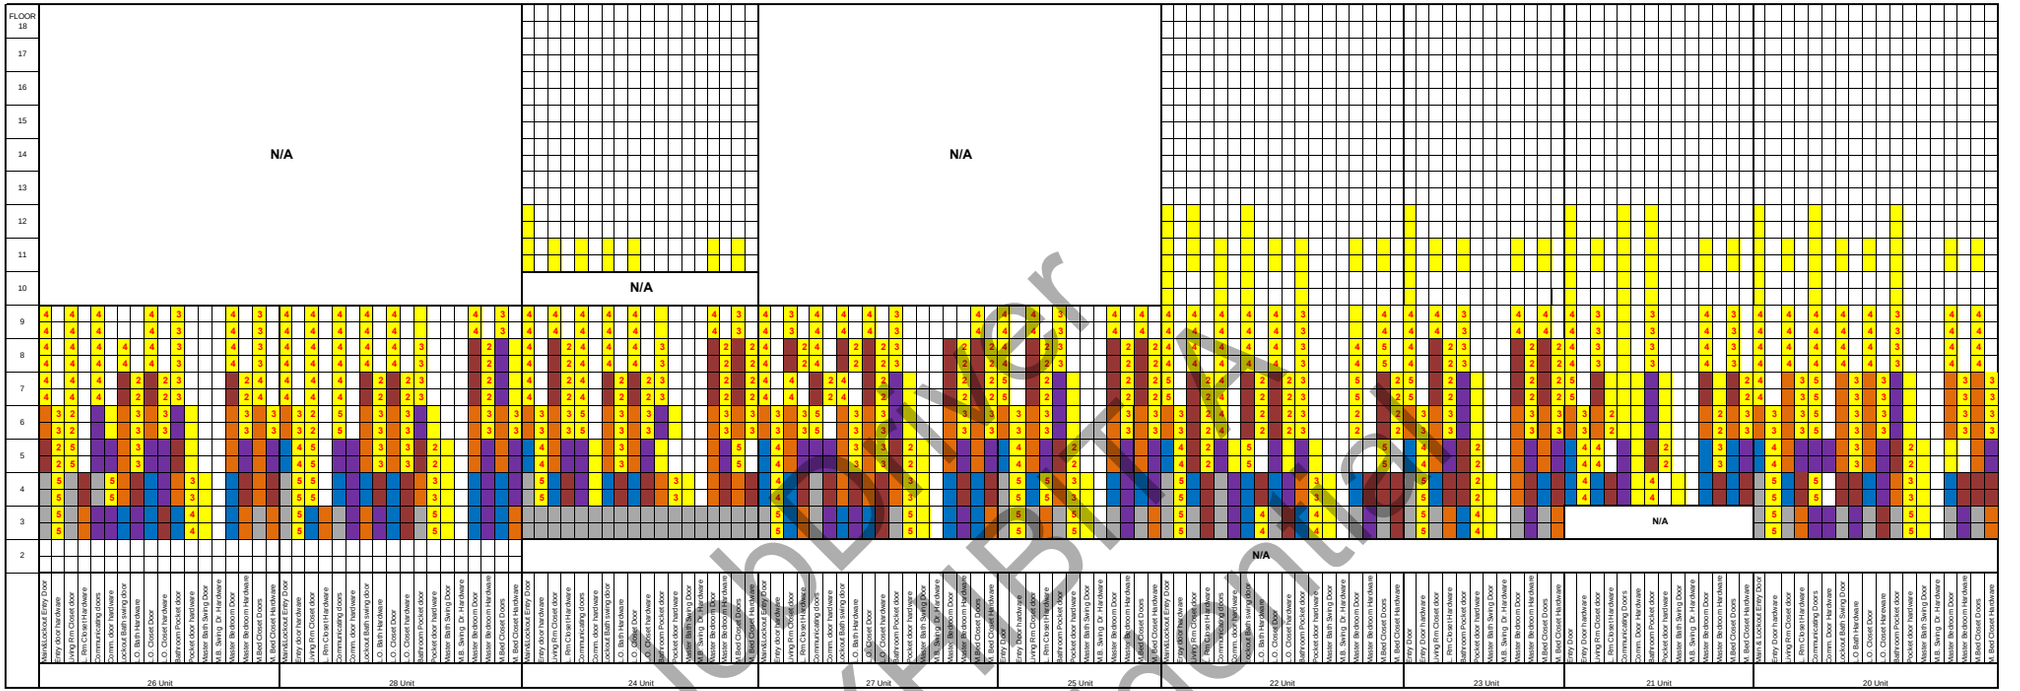

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

WORK COMPLETE TO DATE 1/27/12
AREAS AVAILABLE FOR YOU TO WORK
AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
WORK COMPLETED TO DATE 2/1/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

INCOMPLETE ITEMS

Job Buyer
EXHIBIT
Confidential

PLEASANTS HARDWARE PROGRESS CHART

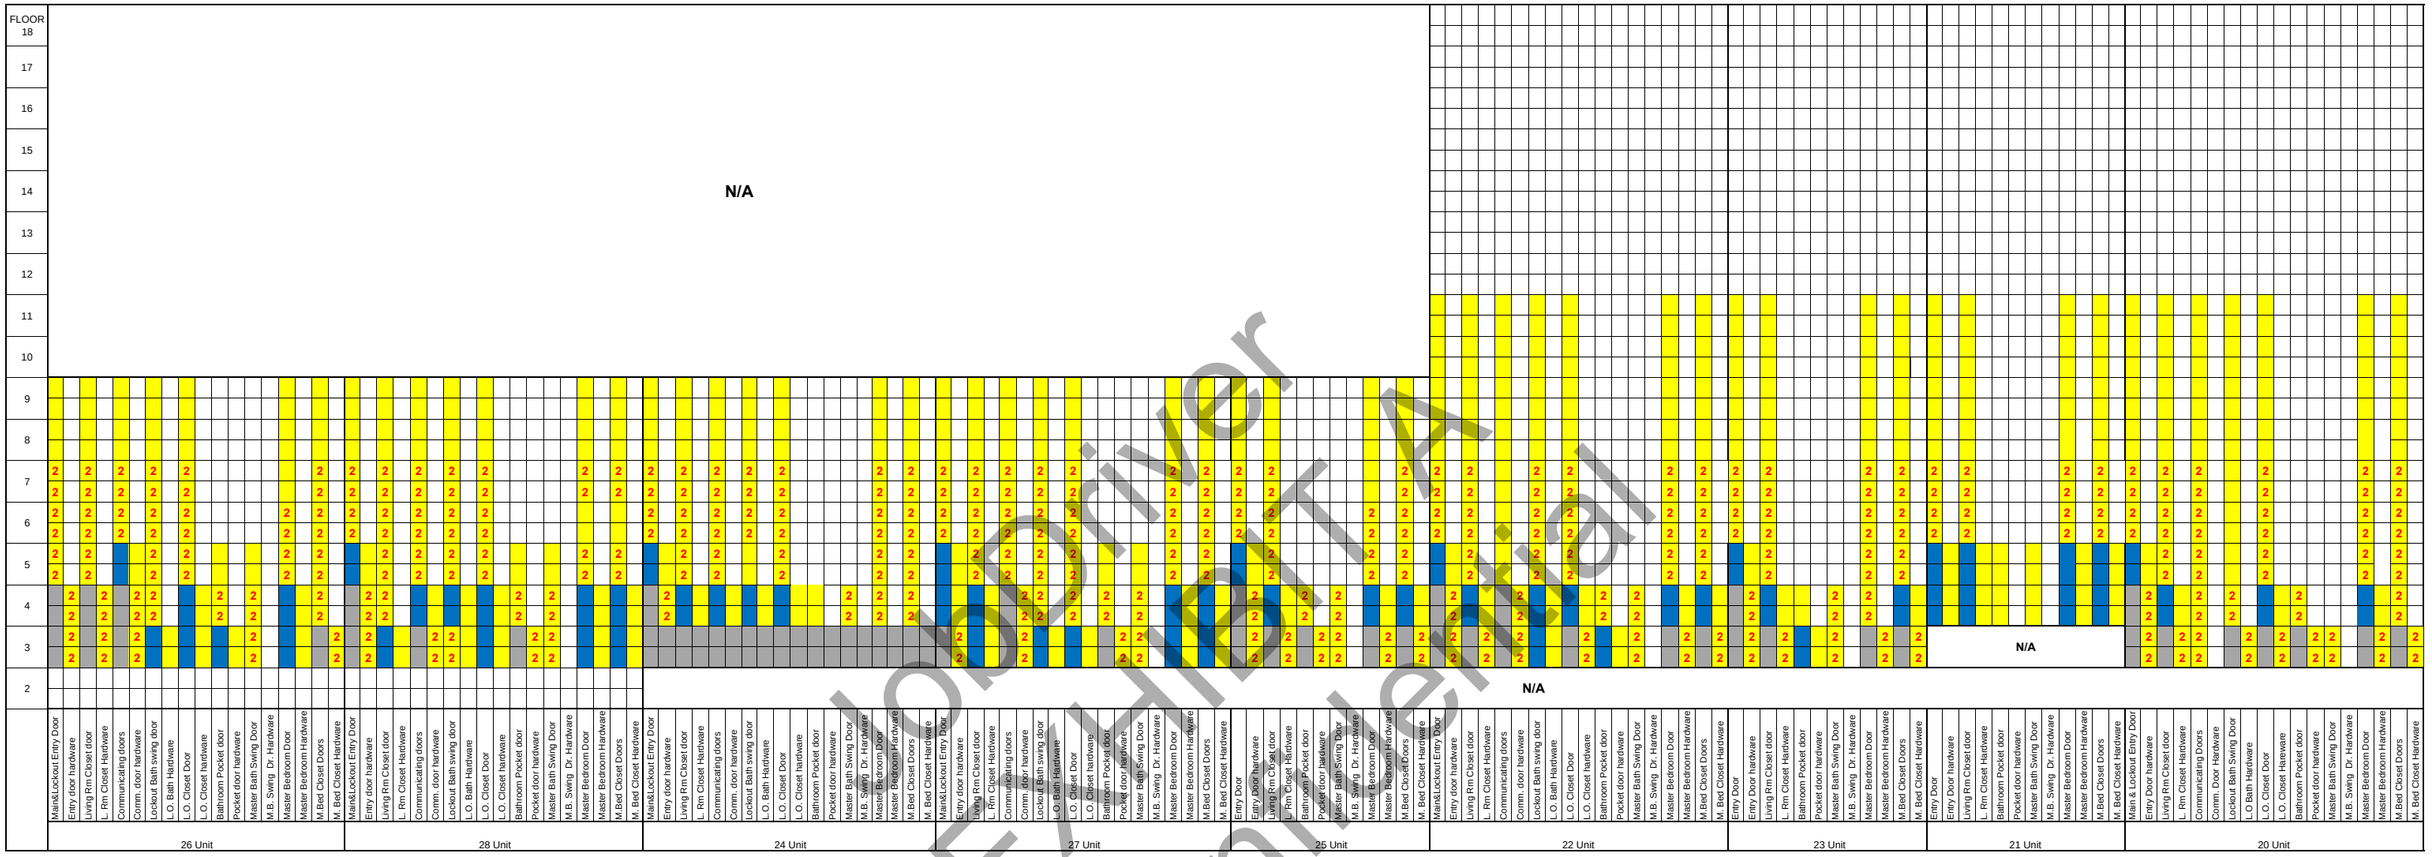

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/1/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012

INCOMPLETE ITEMS

Exhibit A
Confidential

PLEASANTS HARDWARE PROGRESS CHART

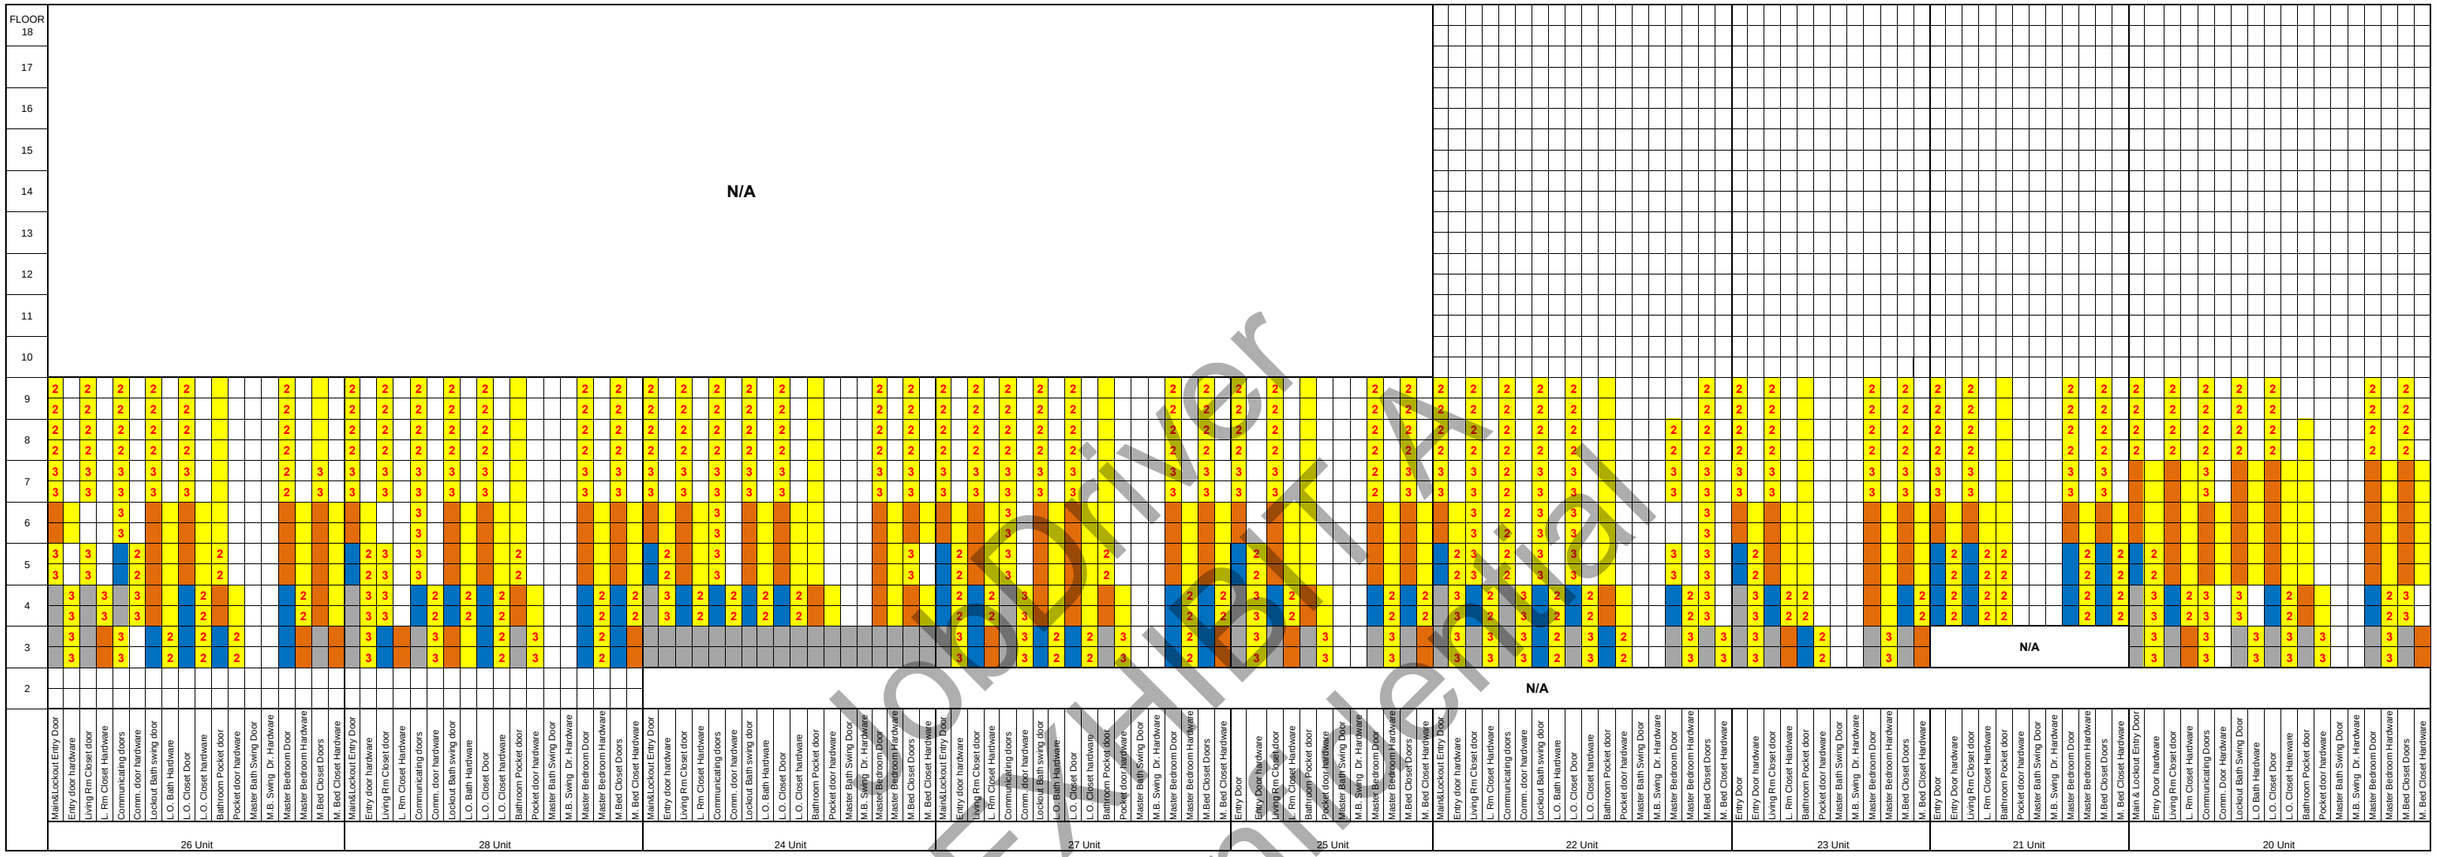

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

INCOMPLETE ITEMS

Job Progress
Exhibit A
Confidential

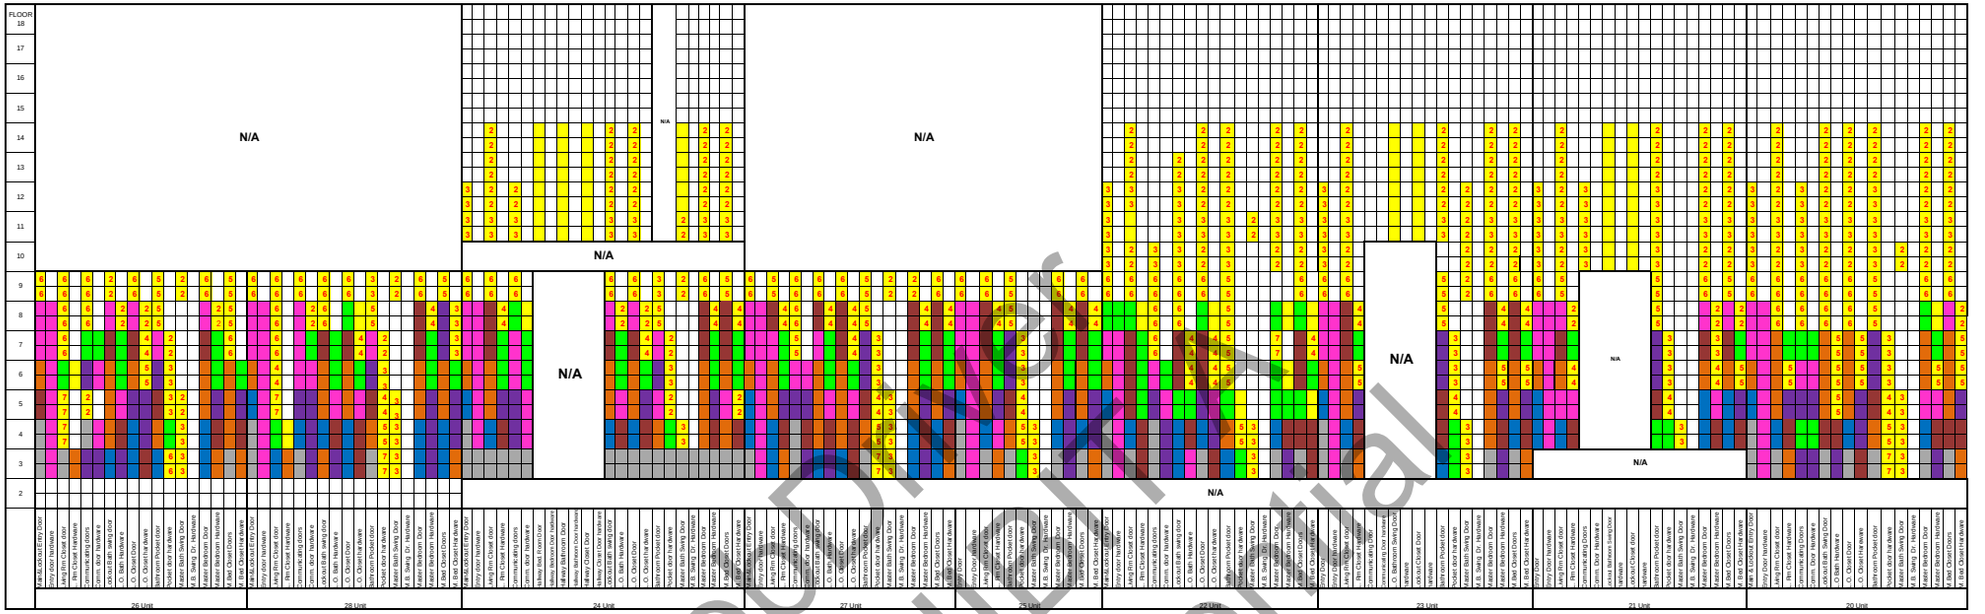

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

INCOMPLETE ITEMS

Job Display
EXHIBIT
Confidential

Pleasants Hardware

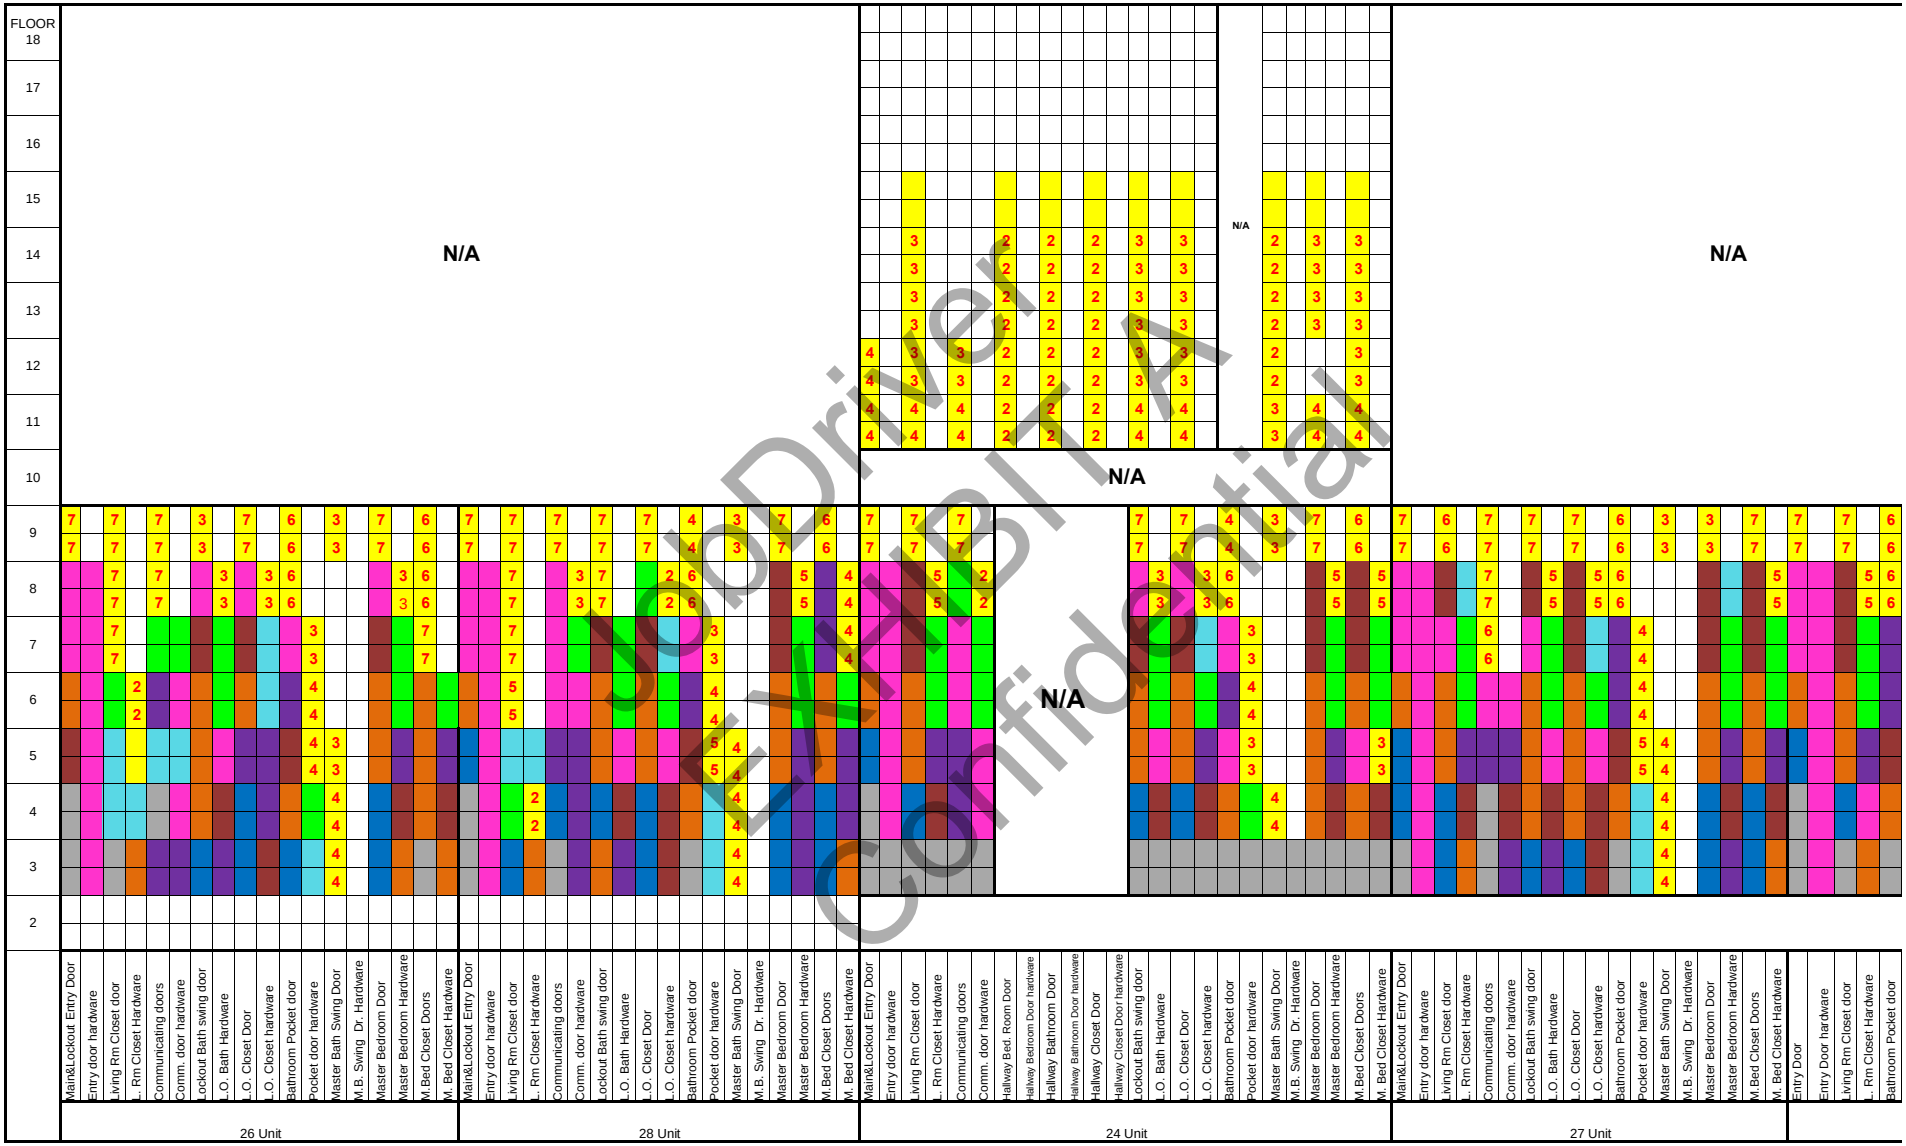

Job Driver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012

INCOMPLETE ITEMS

Pleasants Hardware

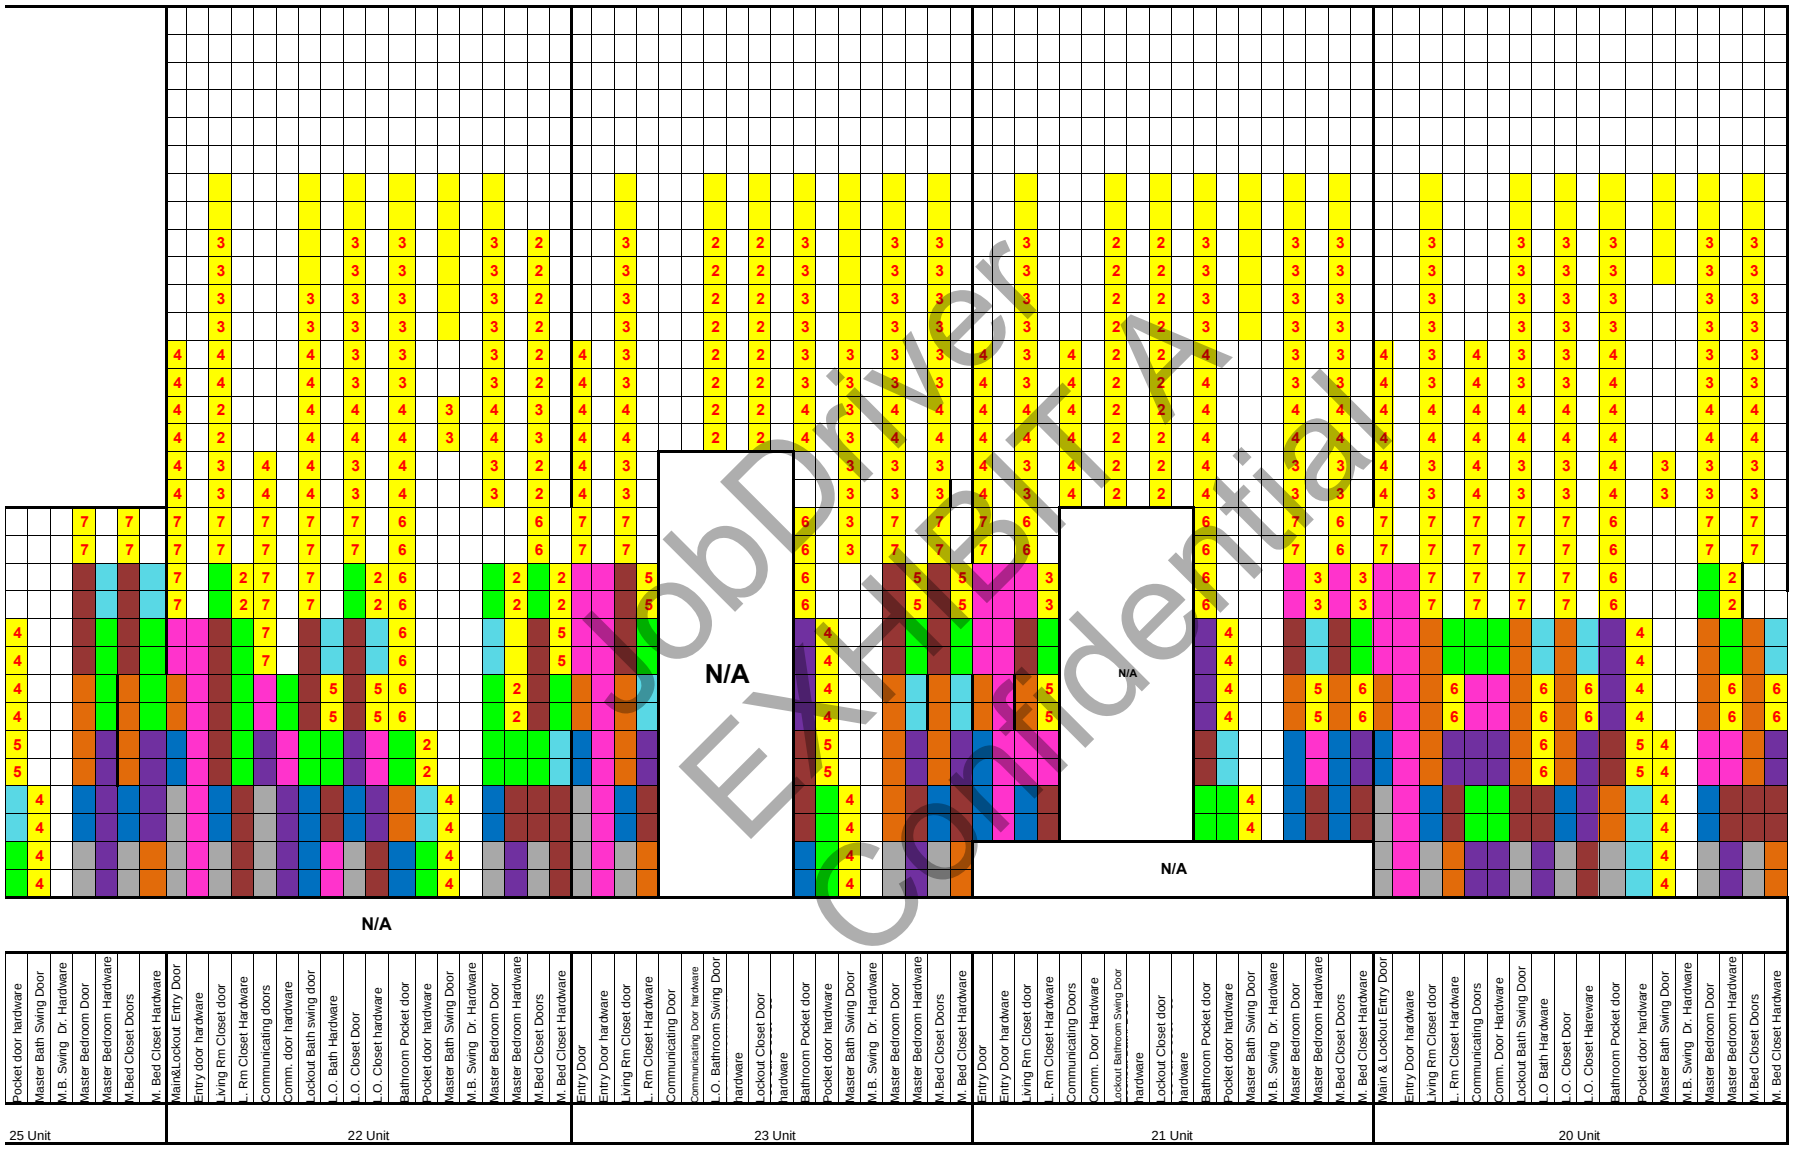

JobDriver EXHIBIT A Confidential

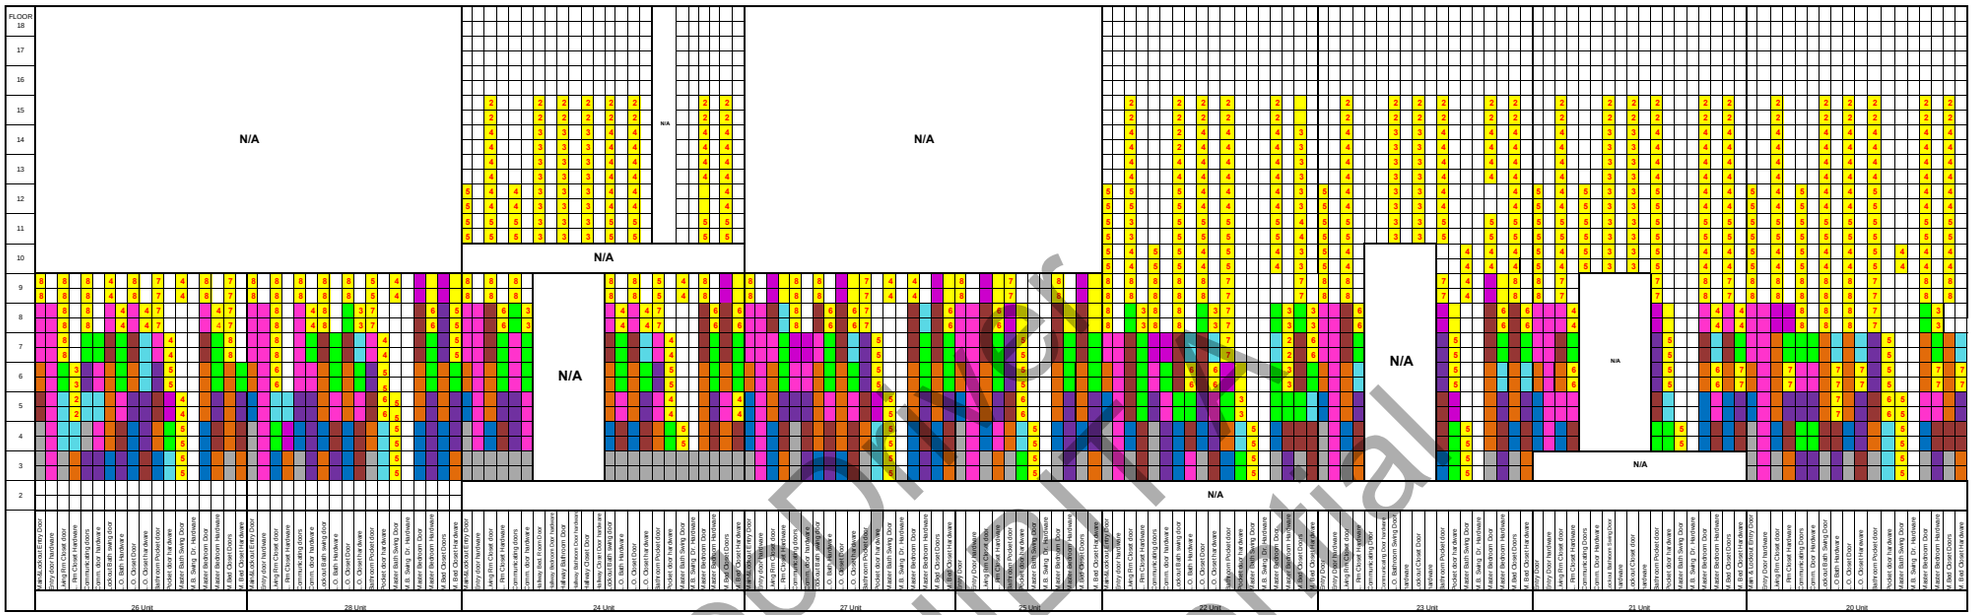

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

WORK COMPLETE TO DATE 1/27/12
AREAS AVAILABLE FOR YOU TO WORK
AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
WORK COMPLETED TO DATE 2/1/2012

All master bedroom swing doors are being re-worked to accommodate new doors.
WORK COMPLETED TO DATE 2/29/2012
WORK COMPLETED TO DATE 3/7/2012
WORK COMPLETED TO DATE 3/14/2012

INCOMPLETE ITEMS

Job Display
EXHIBIT
Confidential

Pleasants Hardware

Job Driven
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

WORK COMPLETE TO DATE 1/27/12
AREAS AVAILABLE FOR YOU TO WORK
\# AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
WORK COMPLETED TO DATE 2/1/2012

All master bedroom swing doors are being re-worked to accommodate new doors.
WORK COMPLETED TO DATE 2/29/2012
WORK COMPLETED TO DATE 3/7/2012
WORK COMPLETED TO DATE 3/14/2012
WORK COMPLETED TO DATE 4/4/2012

INCOMPLETE ITEMS

Pleasants Hardware

JobDriver
Exhibit A
Confidential

Pleasants Hardware

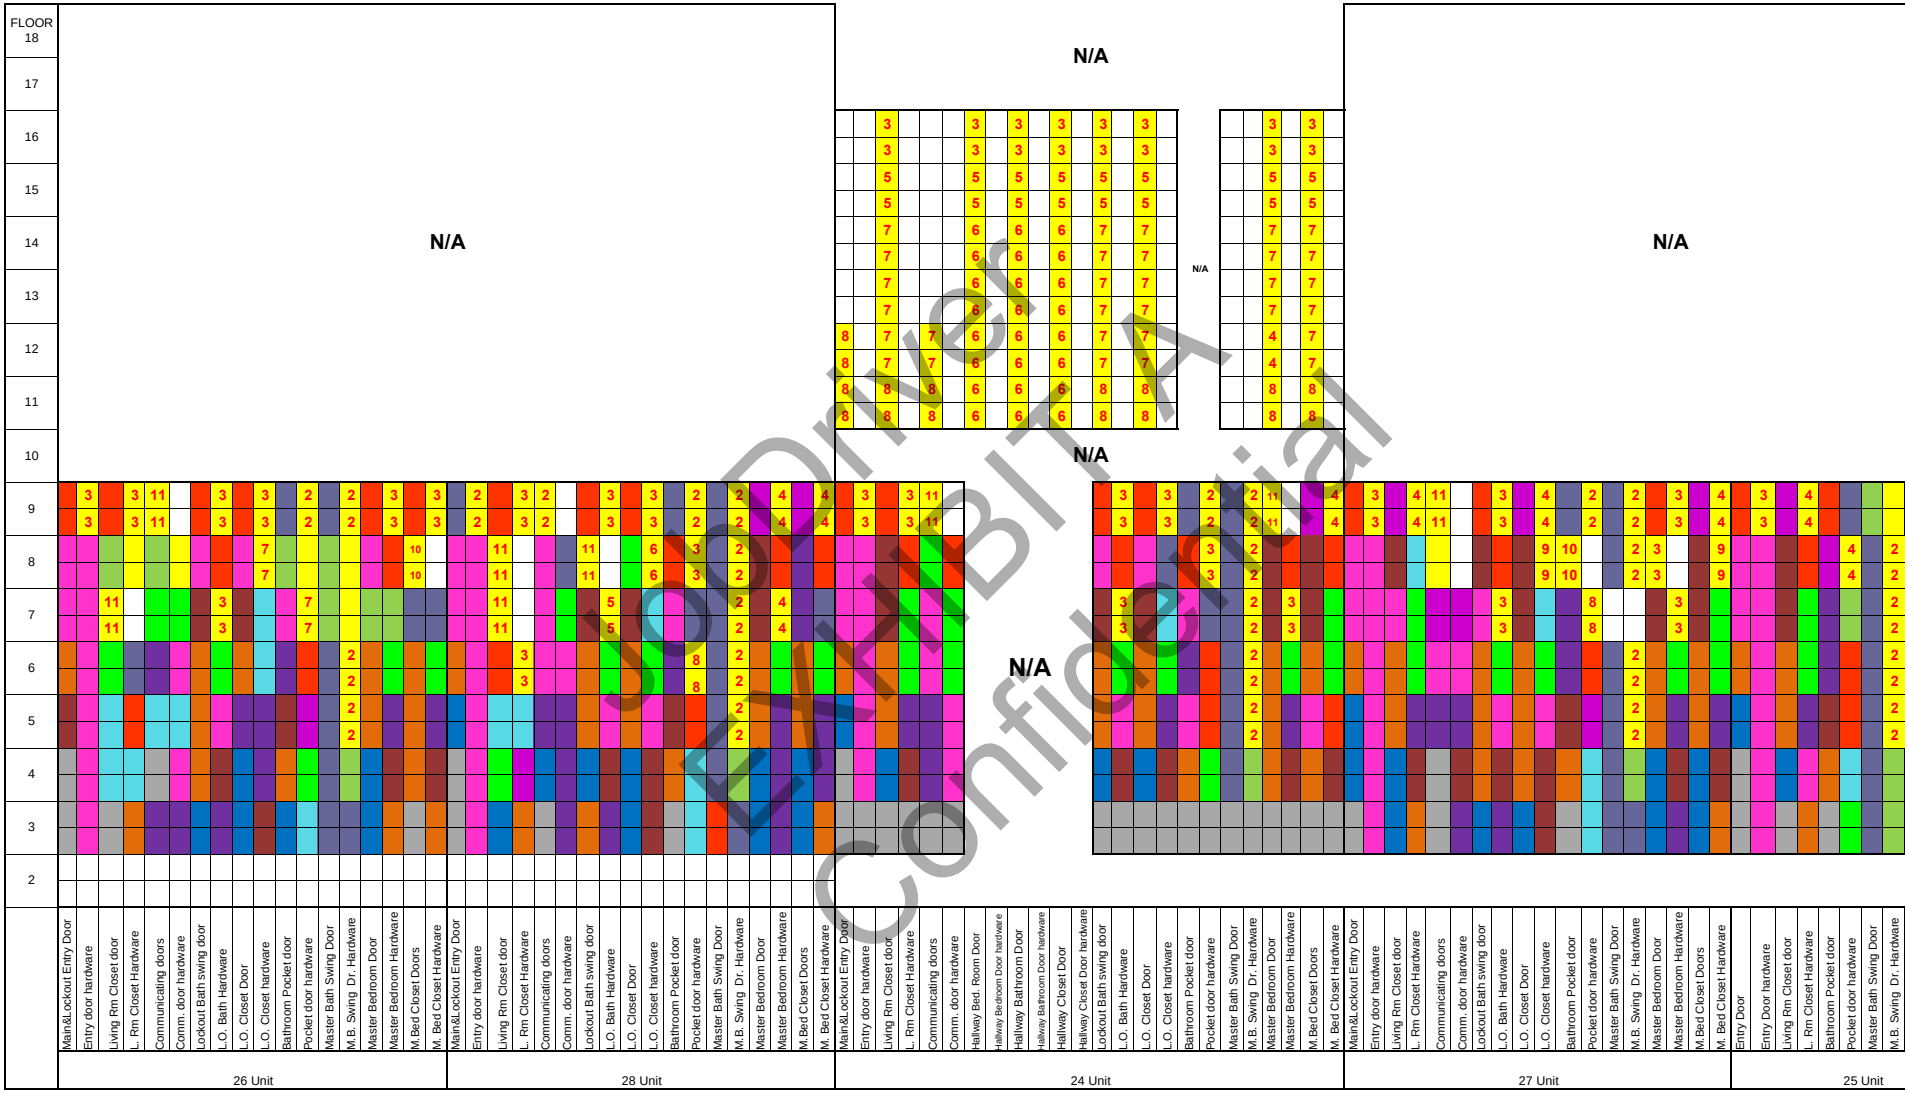

Job Driver EXHIBIT A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012

INCOMPLETE ITEMS

Pleasants Hardware

Job Driver
EXHIBIT A
Confidential

Pleasants Hardware

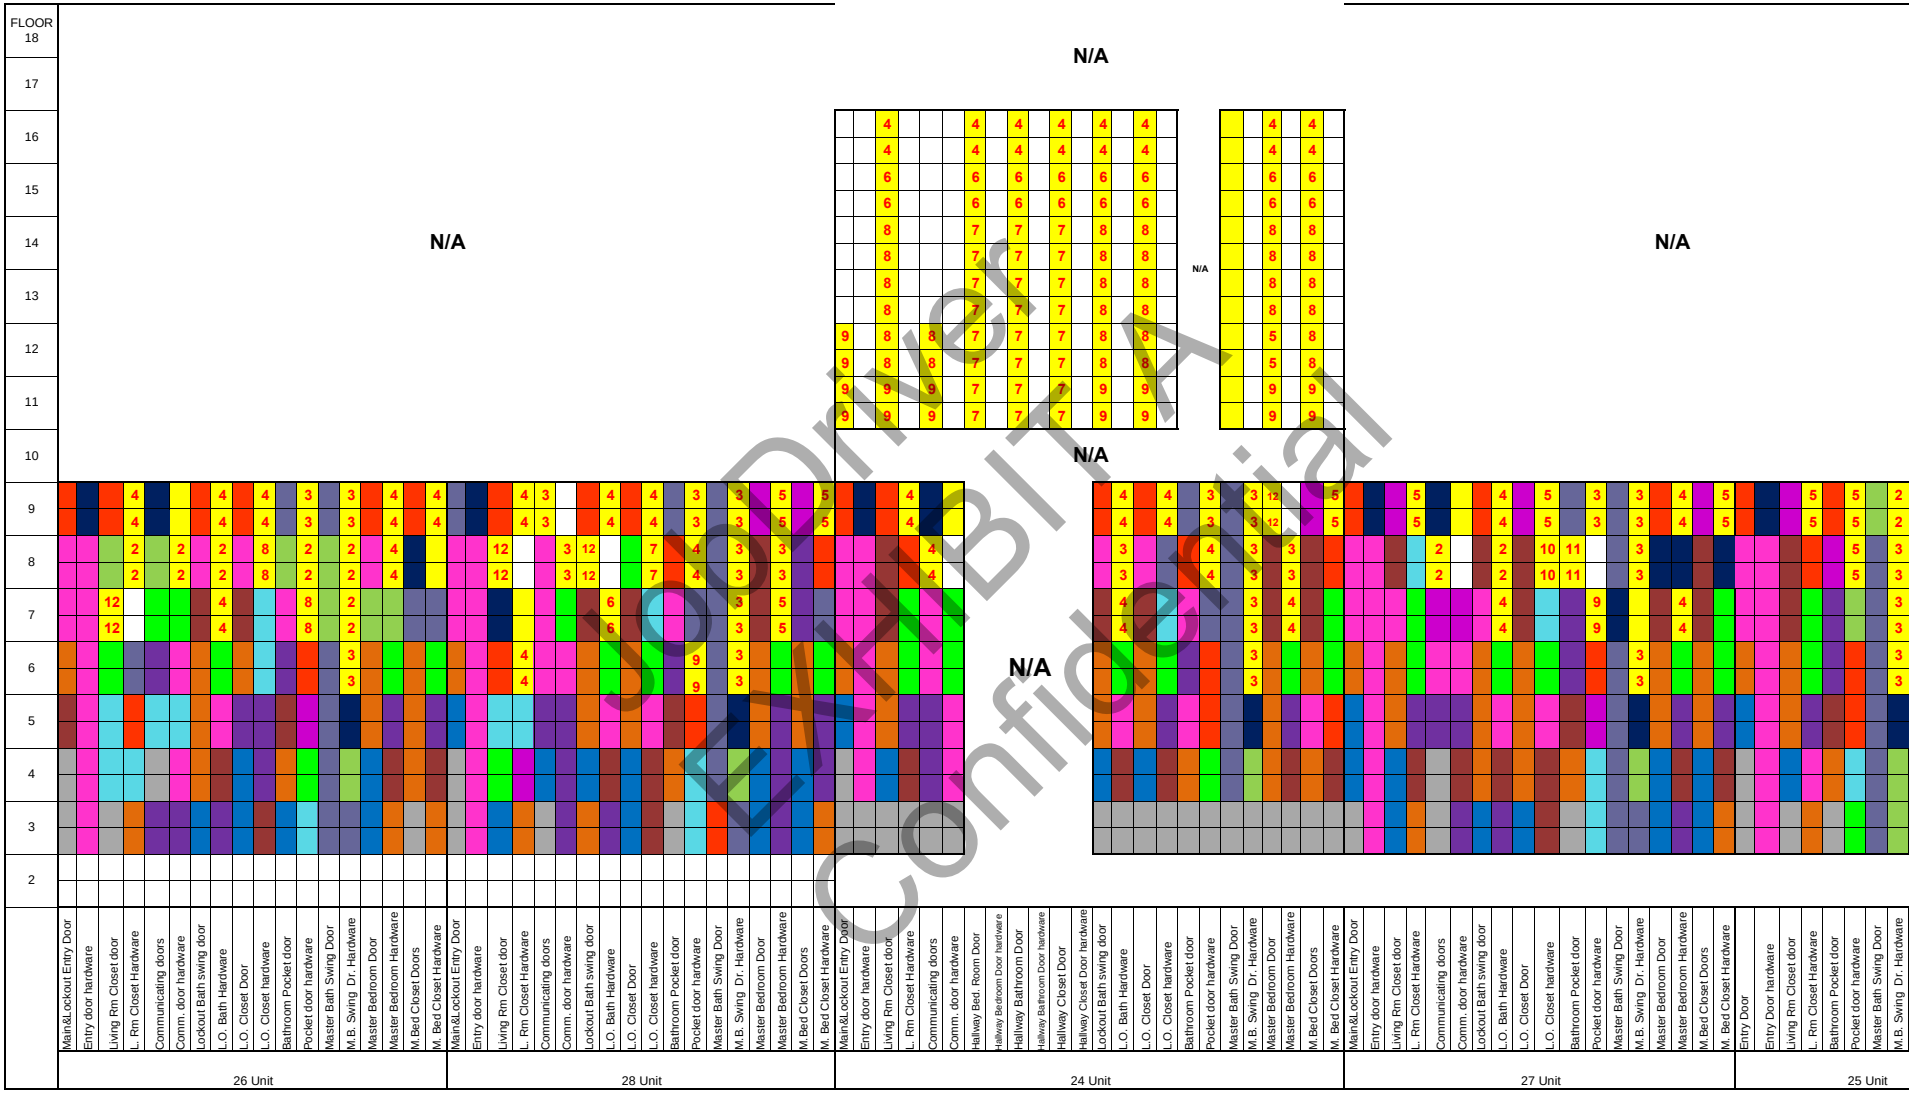

Job Driver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012

INCOMPLETE ITEMS

Pleasants Hardware

Job Driver
EXHIBIT A
Confidential

Pleasants Hardware

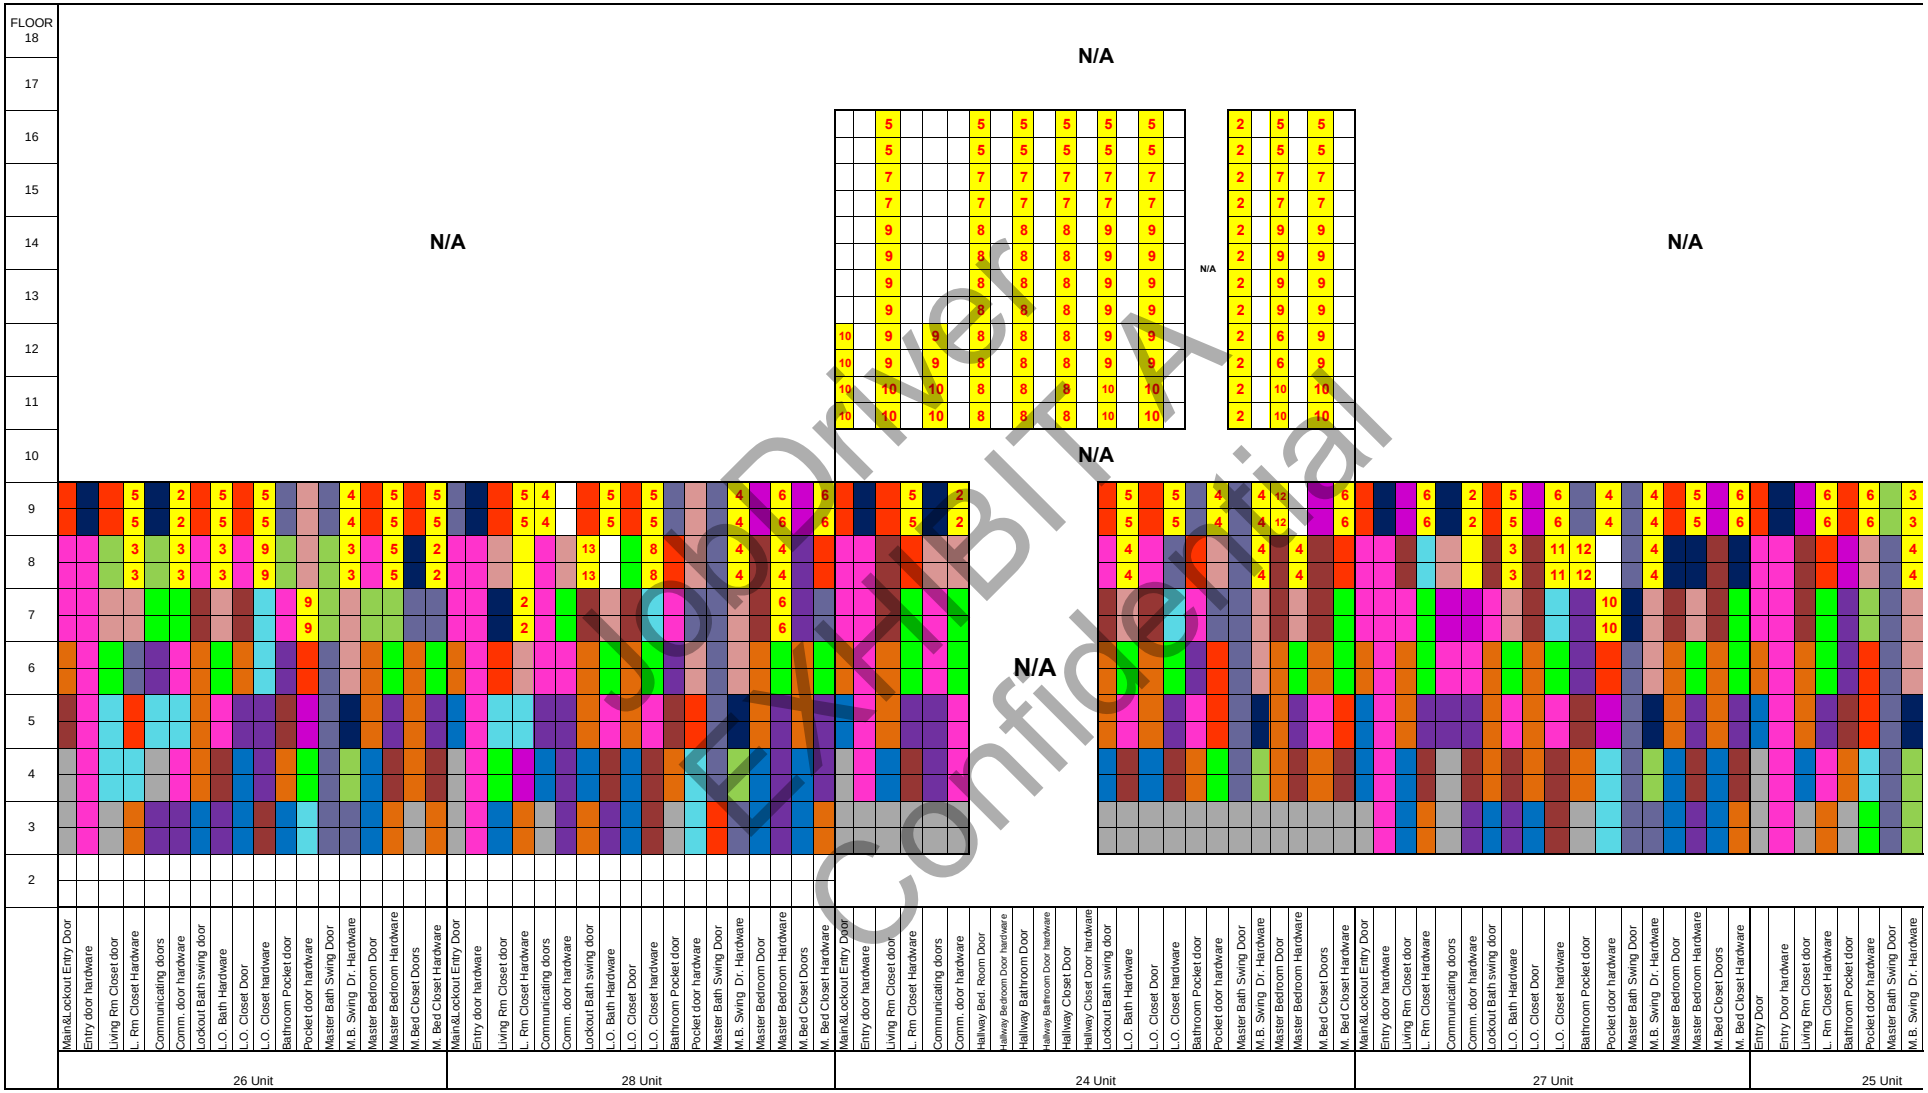

Job Driver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012

INCOMPLETE ITEMS

Pleasants Hardware

Job River
EXHIBIT A
Confidential

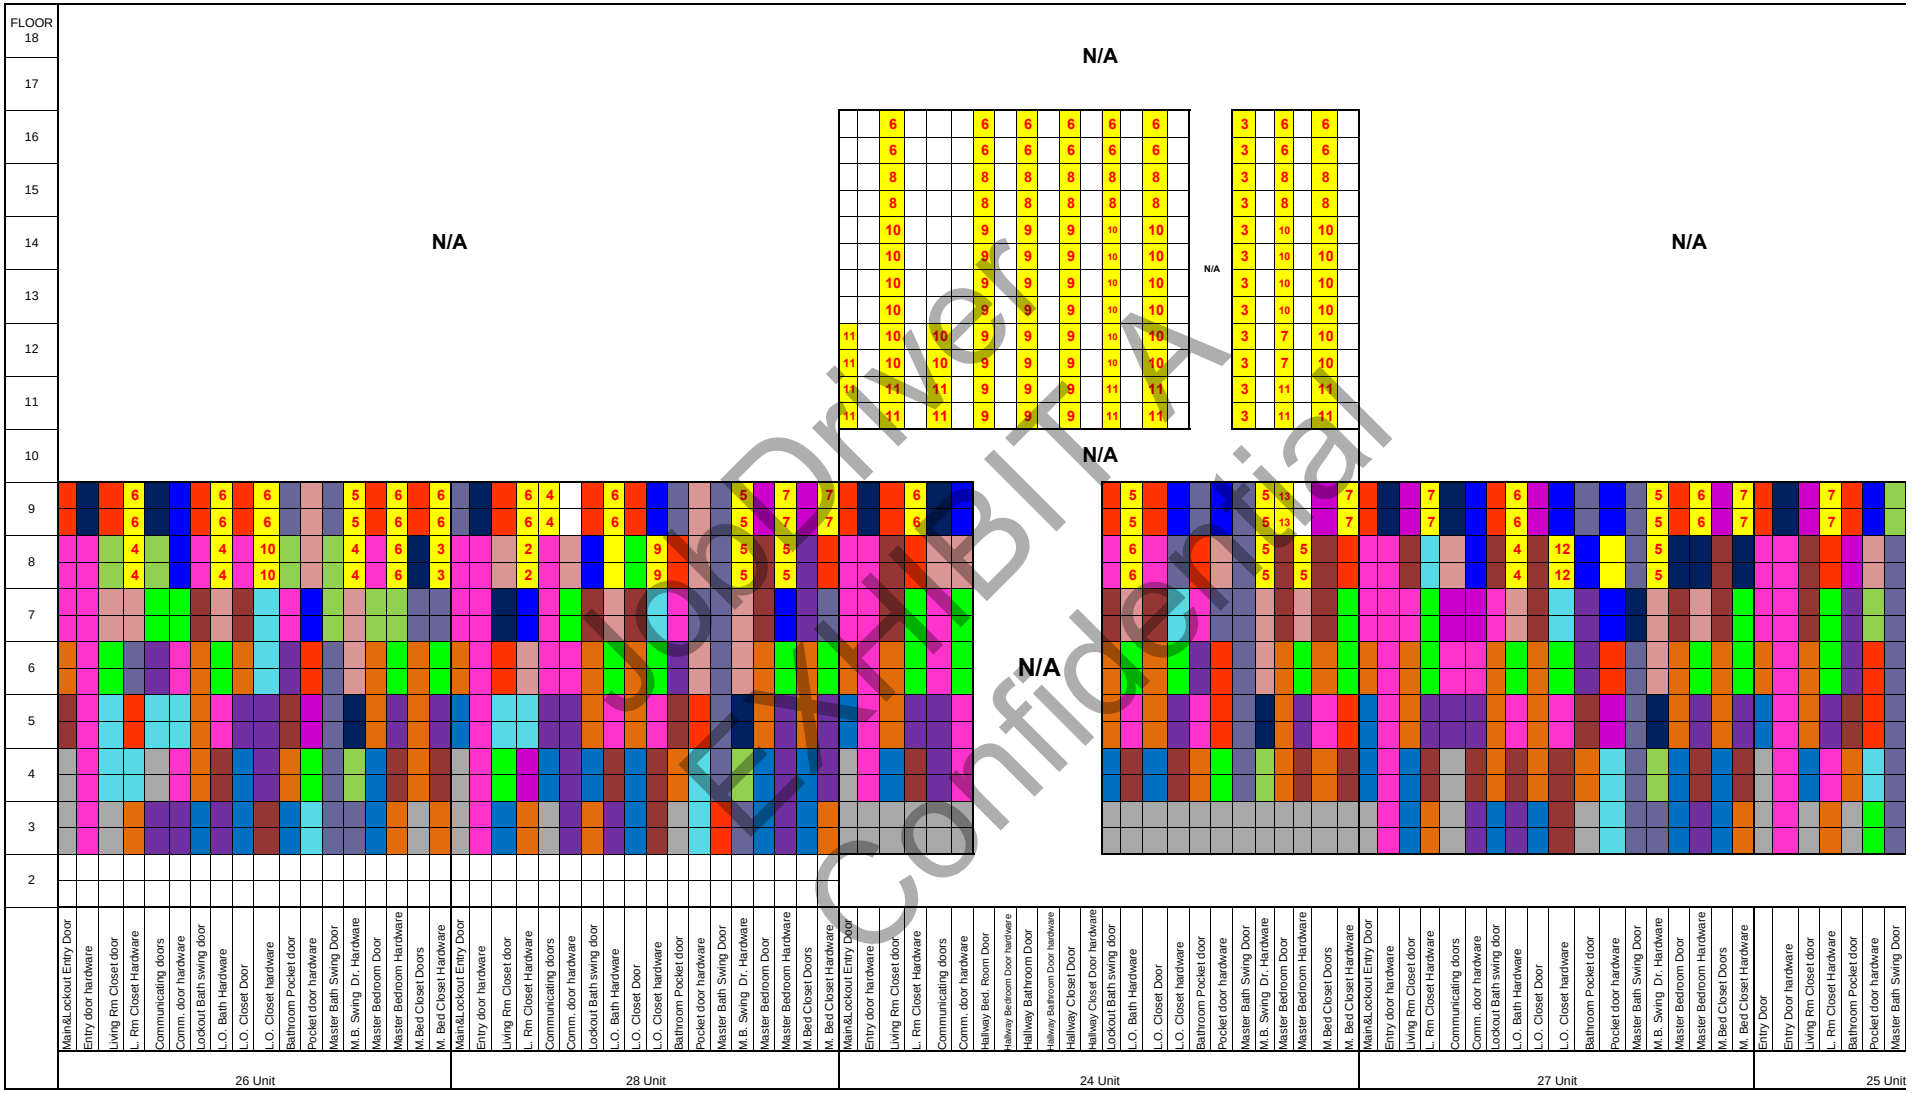

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012

INCOMPLETE ITEMS

Pleasants Hardware

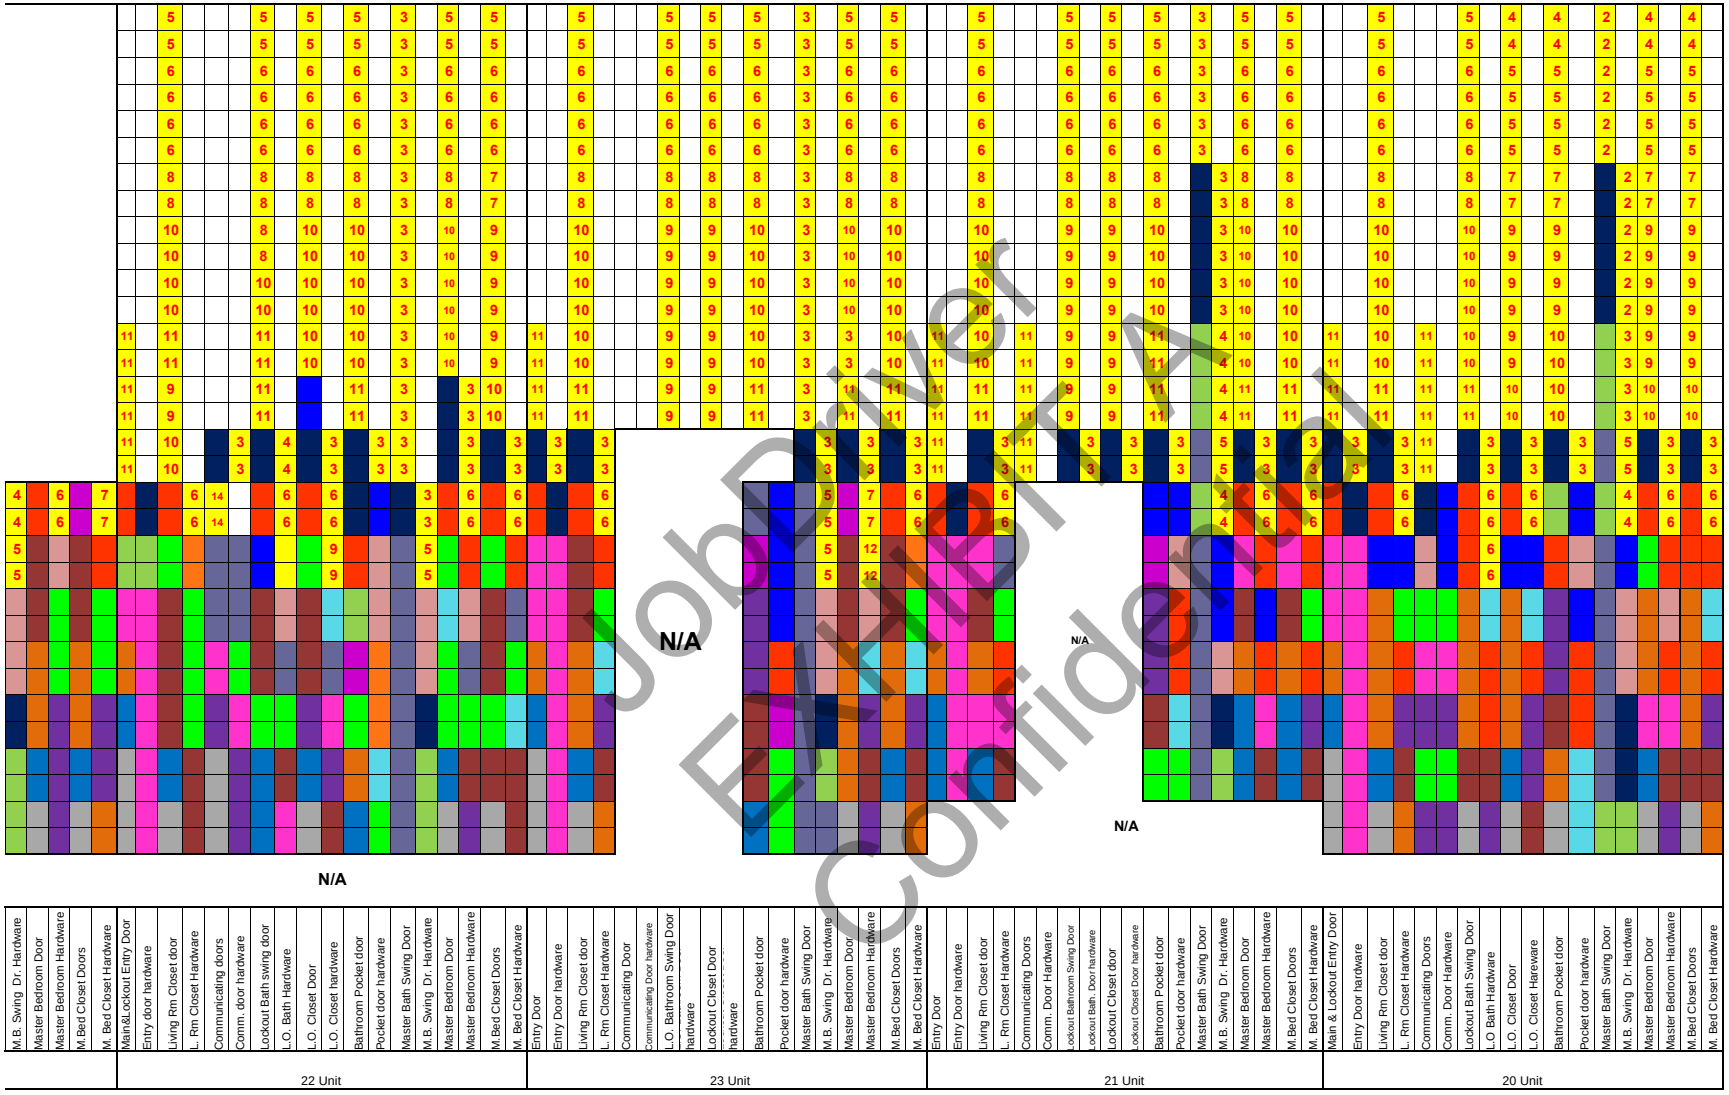

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

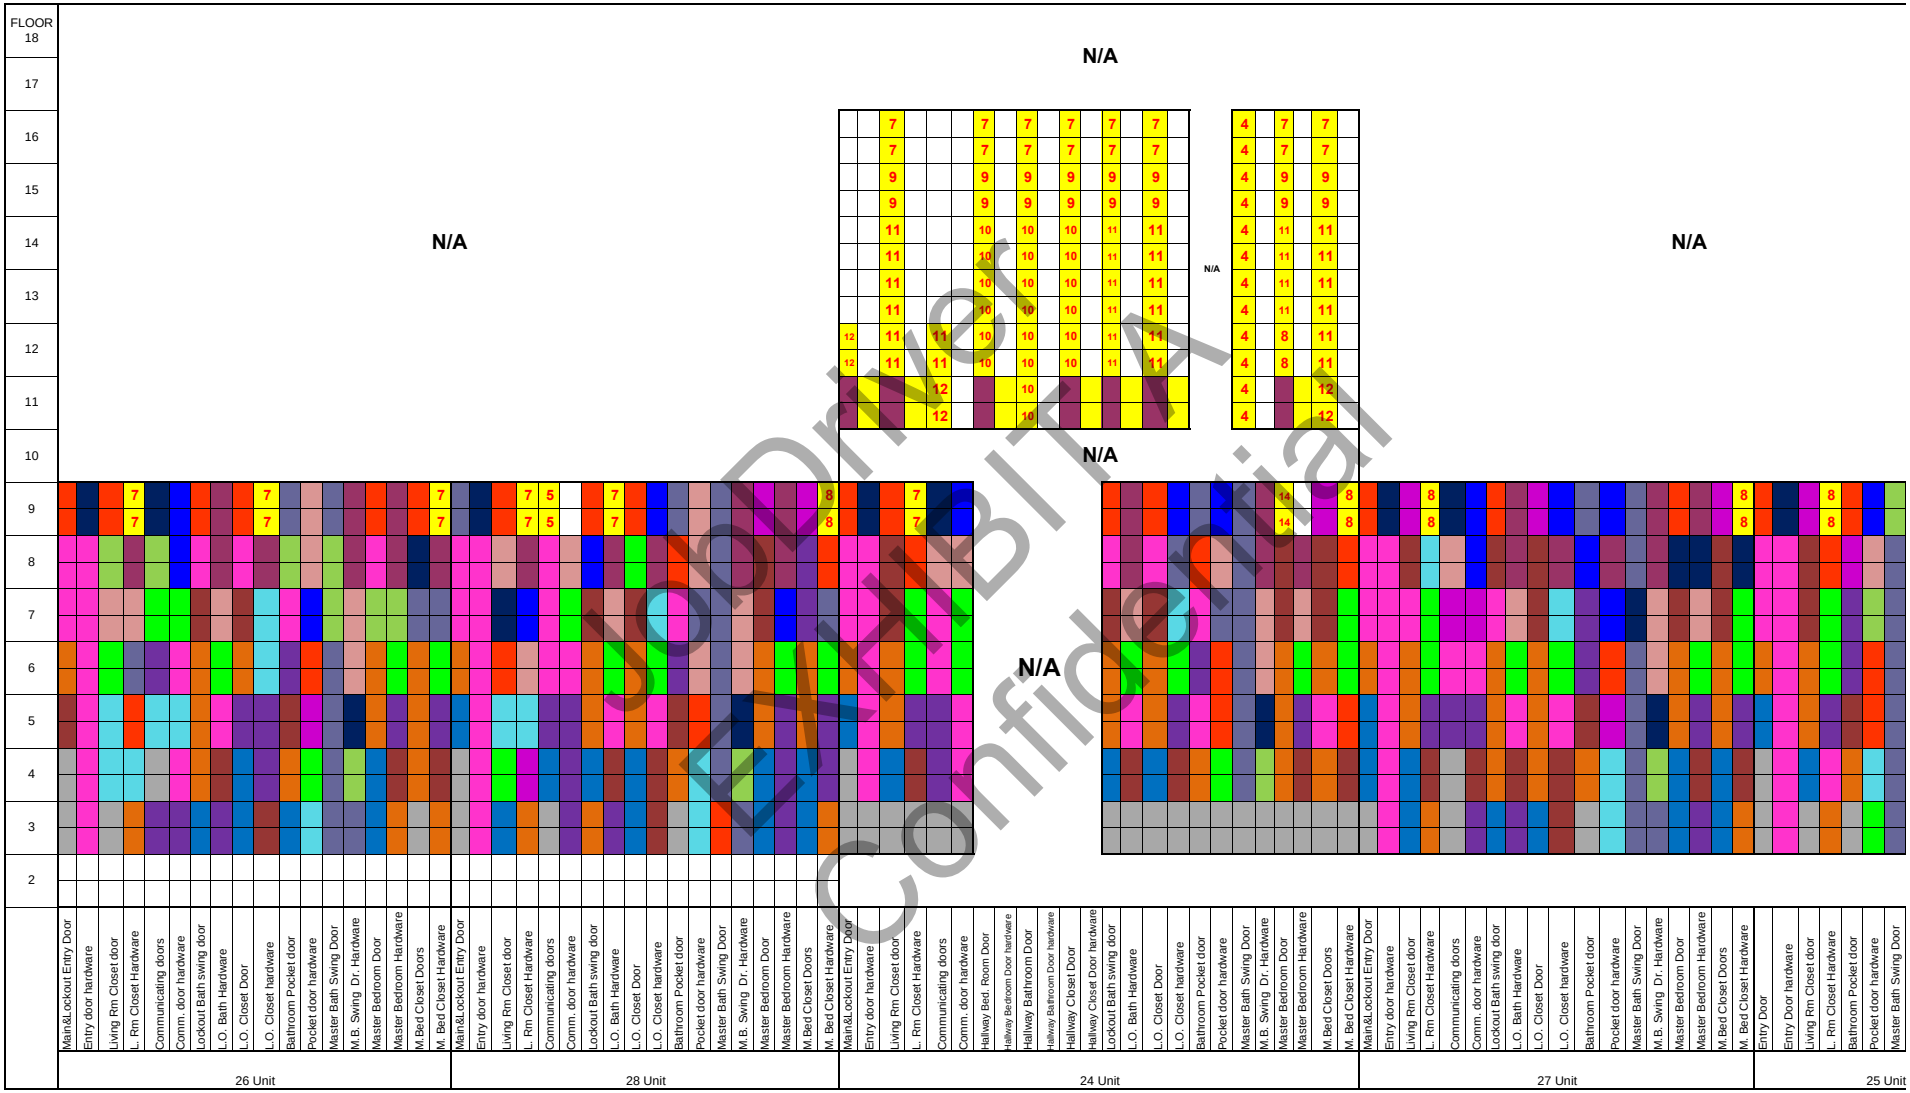

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012

INCOMPLETE ITEMS

Pleasants Hardware

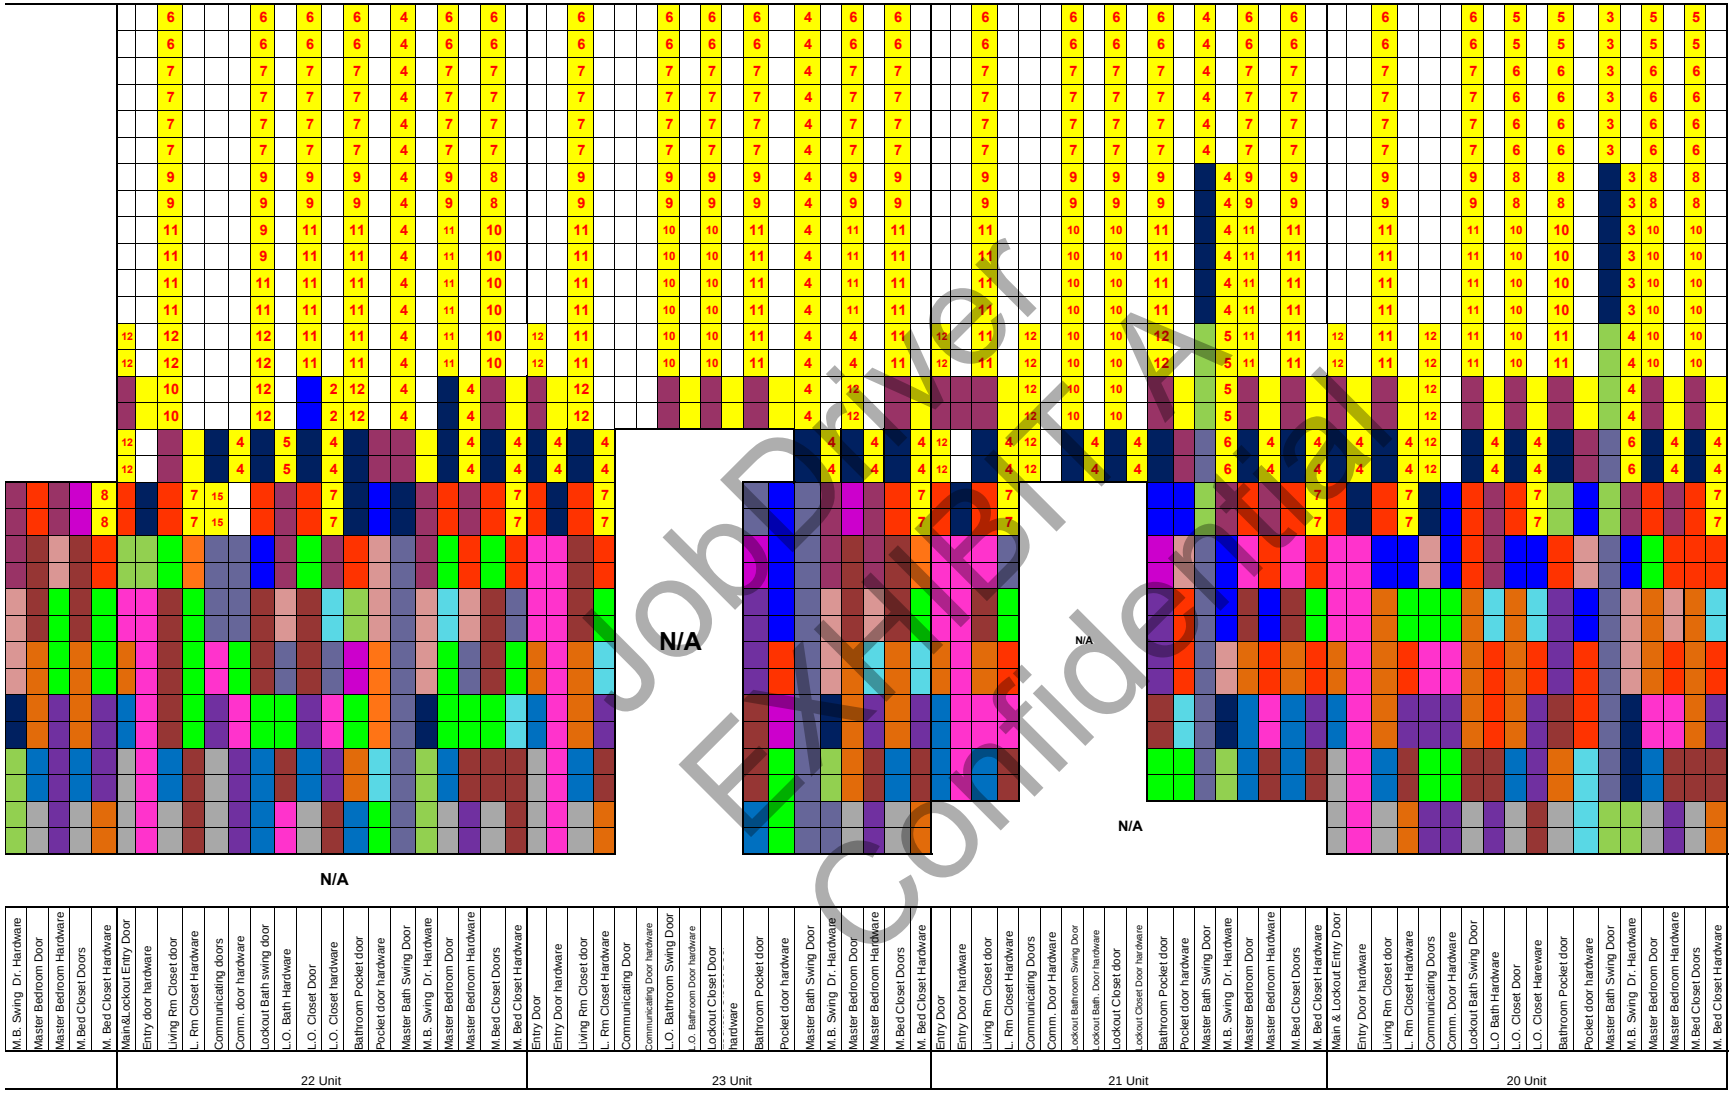

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

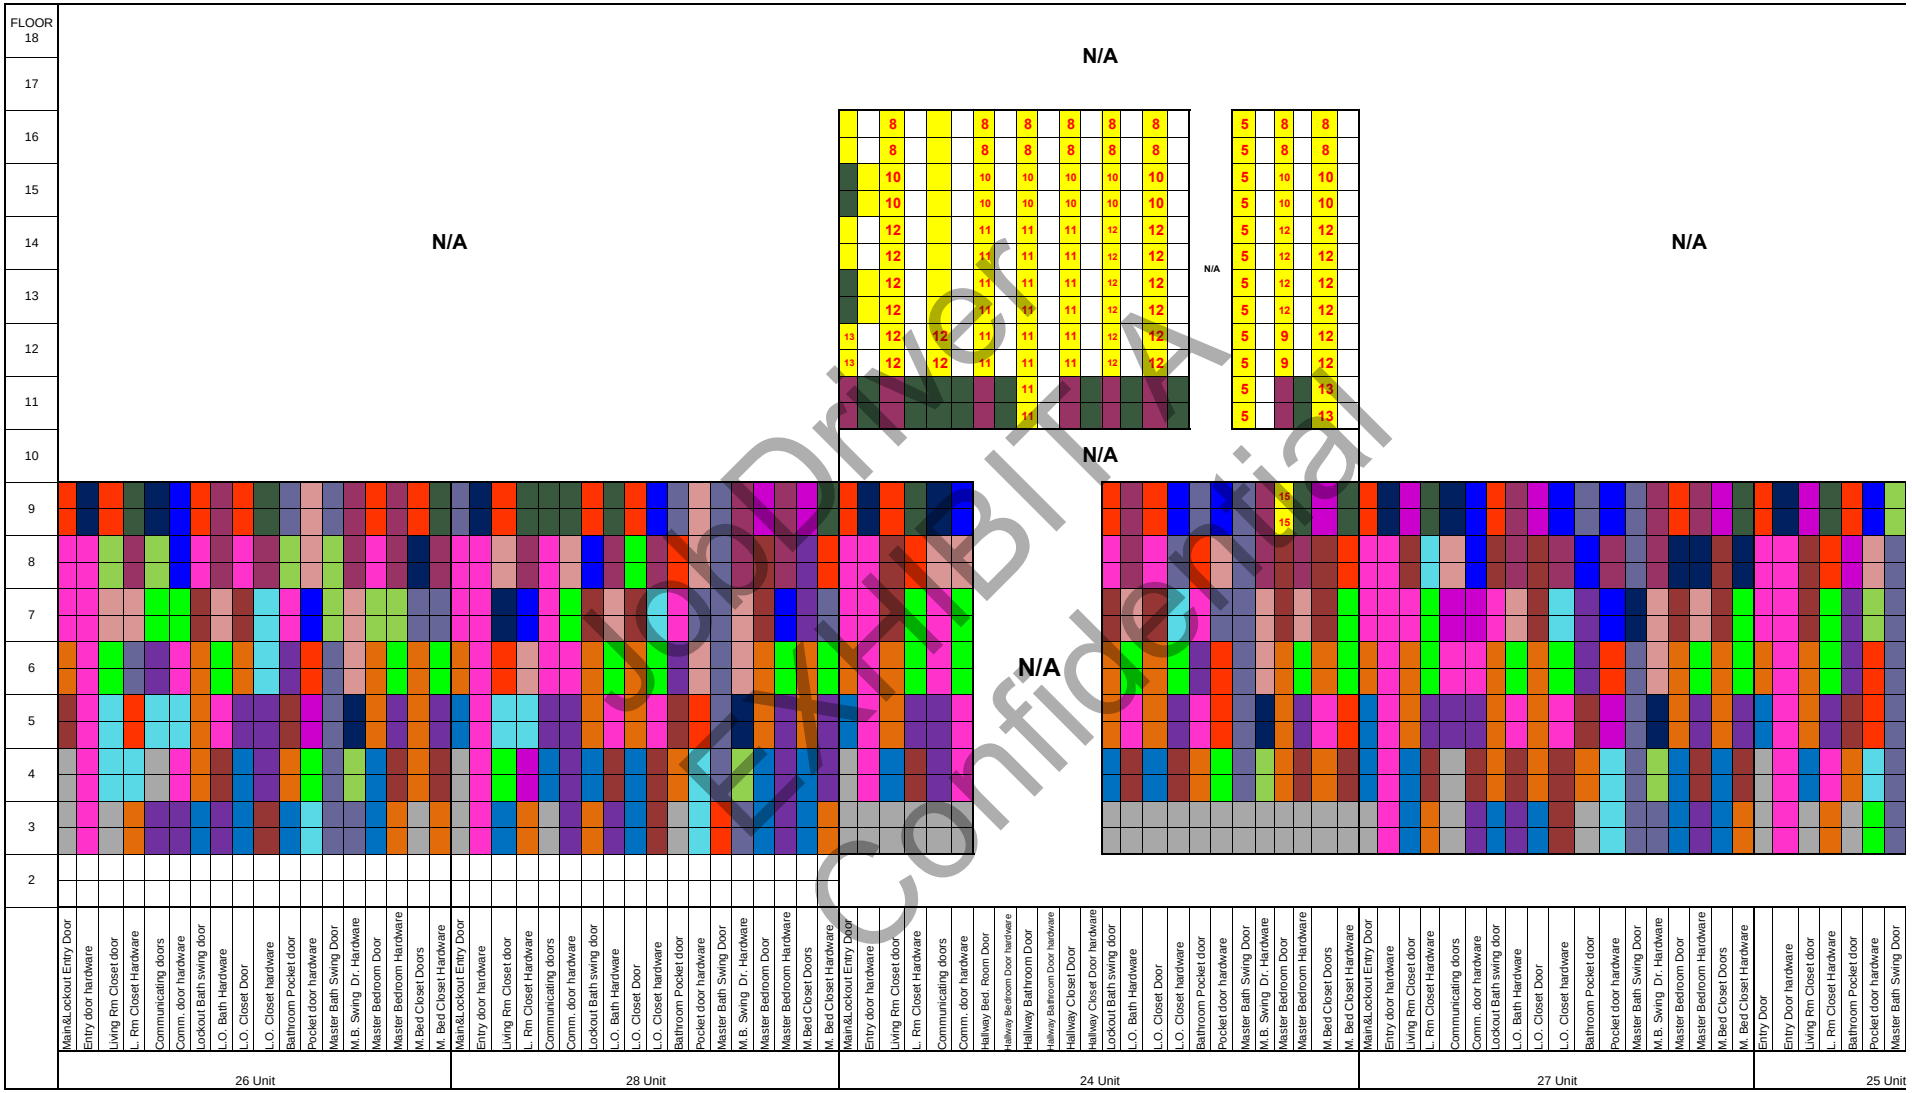

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012

INCOMPLETE ITEMS

Pleasants Hardware

JobDiver
EXHIBIT A
Confidential

Pleasants Hardware

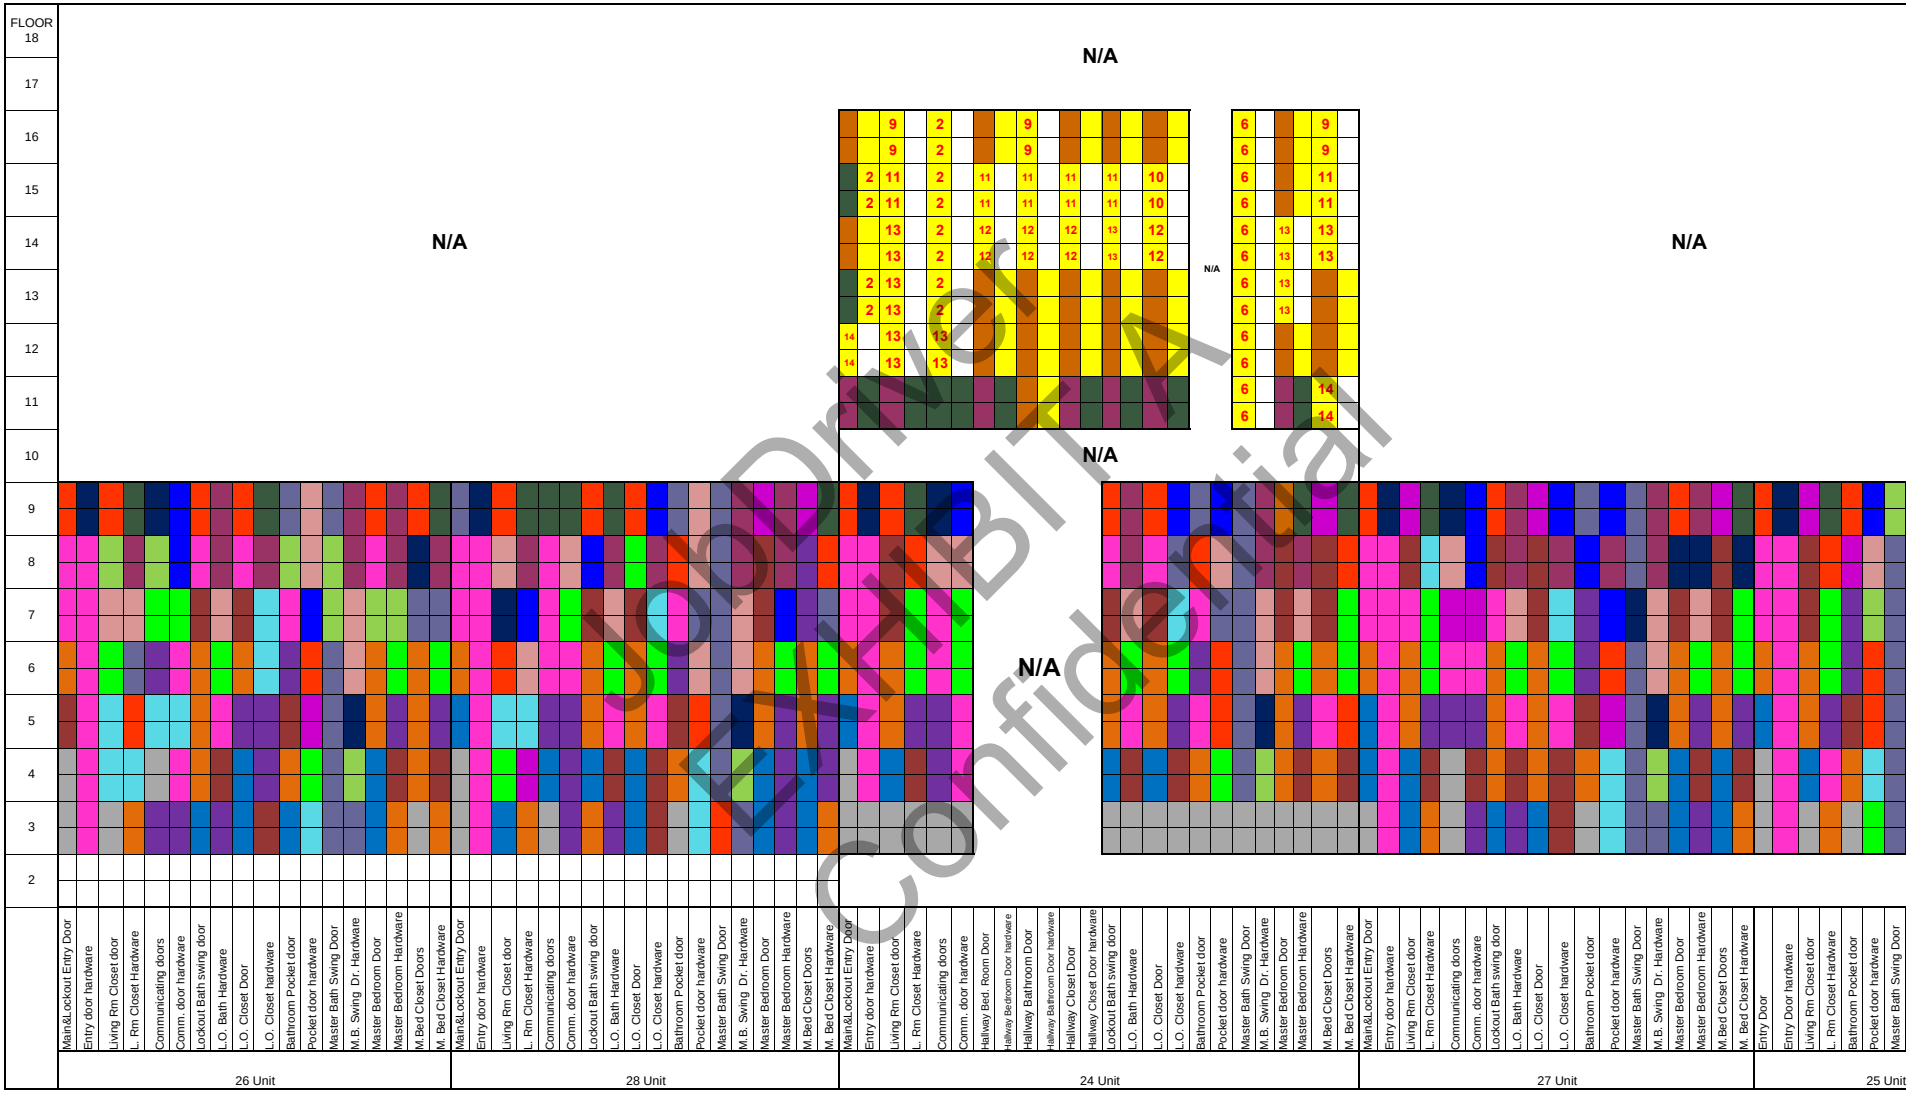

Job Drwer
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012

INCOMPLETE ITEMS

Pleasants Hardware

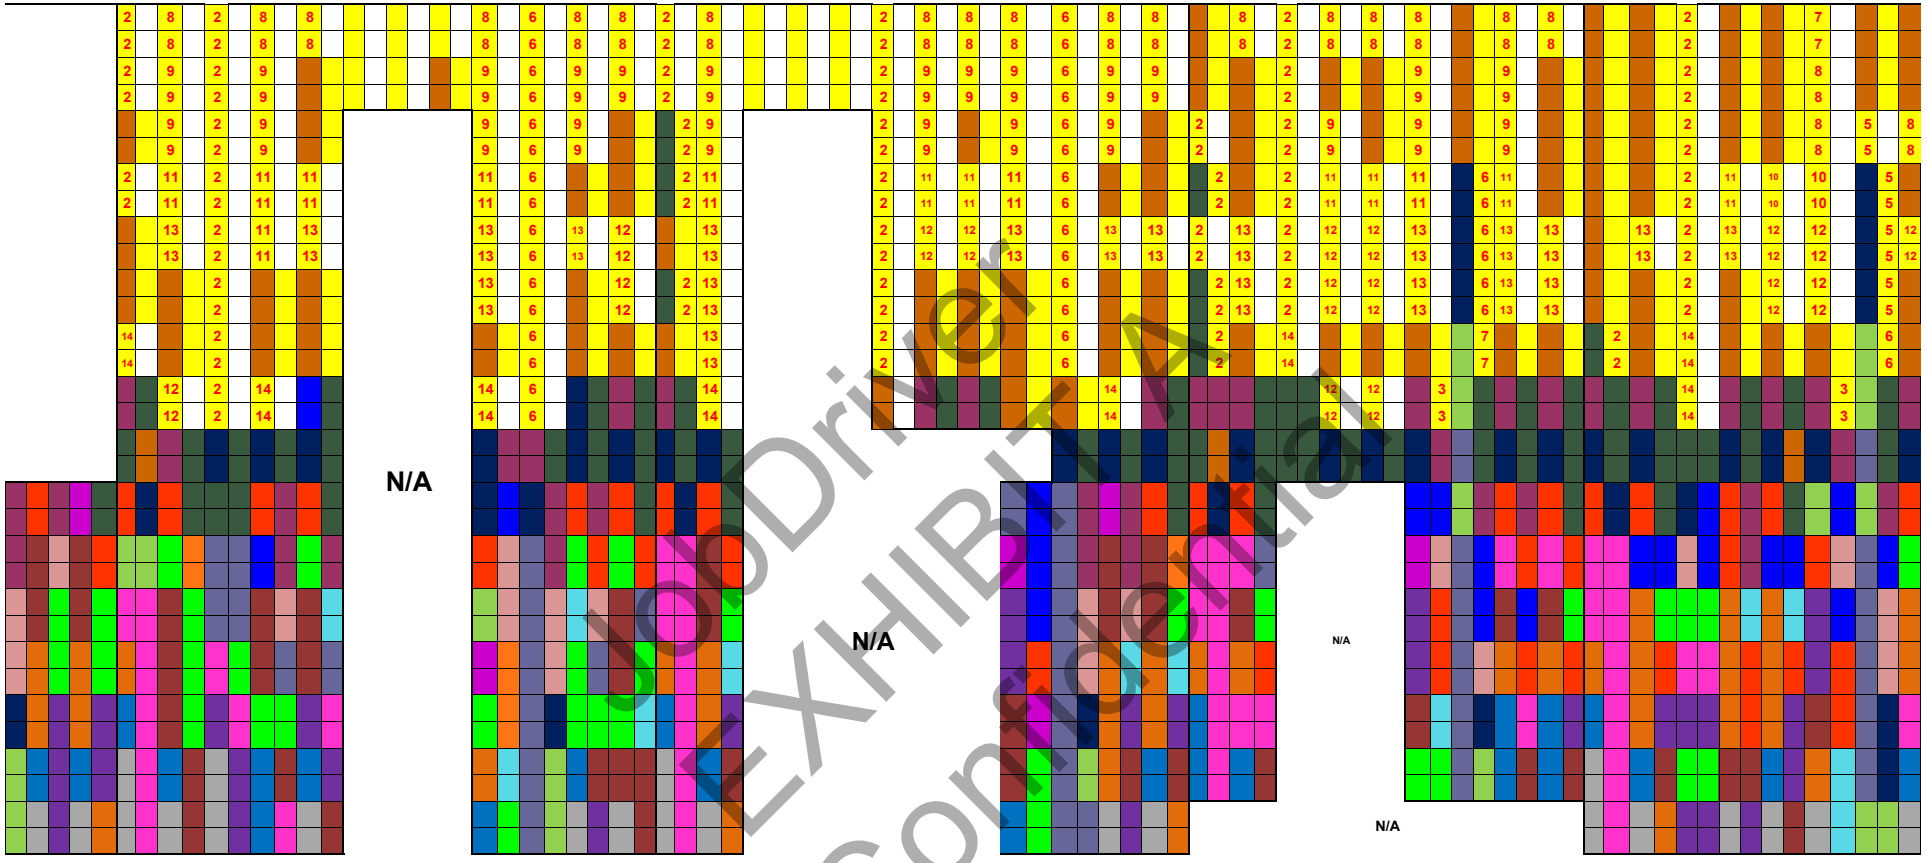

JobDriver
EXHIBIT A
Confidential

| 22 Unit | | |

Master Bedroom Hardware
M.Bed Closet Doors
M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

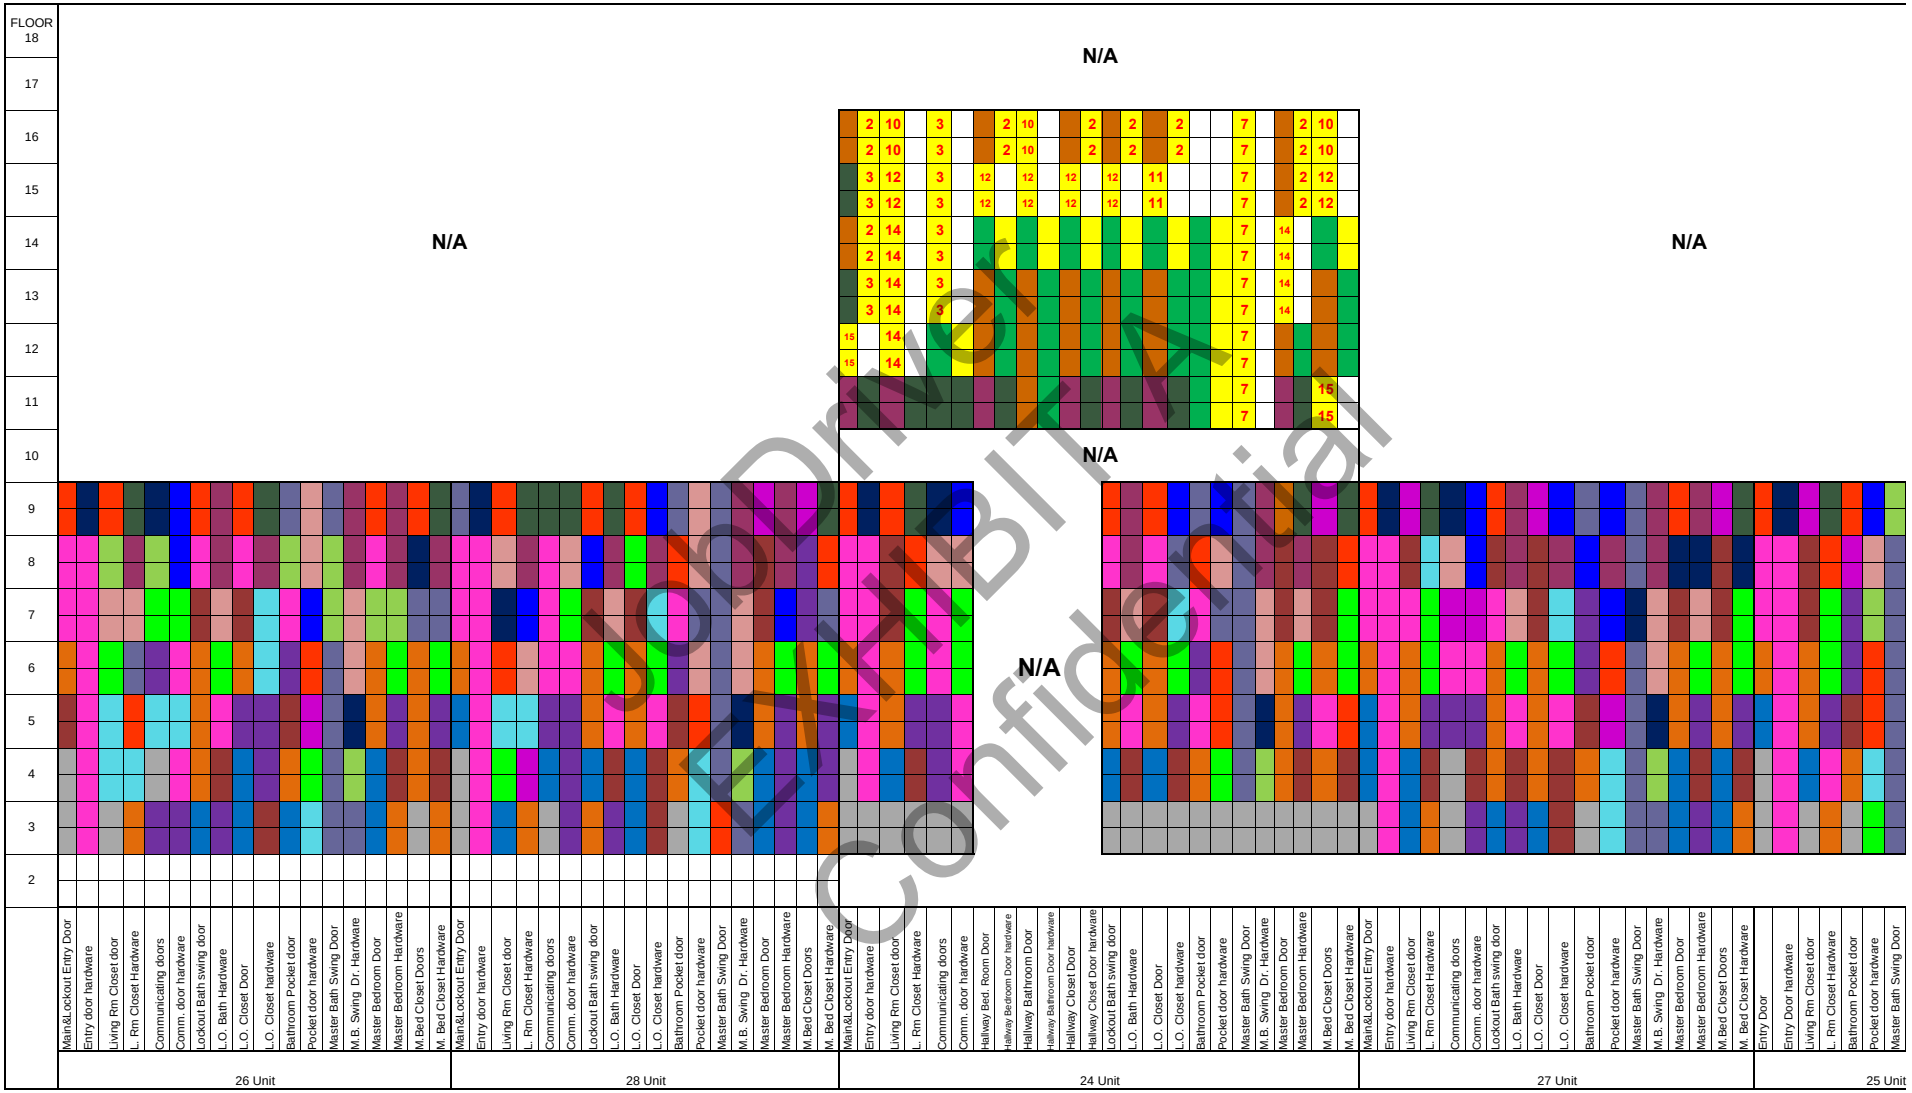

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012

INCOMPLETE ITEMS

Pleasants Hardware

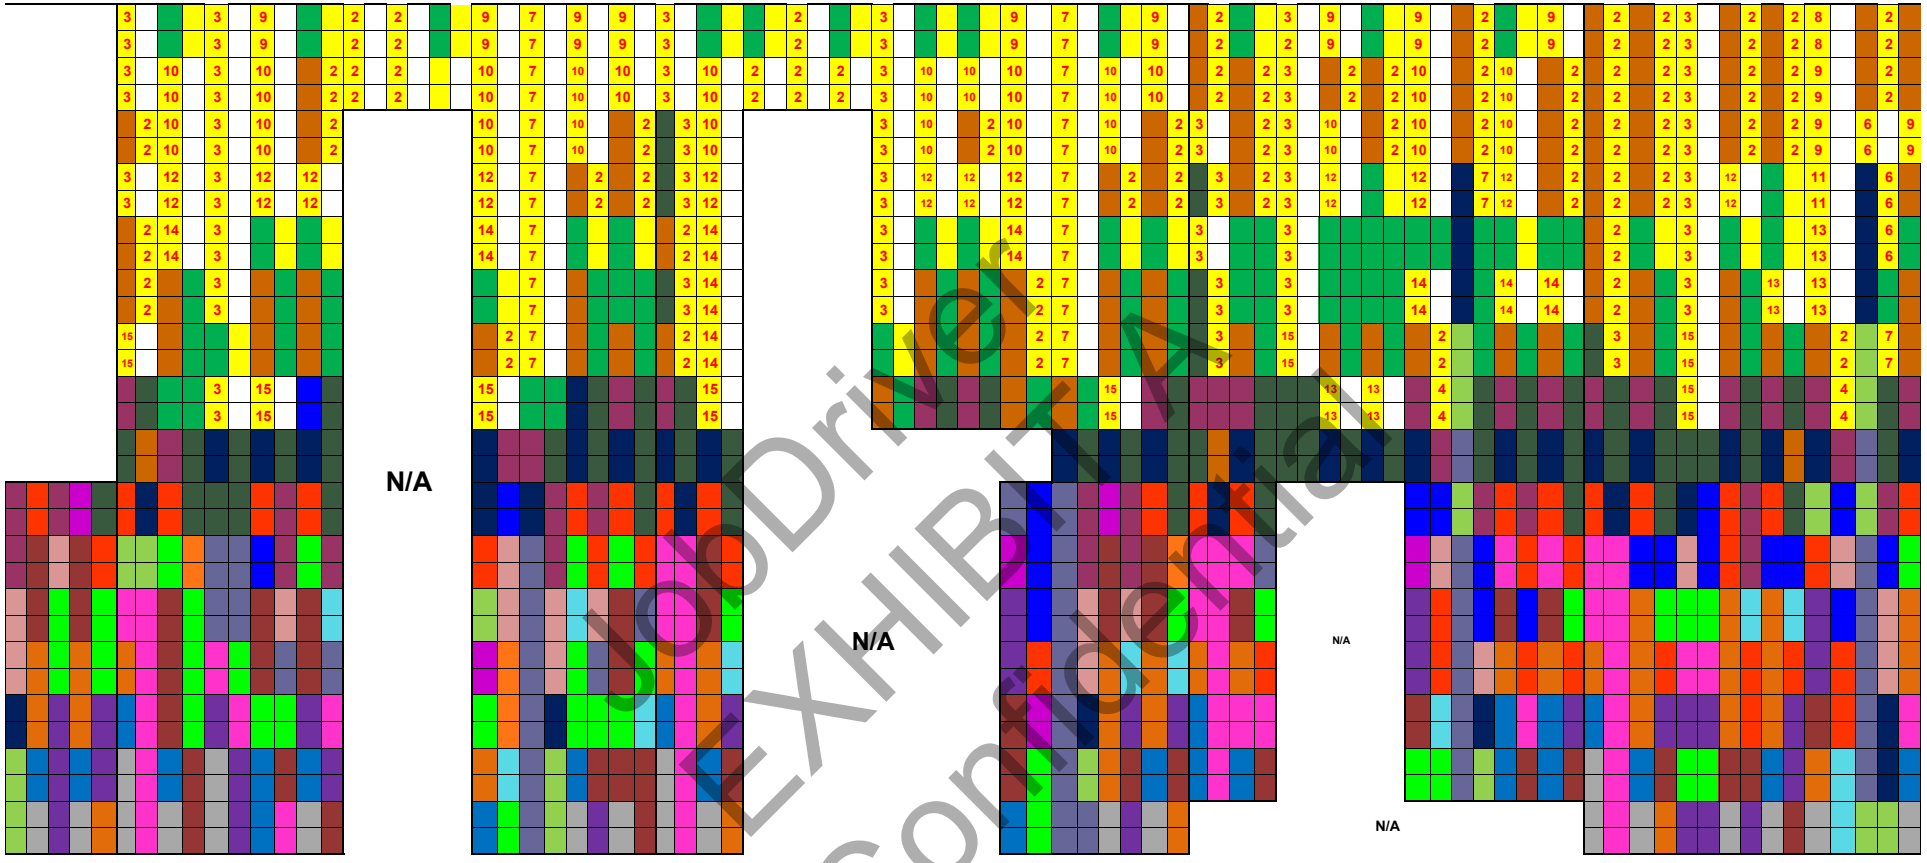

JobDriver
EXHIBIT A
Confidential

| 22 Unit | | |

2
2
2

Pleasants Hardware

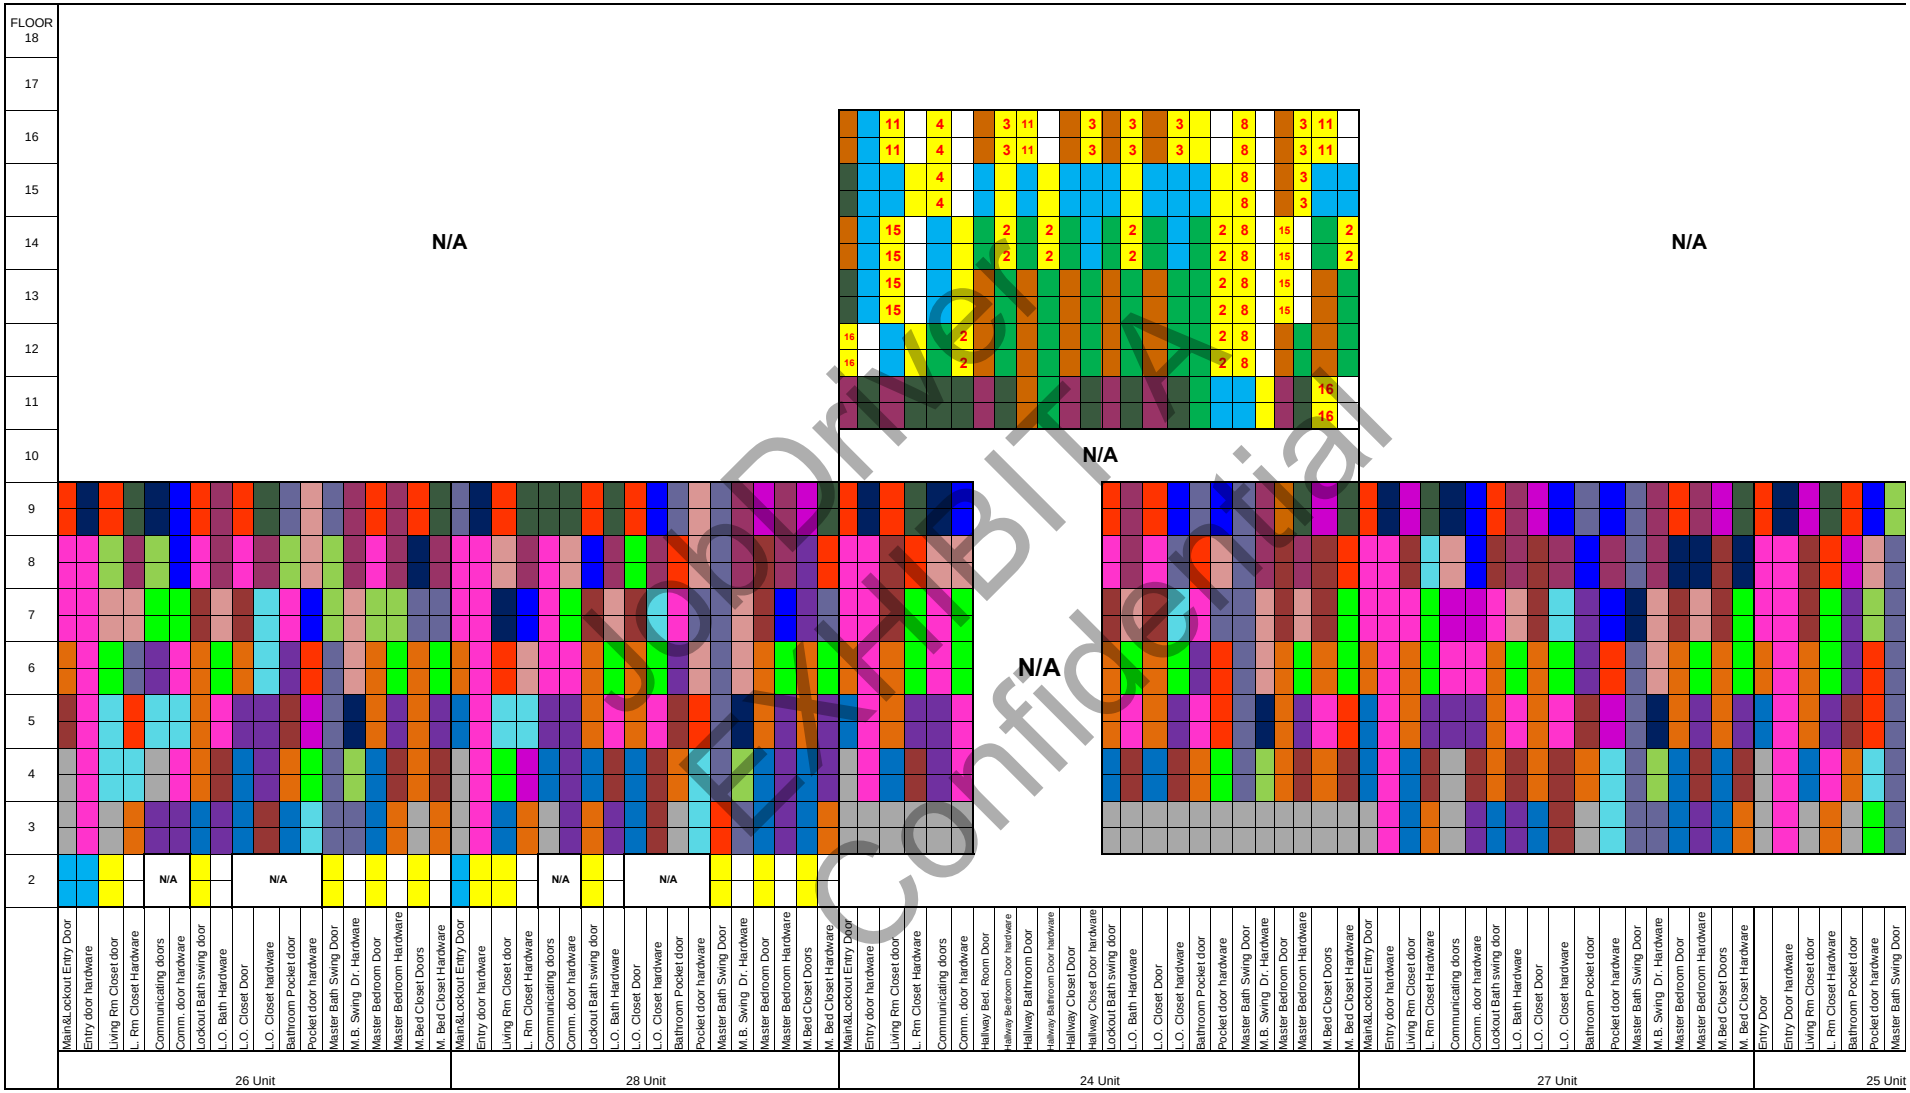

Job Driver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012

INCOMPLETE ITEMS

Pleasants Hardware

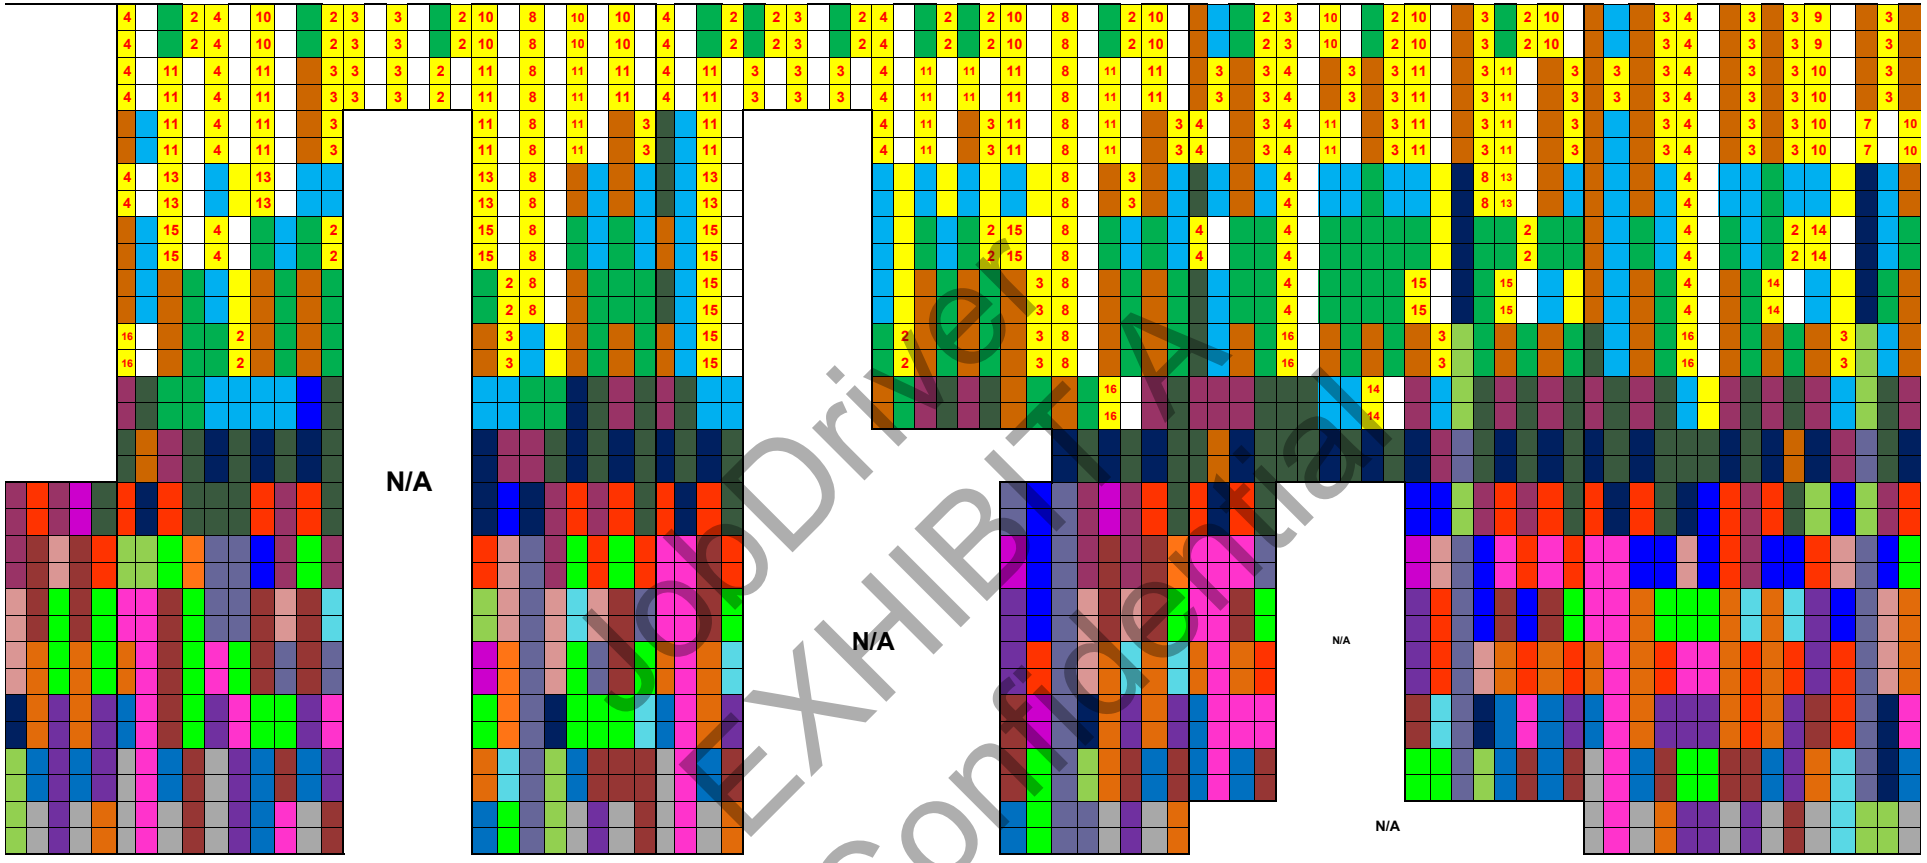

JobDrive
EXHIBIT A
Confidential

| | 22 Unit | | |

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

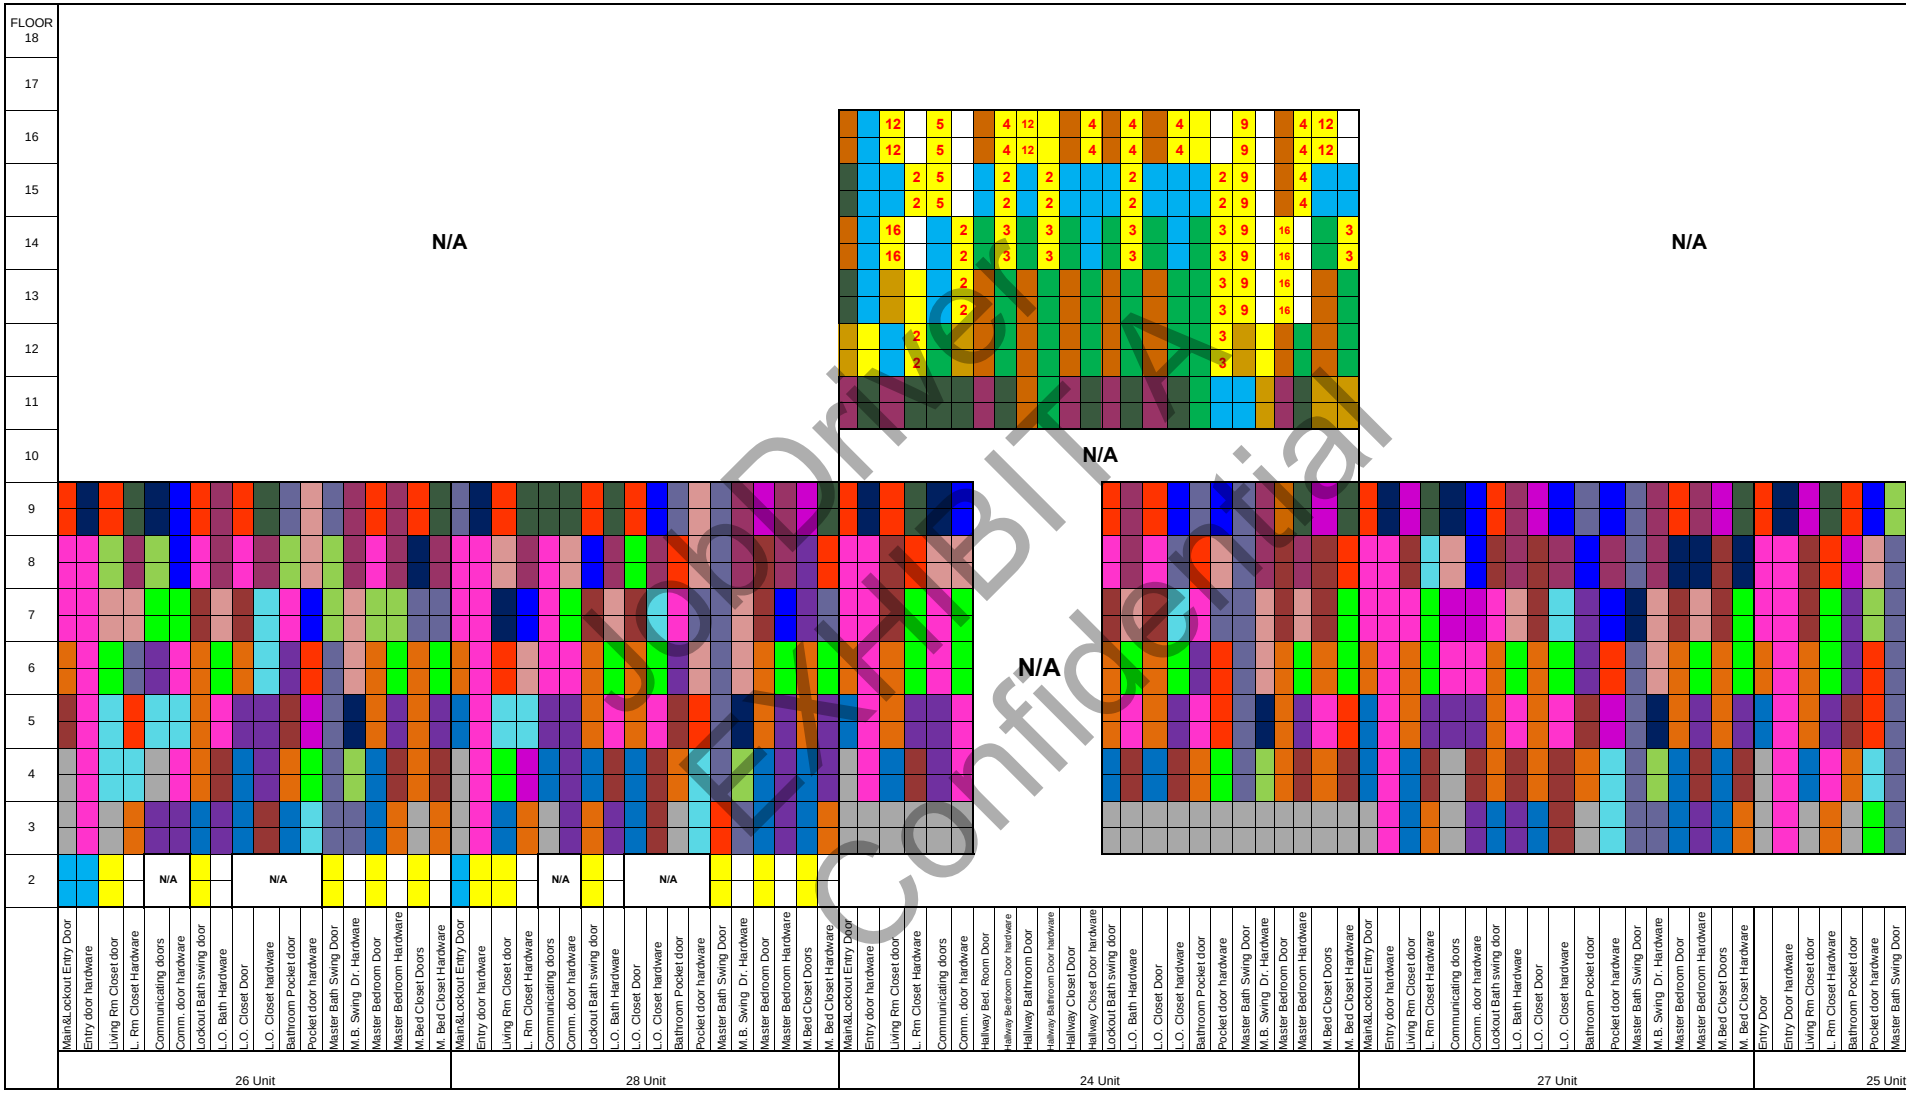

Job Drive
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012

INCOMPLETE ITEMS

Pleasants Hardware

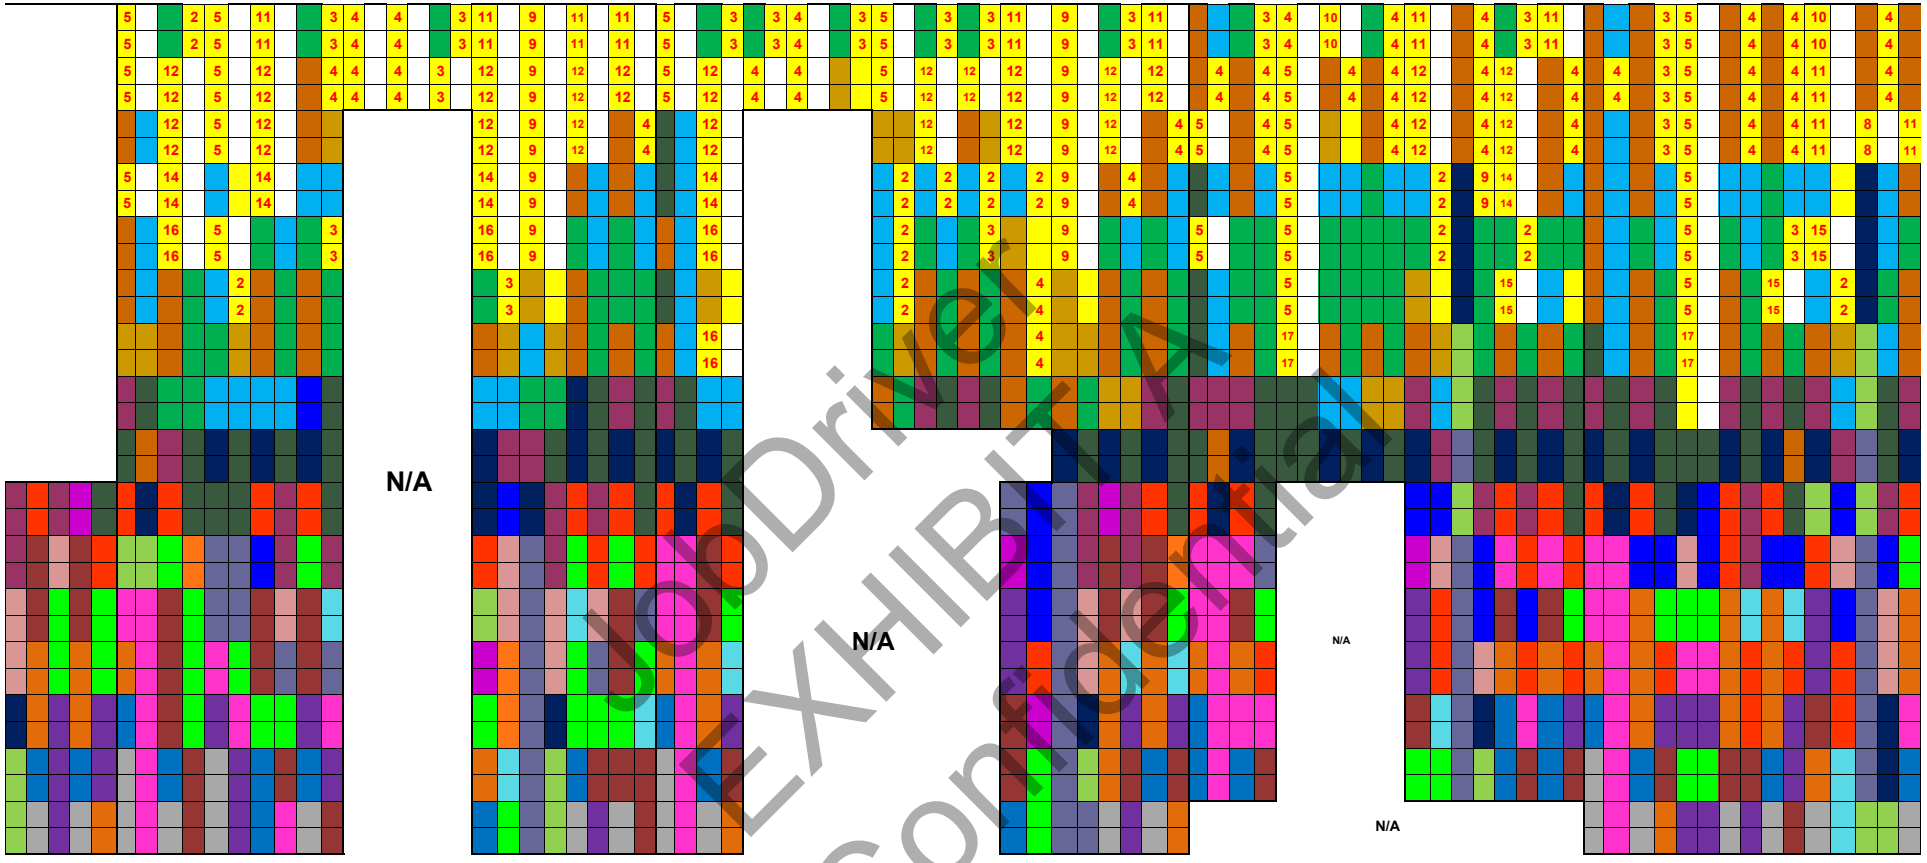

JobDrive
EXHIBIT A
Confidential

| 22 Unit | | |

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

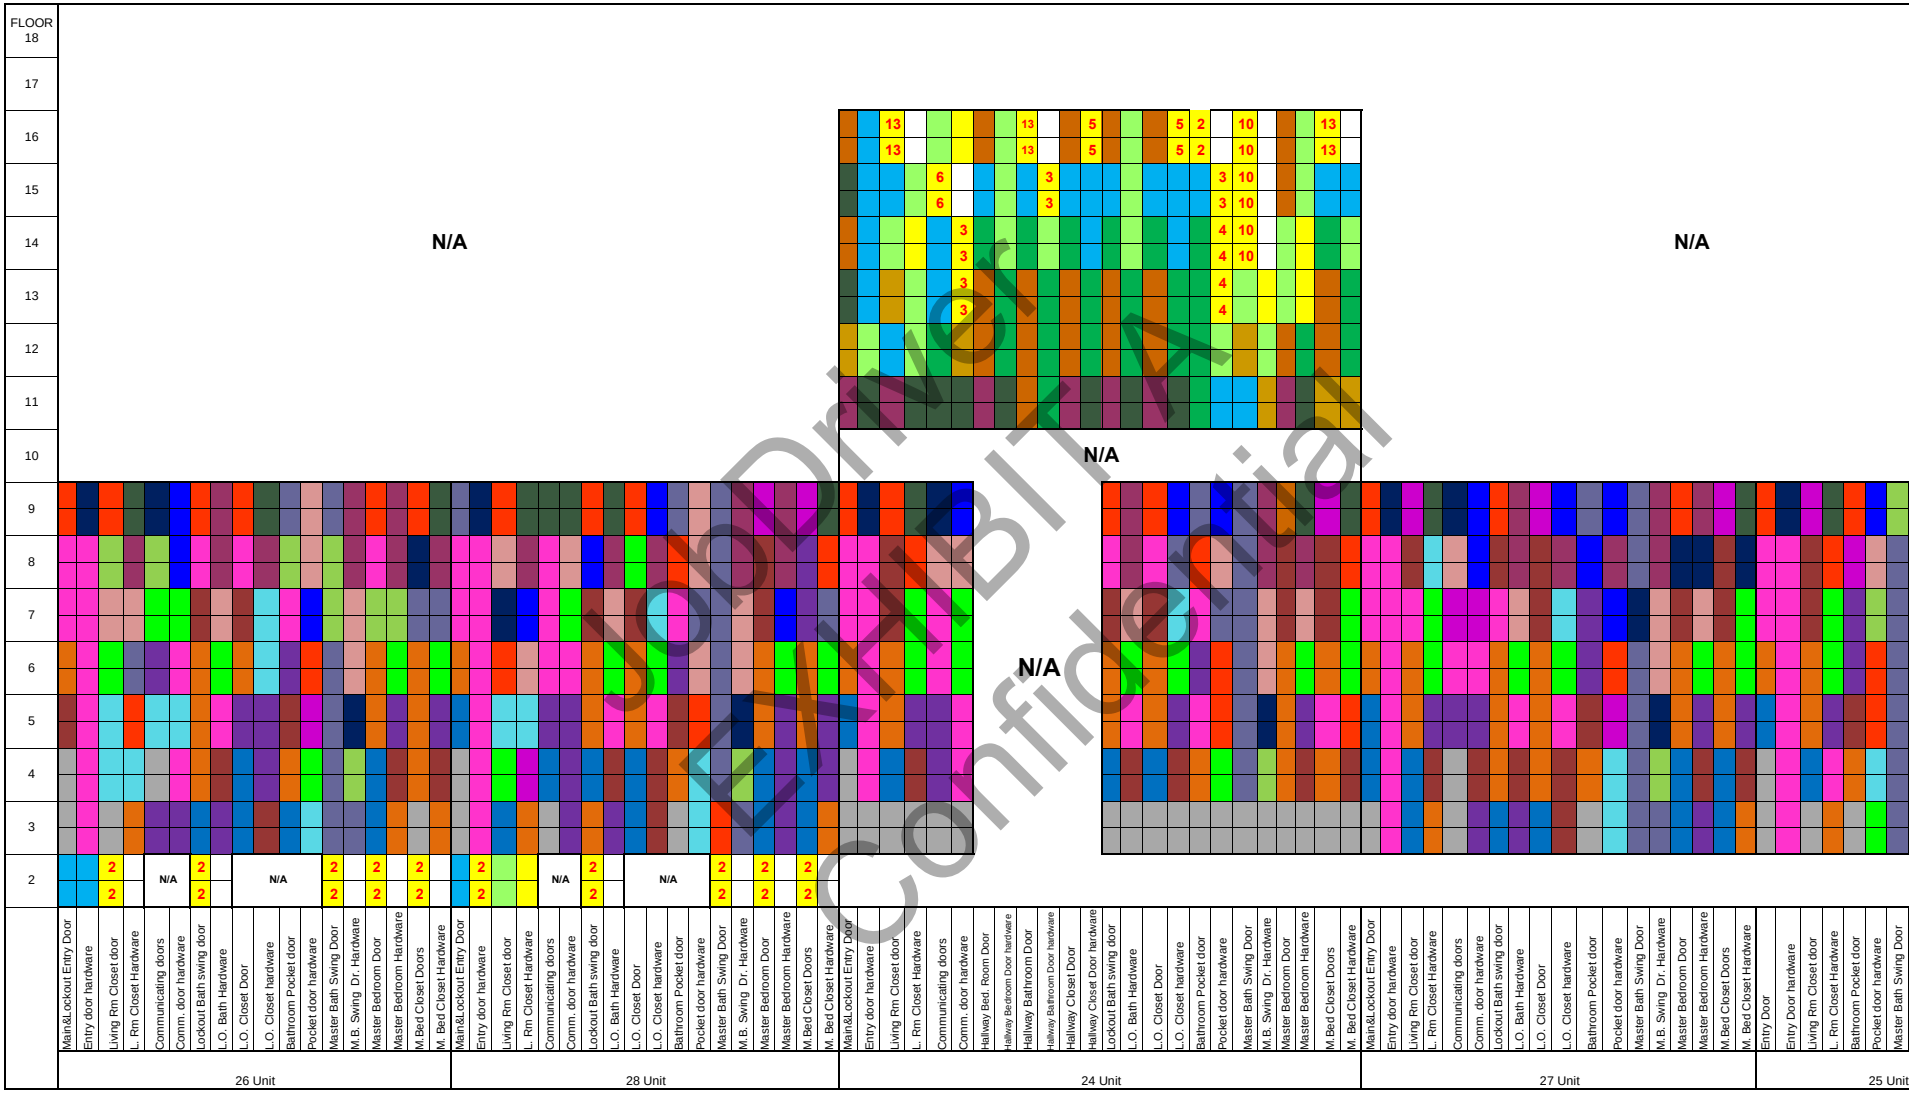

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012

INCOMPLETE ITEMS

Pleasants Hardware

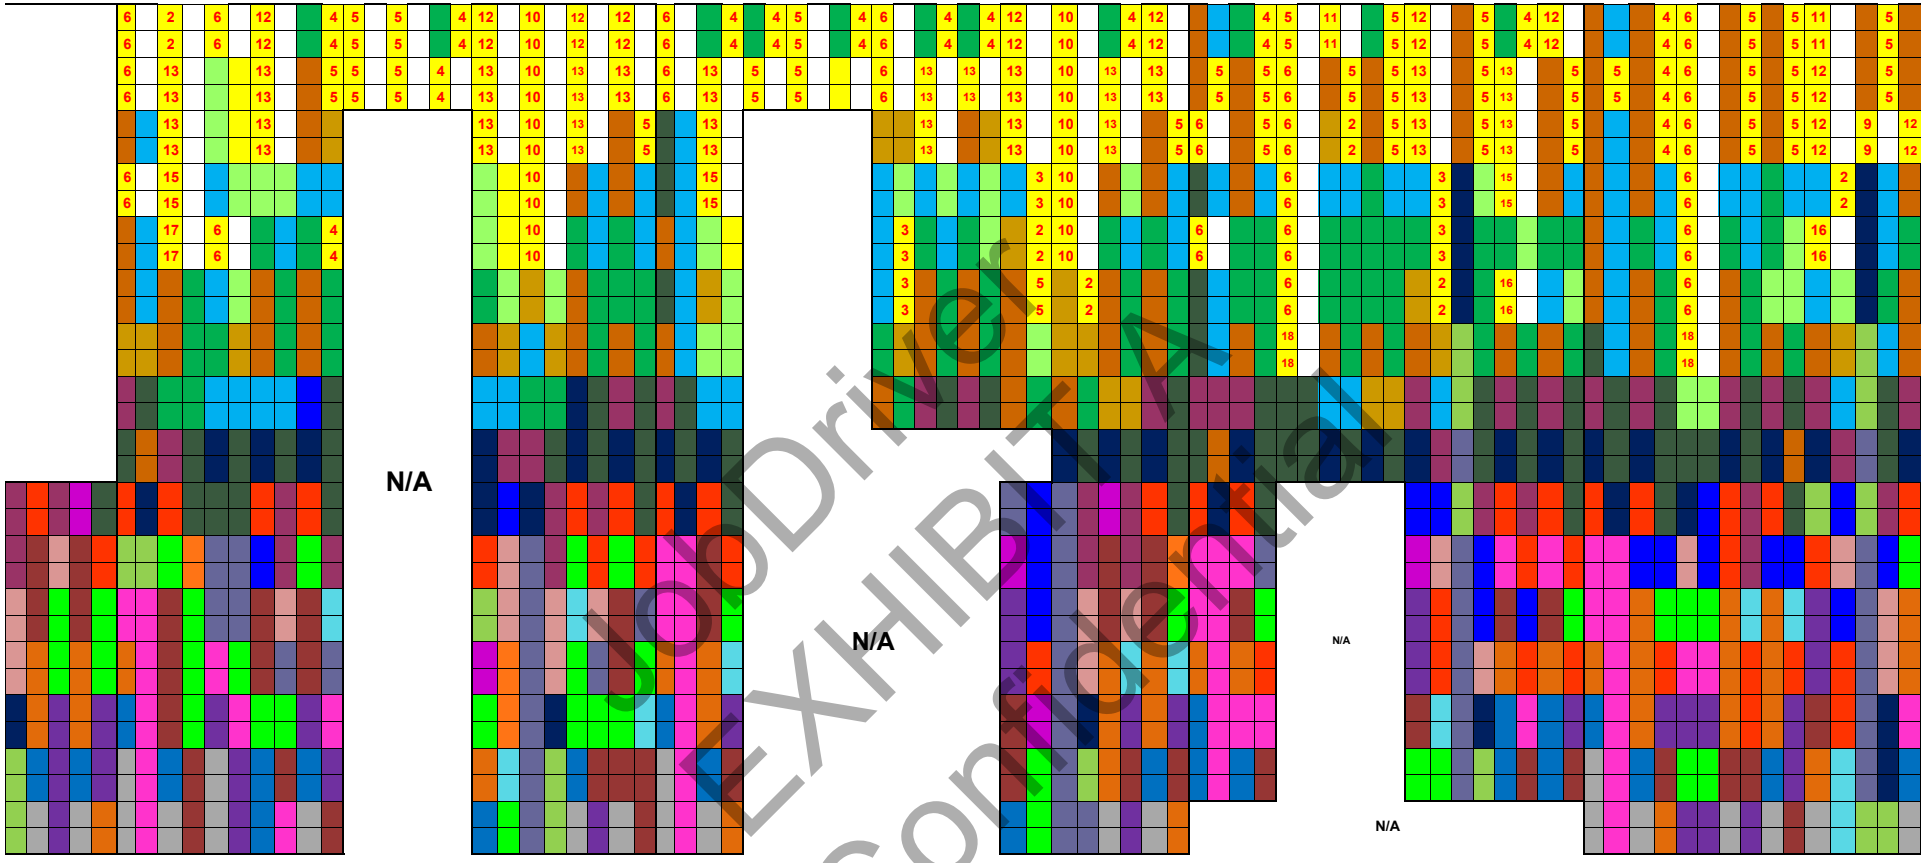

JobDriver
EXHIBIT A
Confidential

22 Unit	23 Unit	21 Unit	20 Unit
M.B. Swing Dr. Hardware	Entry Door	Entry Door	Main & Lockout Entry Door
Master Bedroom Door	Entry Door hardware	Entry Door hardware	Entry Door hardware
Master Bedroom Hardware	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door
M.Bed Closet Doors	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware
M. Bed Closet Hardware	Hallway Bed. Room door	Communicating Doors	Communicating Doors
Main&Lockout Entry Door	Hallway Bed. Room door hardware	Comm. Door Hardware	Comm. Door Hardware
Entry door hardware	Hallway Bathroom door	Lockout Bathroom Swing Door	Lockout Bath Swing Door
Living Rm Closet door	Hallway Bath. Room door hardware	Lockout Bath. Door hardware	L.O Bath Hardware
L. Rm Closet Hardware	Hallway Closet Door	Lockout Closet door	L.O. Closet Door
Communicating doors	Hallway Closet Door hardware	Lockout Closet Door hardware	L.O. Closet Hareware
Comm. door hardware	Communicating Doors	Bathroom Pocket door	Bathroom Pocket door
Lockout Bath swing door	Communicating Door hardware	Pocket door hardware	Pocket door hardware
L.O. Bath Hardware	L.O. Bathroom Swing Door	Master Bath Swing Door	Master Bath Swing Door
L.O. Closet Door	L.O. Bathroom Door hardware	M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware
L.O. Closet hardware	Lockout Closet Door	Master Bedroom Door	Master Bedroom Door
Hallway Bed. Room door	Lockout Closet Door hardware	Master Bedroom Hardware	
Hallway Bed. Room door hardware	Bathroom Pocket door	M.Bed Closet Doors	
Hallway Bathroom door	Pocket door hardware	M. Bed Closet Hardware	
Hallway Bath. Room door hardware	Master Bath Swing Door		
Hallway Closet Door	M.B. Swing Dr. Hardware		
Hallway Closet Door hardware	Master Bedroom Door		
Bathroom Pocket door	Master Bedroom Hardware		
Pocket door hardware	M.Bed Closet Doors		
Master Bath Swing Door	M. Bed Closet Hardware		
M.B. Swing Dr. Hardware			
Master Bedroom Door			
Master Bedroom Hardware			
M.Bed Closet Doors			
M. Bed Closet Hardware			

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

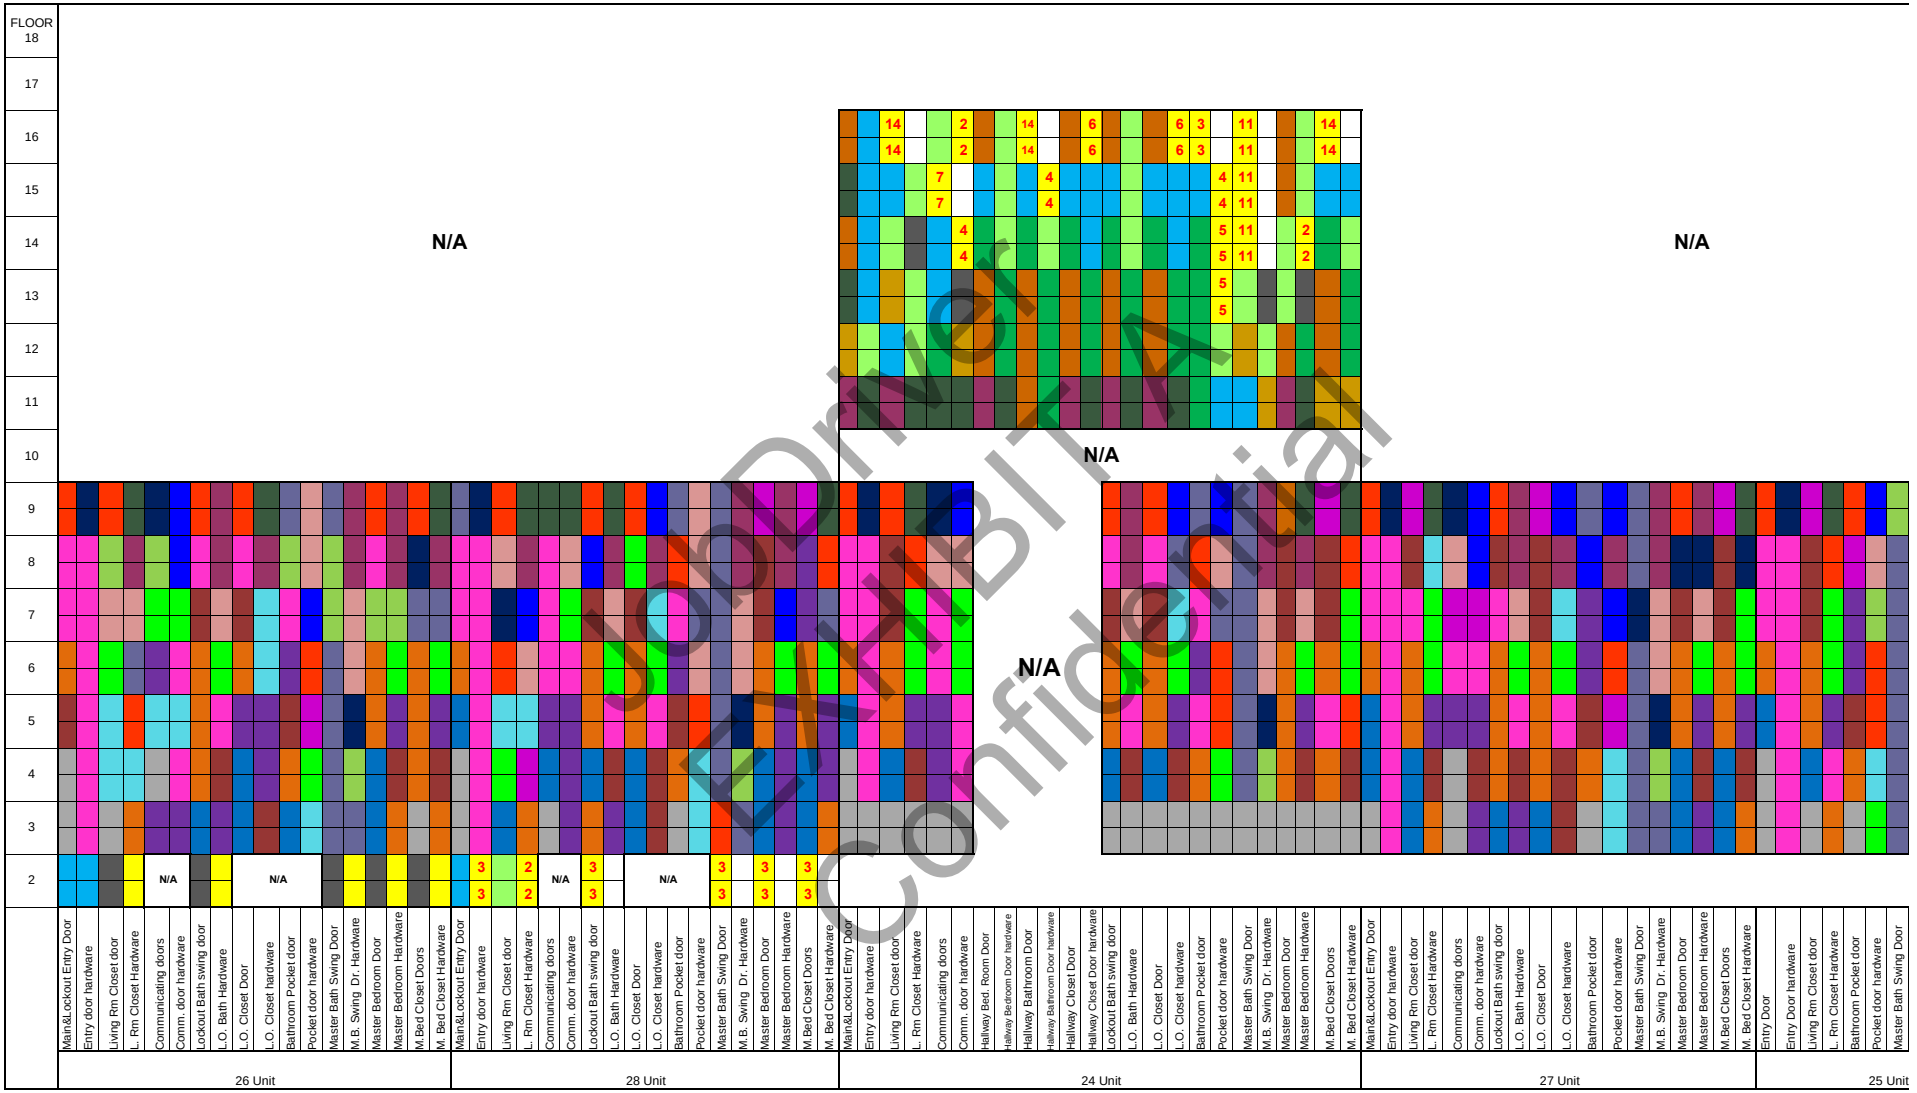

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012

INCOMPLETE ITEMS

Pleasants Hardware

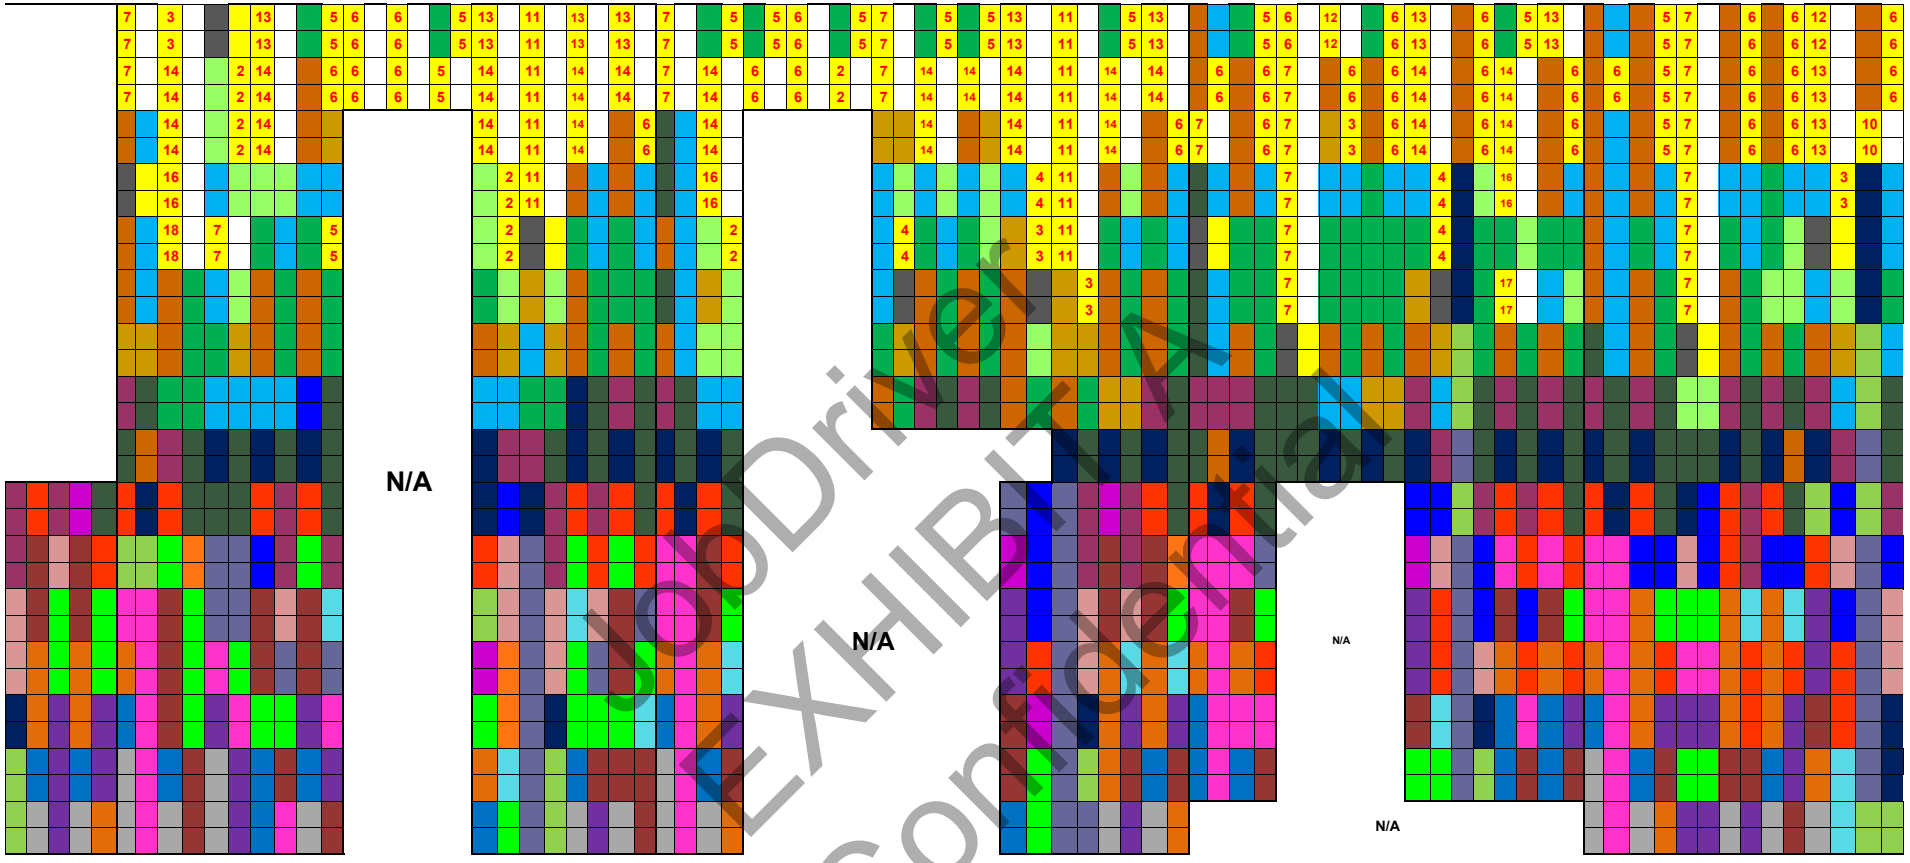

JobDriver
EXHIBIT A
Confidential

| | 22 Unit | | |

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

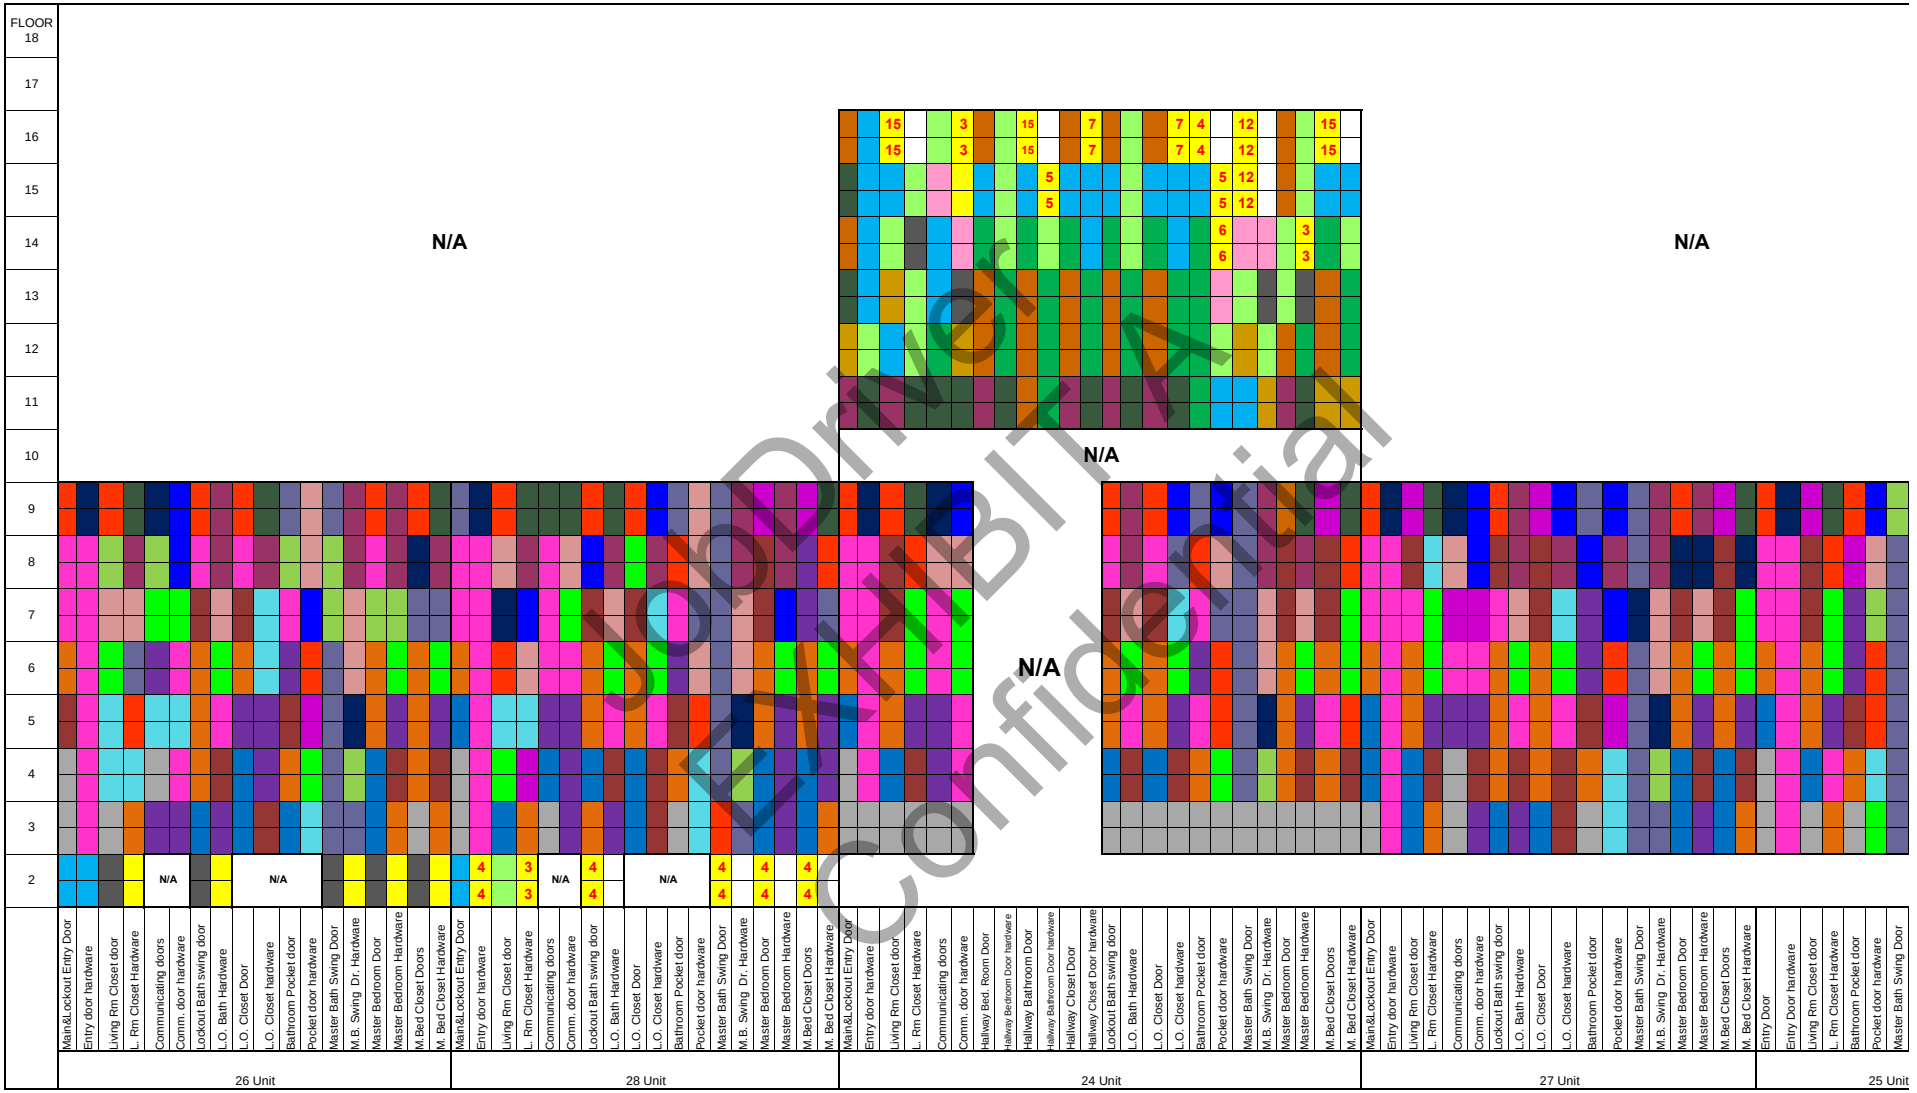

JobDrive
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012

INCOMPLETE ITEMS

Pleasants Hardware

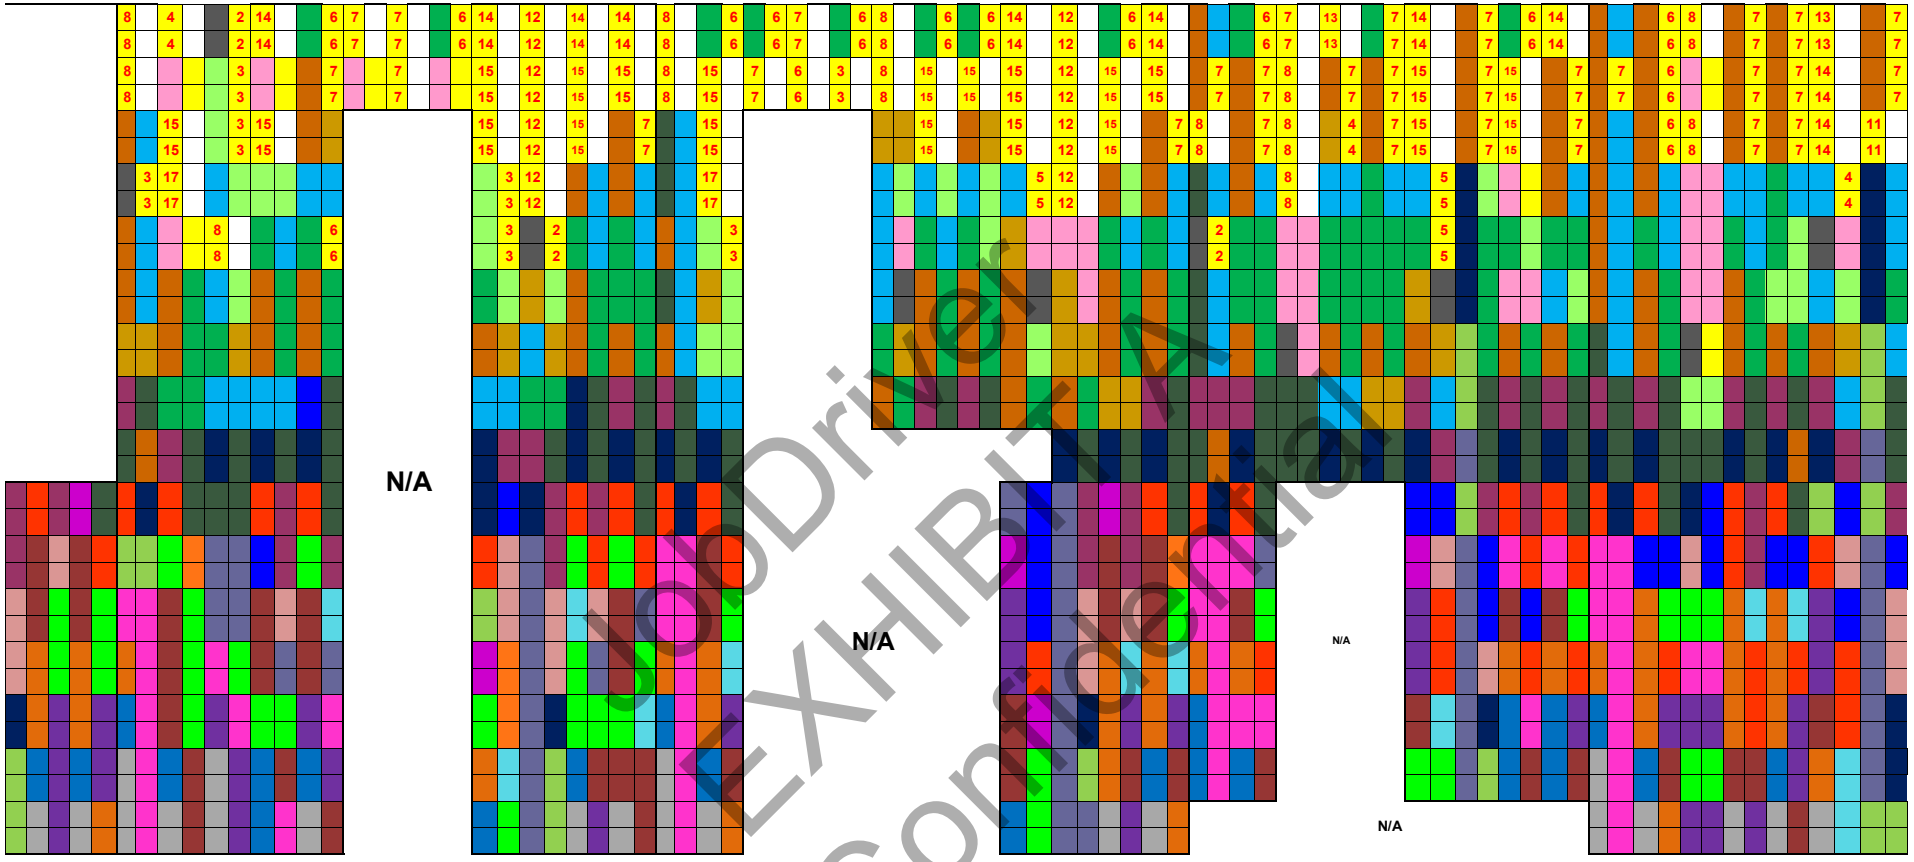

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | Mt. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door | L.O. Closet Hareware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware |
|---|---|---

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

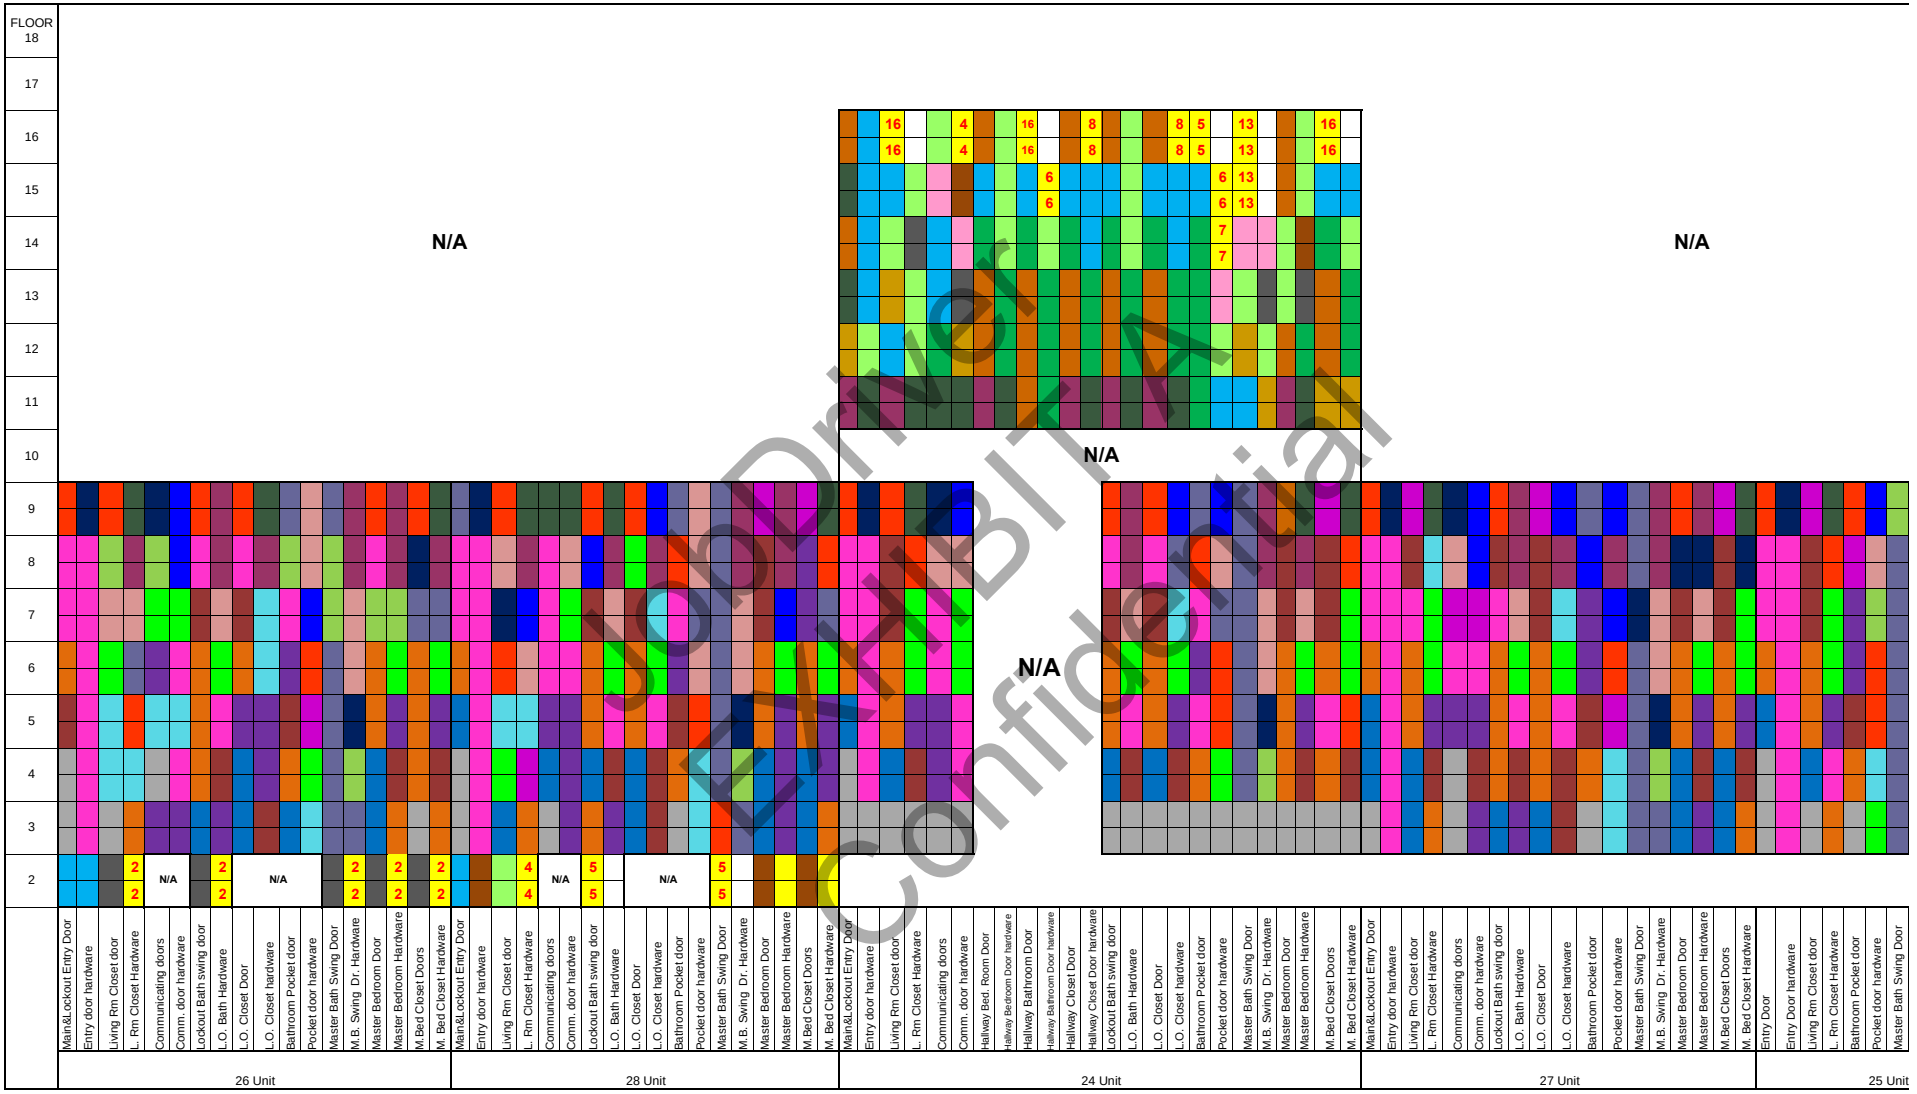

JobDriver EXHIBIT A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

Pleasants Hardware

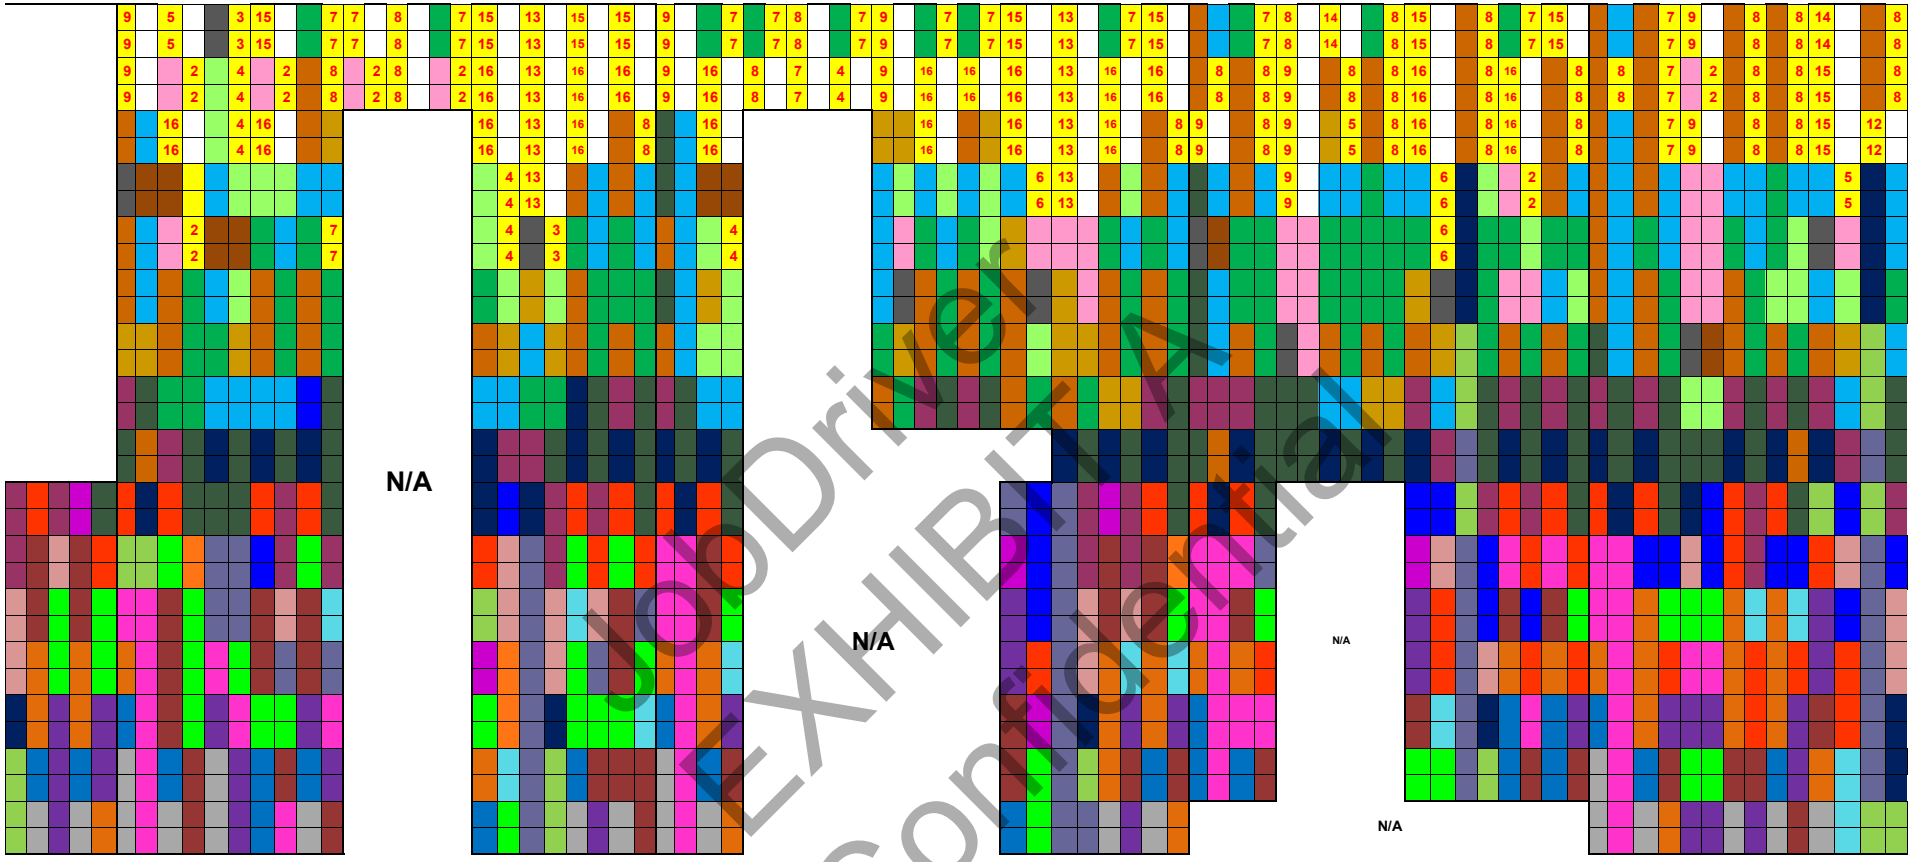

JobDriver
EXHIBIT A
Confidential

| | 22 Unit | | |

Master Bedroom Door
Master Bedroom Hardware
M.Bed Closet Doors
M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

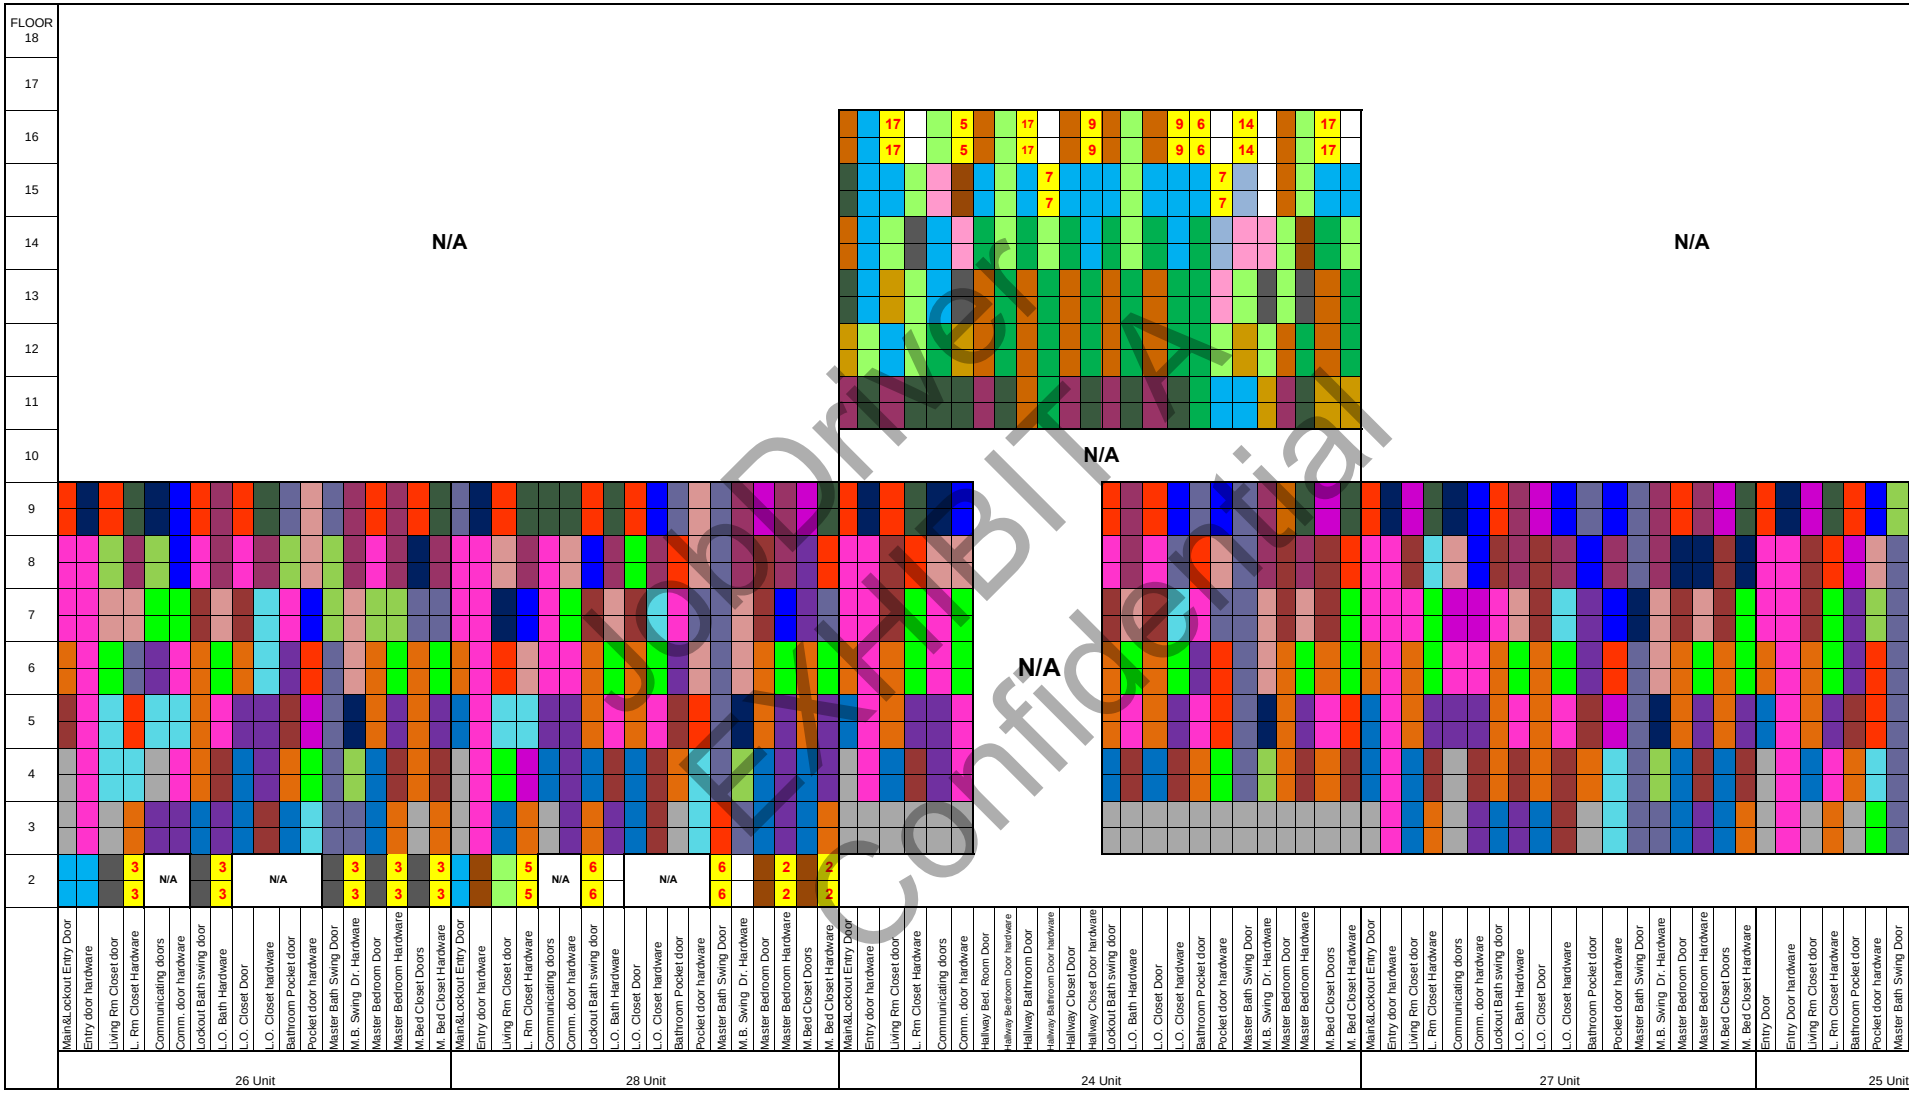

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE

Pleasants Hardware

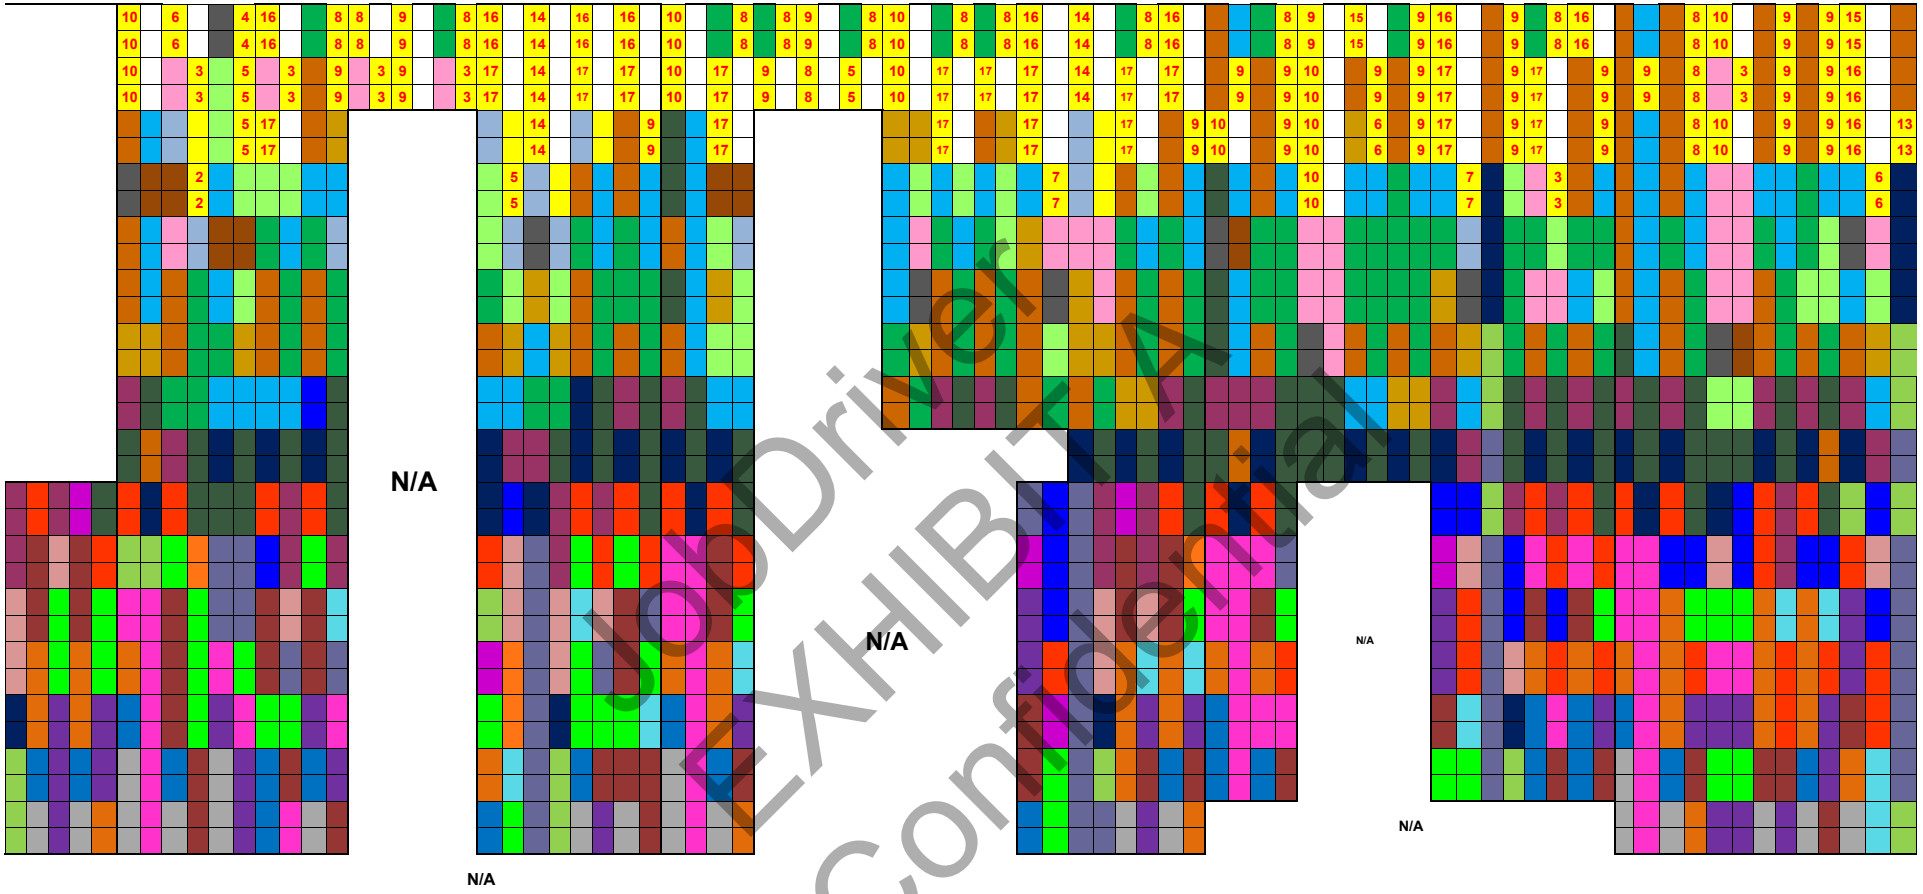

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Hardware | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door | L.O. Closet Hareware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door |
|---|---|---

JobDriver
EXHIBIT A
Confidential

Pleasants Hardware

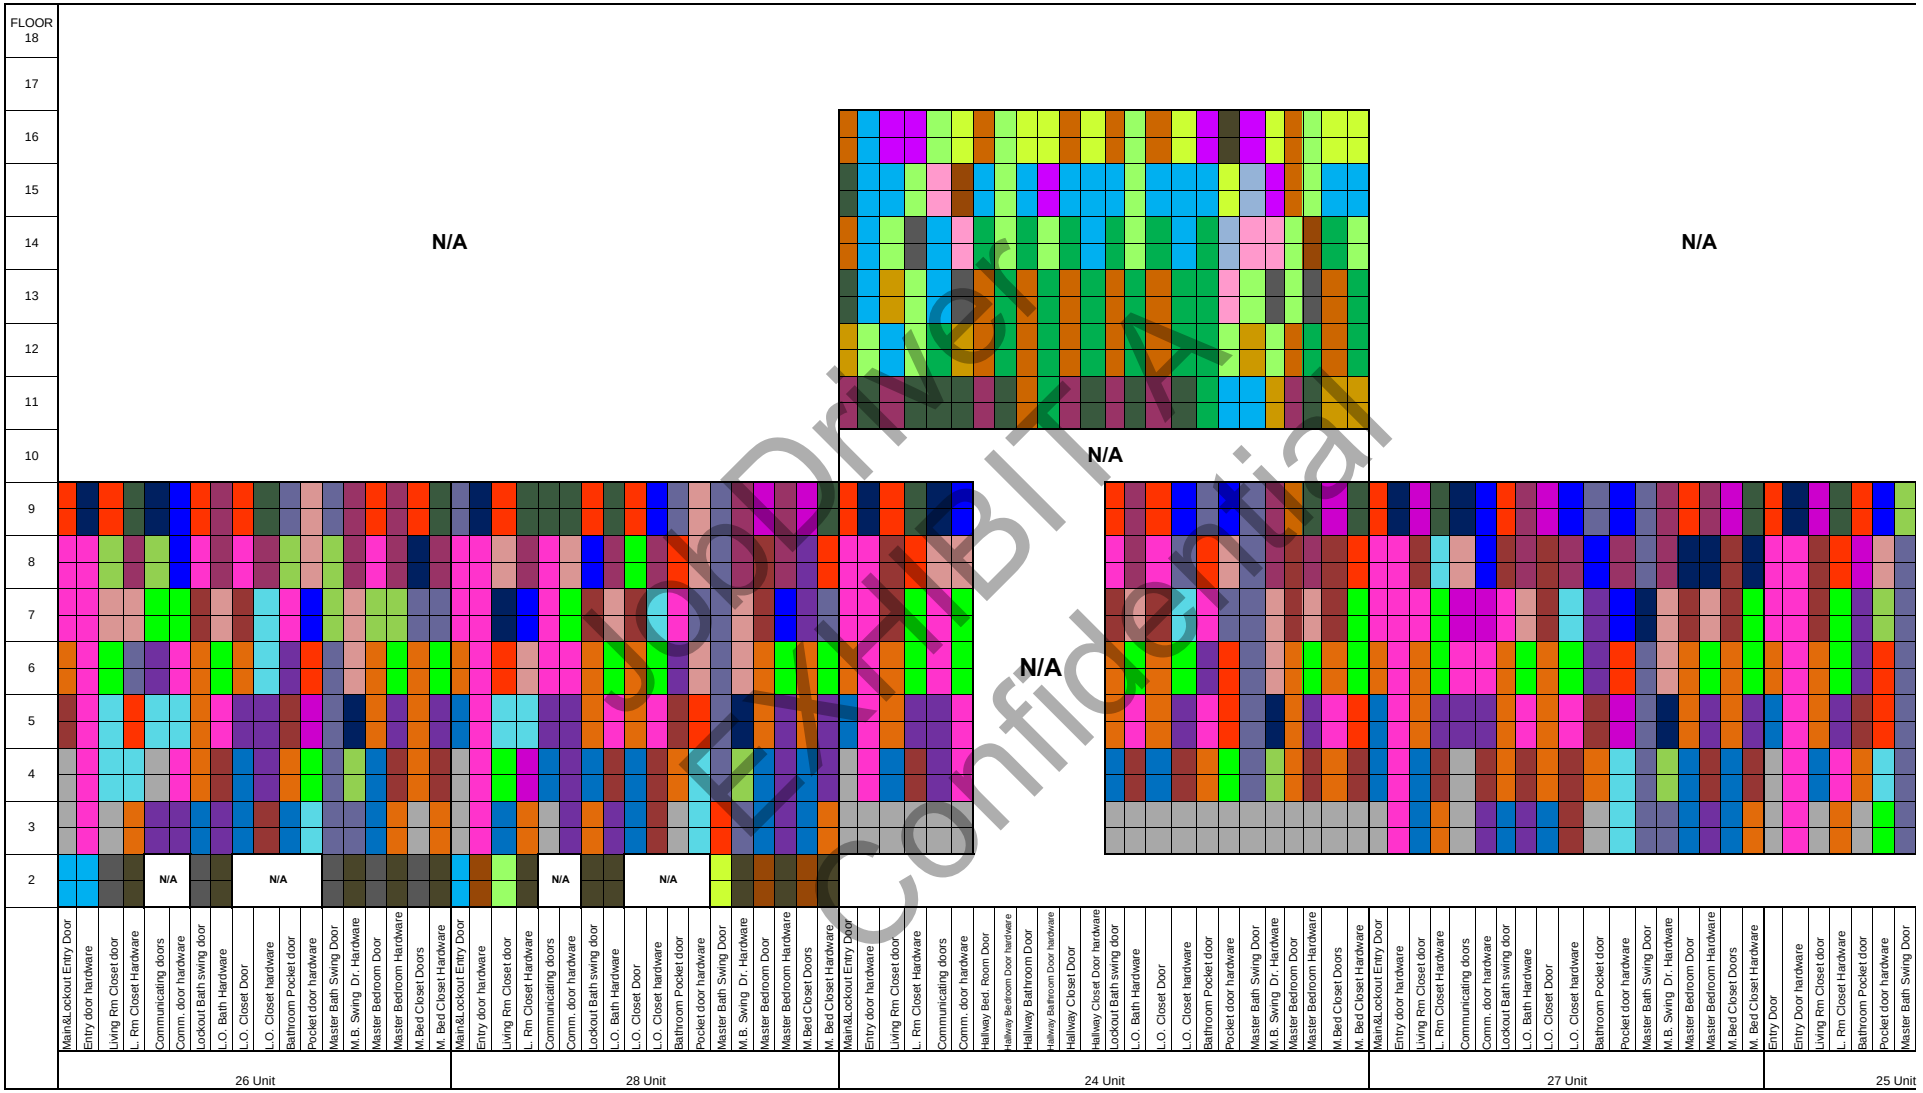

JobDriver
EXHIBIT A
Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

Pleasants Hardware

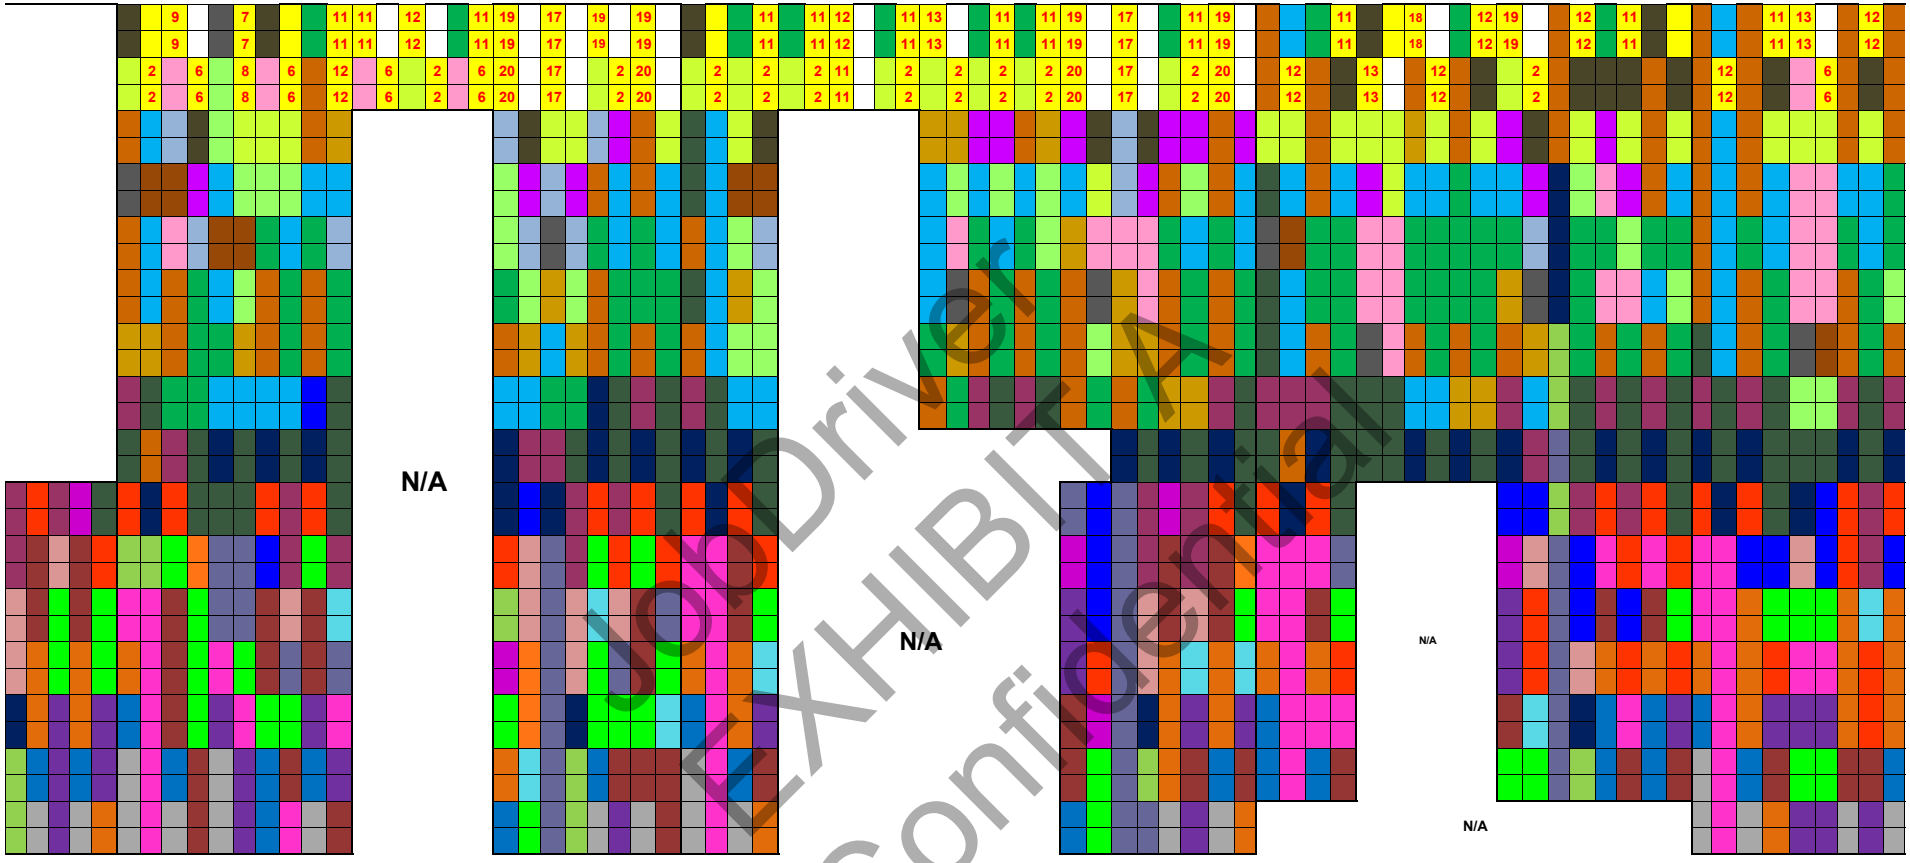

JobDriver
EXHIBIT A
Confidential

	22 Unit	23 Unit	21 Unit	20
M.B. Swing Dr. Hardware	Main&Lockout Entry Door	Entry Door	Entry Door	Main & Lockout Entry Door
Master Bedroom Door	Entry door hardware	Entry Door hardware	Entry Door hardware	Entry Door hardware
Master Bedroom Hardware	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door	Living Rm Closet door
M.Bed Closet Doors	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware	L. Rm Closet Hardware
M. Bed Closet Hardware	Communicating doors	Hallway Bed. Room door	Communicating Doors	Communicating Doors
	Comm. door hardware	Hallway Bed. Room door hardware	Comm. Door Hardware	Comm. Door Hardware
	Lockout Bath swing door	Hallway Bathroom door	Lockout Bath. Door hardware	Lockout Bath Swing Door
	L.O. Bath Hardware	Hallway Bath. Room door hardware	Lockout Closet door	L.O Bath Hardware
	L.O. Closet Door	Hallway Closet Door	Lockout Closet Door hardware	L.O. Closet Door
	L.O. Closet hardware	Hallway Closet Door hardware	Bathroom Pocket door	
	Hallway Bed. Room door	Communicating Door	Pocket door hardware	
	Hallway Bed. Room door hardware	Communicating Door hardware	Master Bath Swing Door	
	Hallway Bathroom door	L.O. Bathroom Swing Door	M.B. Swing Dr. Hardware	
	Hallway Bath. Room door hardware	L.O. Bathroom Door hardware	Master Bedroom Door	
	Hallway Closet Door	Lockout Closet Door	Master Bedroom Hardware	
	Hallway Closet Door hardware	Lockout Closet Door hardware	M.Bed Closet Doors	
	Bathroom Pocket door	Bathroom Pocket door	M. Bed Closet Hardware	
	Pocket door hardware	Pocket door hardware		
	Master Bath Swing Door	Master Bath Swing Door		
	M.B. Swing Dr. Hardware	M.B. Swing Dr. Hardware		
	Master Bedroom Door	Master Bedroom Door		
	Master Bedroom Hardware	Master Bedroom Hardware		
	M.Bed Closet Doors	M.Bed Closet Doors		
	M. Bed Closet Hardware	M. Bed Closet Hardware		

: 7/18/2012
: 7/25/2012
: 8/1/2012
: 8/8/2012



Unit	
	L.O. Closet Hareware
	Bathroom Pocket door
	Pocket door hardware
	Master Bath Swing Door
	M.B. Swing Dr. Hardware
	Master Bedroom Door
	Master Bedroom Hardware
	M.Bed Closet Doors
	M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

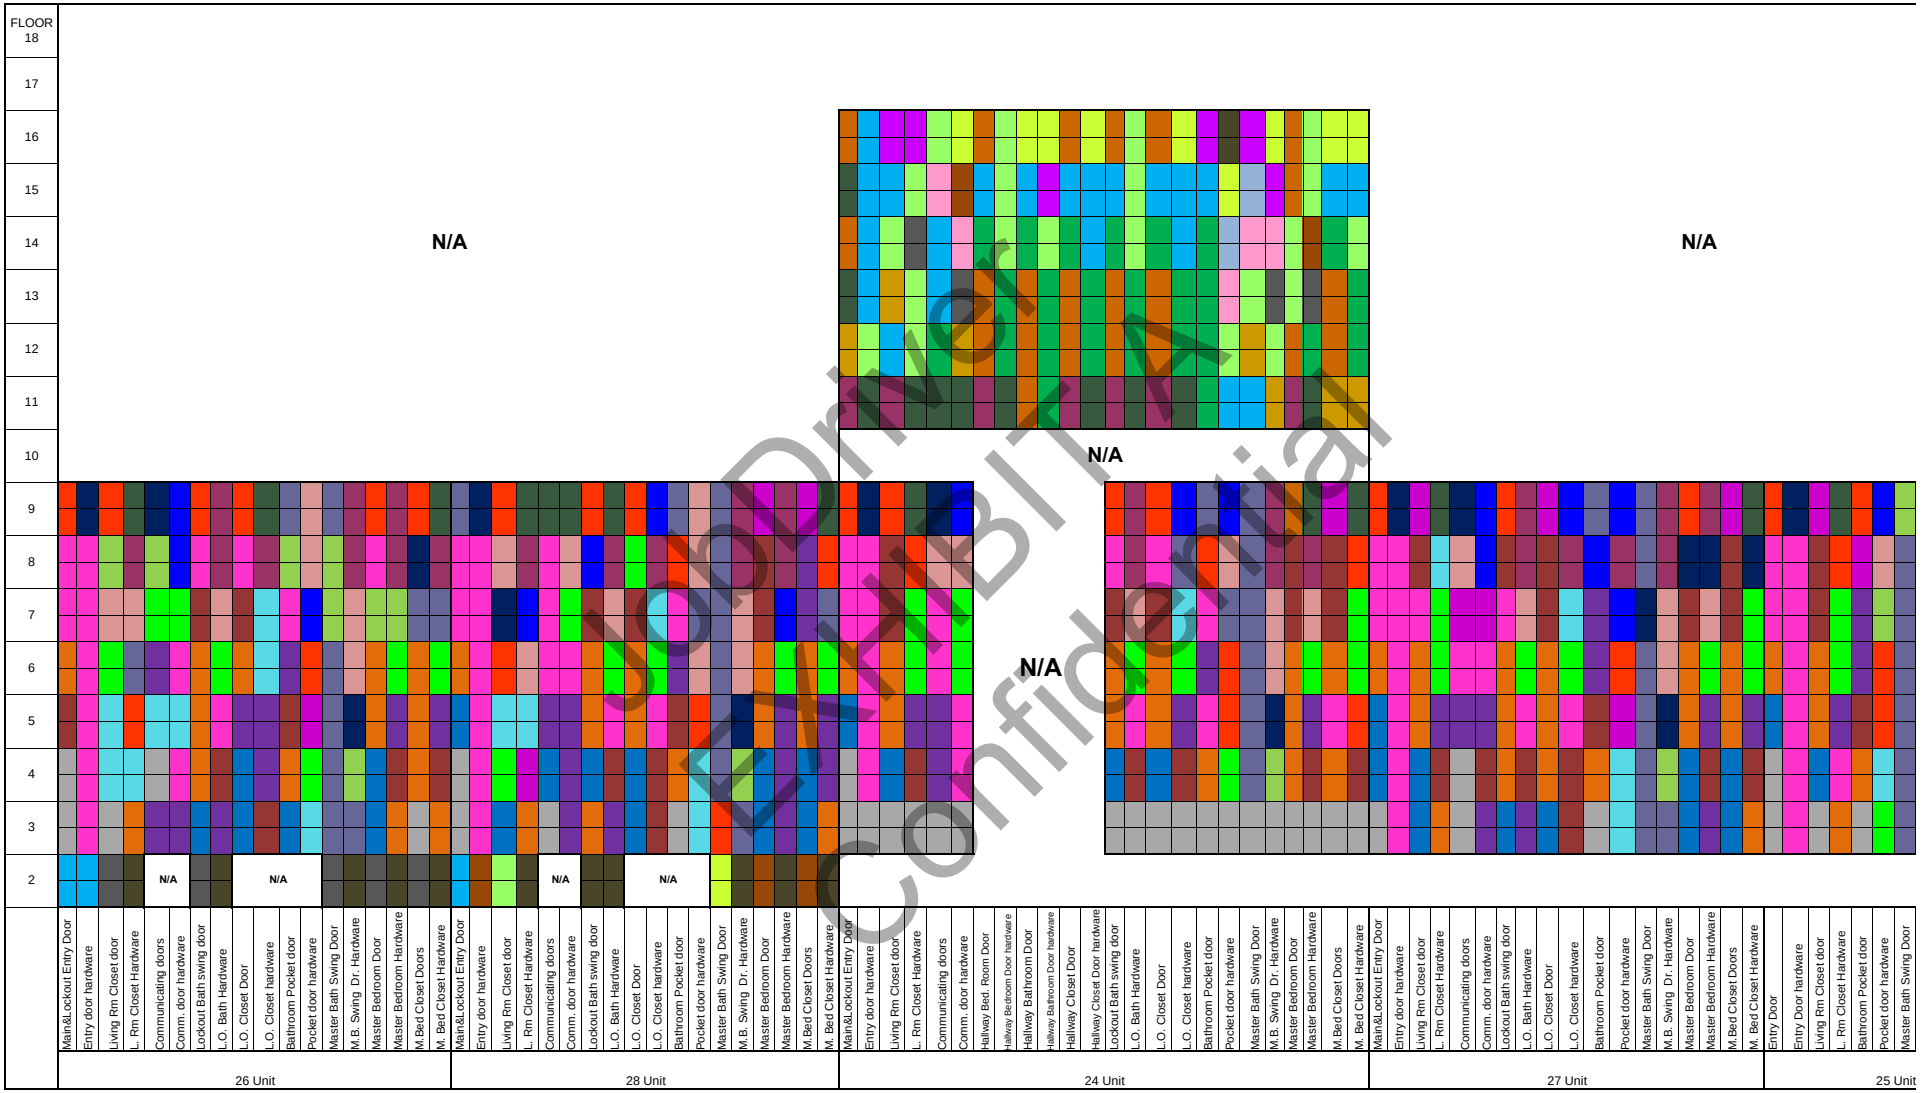

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

Pleasants Hardware

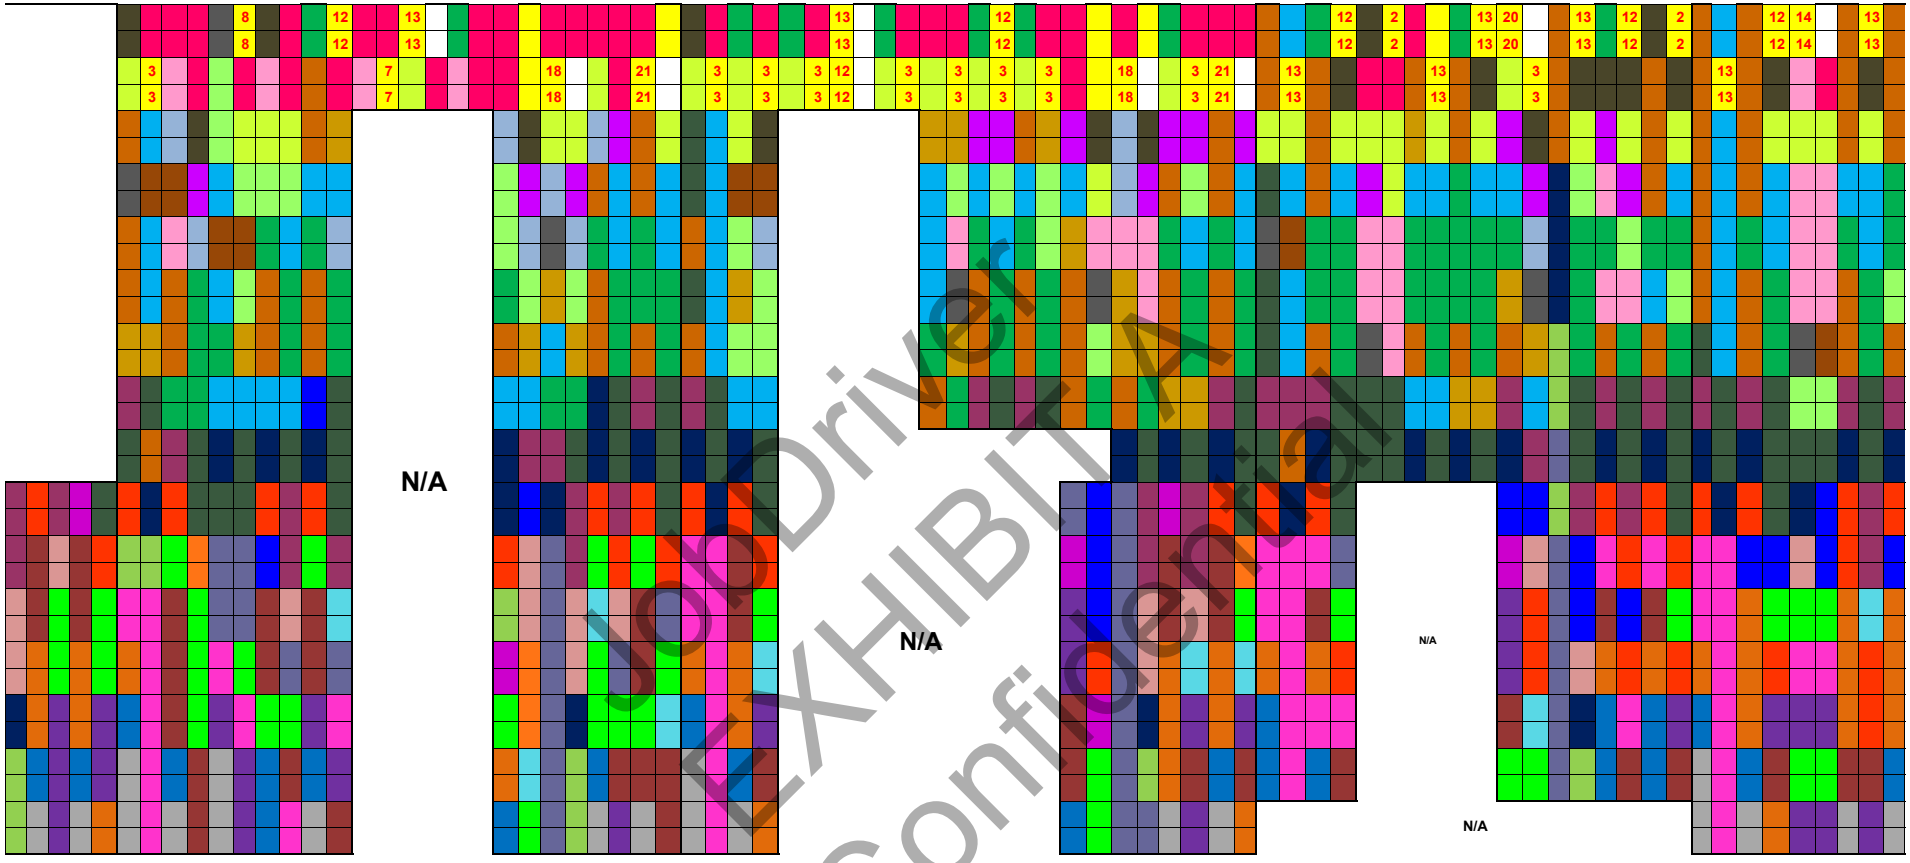

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Hardware | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door |
|---|---|---



Unit	
	L.O. Closet Hareware
	Bathroom Pocket door
	Pocket door hardware
	Master Bath Swing Door
	M.B. Swing Dr. Hardware
	Master Bedroom Door
	Master Bedroom Hardware
	M.Bed Closet Doors
	M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

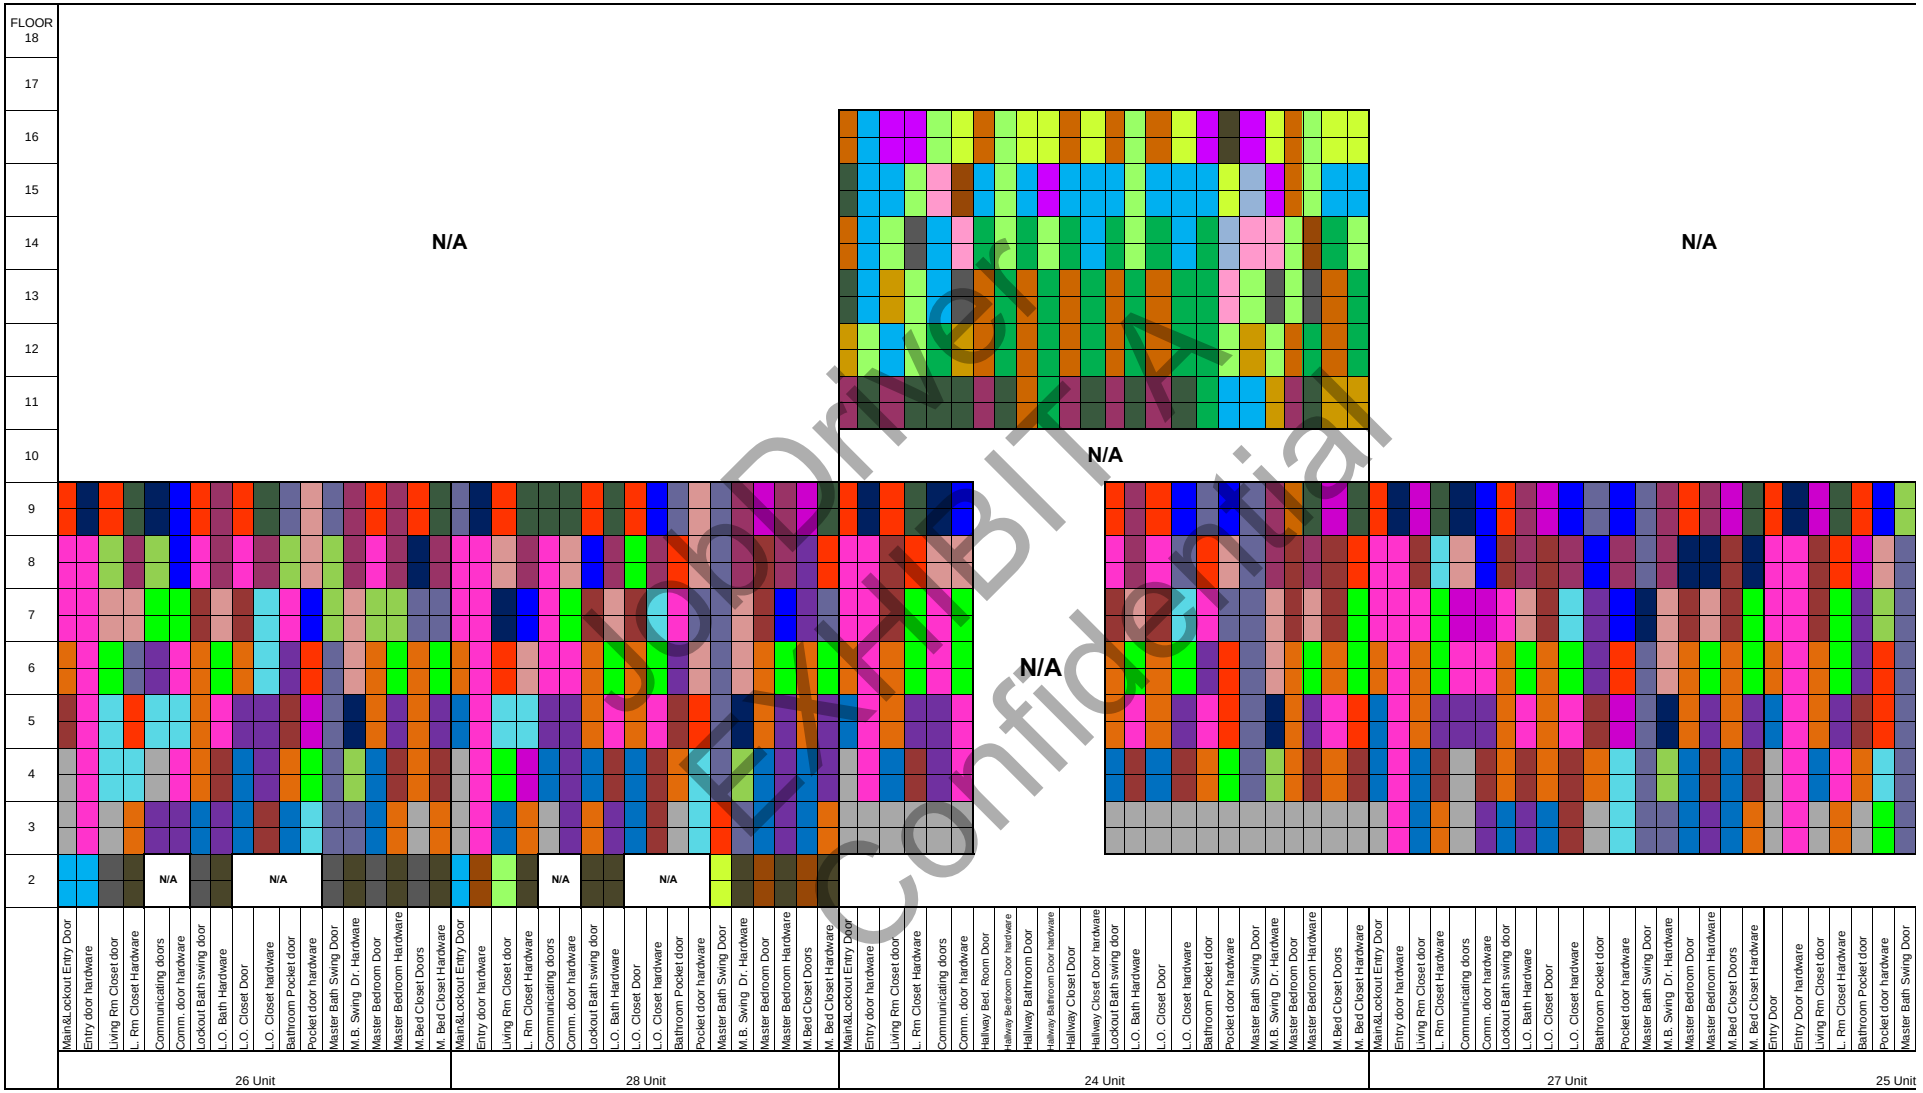

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

Pleasants Hardware

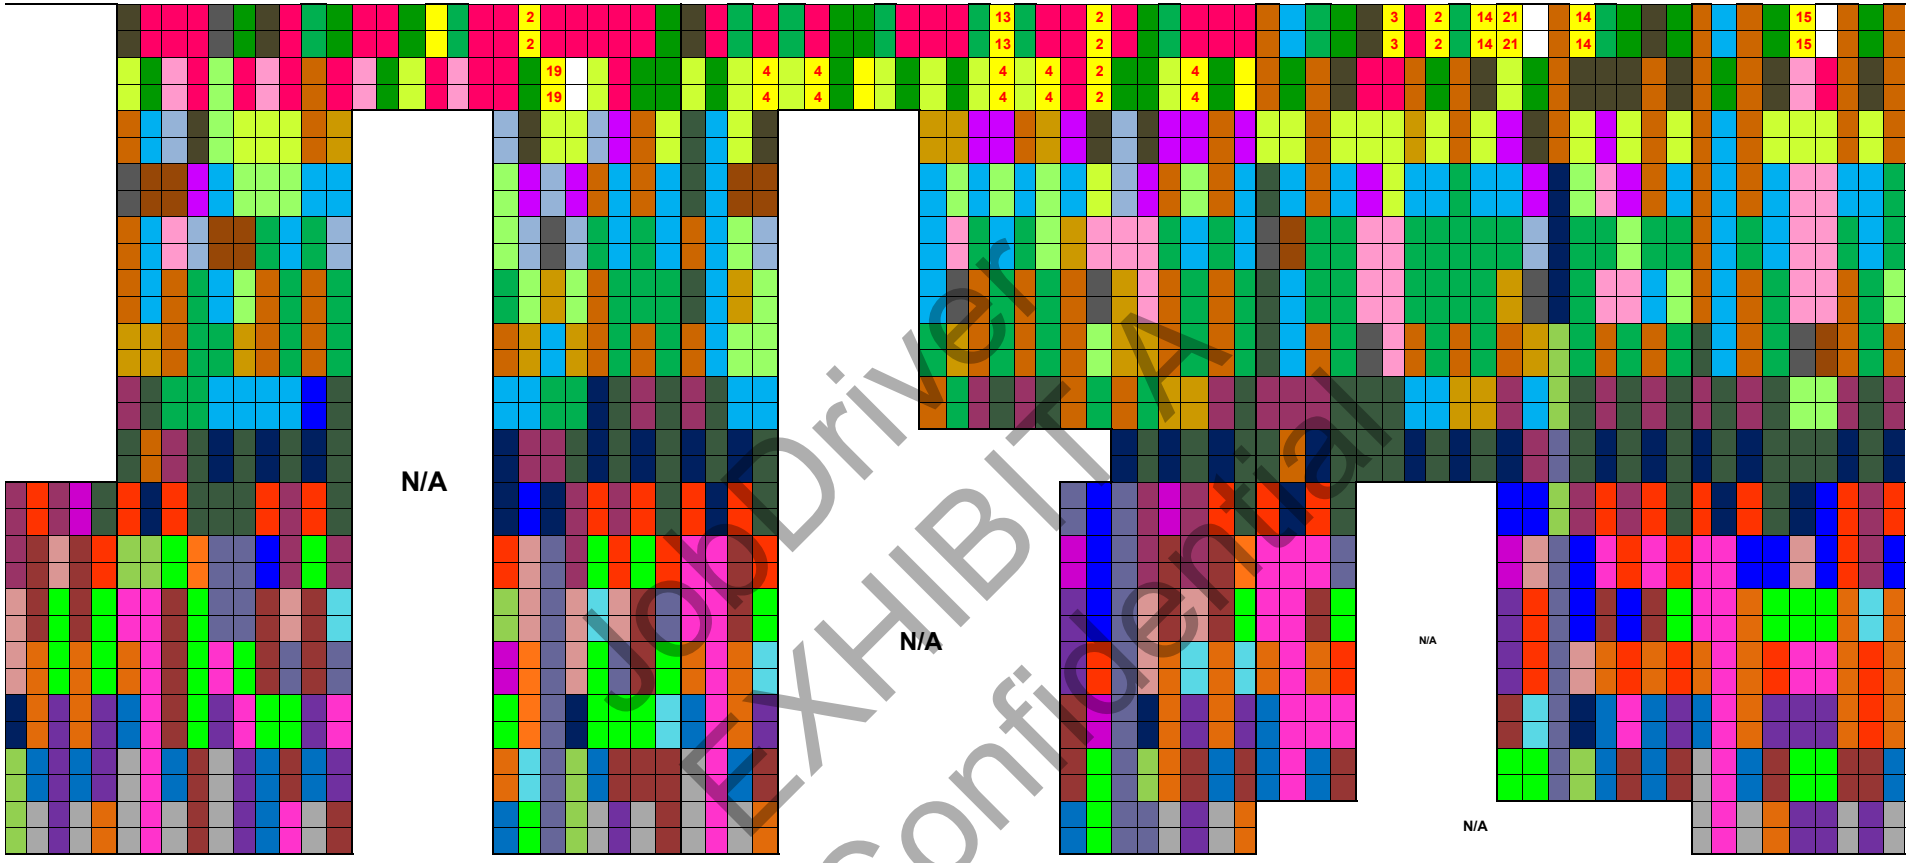

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Hardware | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door |
|---|---|---



Unit	
	L.O. Closet Hareware
	Bathroom Pocket door
	Pocket door hardware
	Master Bath Swing Door
	M.B. Swing Dr. Hardware
	Master Bedroom Door
	Master Bedroom Hardware
	M.Bed Closet Doors
	M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

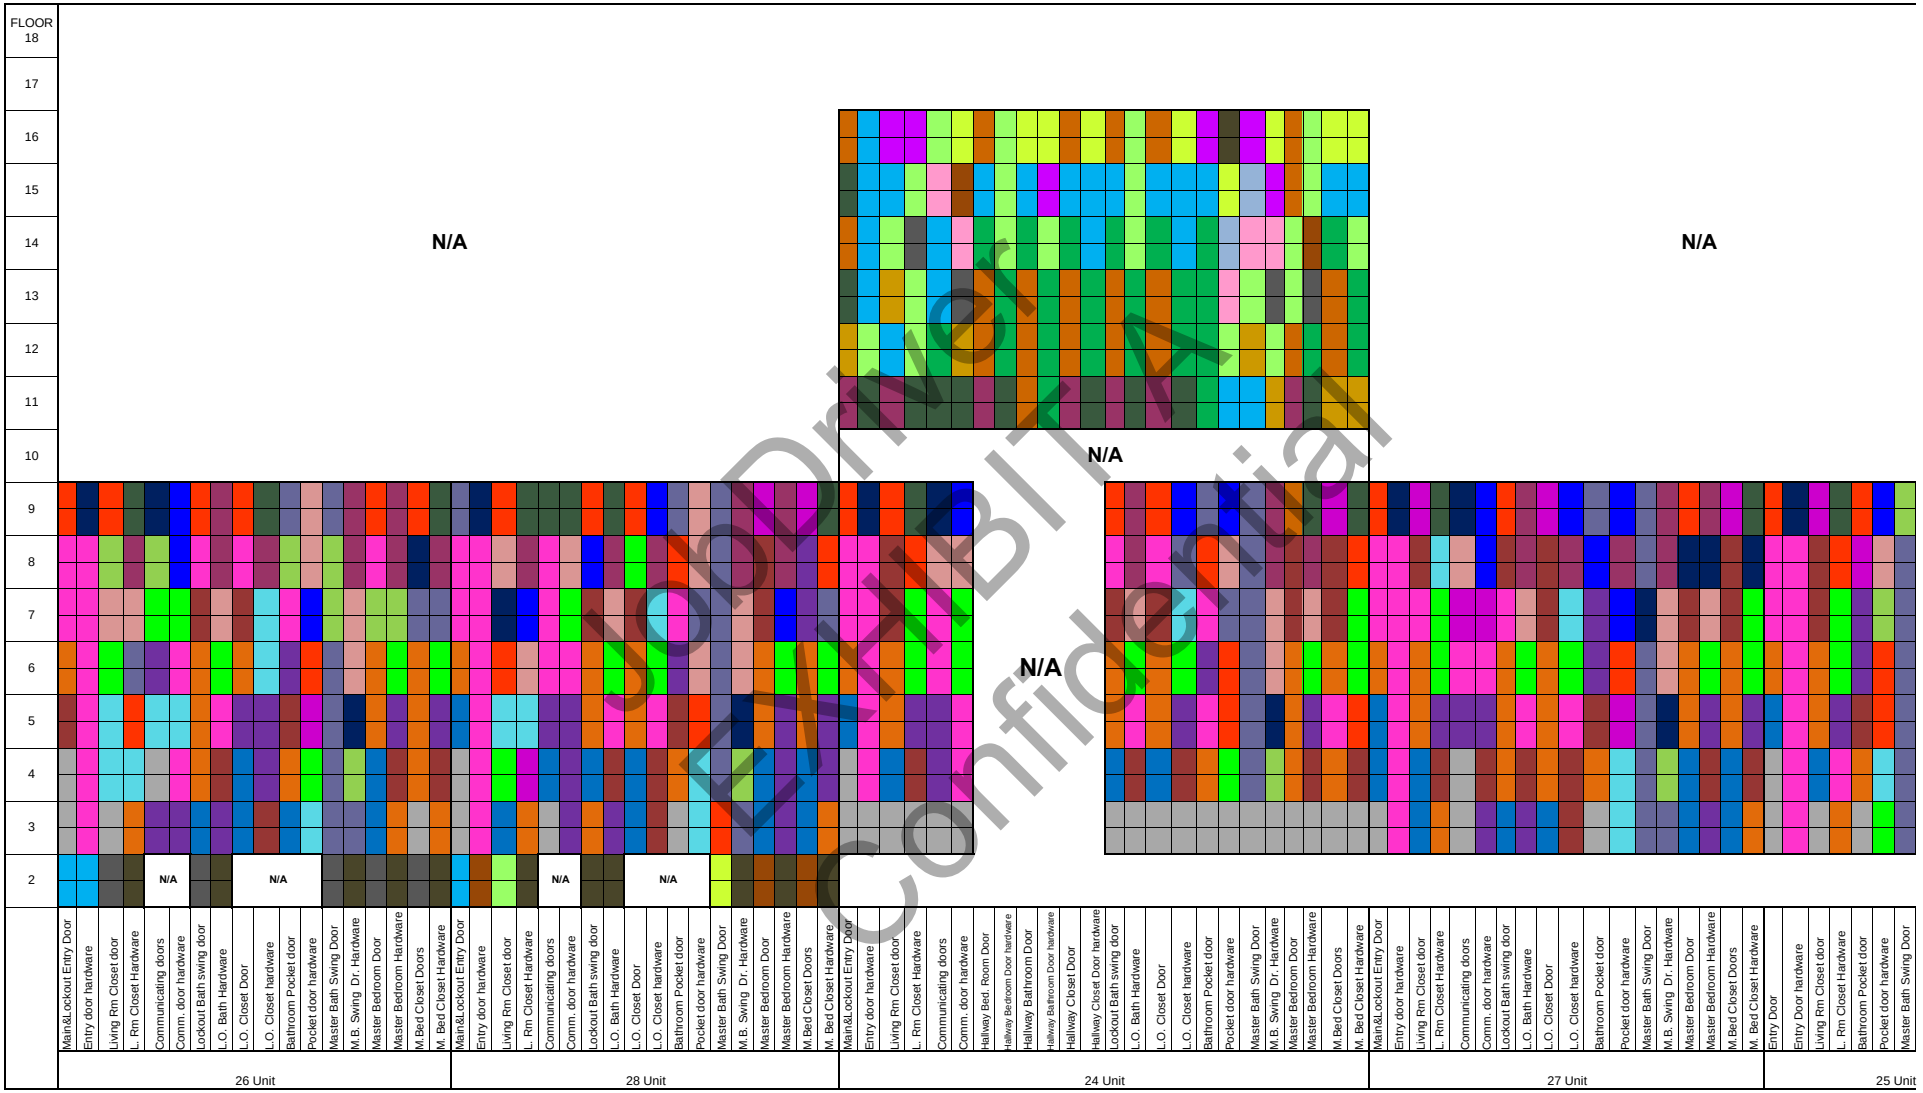

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

Pleasants Hardware

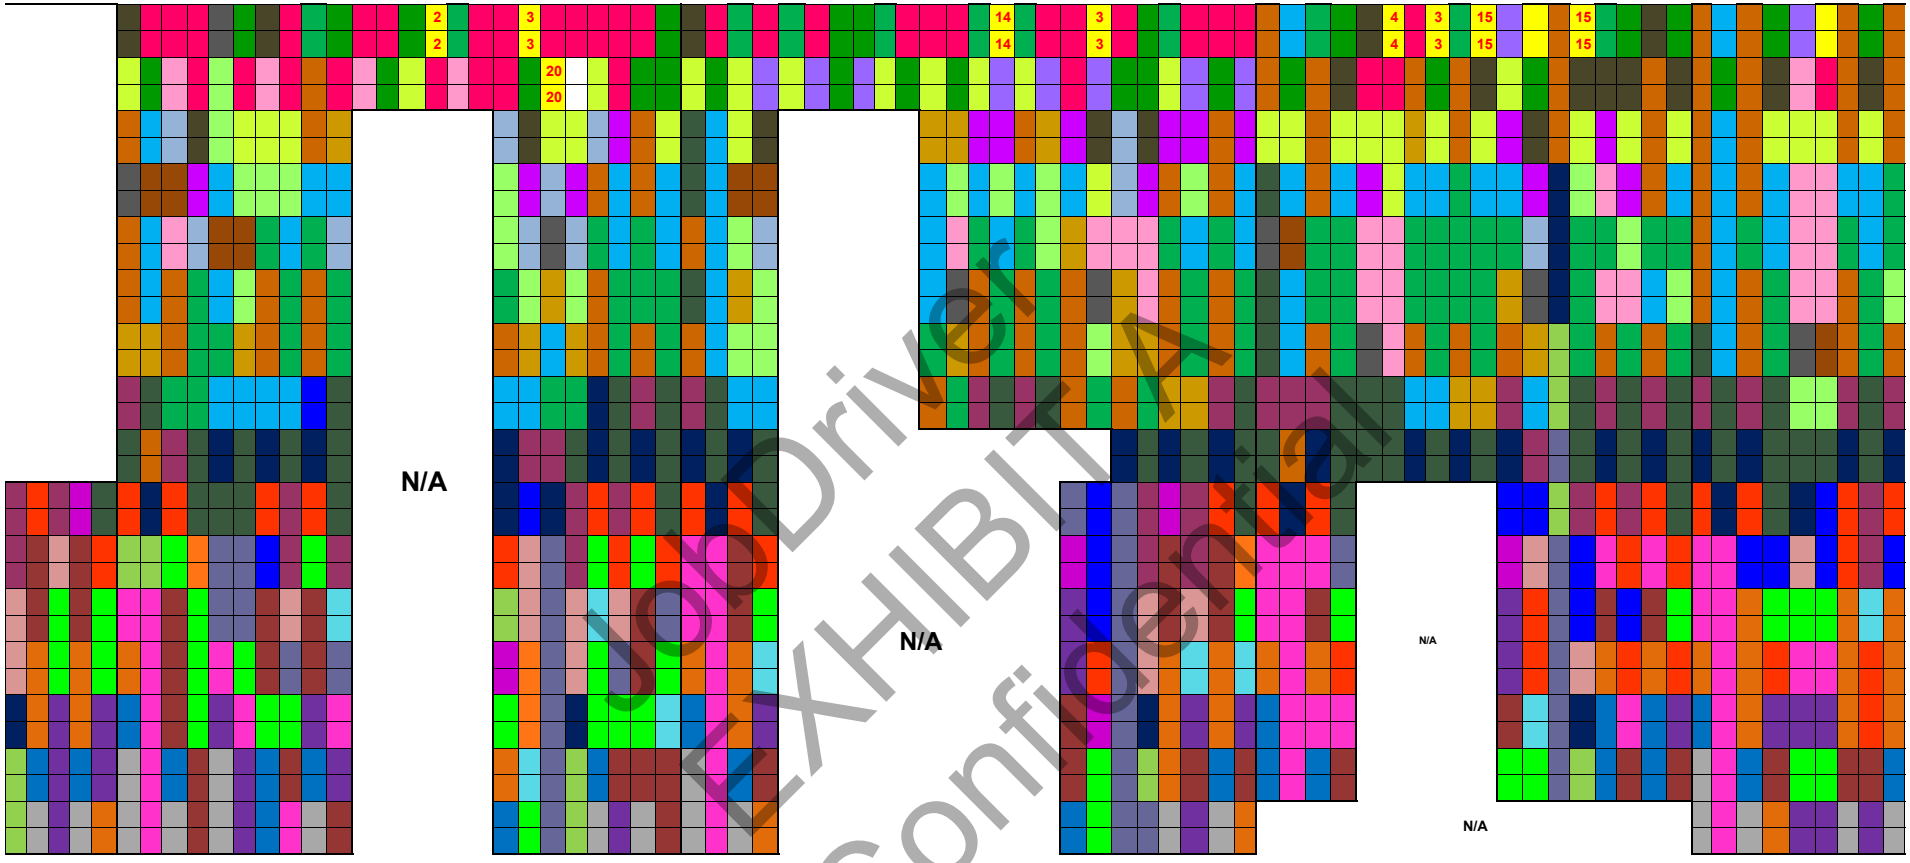

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door |
|---|---|---

Pleasants Hardware



Unit	
	L.O. Closet Hareware
	Bathroom Pocket door
	Pocket door hardware
	Master Bath Swing Door
	M.B. Swing Dr. Hardware
	Master Bedroom Door
	Master Bedroom Hardware
	M.Bed Closet Doors
	M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

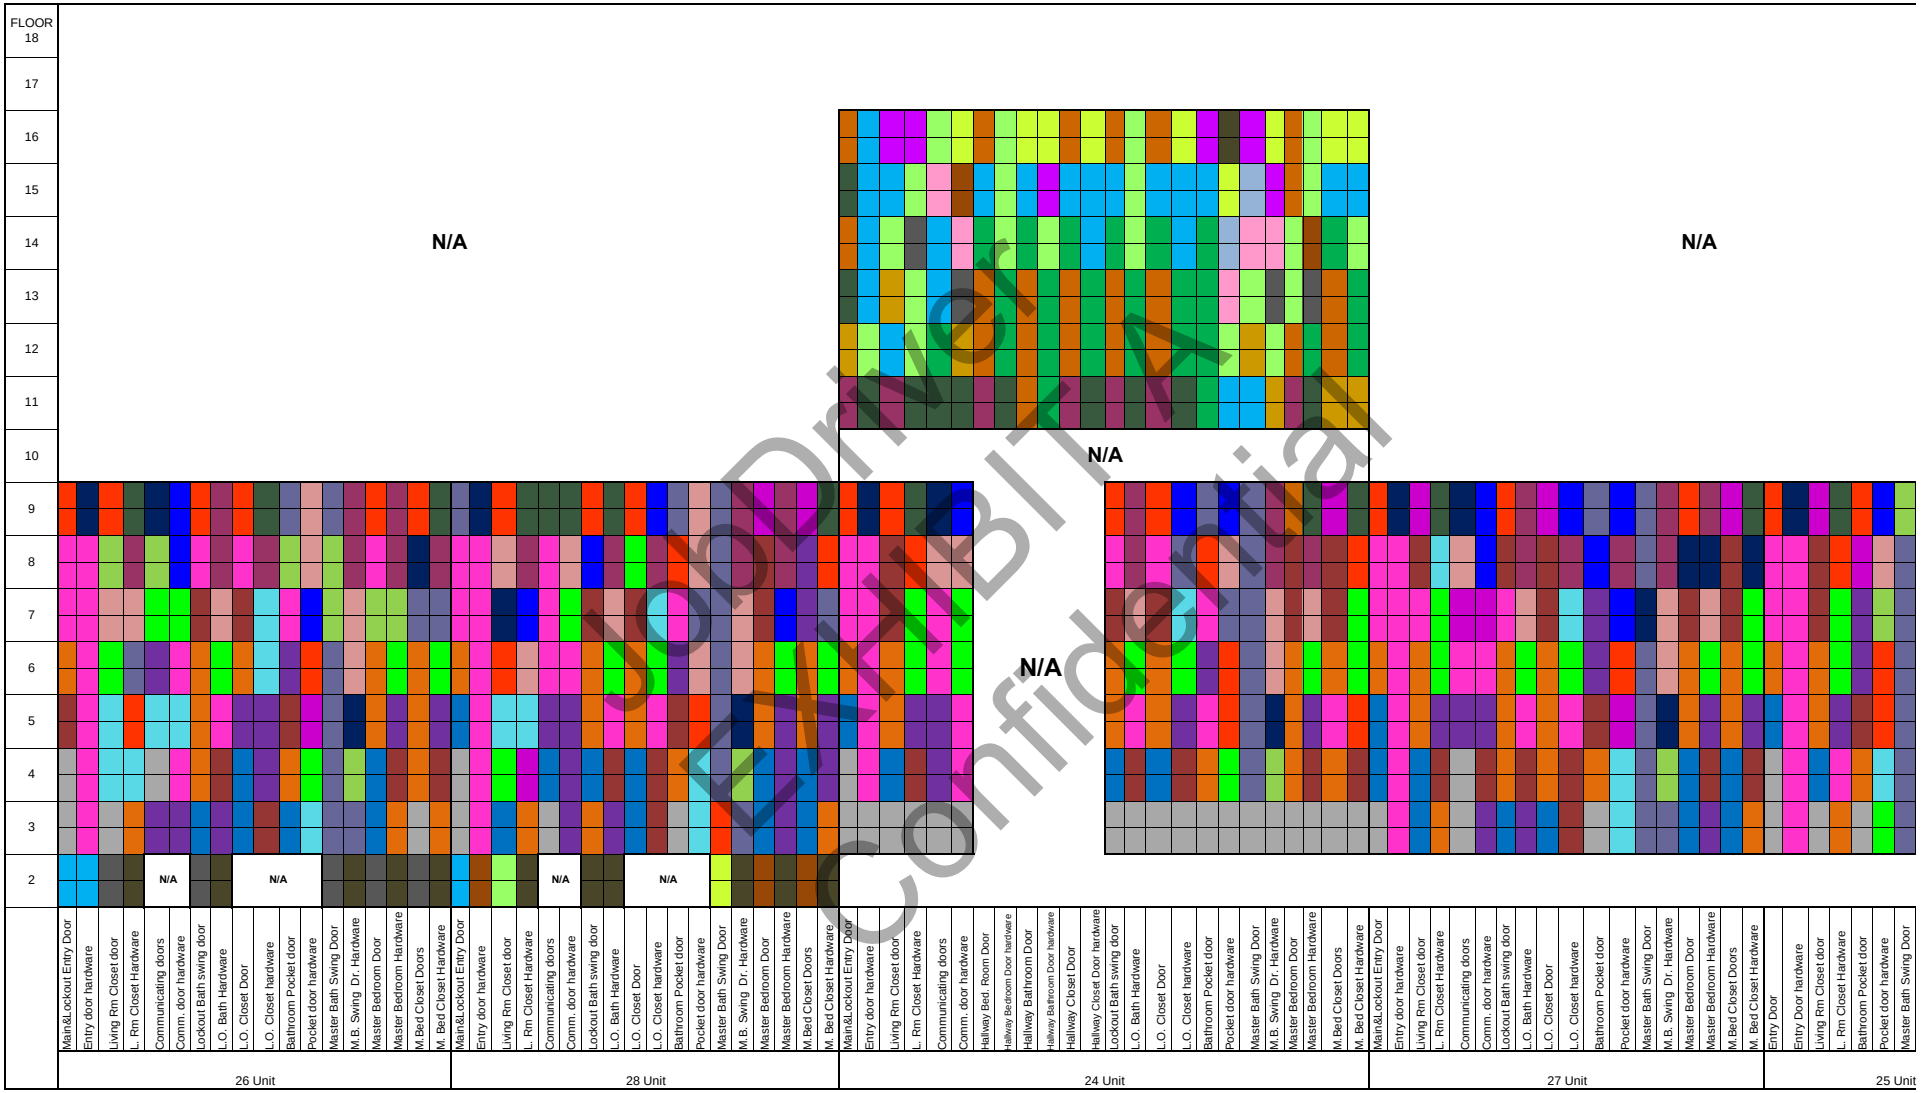

JobDriver Exhibit A Confidential

PLEASEANT HARDWARE PROGRESS CHART

RUN DATE : 2/8/2012

- WORK COMPLETE TO DATE 1/27/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

All master bedroom swing doors are being re-worked to accommodate new doors.

- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETED TO DATE 328.2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/6/2012
- WORK COMPLETED TO DATE 6/13/2012
- WORK COMPLETED TO DATE 6/20/2012
- WORK COMPLETED TO DATE 6/27/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/11/2012

INCOMPLETE ITEMS

- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

Pleasants Hardware

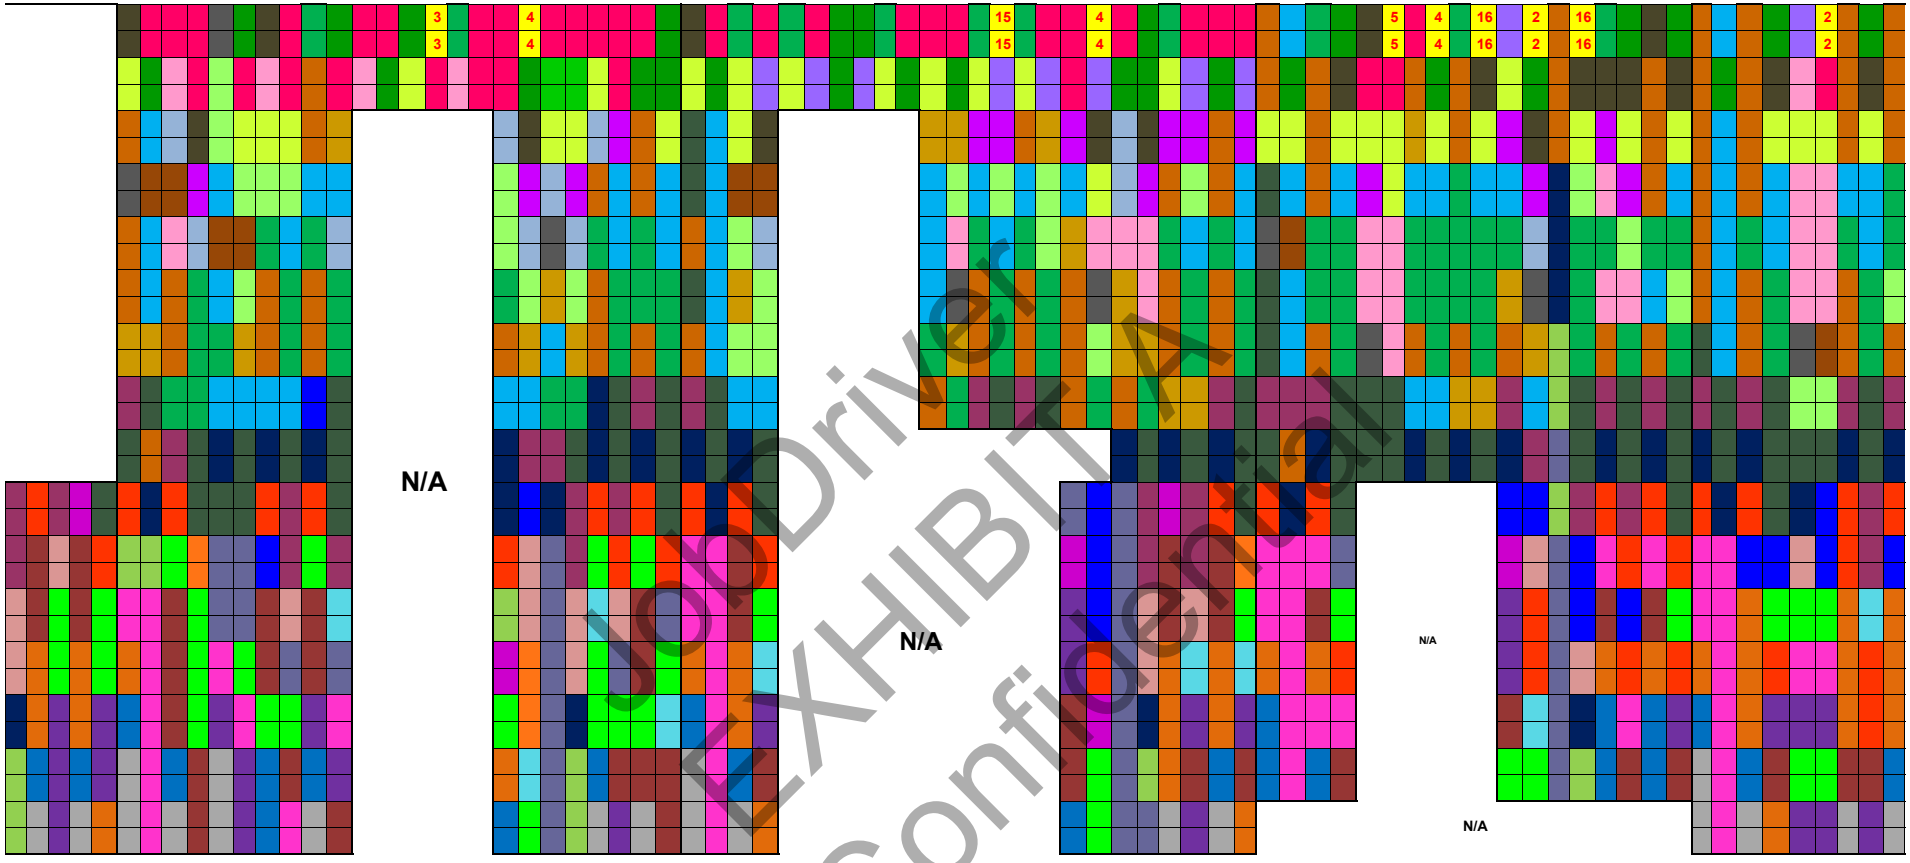

JobDriver
EXHIBIT A
Confidential

| M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main&Lockout Entry Door | Entry door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating doors | Comm. door hardware | Lockout Bath swing door | L.O. Bath Hardware | L.O. Closet Door | L.O. Closet hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Hallway Bed. Room door | Hallway Bed. Room door hardware | Hallway Bathroom door | Hallway Bath. Room door hardware | Hallway Closet Door | Hallway Closet Door hardware | Communicating Door | Communicating Door hardware | L.O. Bathroom Swing Door | L.O. Bathroom Door hardware | Lockout Closet Door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bathroom Swing Door | Lockout Bath. Door hardware | Lockout Closet door | Lockout Closet Door hardware | Bathroom Pocket door | Pocket door hardware | Master Bath Swing Door | M.B. Swing Dr. Hardware | Master Bedroom Door | Master Bedroom Hardware | M.Bed Closet Doors | M. Bed Closet Hardware | Main & Lockout Entry Door | Entry Door hardware | Living Rm Closet door | L. Rm Closet Hardware | Communicating Doors | Comm. Door Hardware | Lockout Bath Swing Door | L.O Bath Hardware | L.O. Closet Door |
|---|---|---

Pleasants Hardware



Unit	
	L.O. Closet Hareware
	Bathroom Pocket door
	Pocket door hardware
	Master Bath Swing Door
	M.B. Swing Dr. Hardware
	Master Bedroom Door
	Master Bedroom Hardware
	M.Bed Closet Doors
	M. Bed Closet Hardware

JobDriver
EXHIBIT A
Confidential

Proxemic Nonlexus

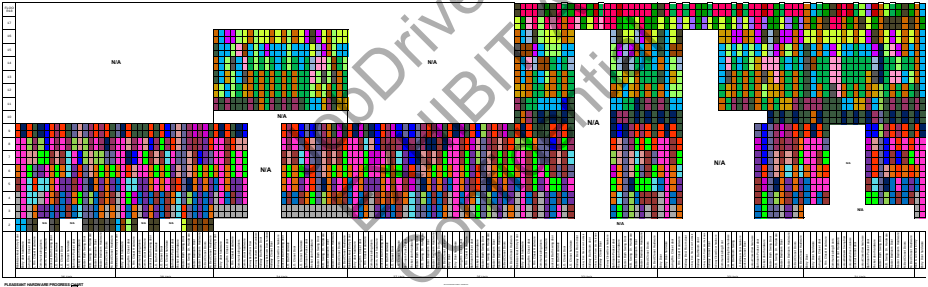
N/A
N/A
N/A



JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

FLOOR										
18										
17										
16										
15										
14	**N/A**									
13										
12										
11										
10										
9										
8										
7										
6										
5										
4										
3										**N/A**
2			**N/A**							
	FOYER TILE	KITCHEN TILE	LOCKOUT BATH SHOWER	LOCKOUT BATH FLOOR	LOCKOUT BATH BASE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3	
	26 Unit									
	FOYER TILE	KITCHEN TILE	LOCKOUT BATH SHOWER	LOCKOUT BATH FLOOR	LOCKOUT BATH BASE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3	
	28 Unit									
	FOYER TILE	KITCHEN TILE	LOCKOUT BATH SHOWER	LOCKOUT BATH FLOOR	LOCKOUT BATH BASE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3	
	24 Unit									
	FOYER TILE	KITCHEN TILE	LOCKOUT BATH SHOWER	LOCKOUT BATH FLOOR	LOCKOUT BATH BASE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3	
	27 Unit									
	FOYER TILE	KITCHEN TILE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3				
	25 Unit									
	FOYER TILE	KITCHEN TILE	LOCKOUT BATH SHOWER	LOCKOUT BATH FLOOR	LOCKOUT BATH BASE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3	
	22 Unit									
	FOYER TILE	KITCHEN TILE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3				
	23 Unit									
	FOYER TILE	KITCHEN TILE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3				
	21 Unit									
	FOYER TILE	KITCHEN TILE	MASTER BATH SHOWER	MASTER BATH FLOOR	MASTER BATH BASE	THRESHOLDS X 3				
	20 Unit									

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12

AREAS AVAILABLE FOR YOU TO WORK

* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

POMPEI TILE PROGRESS CHART

| FLOOR | FOYER TILE | KITCHEN TILE | LOCKOUT BATH SHOWER | LOCKOUT BATH FLOOR | LOCKOUT BATH BASE | MASTER BATH SHOWER | MASTER BATH FLOOR | MASTER BATH BASE | THRESHOLDS X 6

POMPEI TILE PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- MASTER BATHROOM IN UNITS 1124 AND 1224 ARE BEING REWORKED. UNIT 1023 BATHROOM BEING REWORKED. 14TH FLOOR NOT READY FOR TILE INSTALLATION. MUDDING CEILINGS AND WALLS.

POMPEI TILE PROGRESS CHART

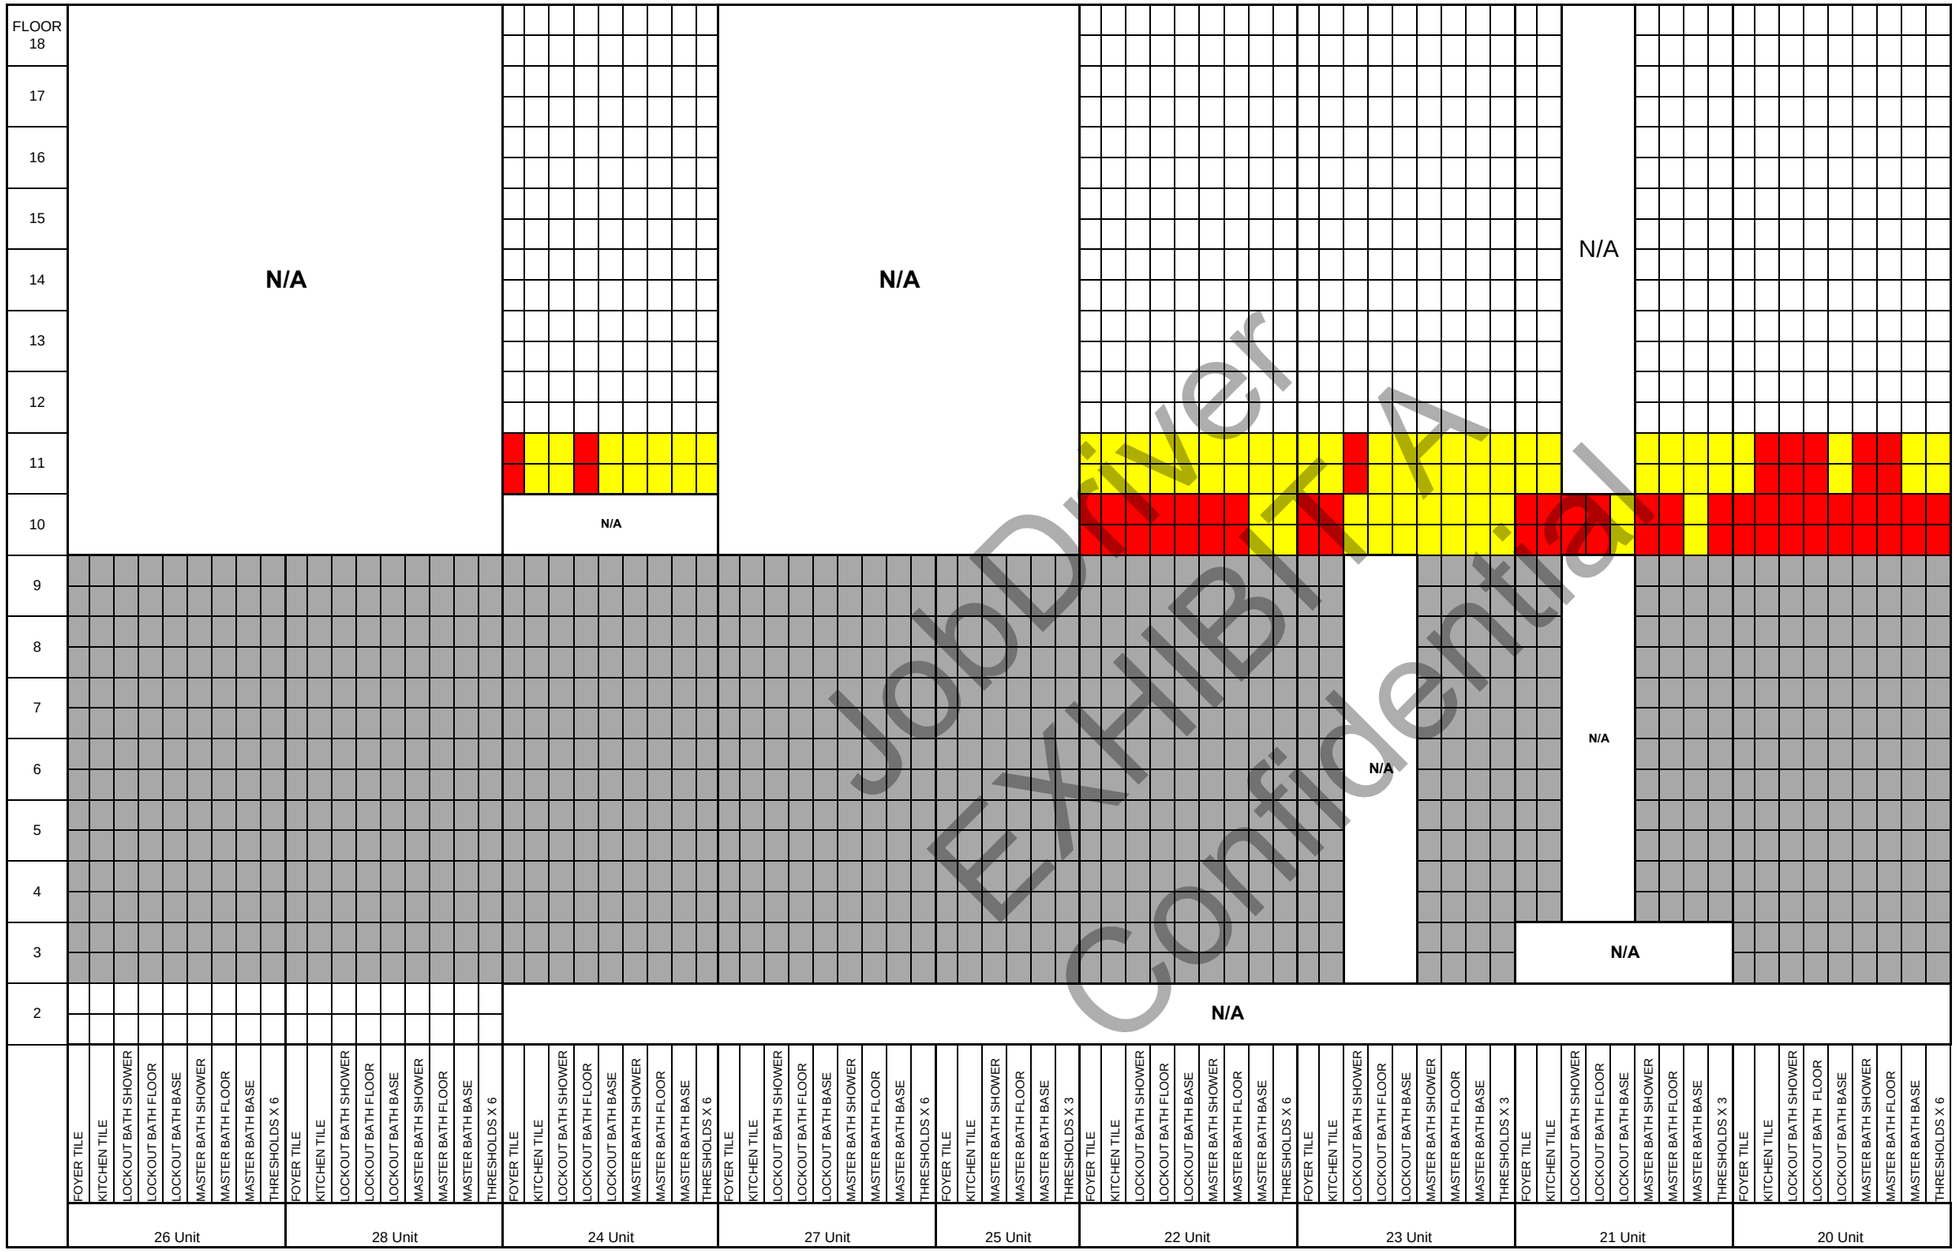

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12
AREAS AVAILABLE FOR YOU TO WORK
AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
WORK COMPLETED TO DATE 2/3/2012

POMPEI TILE PROGRESS CHART

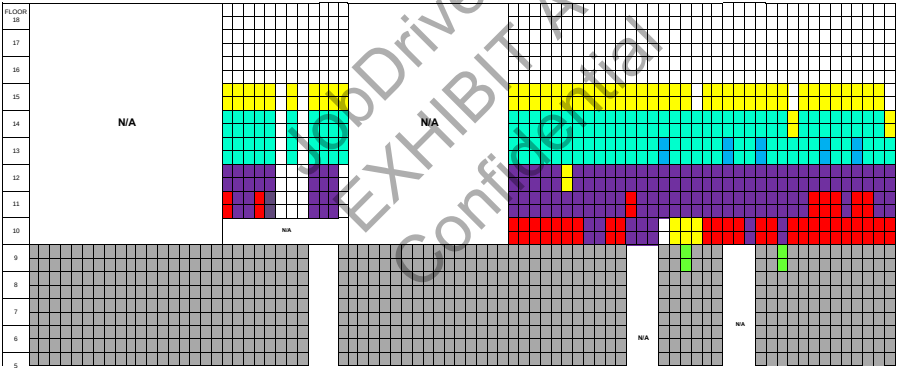

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART



POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 8th floors

EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 8th floors

POMPEI TILE PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 8th floors

POMPEI TILE PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012

Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 8th floors

POMPEI TILE PROGRESS CHART

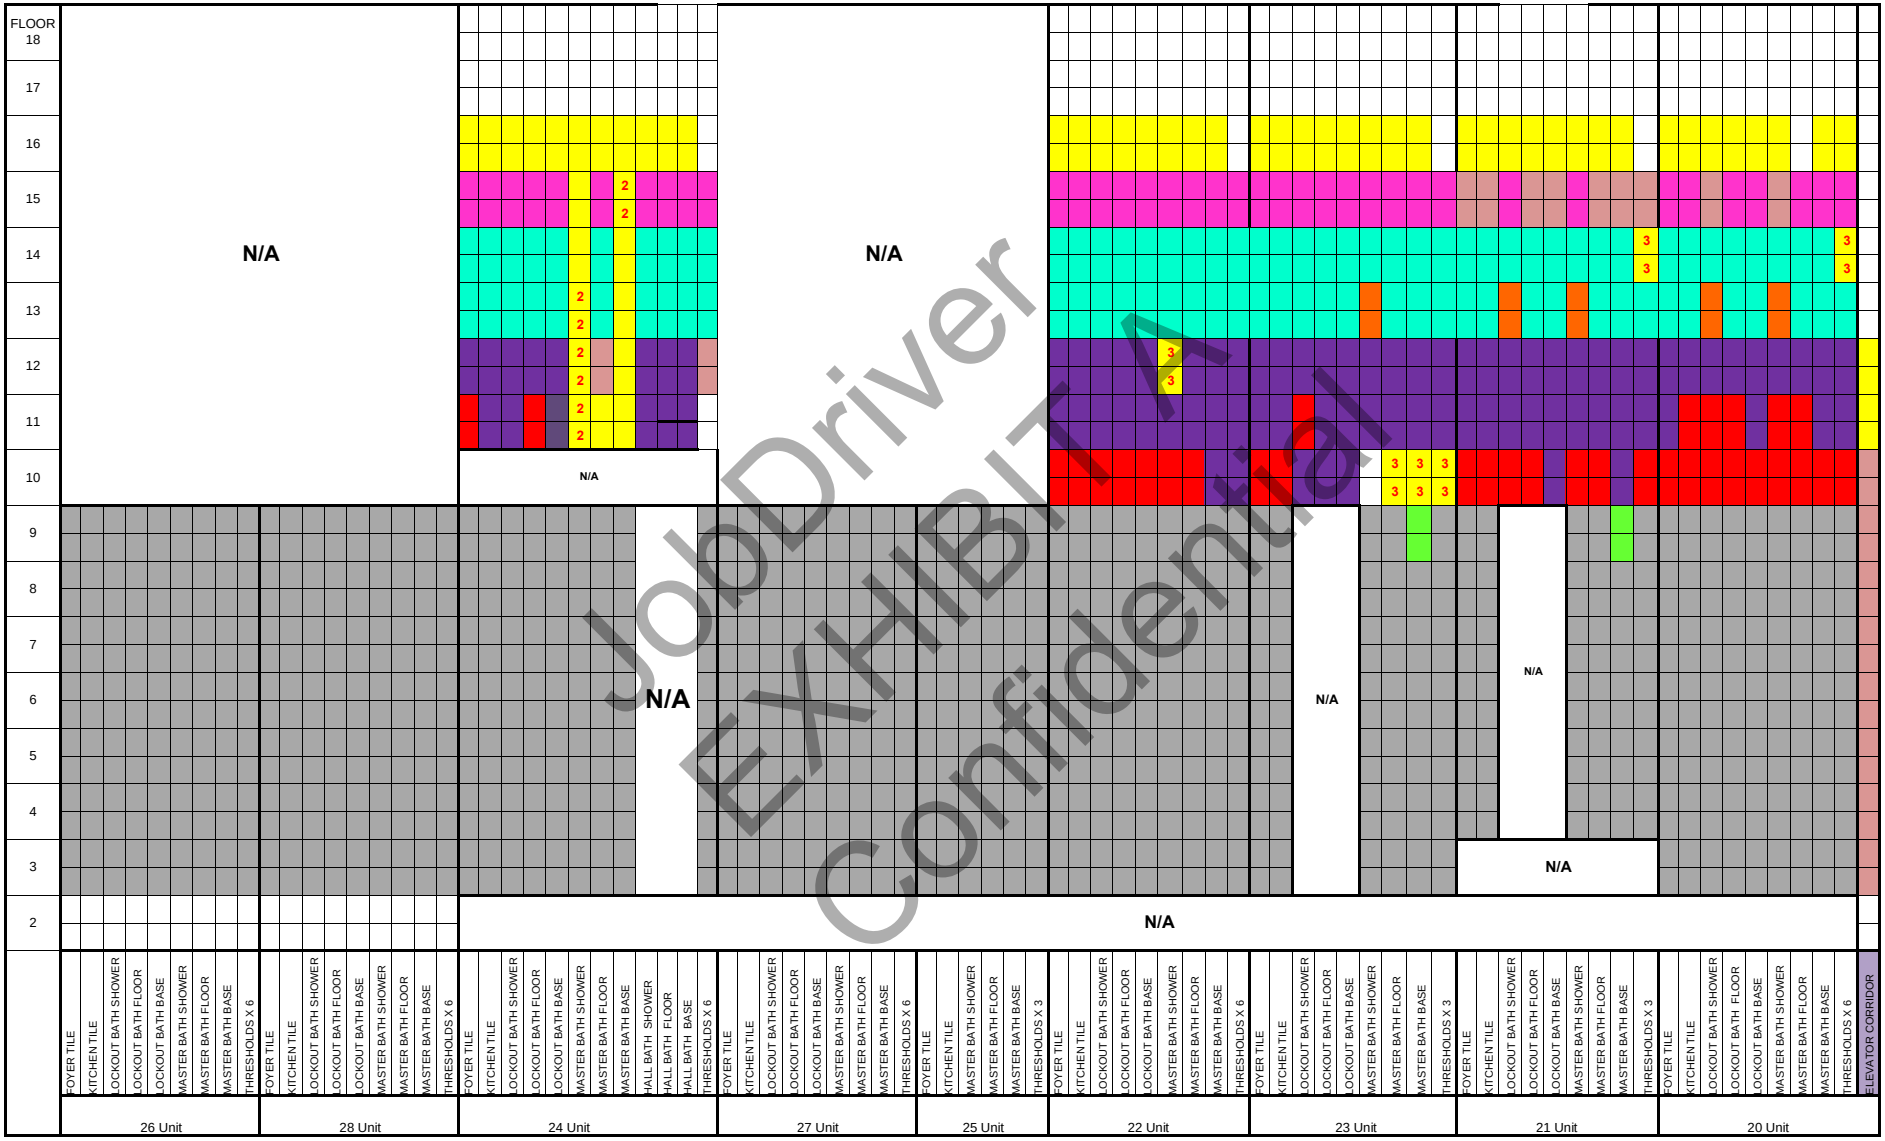

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 8th floors
- WORK COMPLETED TO DATE 3-30-2012

POMPEI TILE PROGRESS CHART

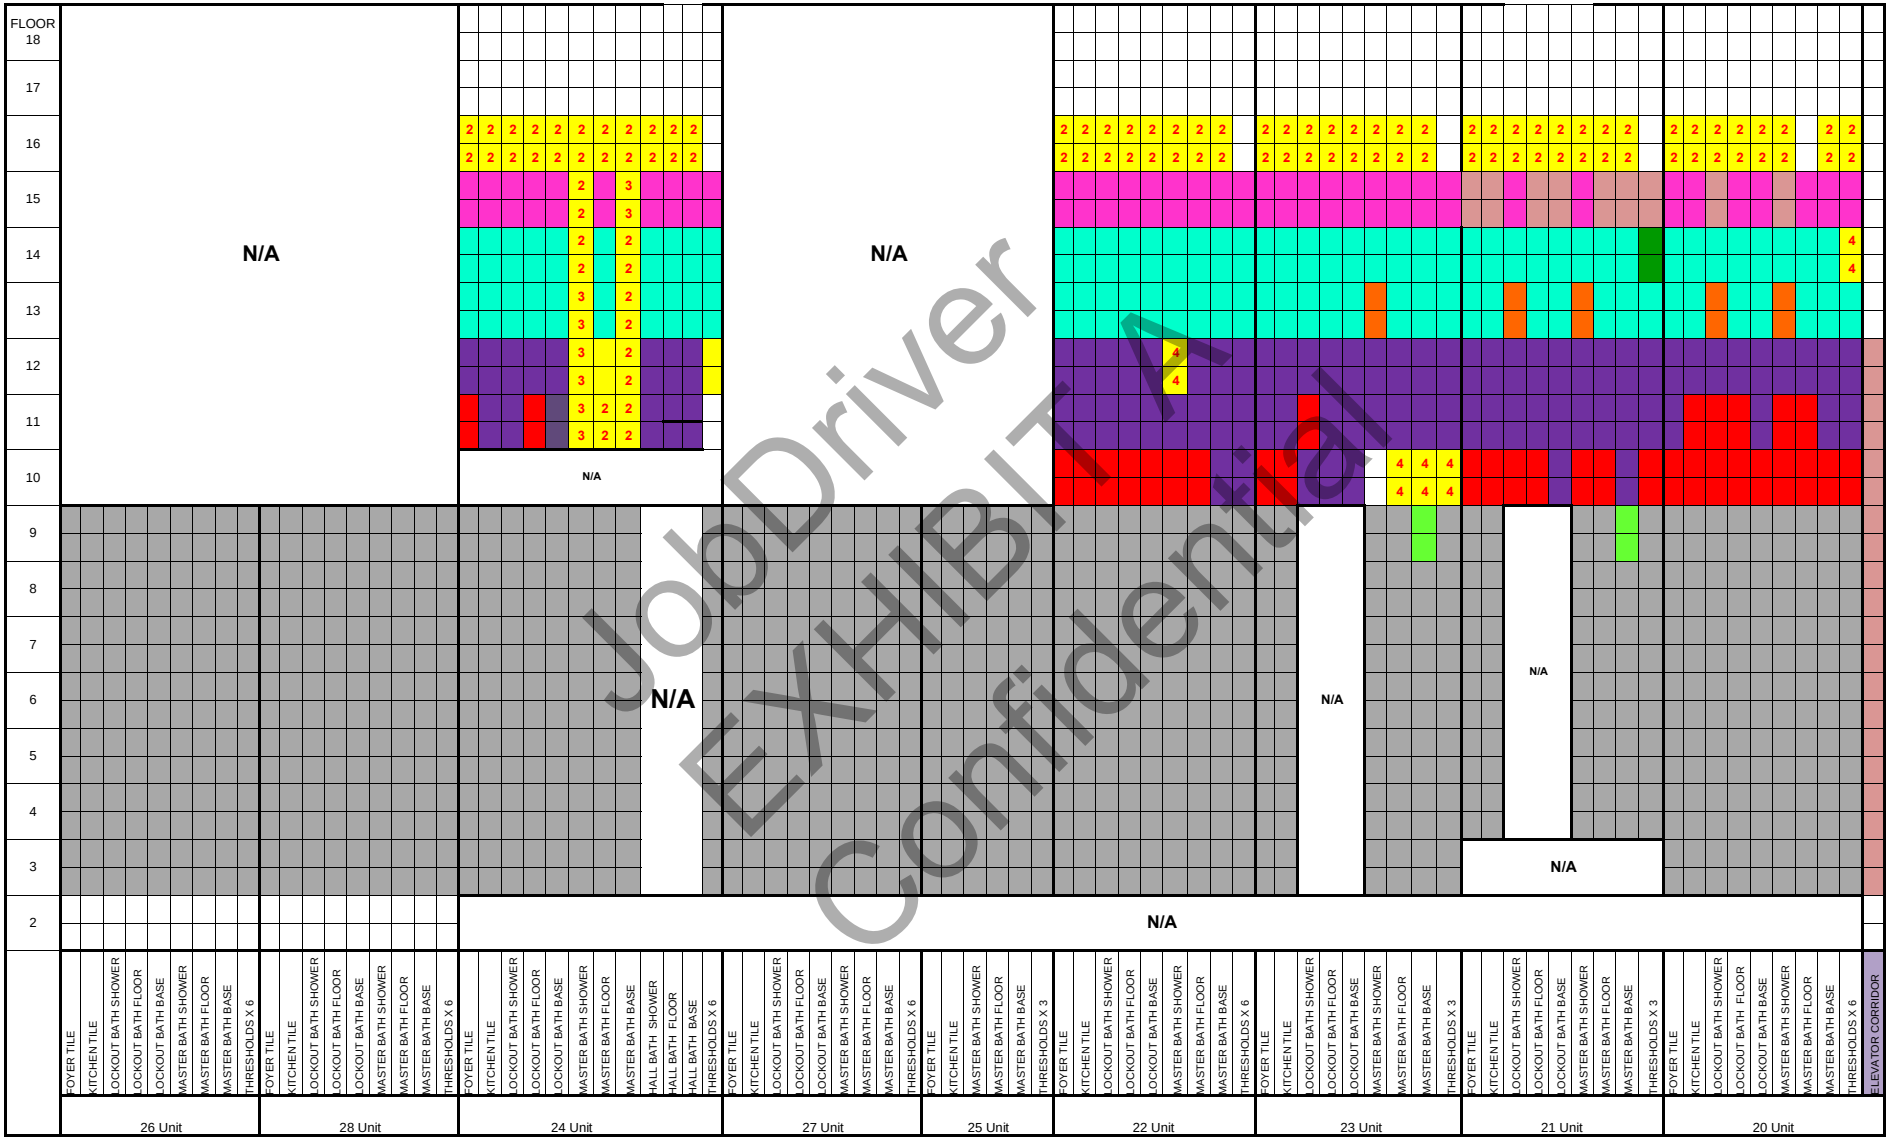

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 9th floors
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012

POMPEI TILE PROGRESS CHART

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 9th floors
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012

POMPEI TILE PROGRESS CHART

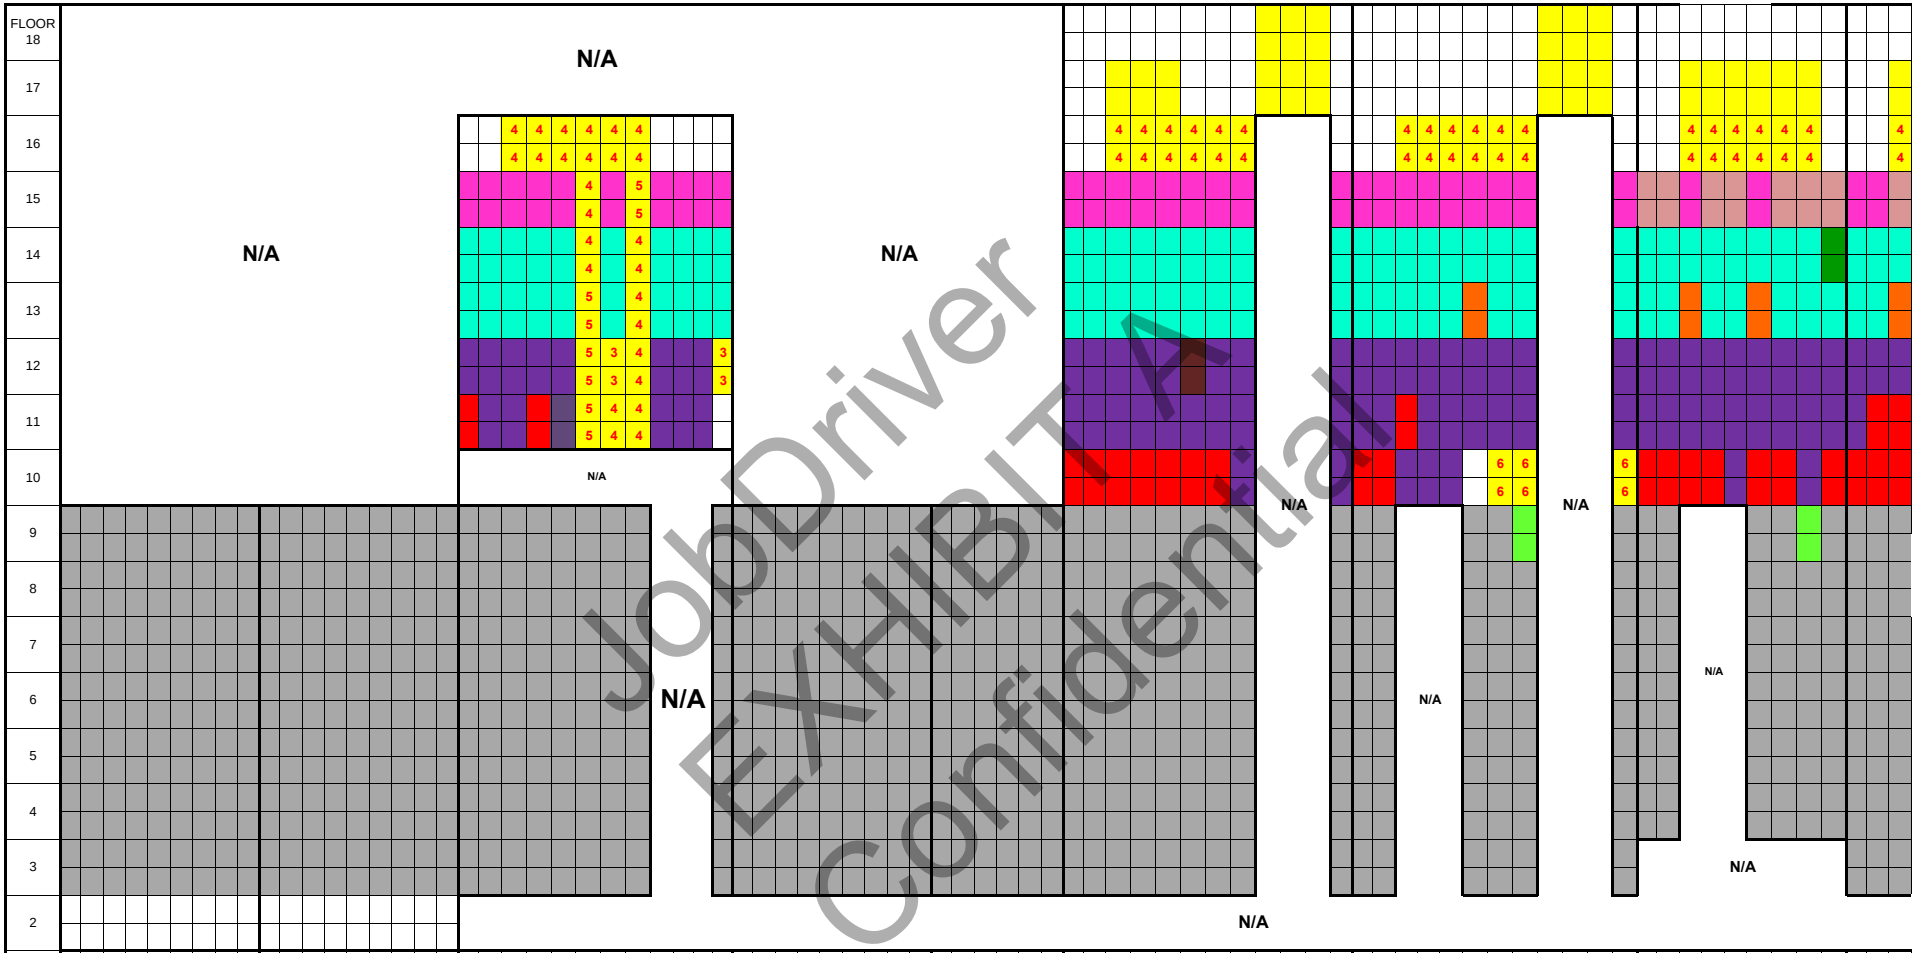

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- Tile required at door jams that are installed in all units in bathrooms from the 3rd through the 9th floors
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012

POMPEI TILE PROGRESS CHART



JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

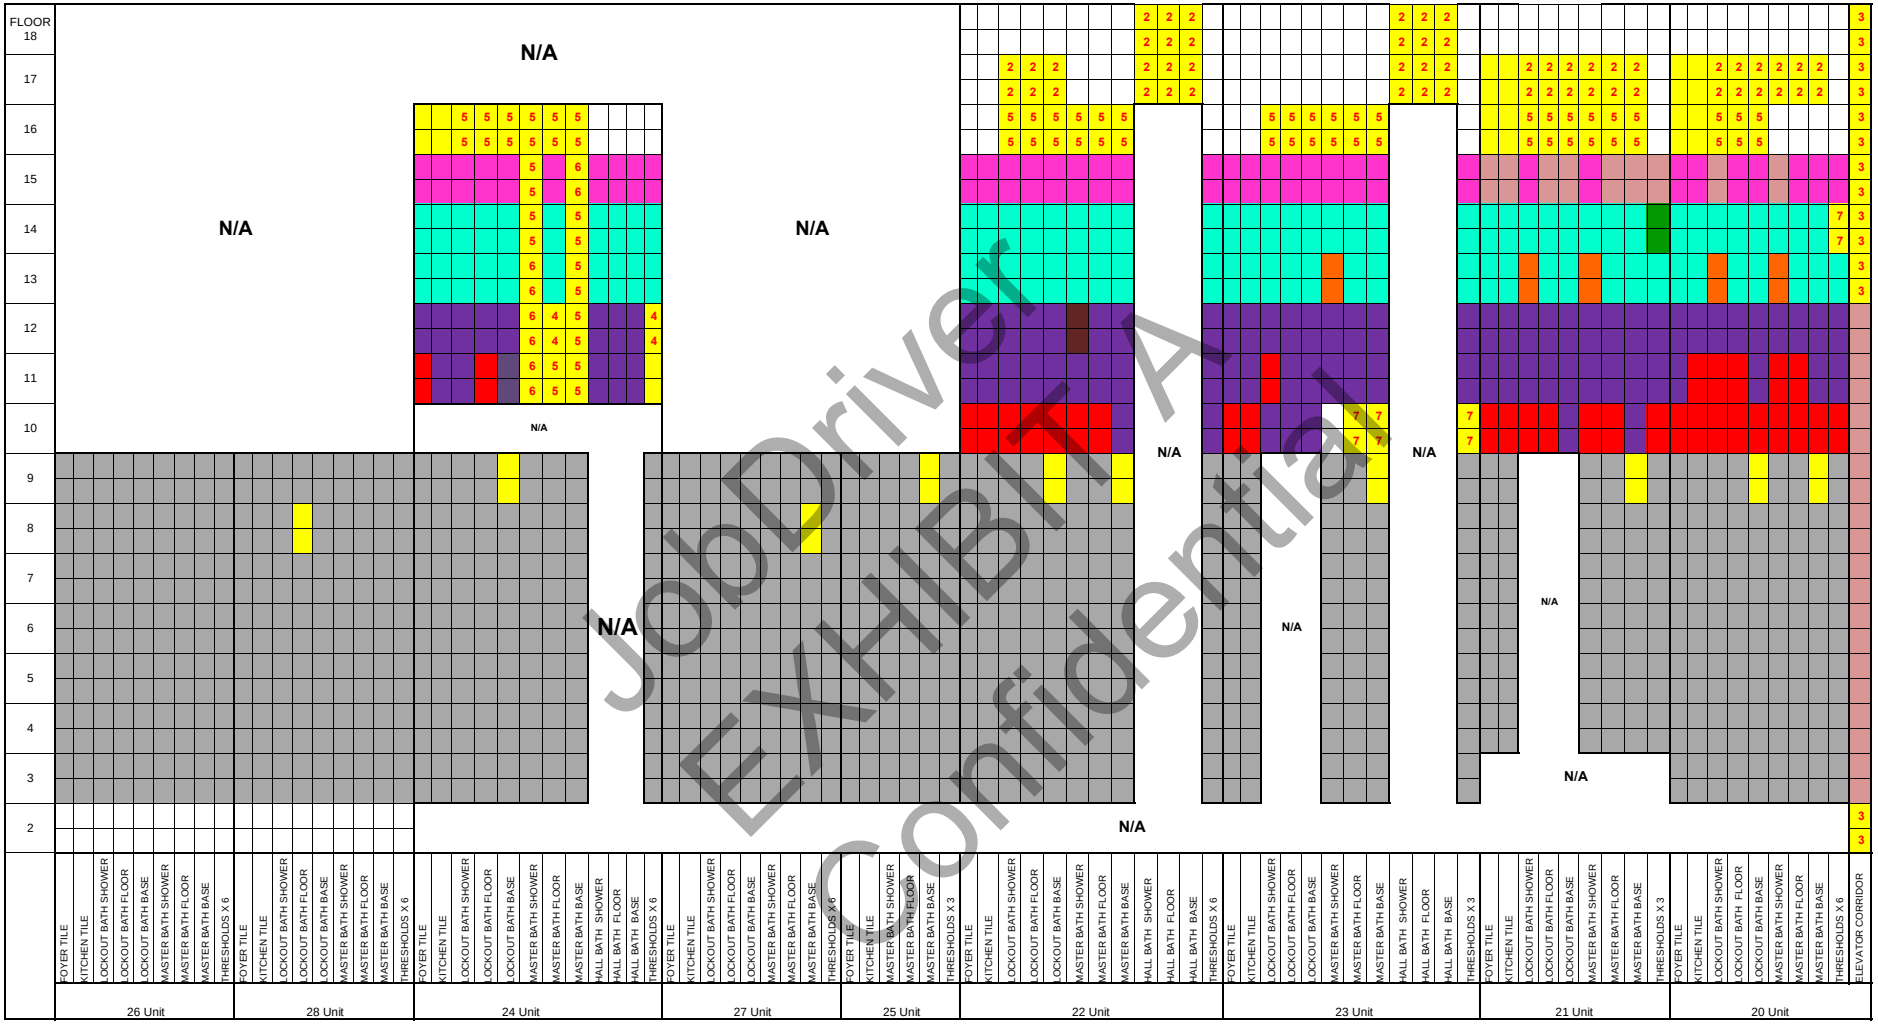

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012

POMPEI TILE PROGRESS CHART

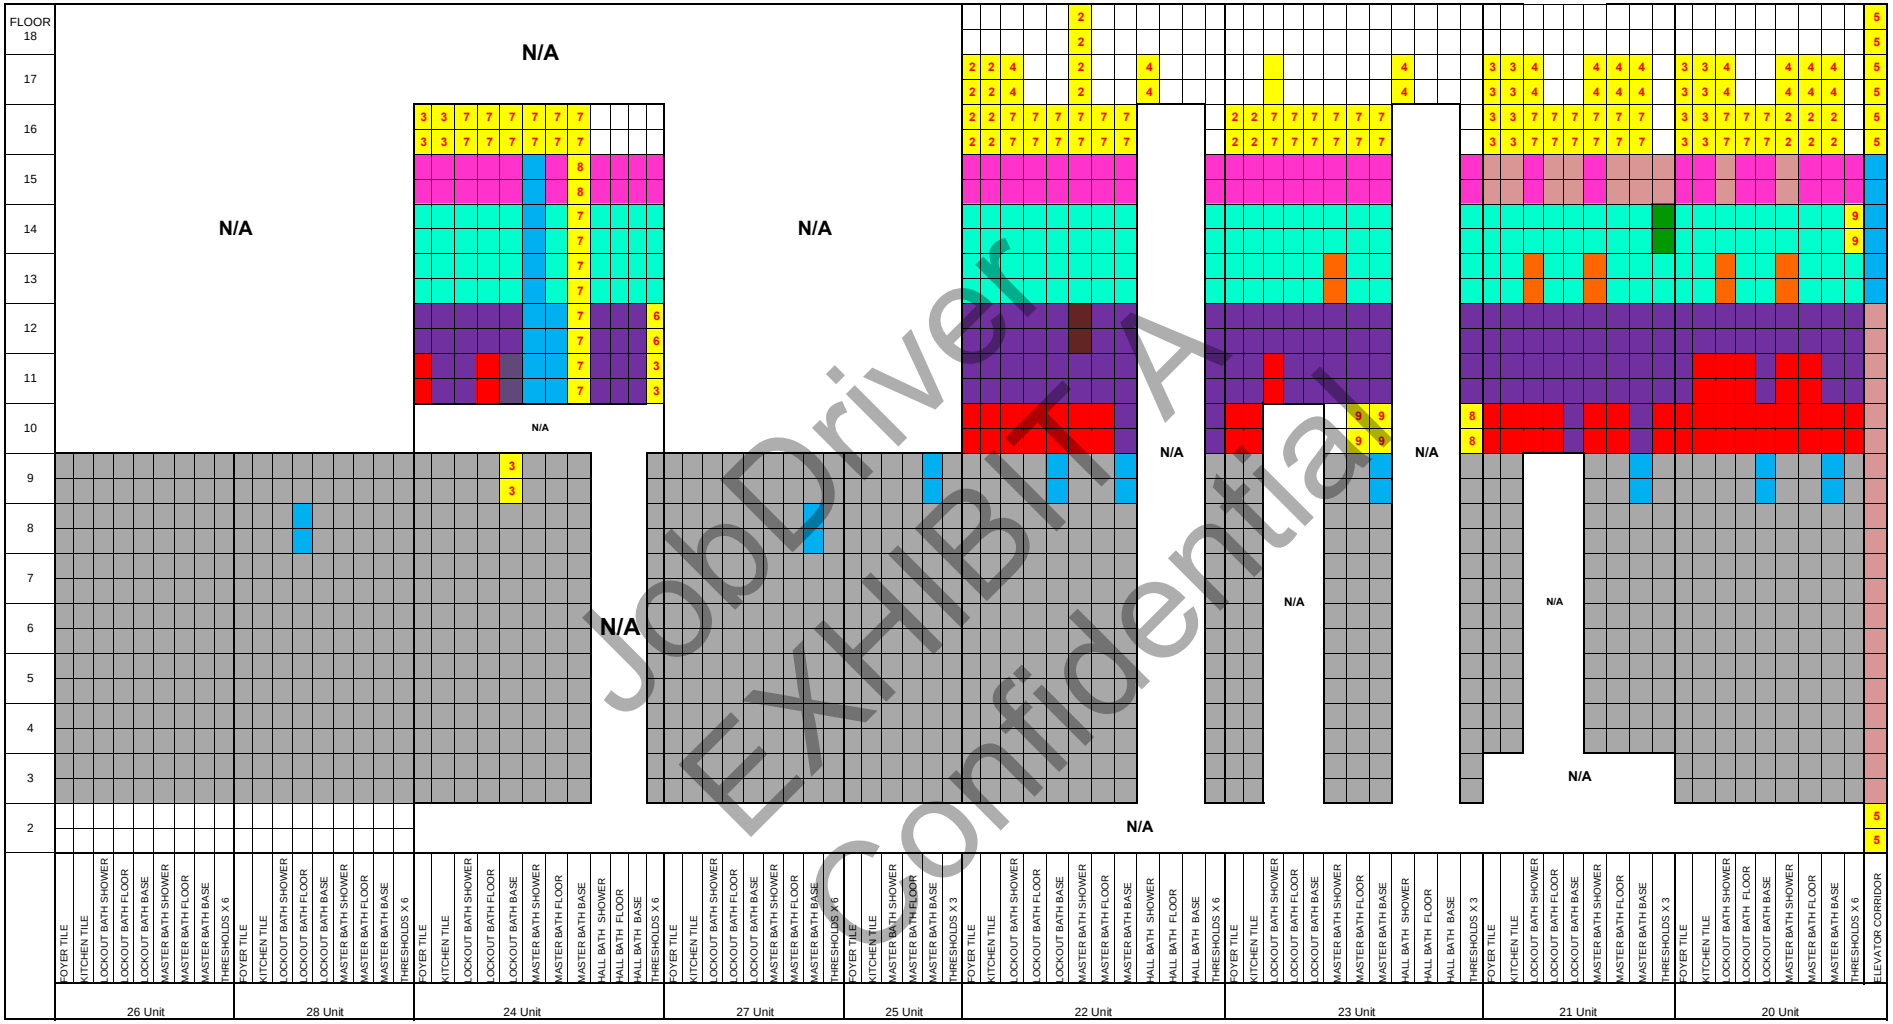

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK

POMPEI TILE PROGRESS CHART

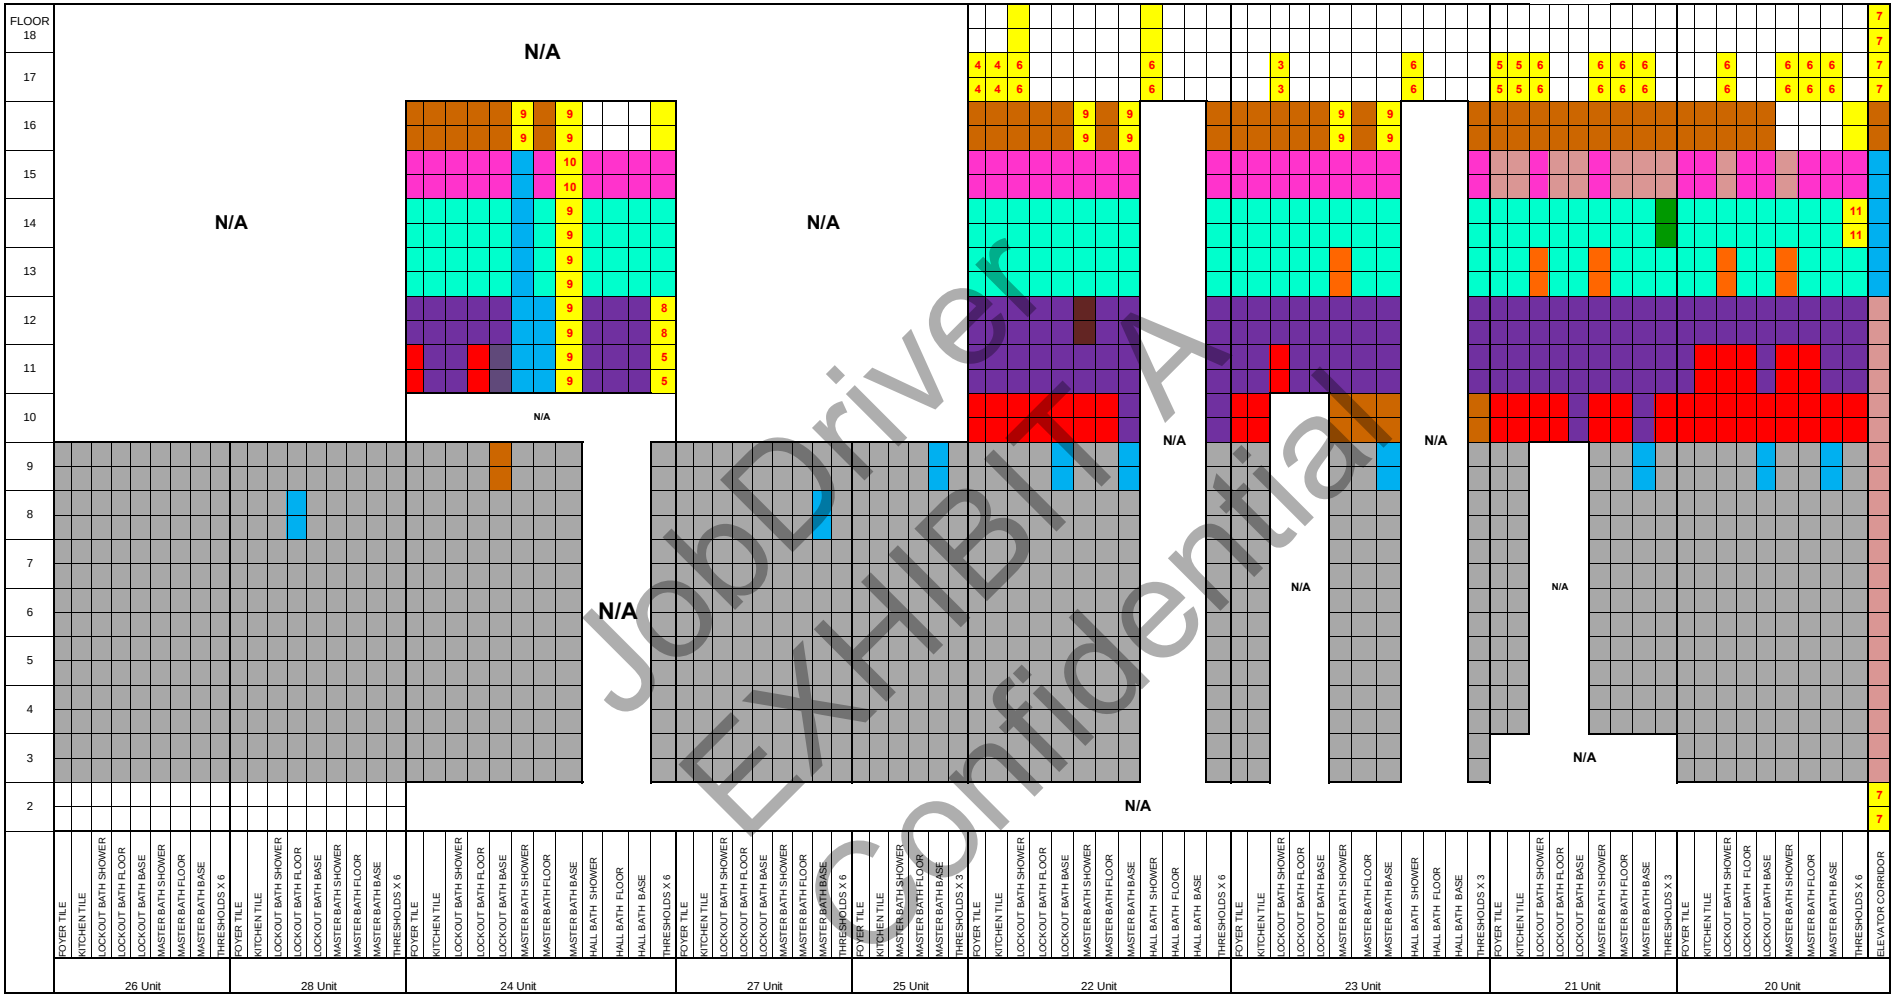

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012

POMPEI TILE PROGRESS CHART

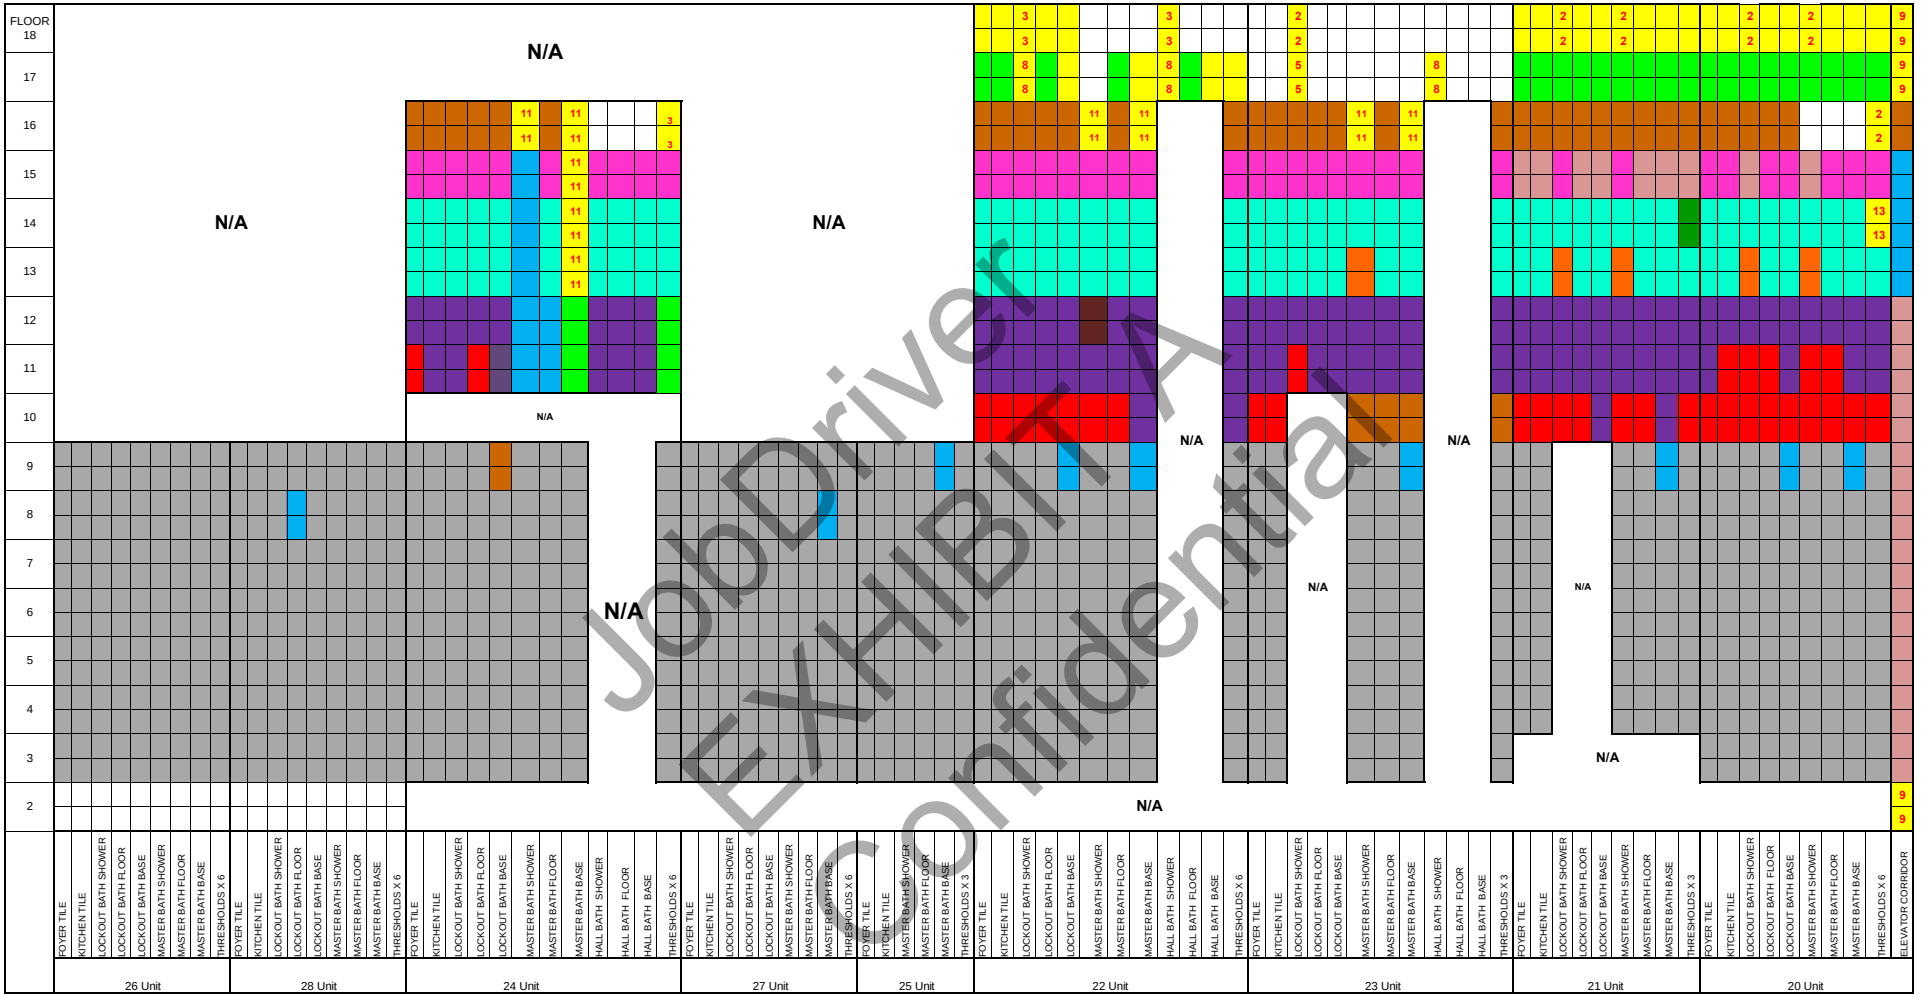

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2012
- Working on floors with no completion 6/8/2012

POMPEI TILE PROGRESS CHART

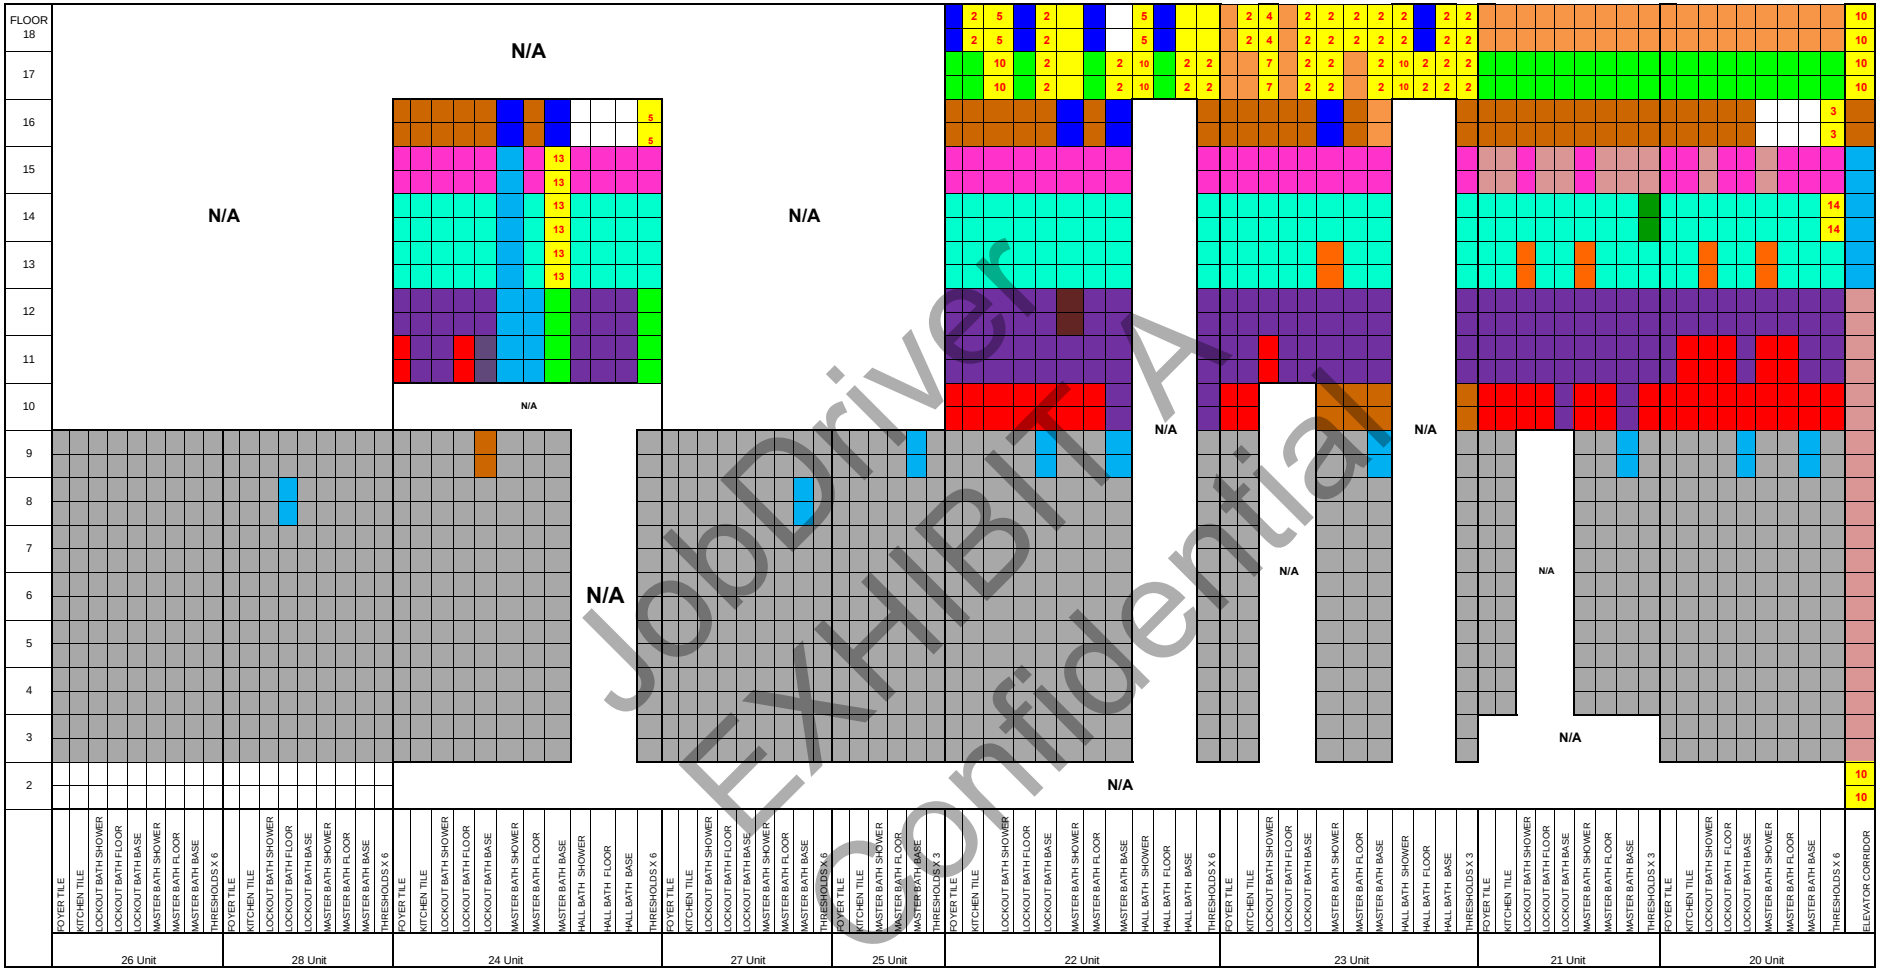

Job Driver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2012
- Working on floors with no completion 6/8/2012
- Work Completed To Date 6/14/2012
- WORK COMPLETED TO DATE 6/22/

POMPEI TILE PROGRESS CHART

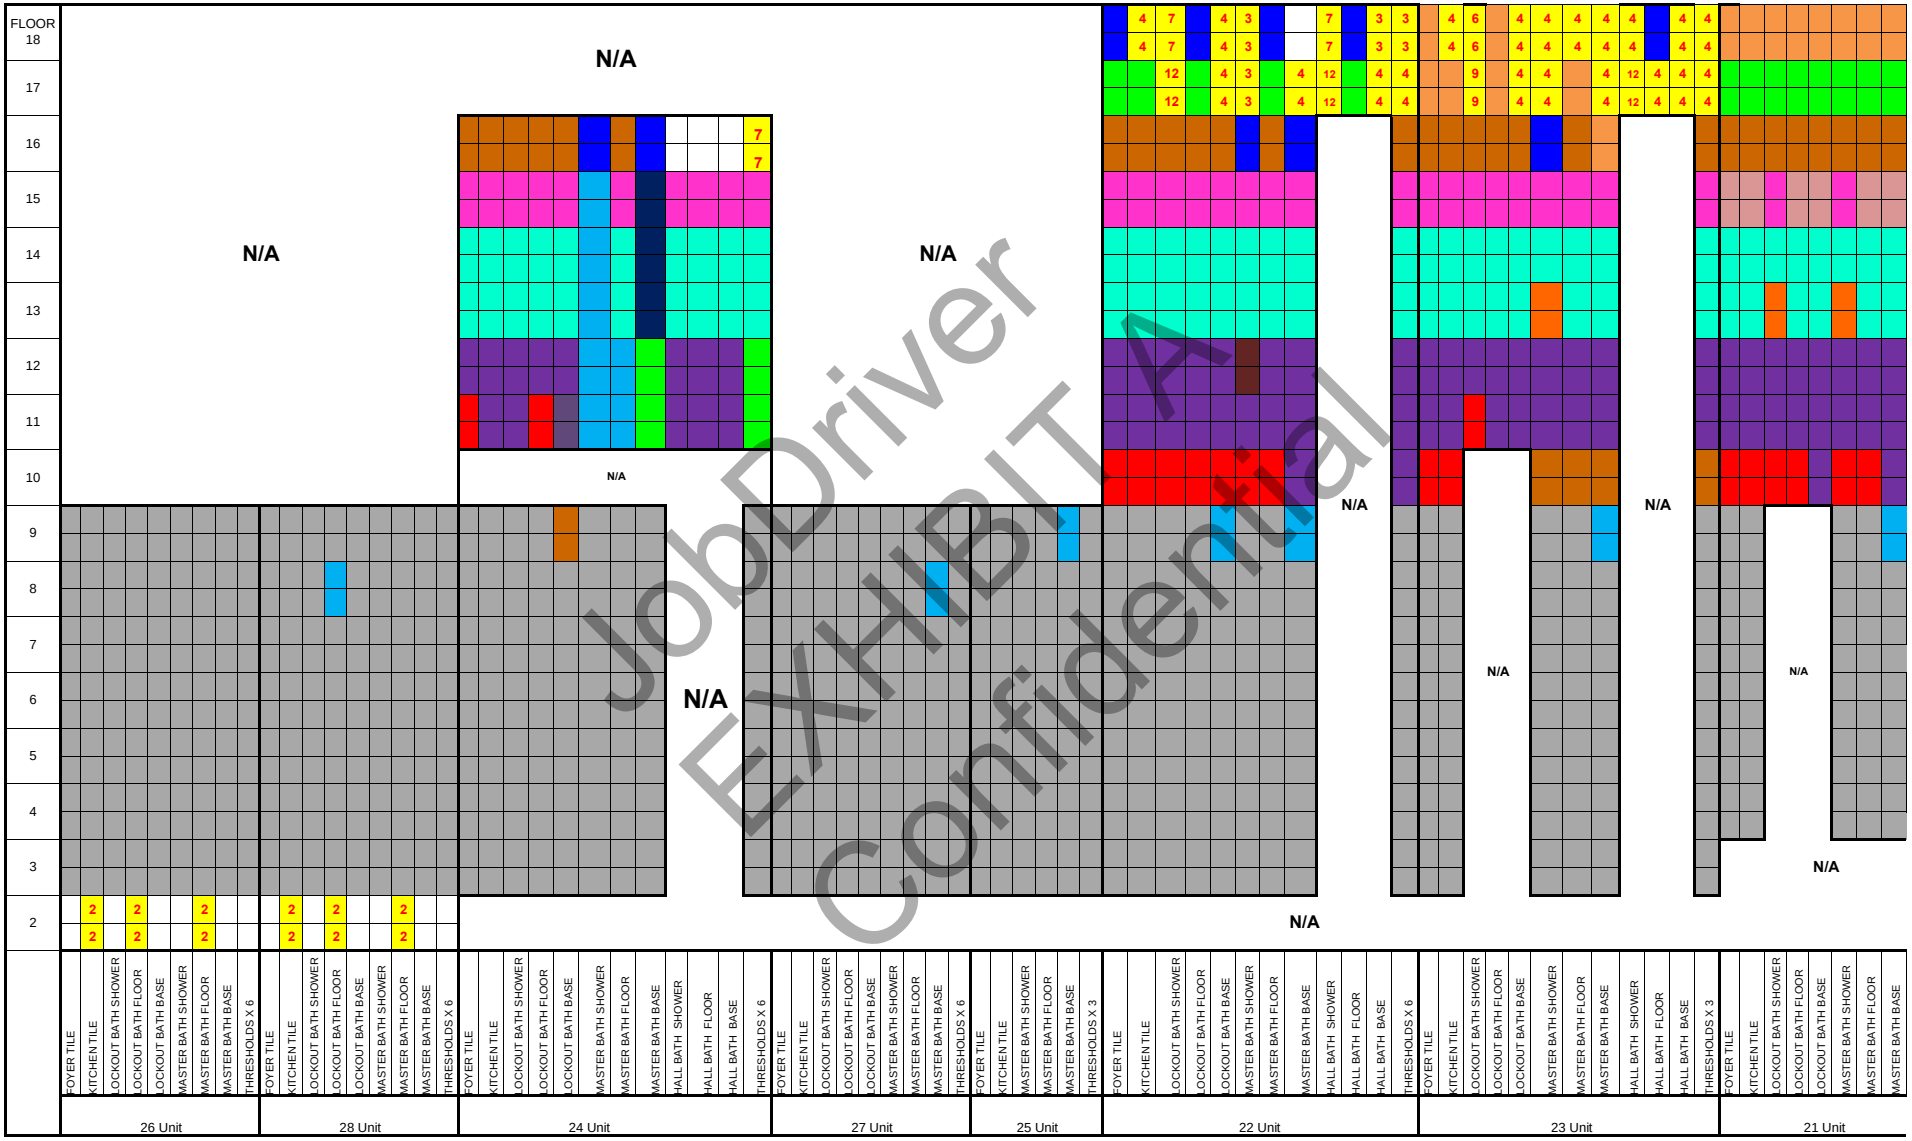

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2
- Working on floors with no completion 6/8/2
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

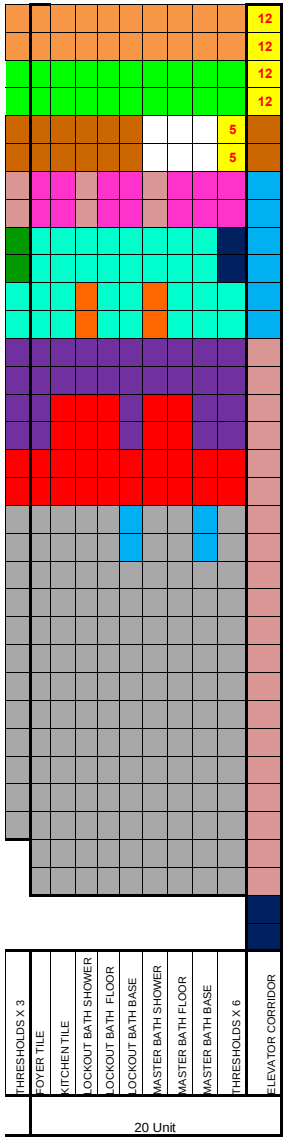

2012 WORK COMPLETED TO DATE 6/22/
2012 WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

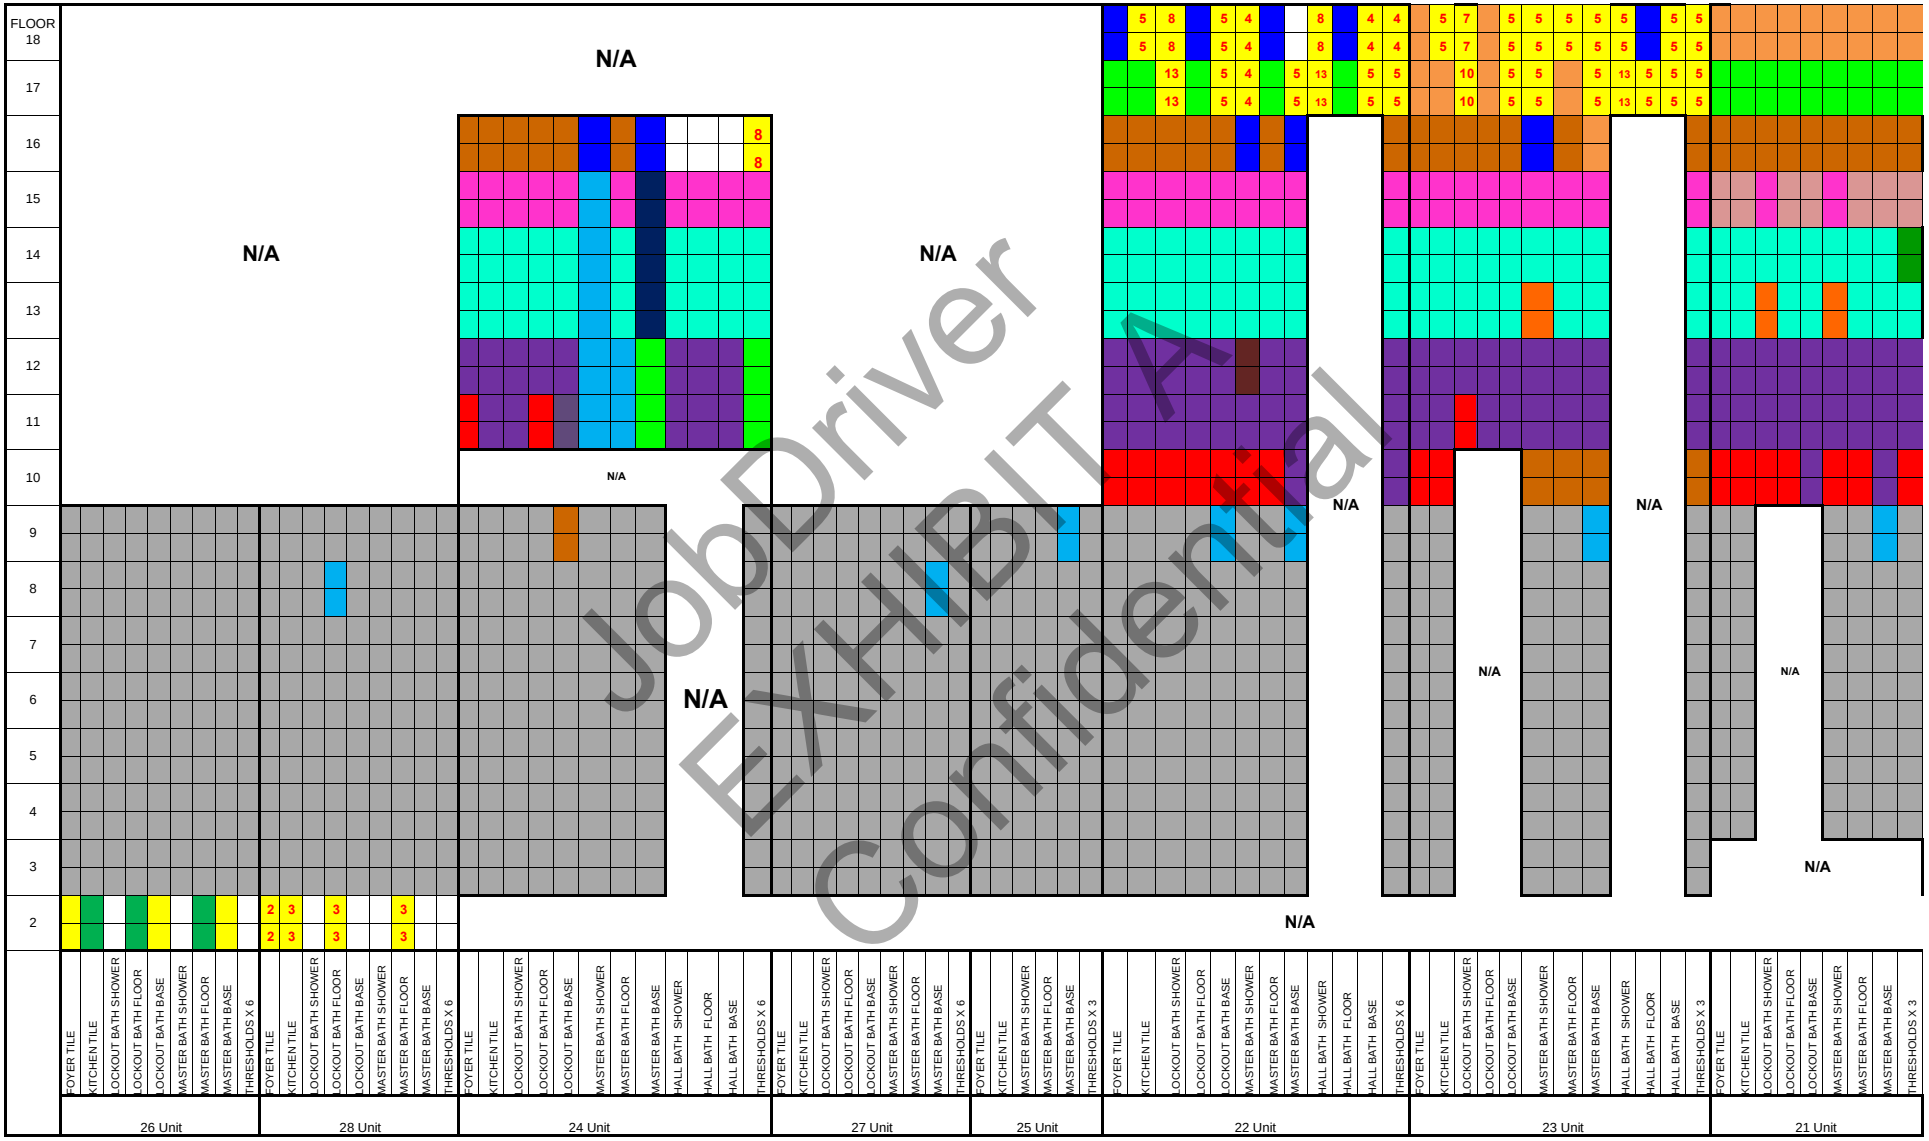

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2012
- Working on floors with no completion 6/8/2012
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

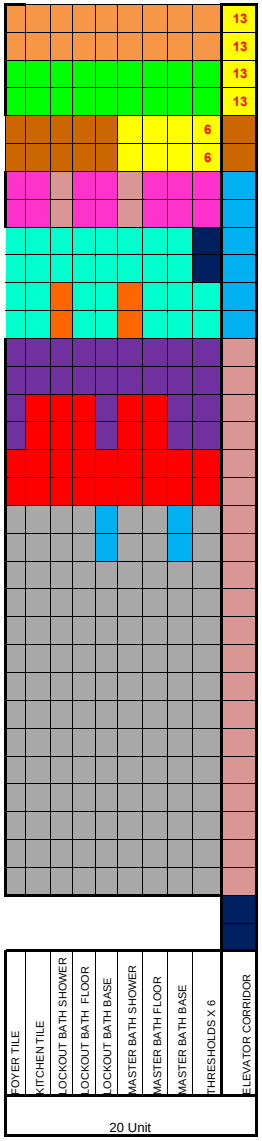

2 WORK COMPLETED TO DATE 6/22/
2 WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

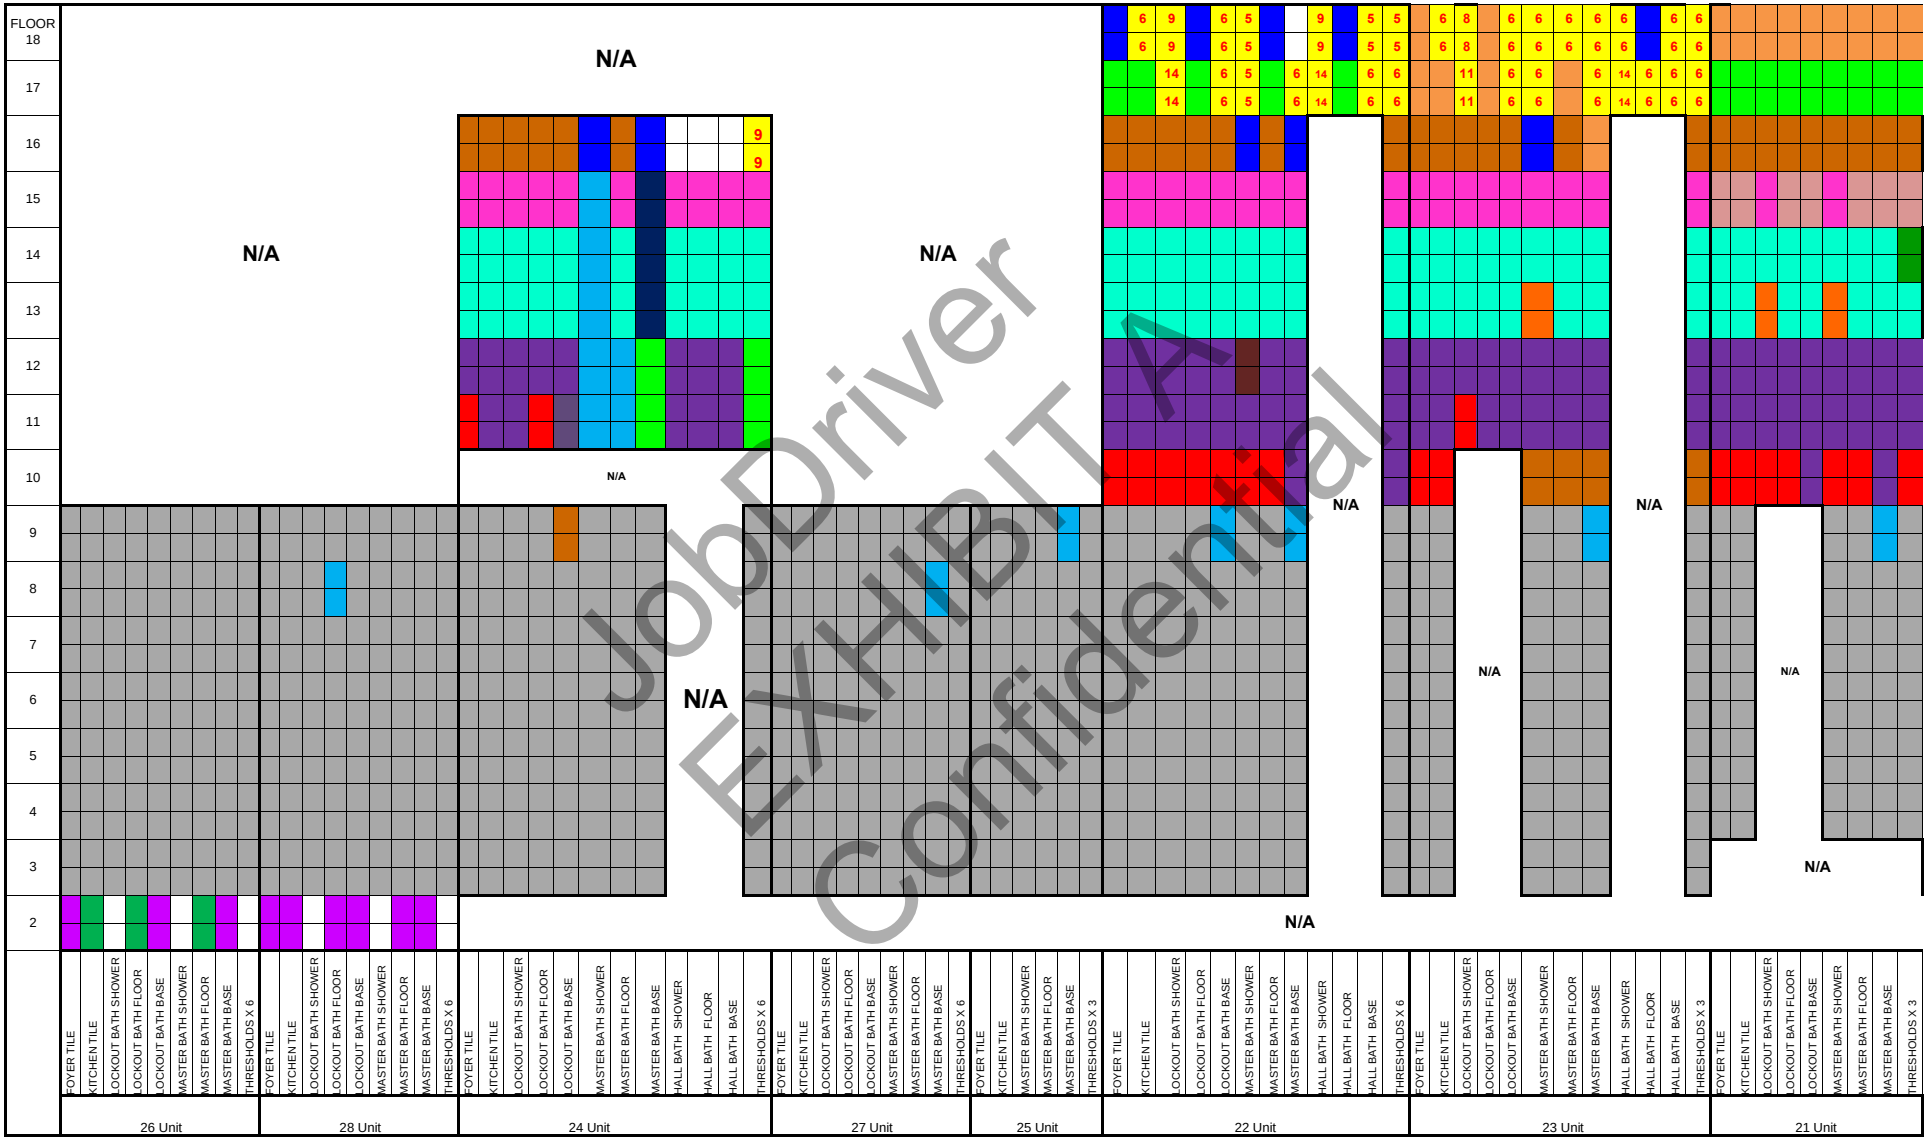

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2012
- Working on floors with no completion 6/8/2012
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

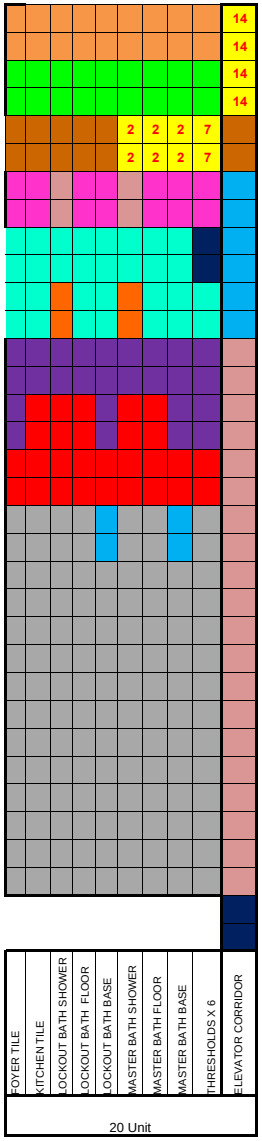

2 WORK COMPLETED TO DATE 6/22/
2 WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

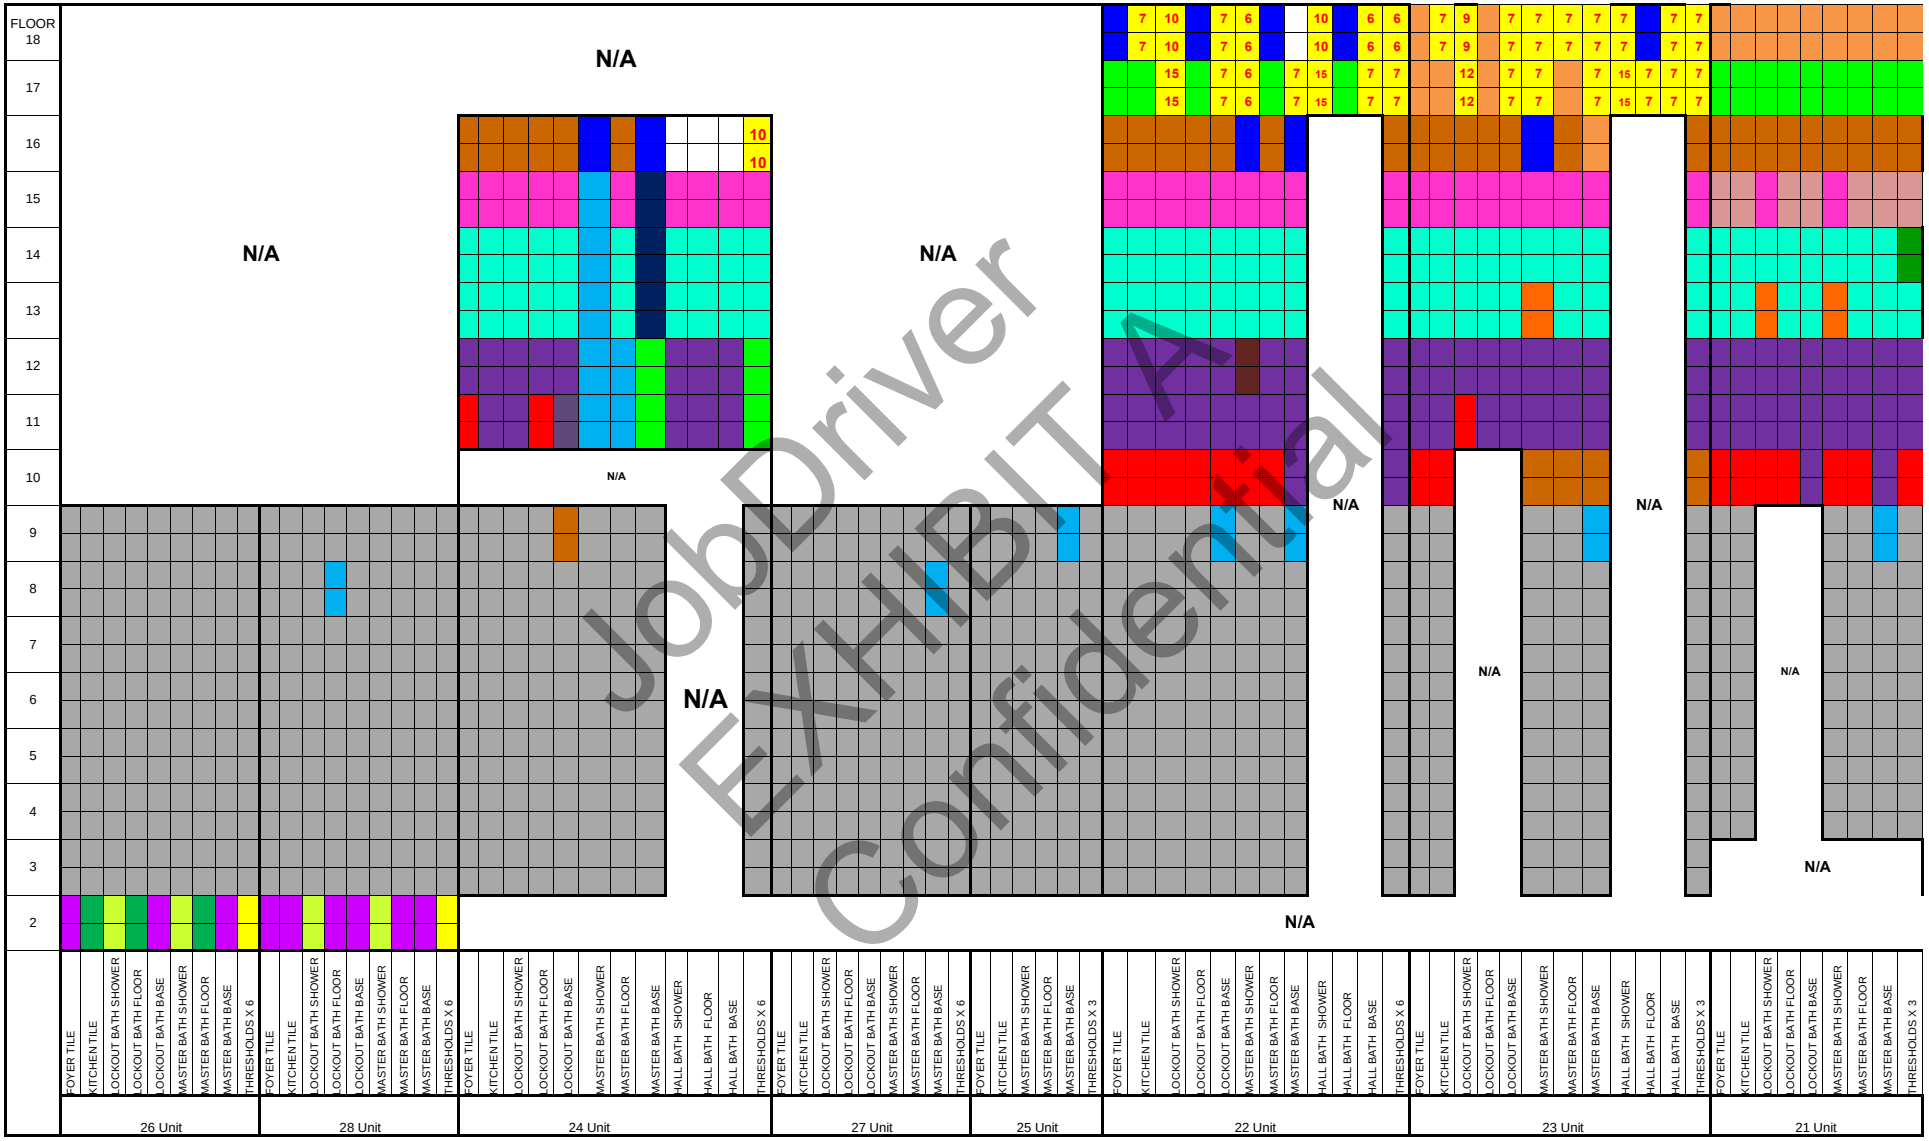

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2012
- Working on floors with no completion 6/8/2012
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

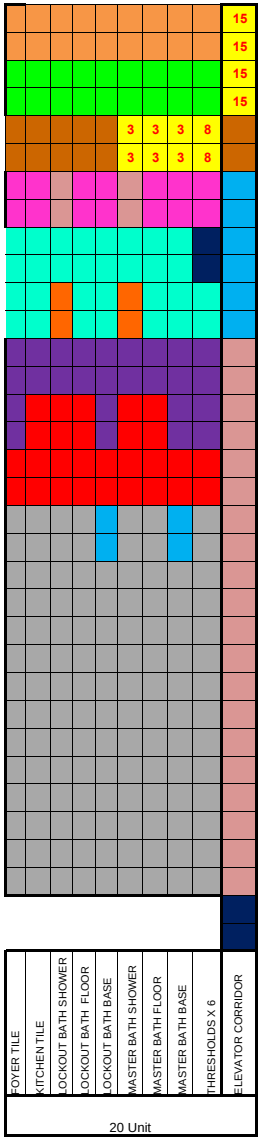

2 WORK COMPLETED TO DATE 6/22/
2 WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

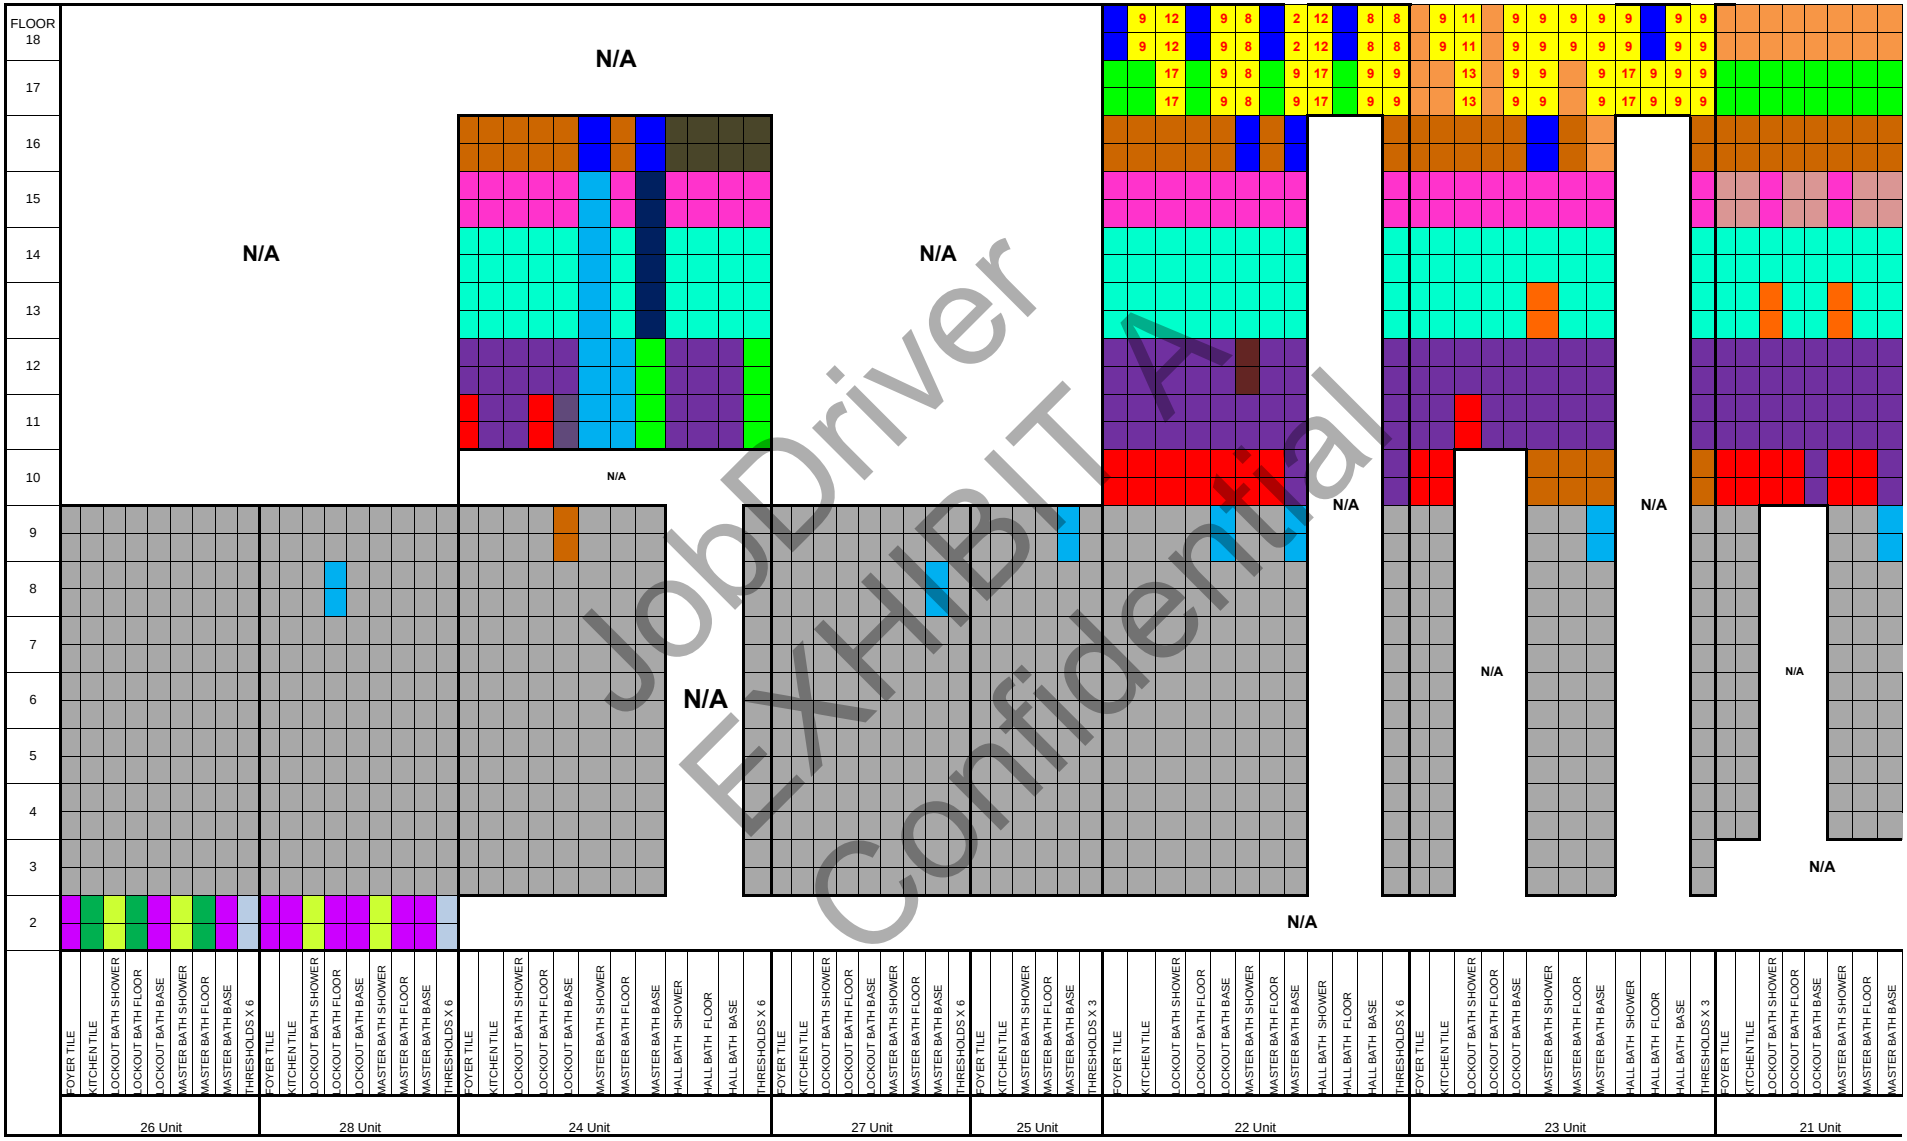

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/1/2
- Working on floors with no completion 6/8/2
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

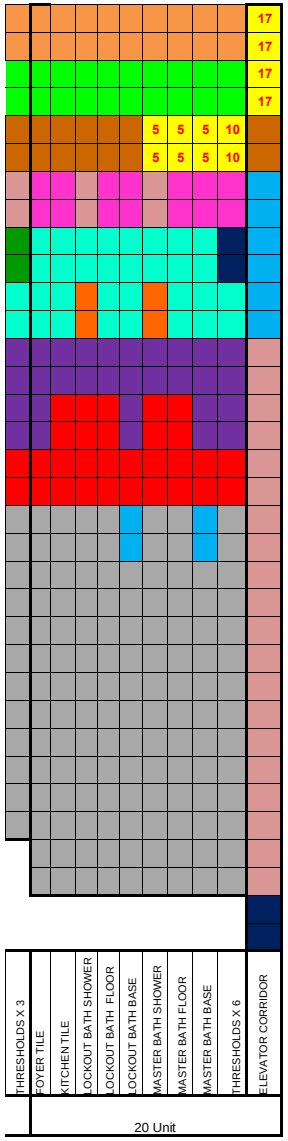

2012 WORK COMPLETED TO DATE 6/22/
2012 WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

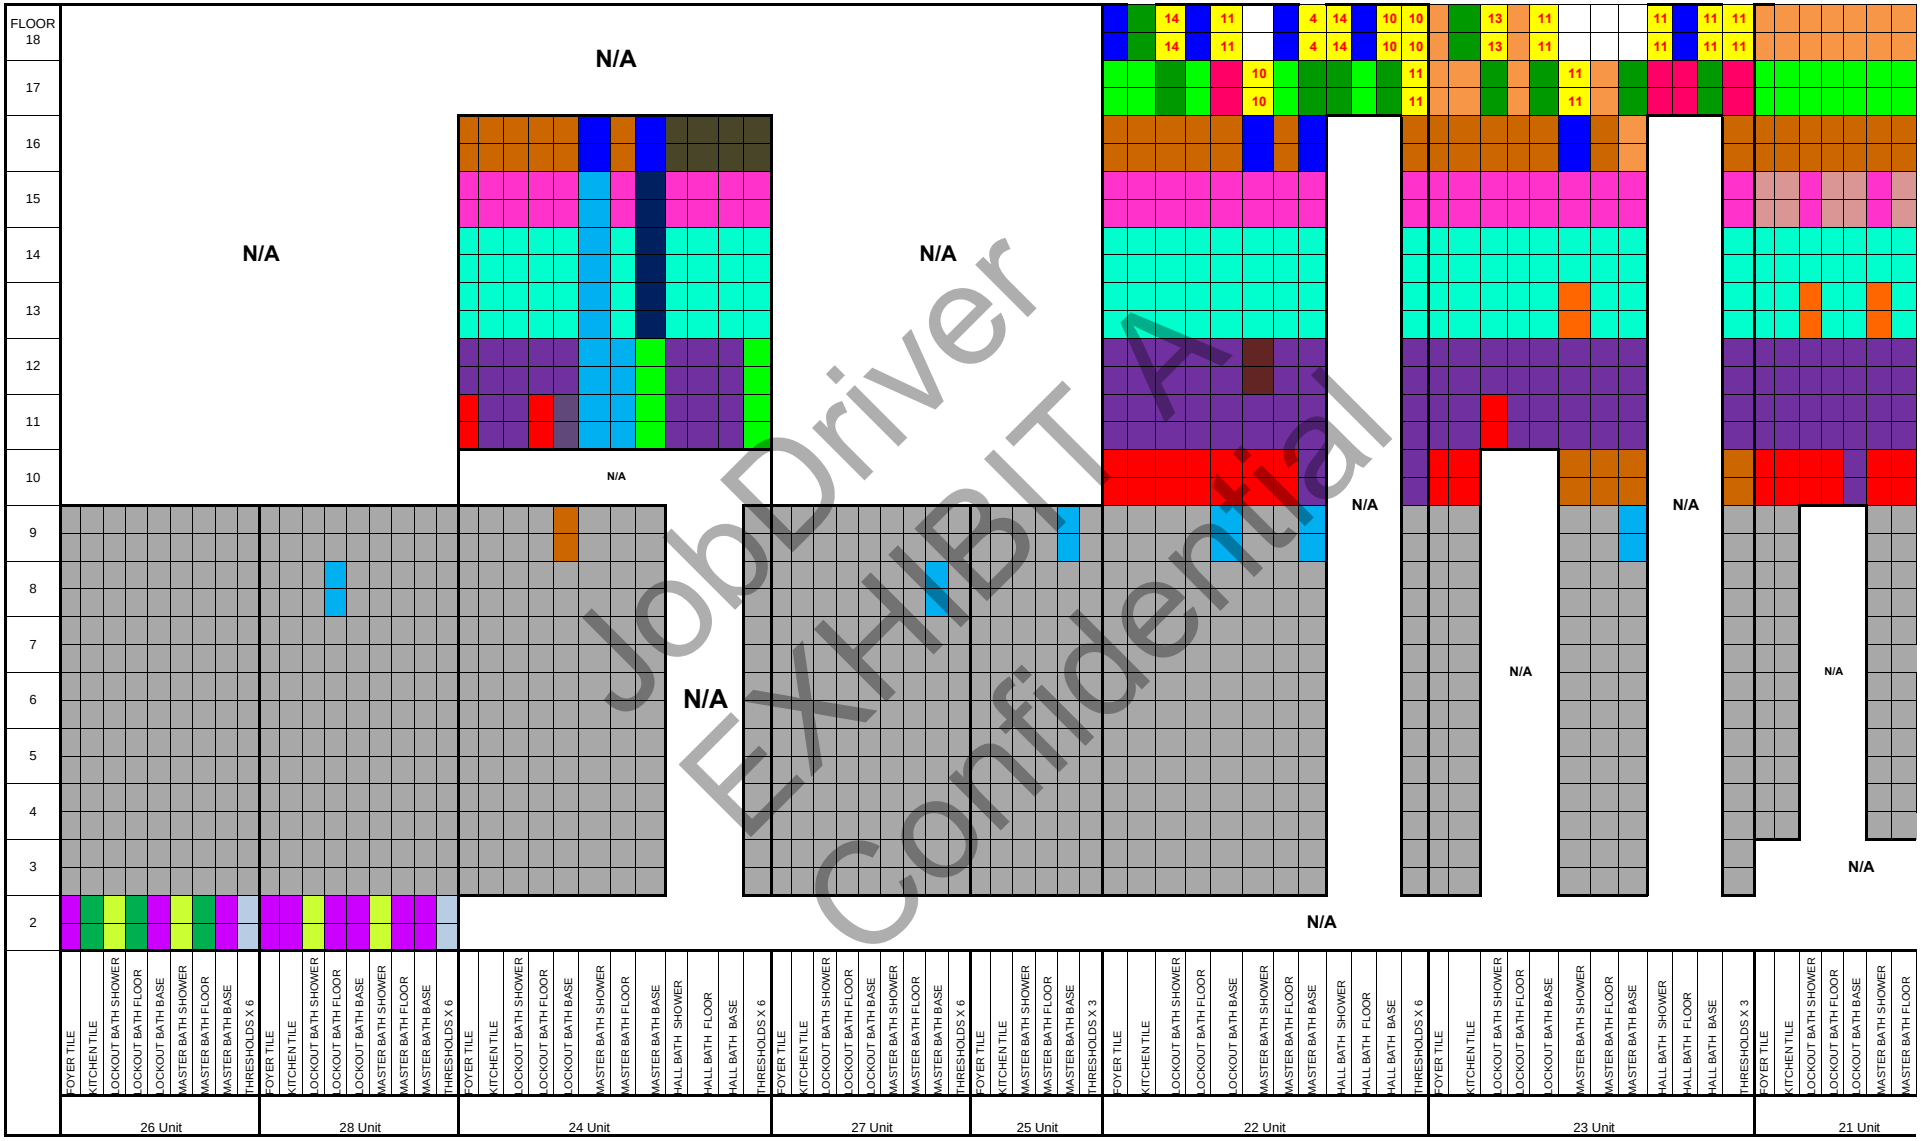

JobDriver
EXHIBIT A
Confidential

POMPEI TILE PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 2/3/2012
- WORK COMPLETED TO DATE 1/10/2012
- WORK COMPLETED TO DATE 3/9/2012
- WORK COMPLETED TO DATE 3/16/2012
- WORK COMPLETED TO DATE 3/23/2012
- WORK COMPLETED TO DATE 3/30/2012
- WORK COMPLETED TO DATE 4/6/2012
- WORK COMPLETED TO DATE 4/13/2012
- WORK COMPLETED TO DATE 4/27/2012
- WORK COMPLETED TO DATE 5/4/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/11/2012
- POMPEI WAS ON FIRST FLOOR ALL WEEK 5/18/2012 Completed elevator 1 and 2 tile
- WORK COMPLETED TO DATE 5/25/2012
- Working on floors with no completion 6/
- Working on floors with no completion 6/
- Work Completed To Date 6/14/2012

POMPEI TILE PROGRESS CHART

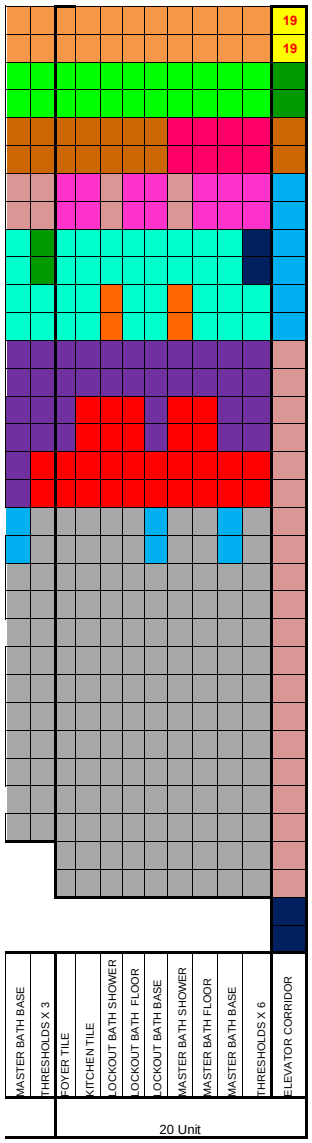

'1/2012
'8/2012

WORK COMPLETED TO DATE 6/22/
WORK COMPLETED TO DATE 7/2/2
7/6 Tile was installed on the 2nd floor n
WORK COMPLETED TO DATE 7/13/

JobDriver
EXHIBIT A
Confidential

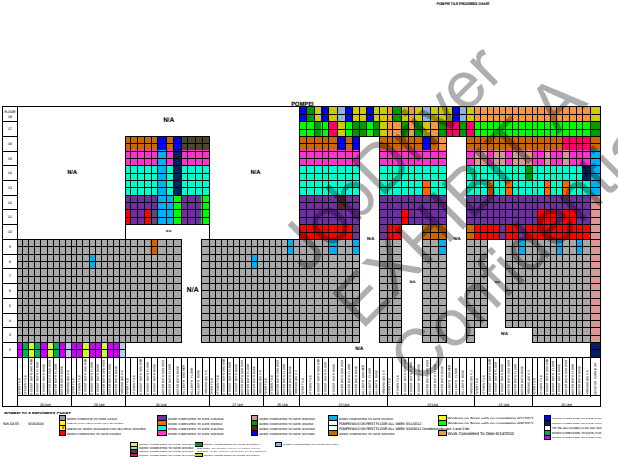
POWER TILE PROGRESS CHART
N/A
N/A
N/A

PREMIER MILLWORK PROGRESS CHART

FLOOR	26 Unit	28 Unit	24 Unit	27 Unit	25 Unit	22 Unit	23 Unit	21 Unit	20 Unit
18	N/A								
17									
16									
15									
14									
13									
12									
11									
10									
9									
8									
7									
6									
5									
4									
3								N/A	
2			N/A						
	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets
	Countertop furring	Countertop furring	Countertop furring	Countertop furring	Countertop furring	Countertop furring	Countertop furring	Countertop furring	Countertop furring
	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence
	Window Valence	Window Valence	Window Valence	Window Valence	Window Valence	Window Valence	Window Valence	Window Valence	Window Valence
	Double Vanity	Double Vanity	Double Vanity	Double Vanity	Double Vanity	Double Vanity	Double Vanity	Double Vanity	Double Vanity
	Single Vanity	Single Vanity	Single Vanity	Single Vanity	Single Vanity	Single Vanity	Single Vanity		
	Lockout Kitchen	Lockout Kitchen	Lockout Kitchen	Lockout Kitchen	Lockout Kitchen	Lockout Kitchen	Lockout Kitchen		
	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb	Master Bath Casing & Jamb
	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror	Living Room Mirror
	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels	Kneewall Wood Panels

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12

AREAS AVAILABLE FOR YOU TO WORK

* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

PREMIER MILLWORK PROGRESS CHART

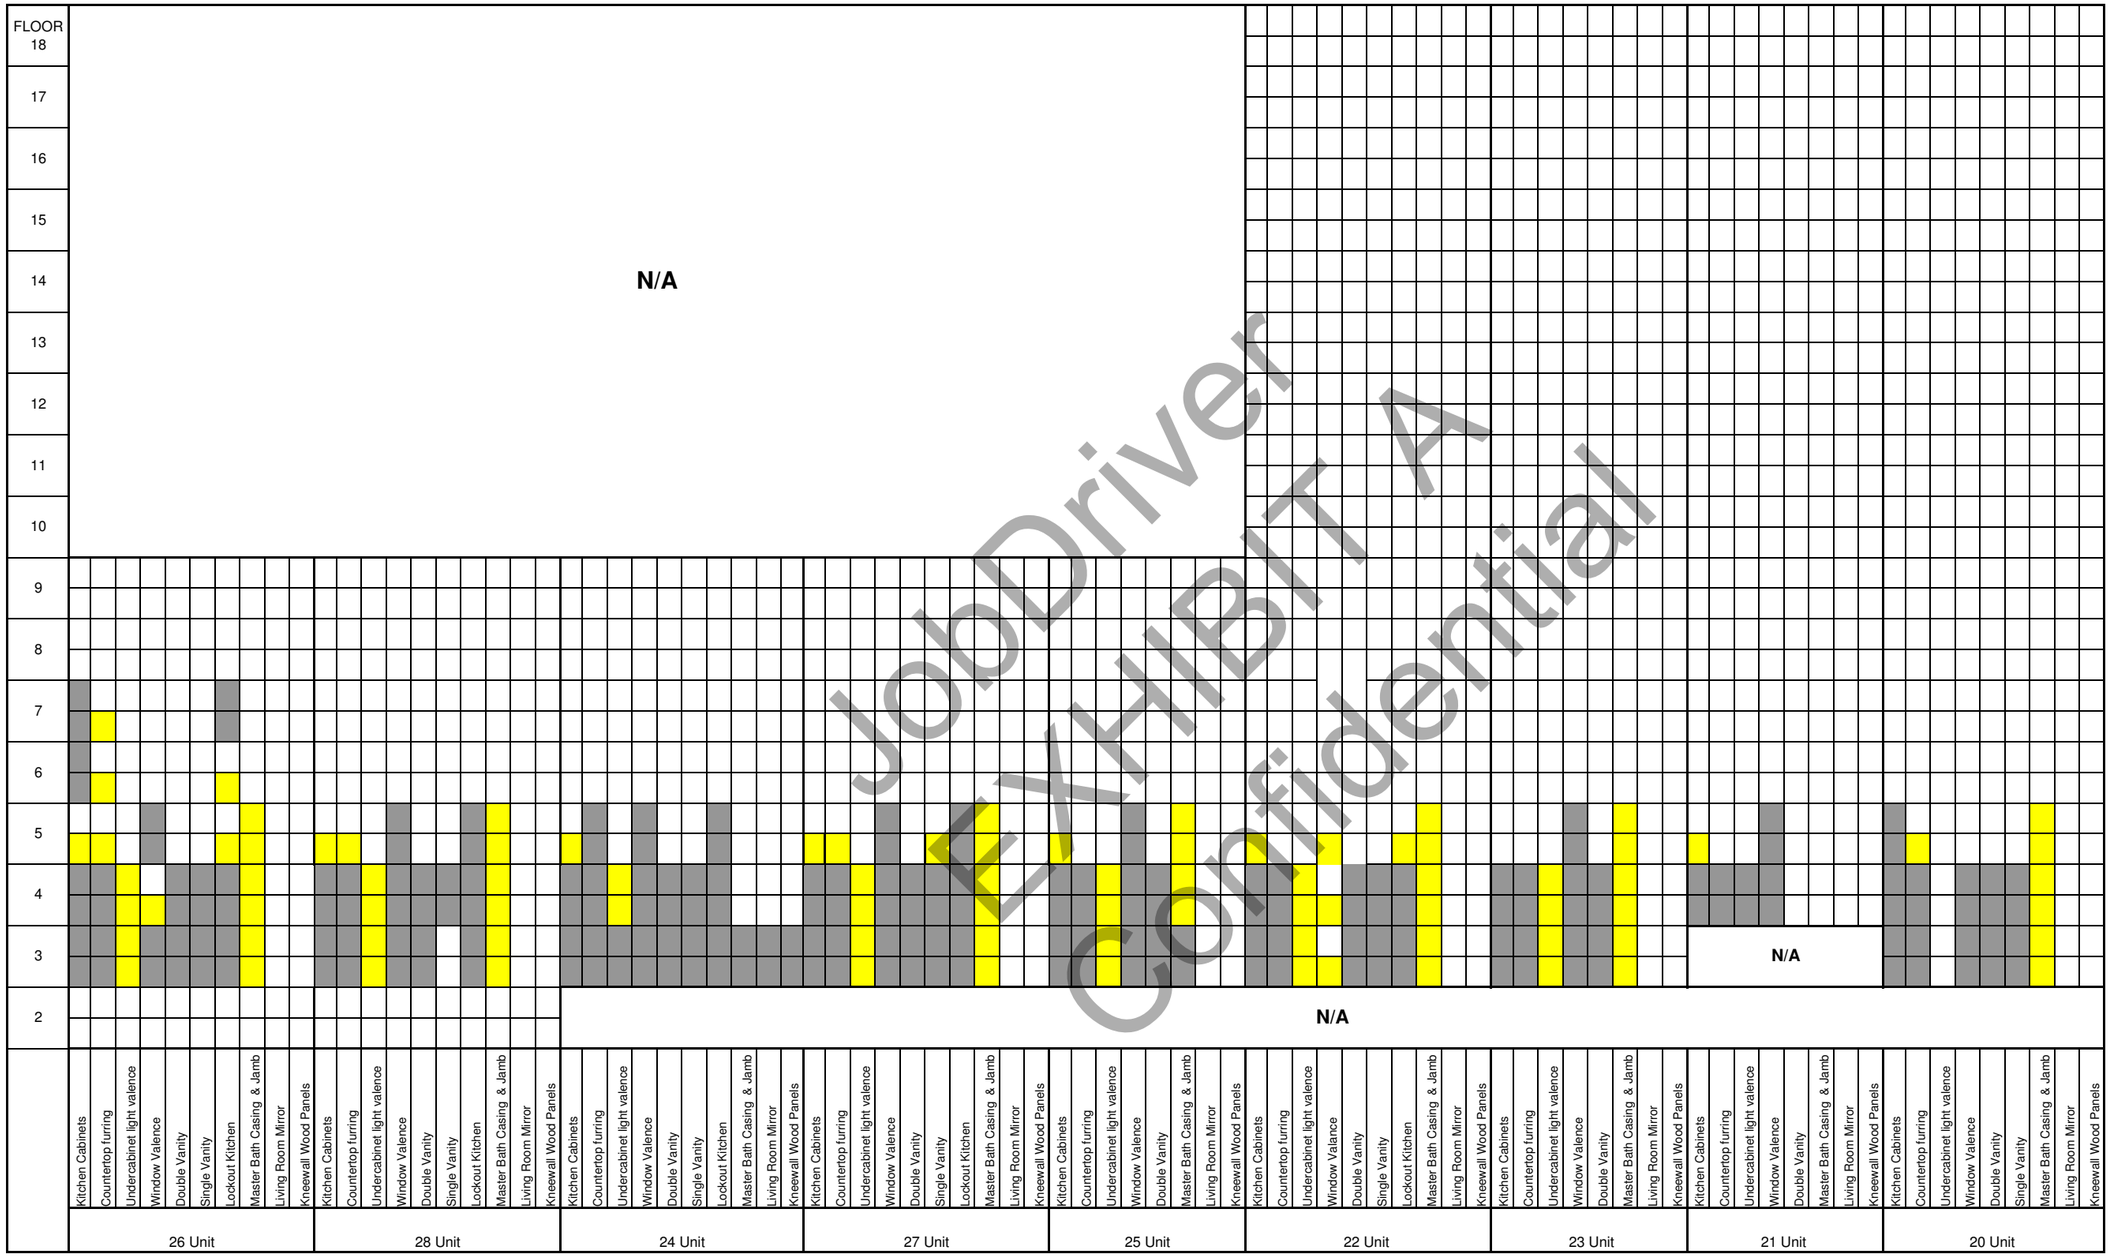

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 1/18/2012

WORK COMPLETE TO DATE 1/13/12

AREAS AVAILABLE FOR YOU TO WORK

AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

PREMIER MILLWORK PROGRESS CHART

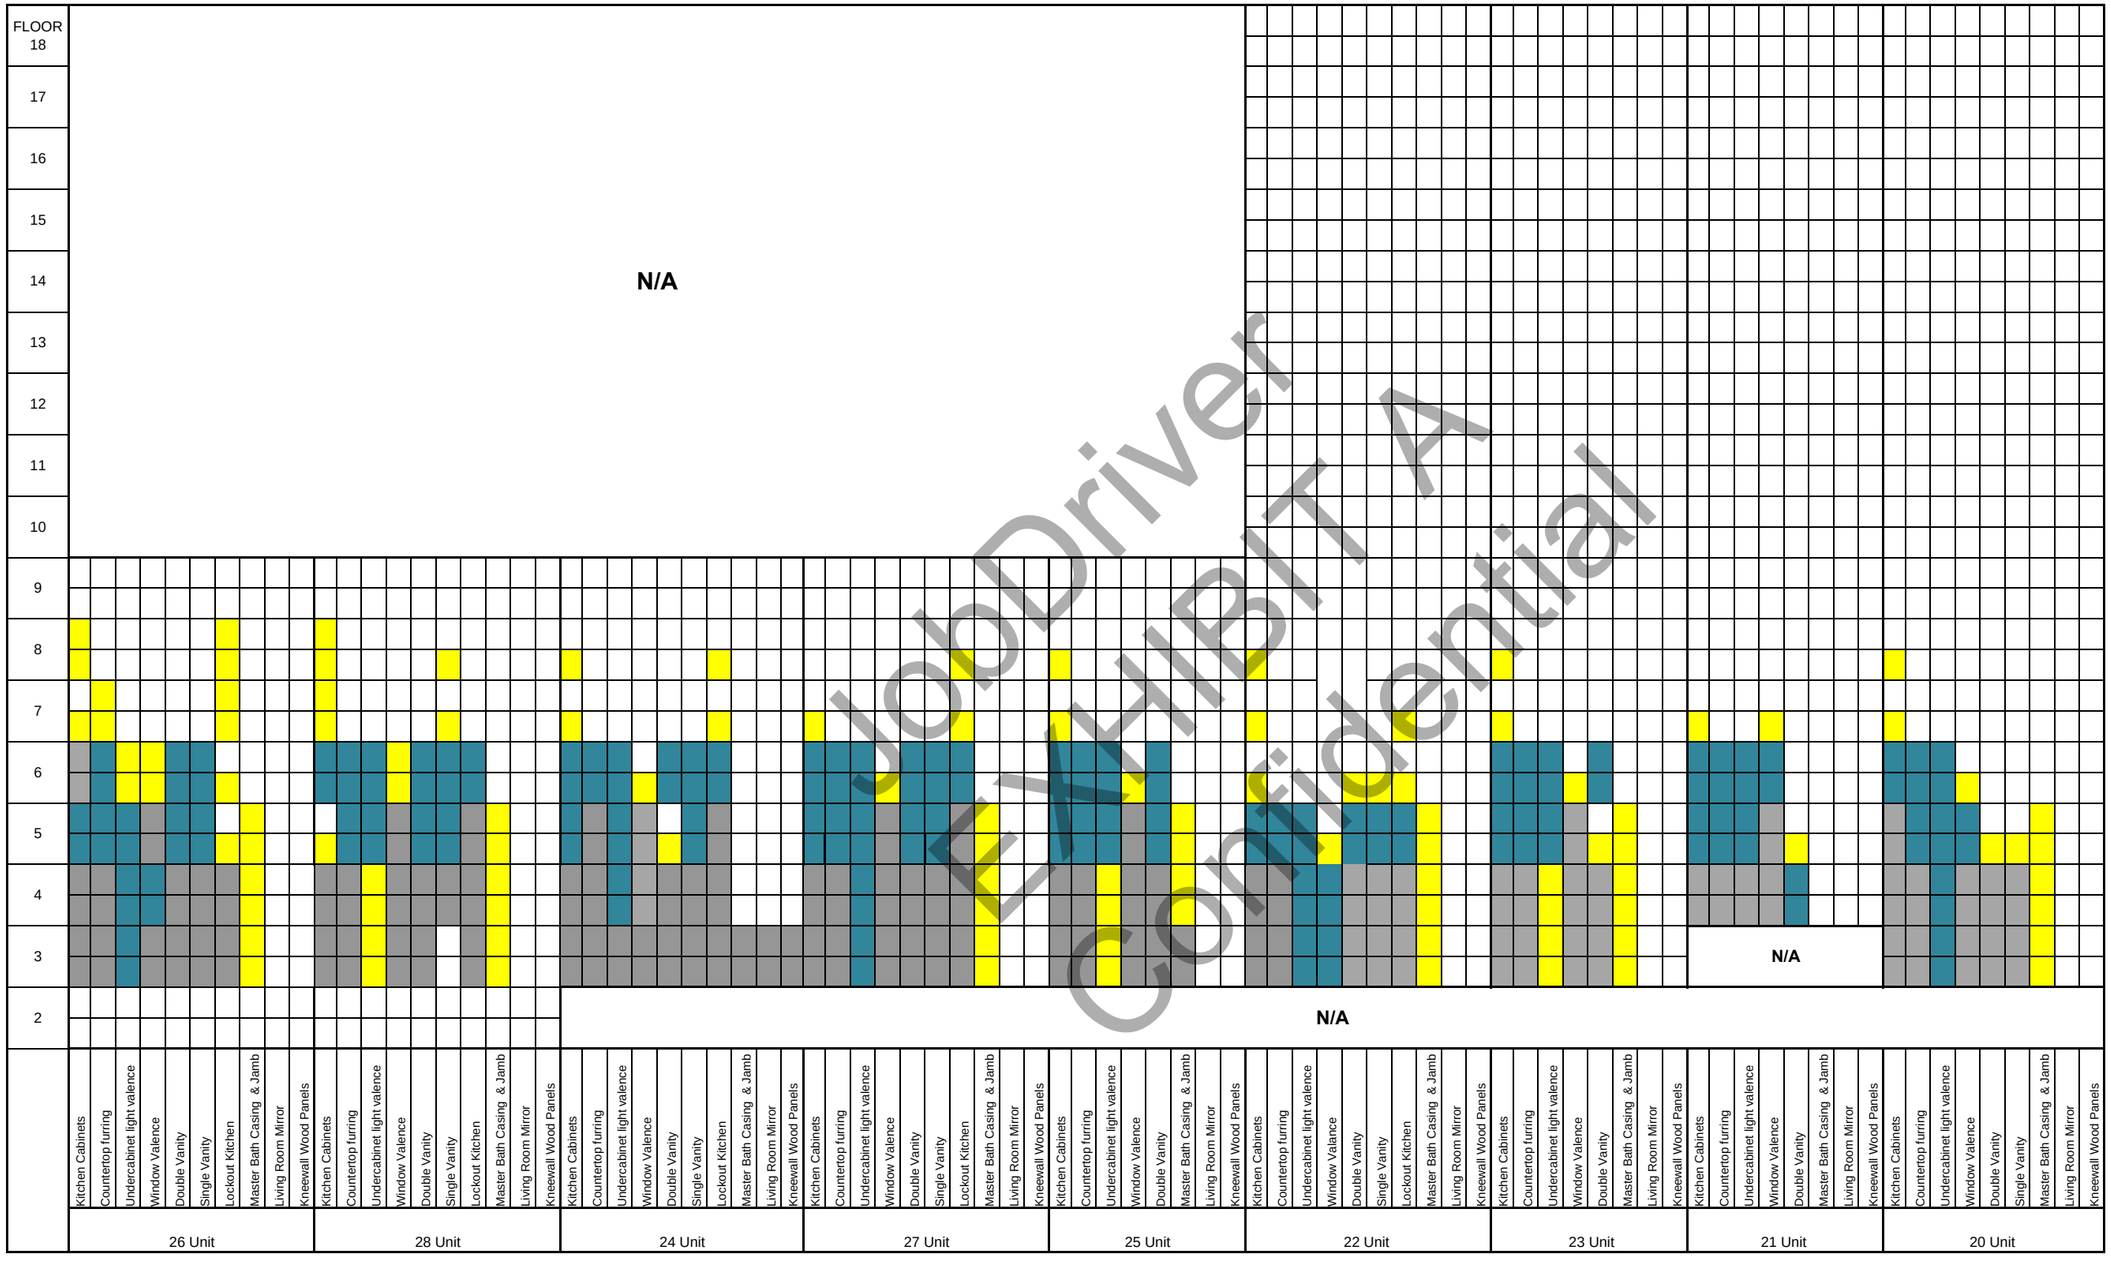

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 1/24/2012

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012

PREMIER MILLWORK PROGRESS CHART

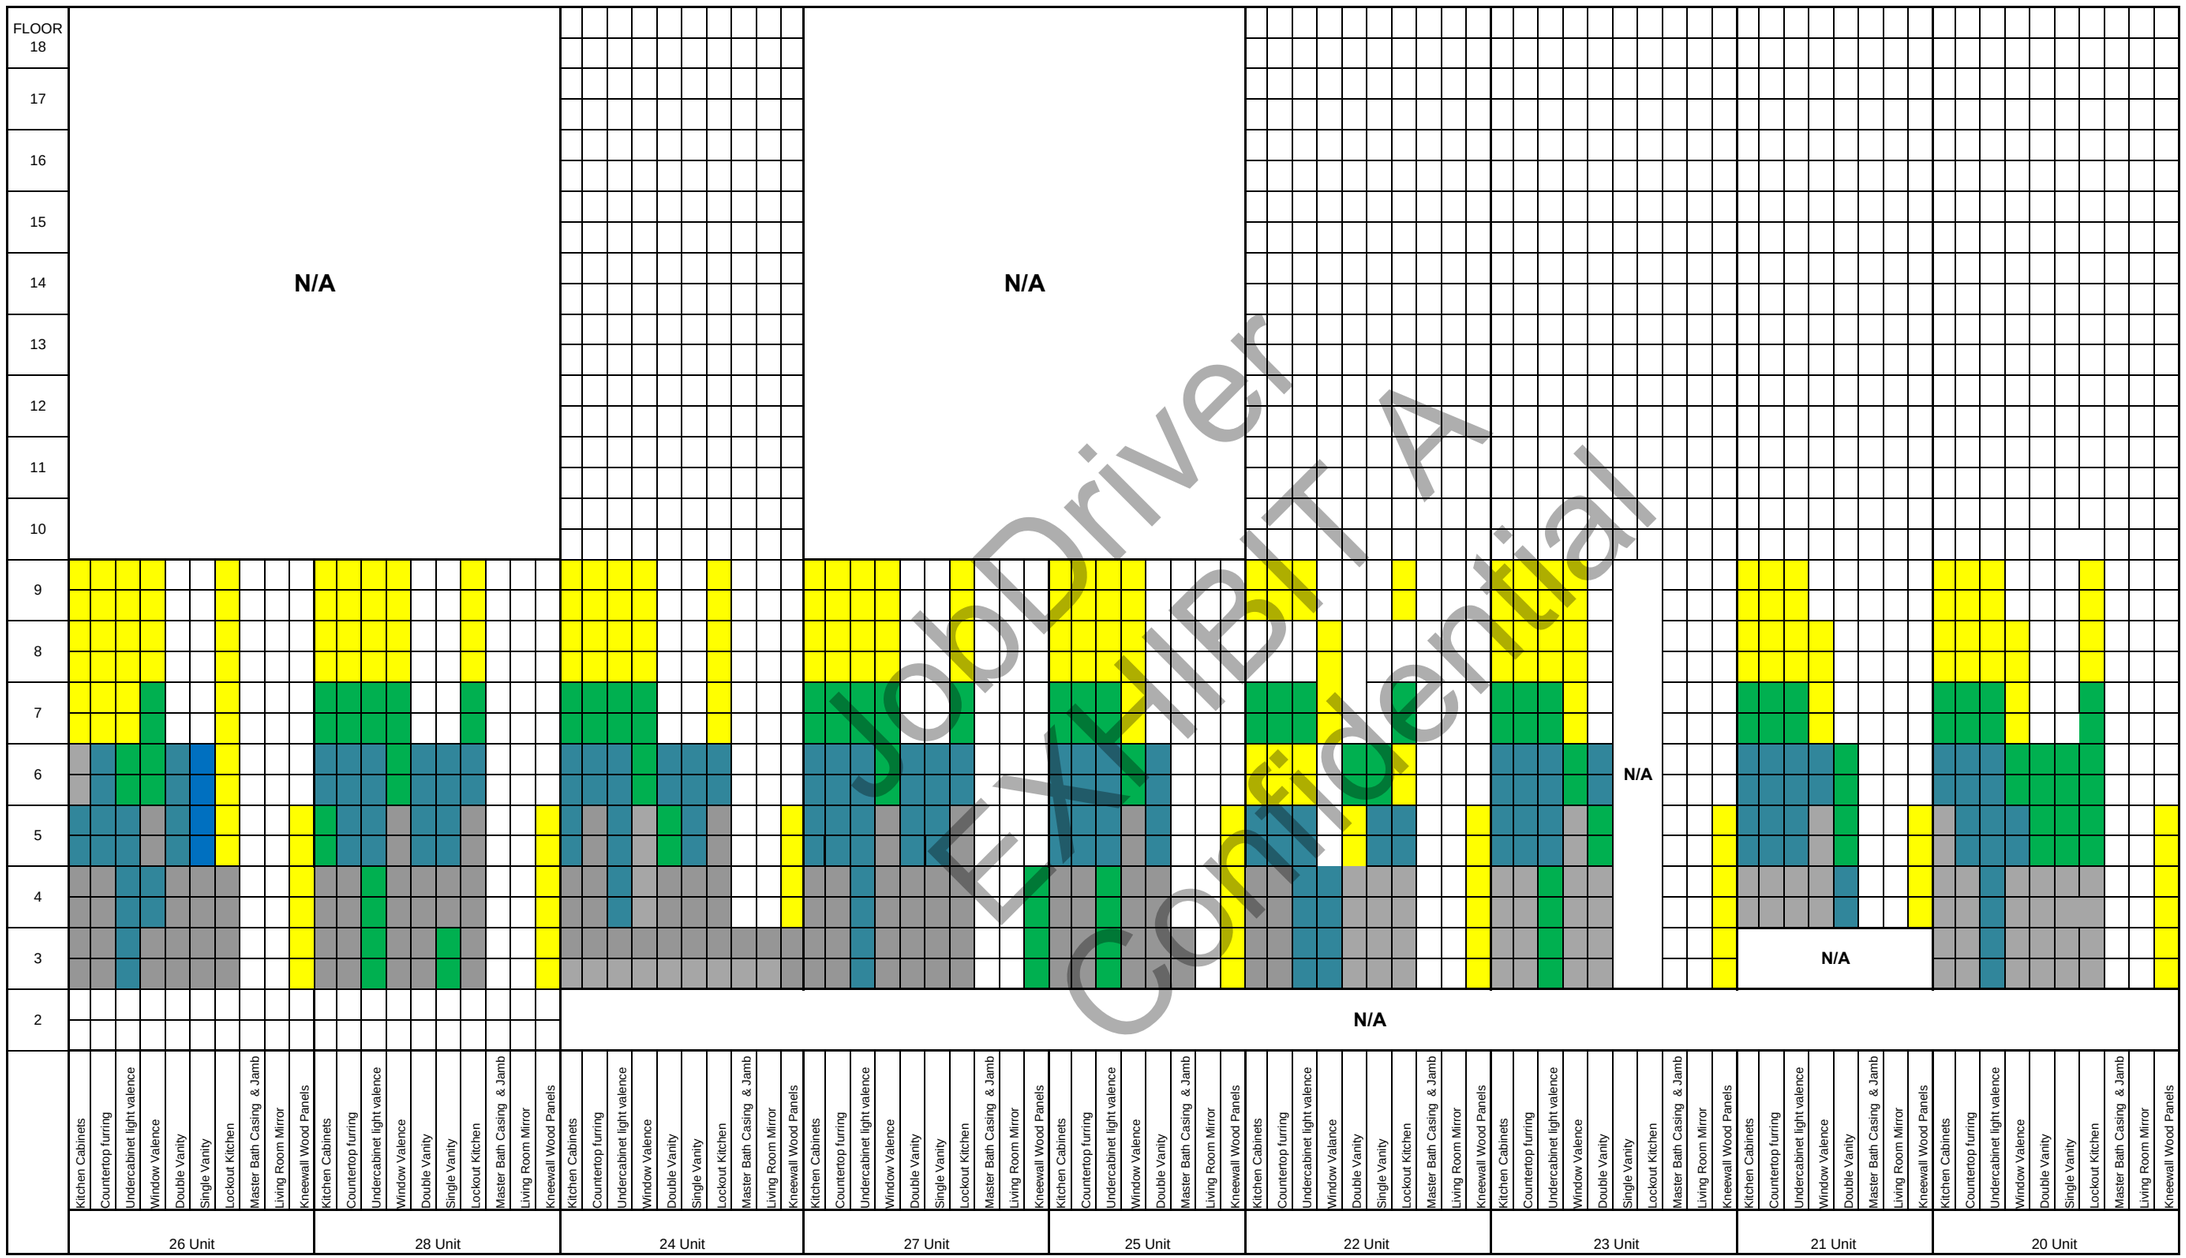

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 1/31/2012

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- * AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012

PREMIER MILLWORK PROGRESS CHART

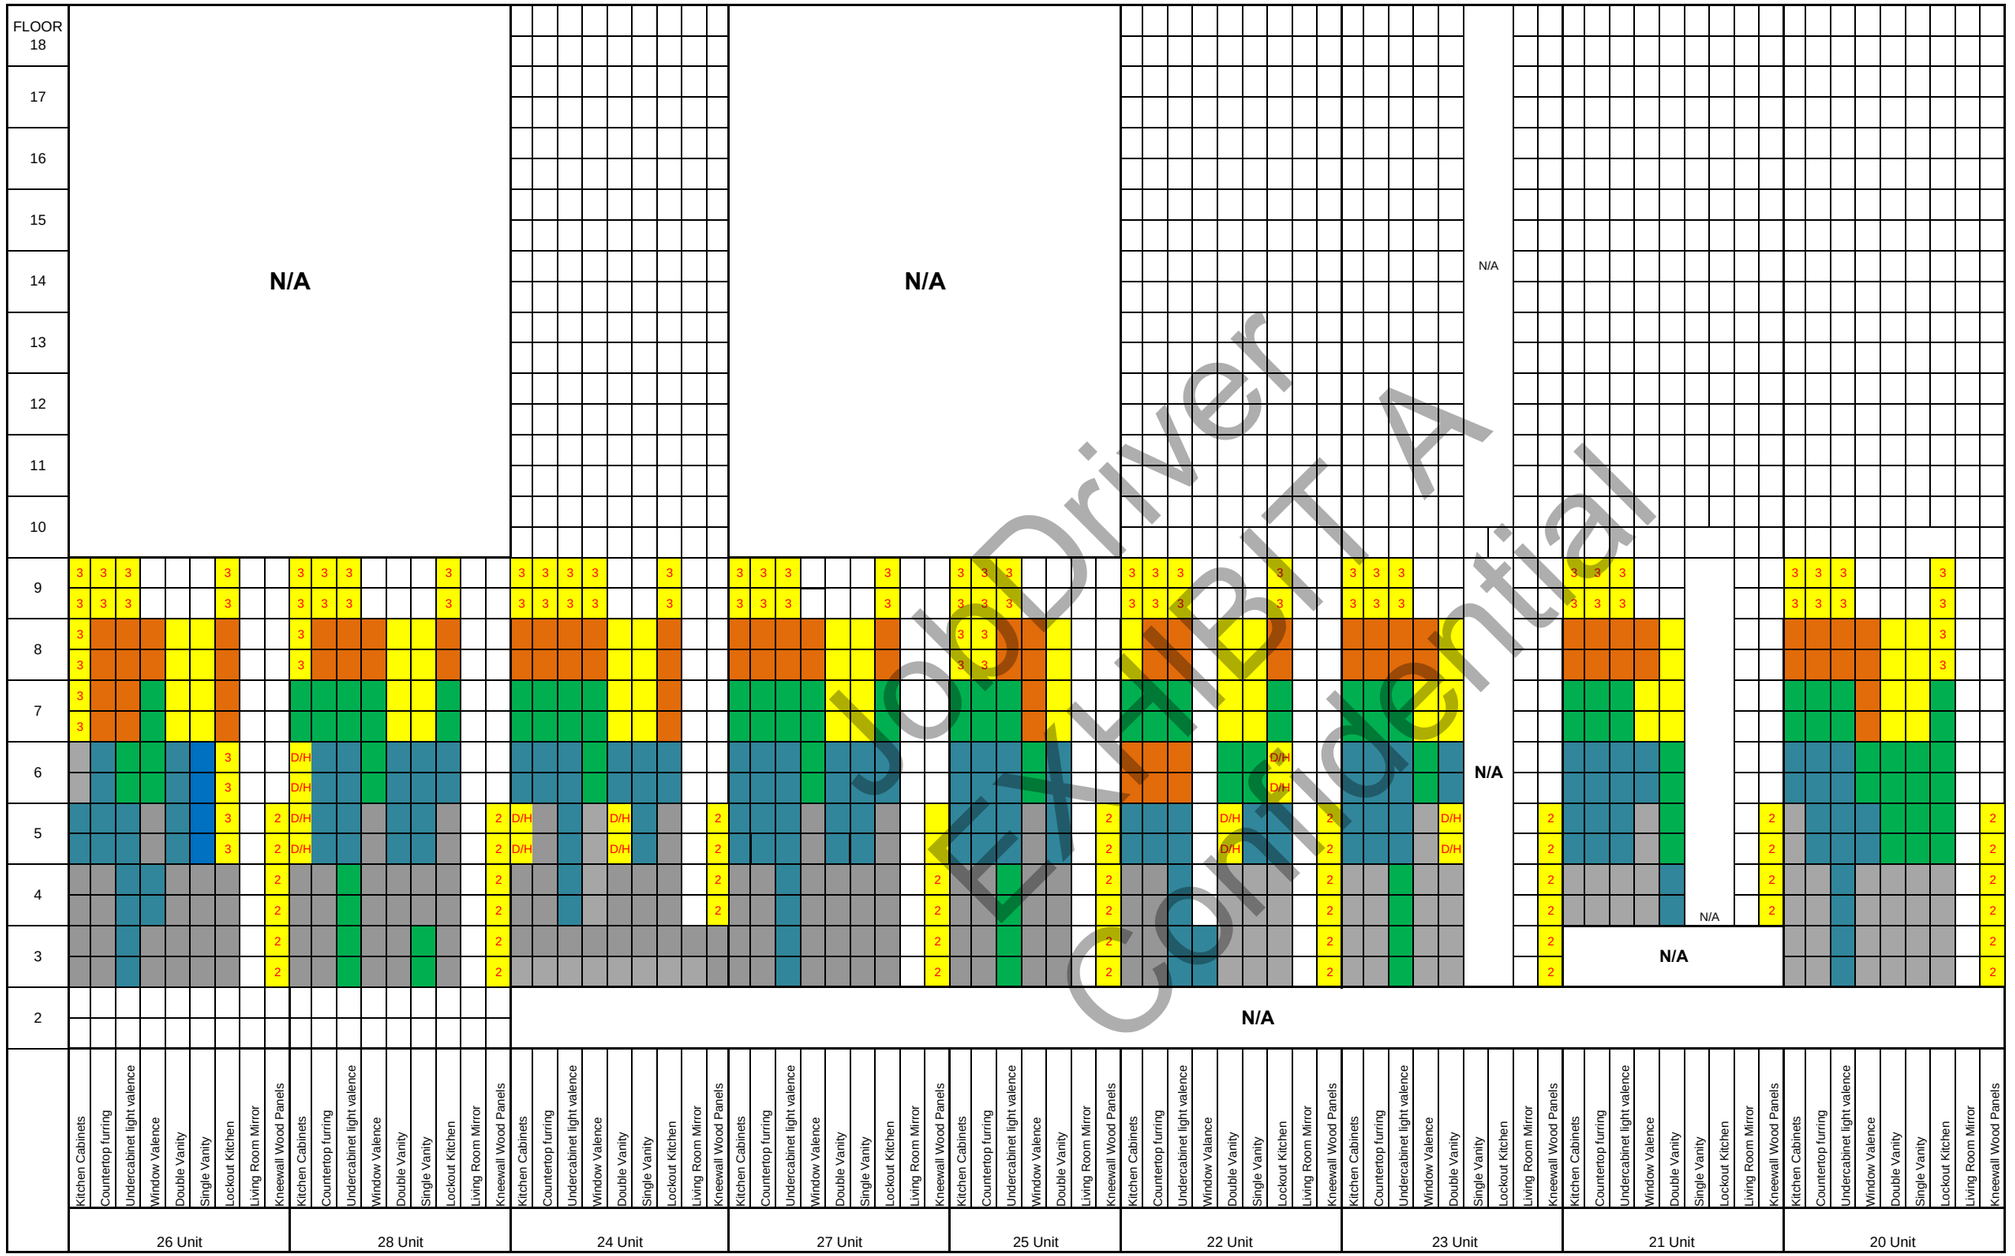

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 2/6/2012

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING

PREMIER MILLWORK PROGRESS CHART

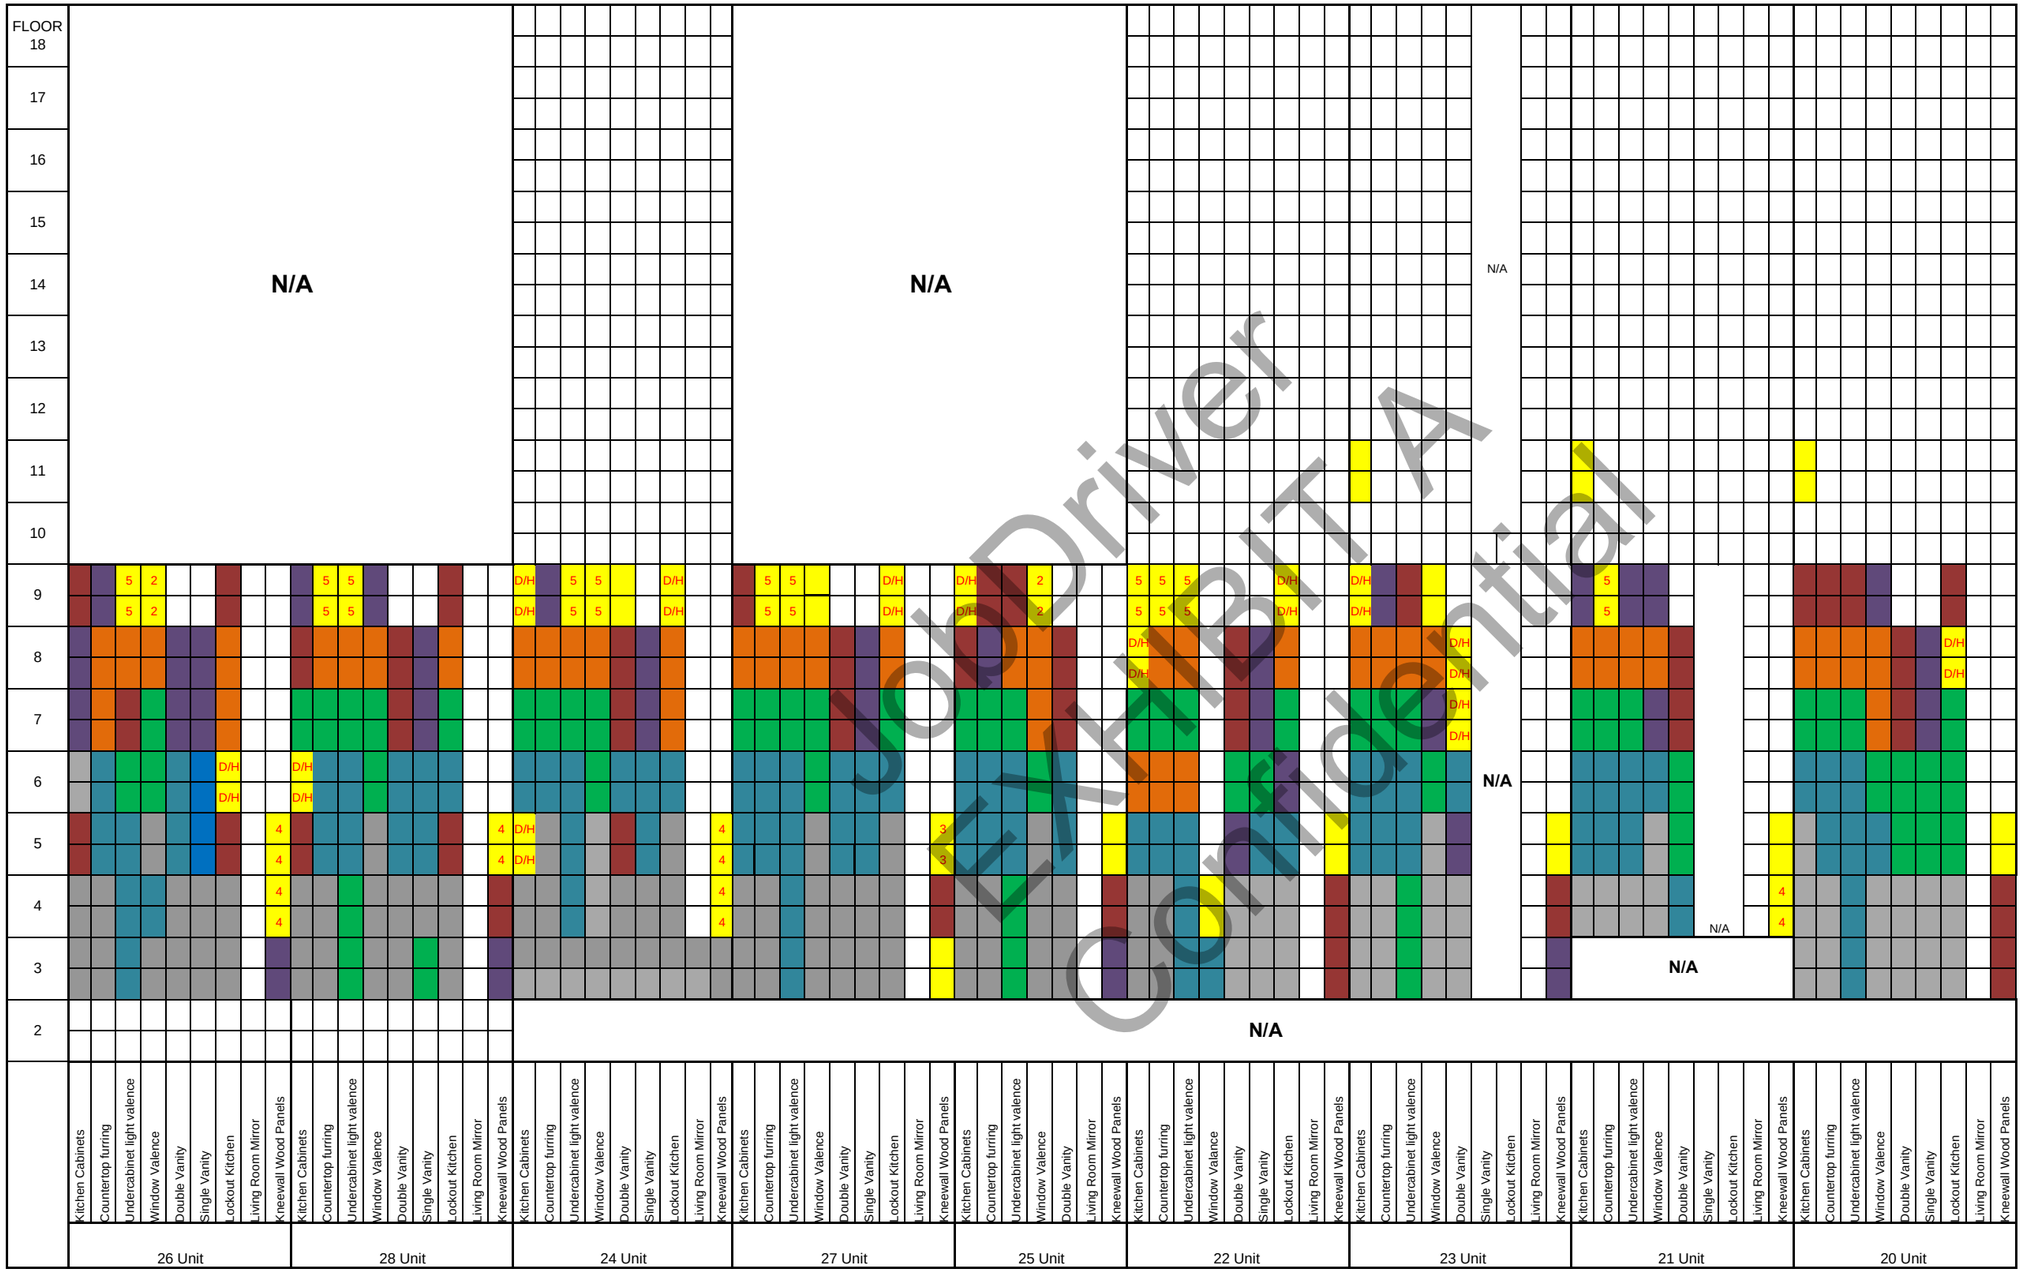

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012

PREMIER MILLWORK PROGRESS CHART

PREMIER

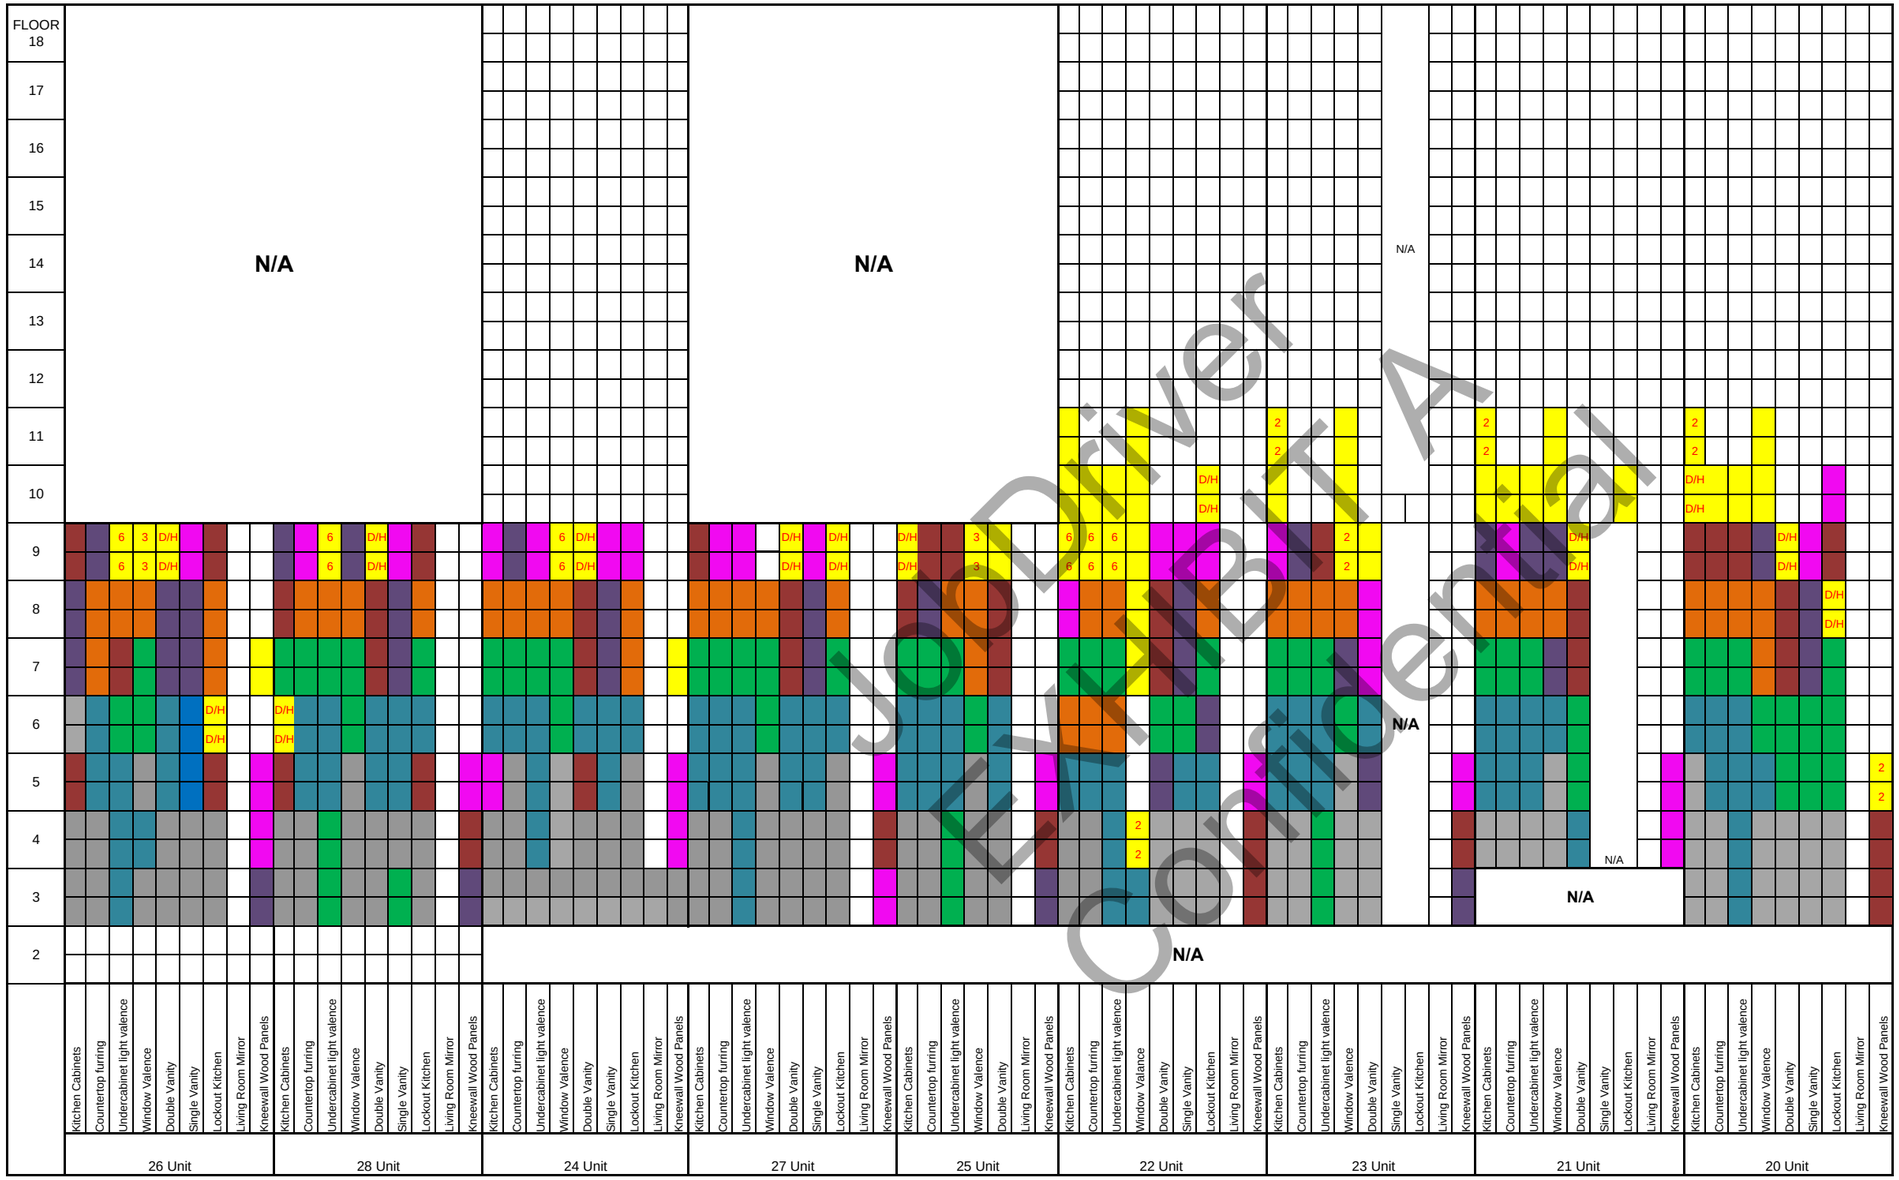

Job Driver
EYE ONLY
Confidential

PREMIER PROGRESS CHART

RUN DATE : 2/27/2012

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED TO DATE 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED TO DATE 2/13/2012
- WORK COMPLETEDTO DATE 2/20/2012
- WORK COMPLETED TO DATE 2-27-2012

PREMIER MILLWORK PROGRESS CHART

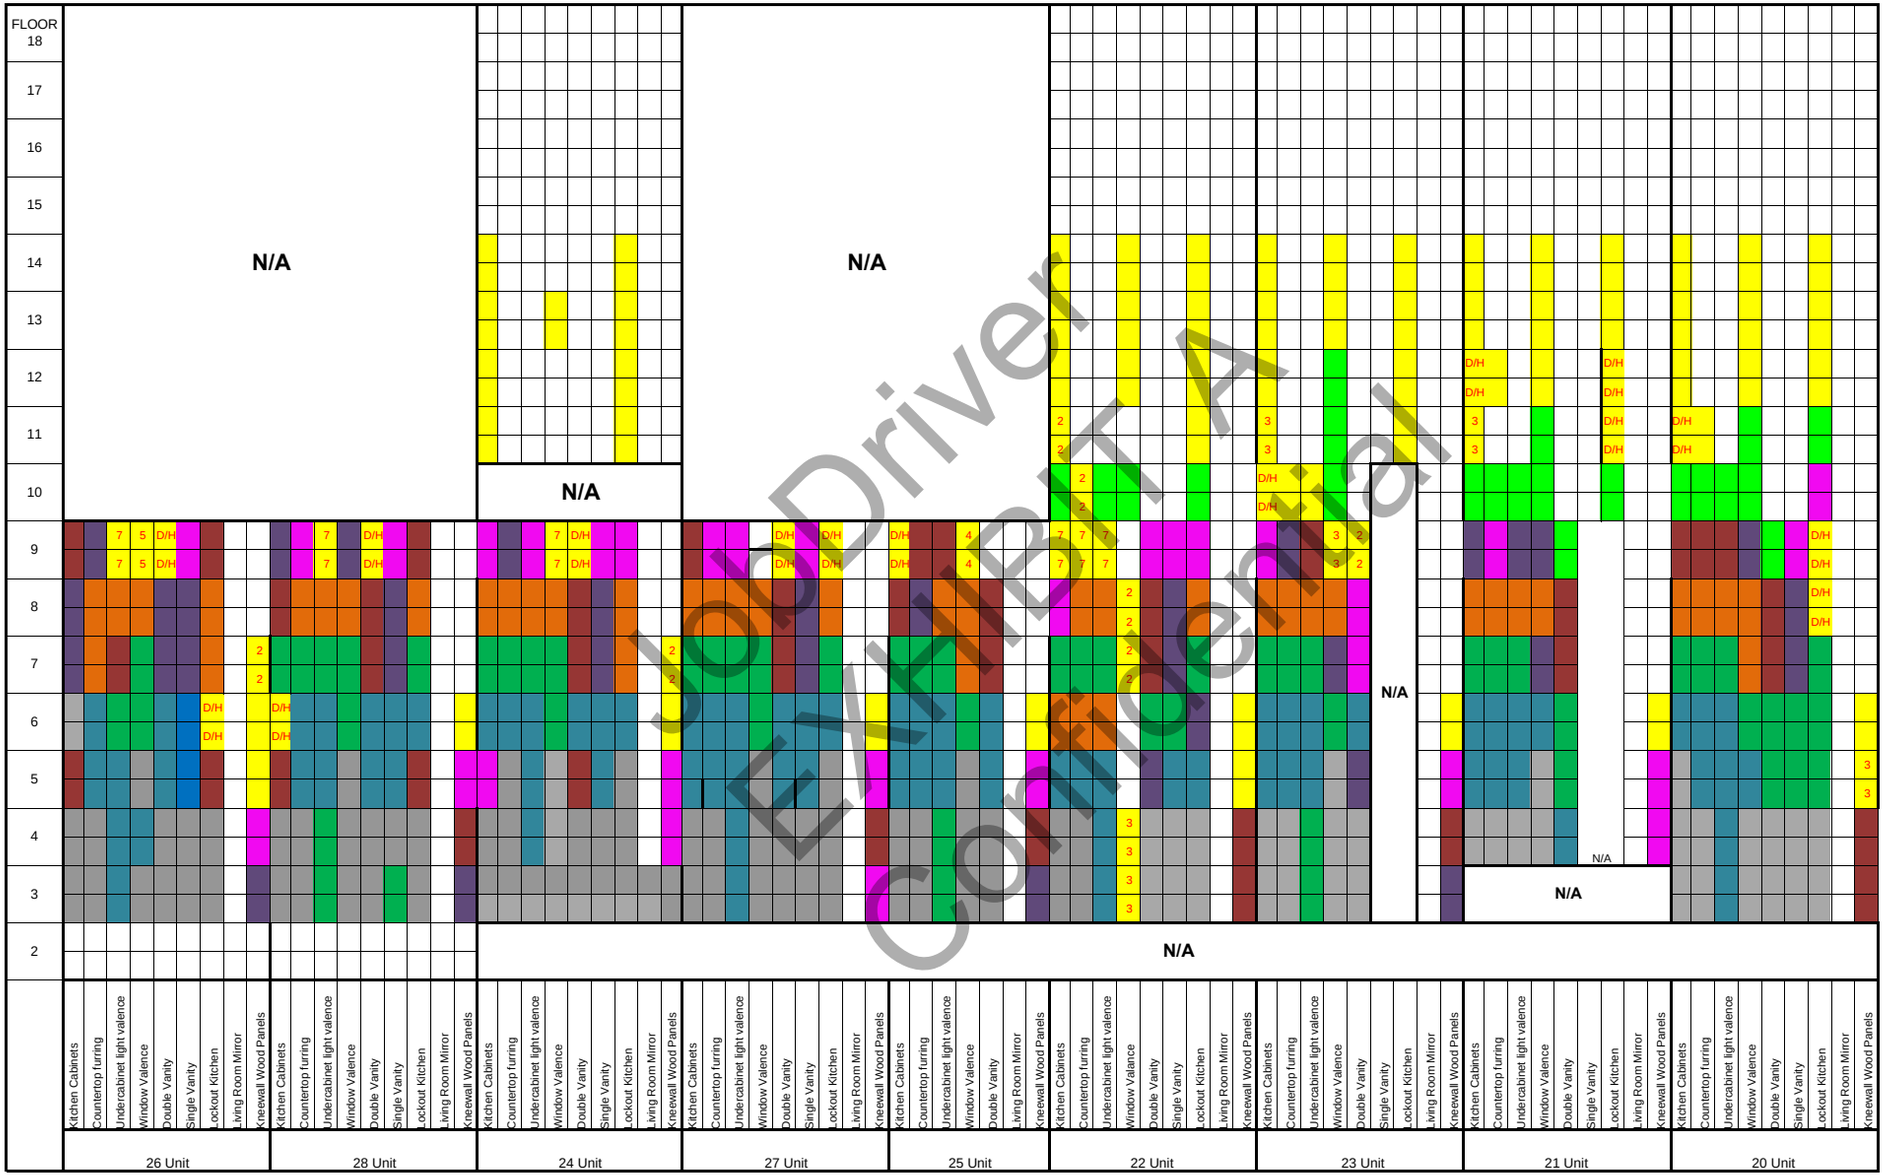

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012

PREMIER MILLWORK PROGRESS CHART

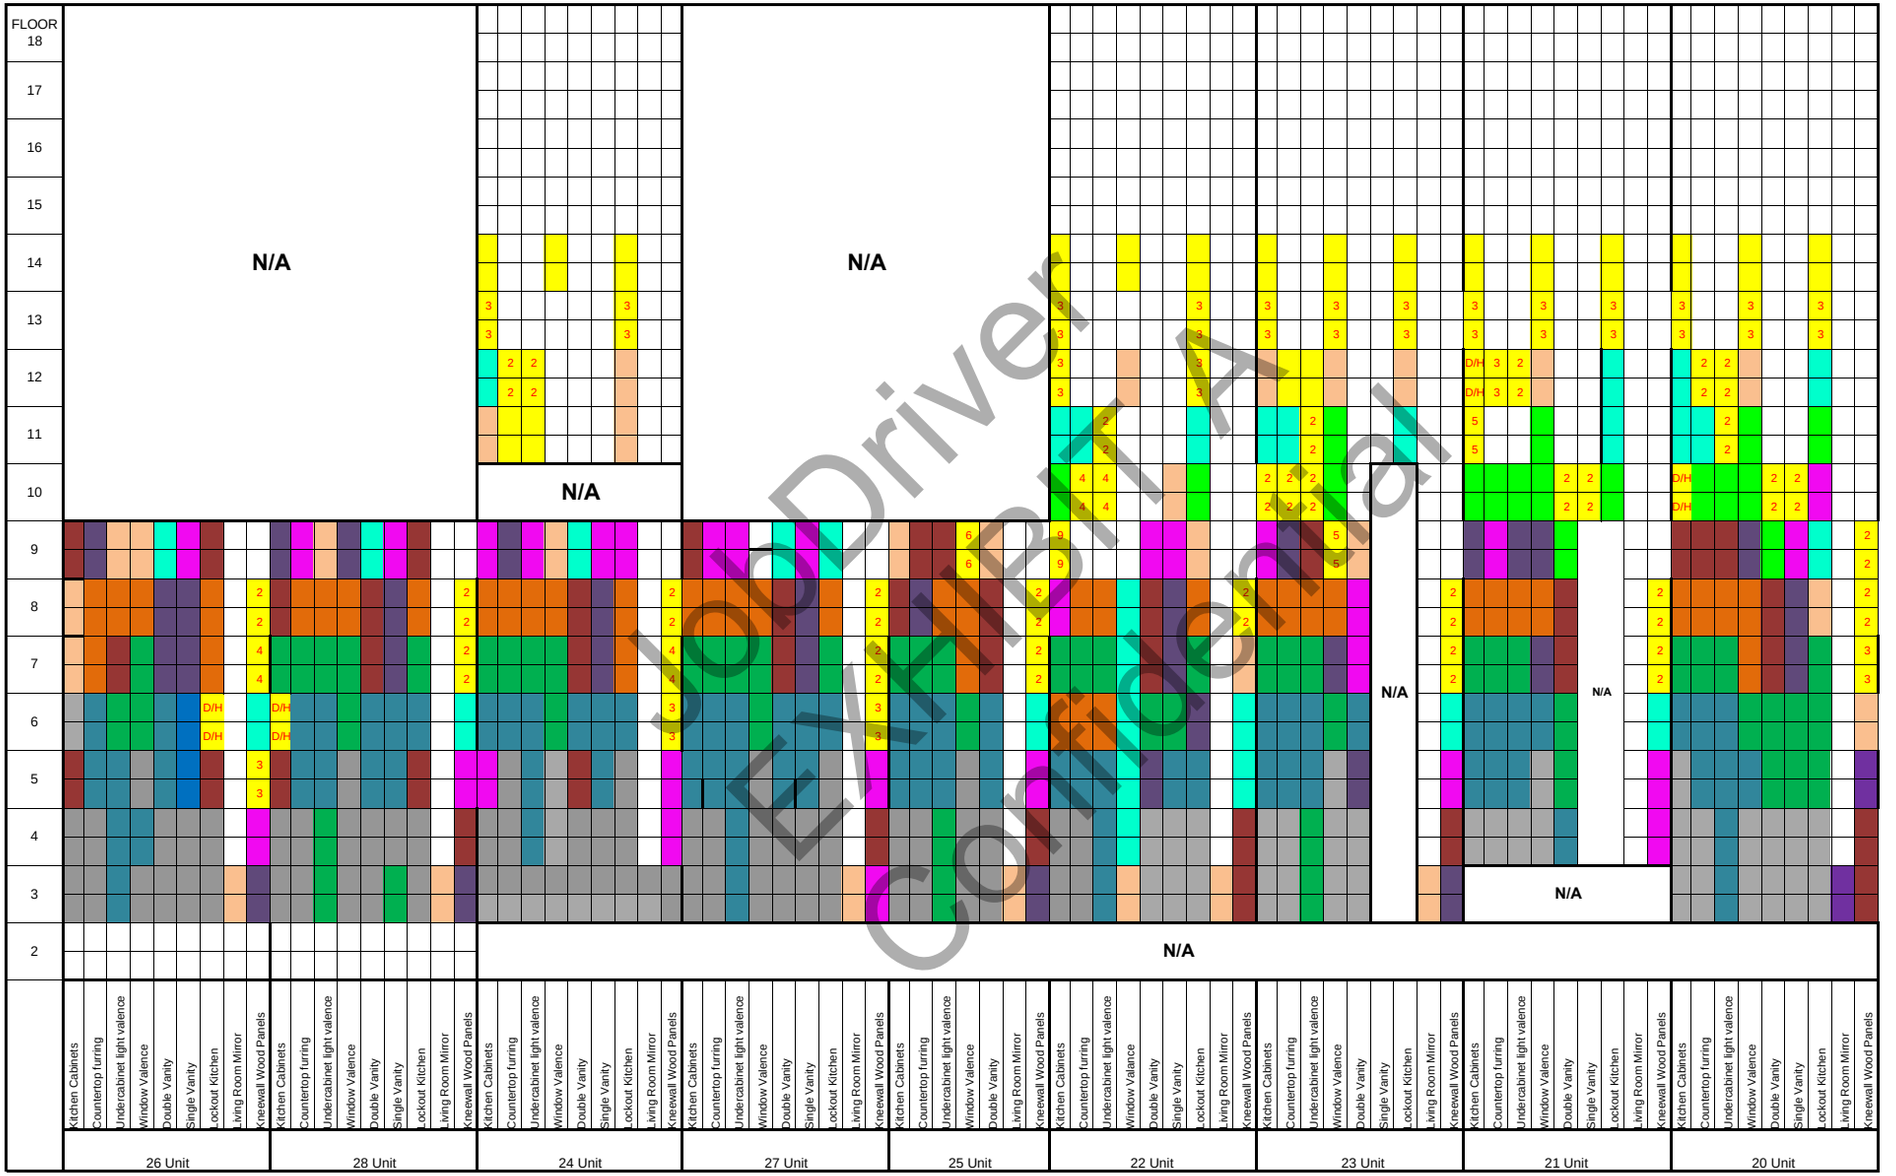

Job Driver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012

PREMIER MILLWORK PROGRESS CHART

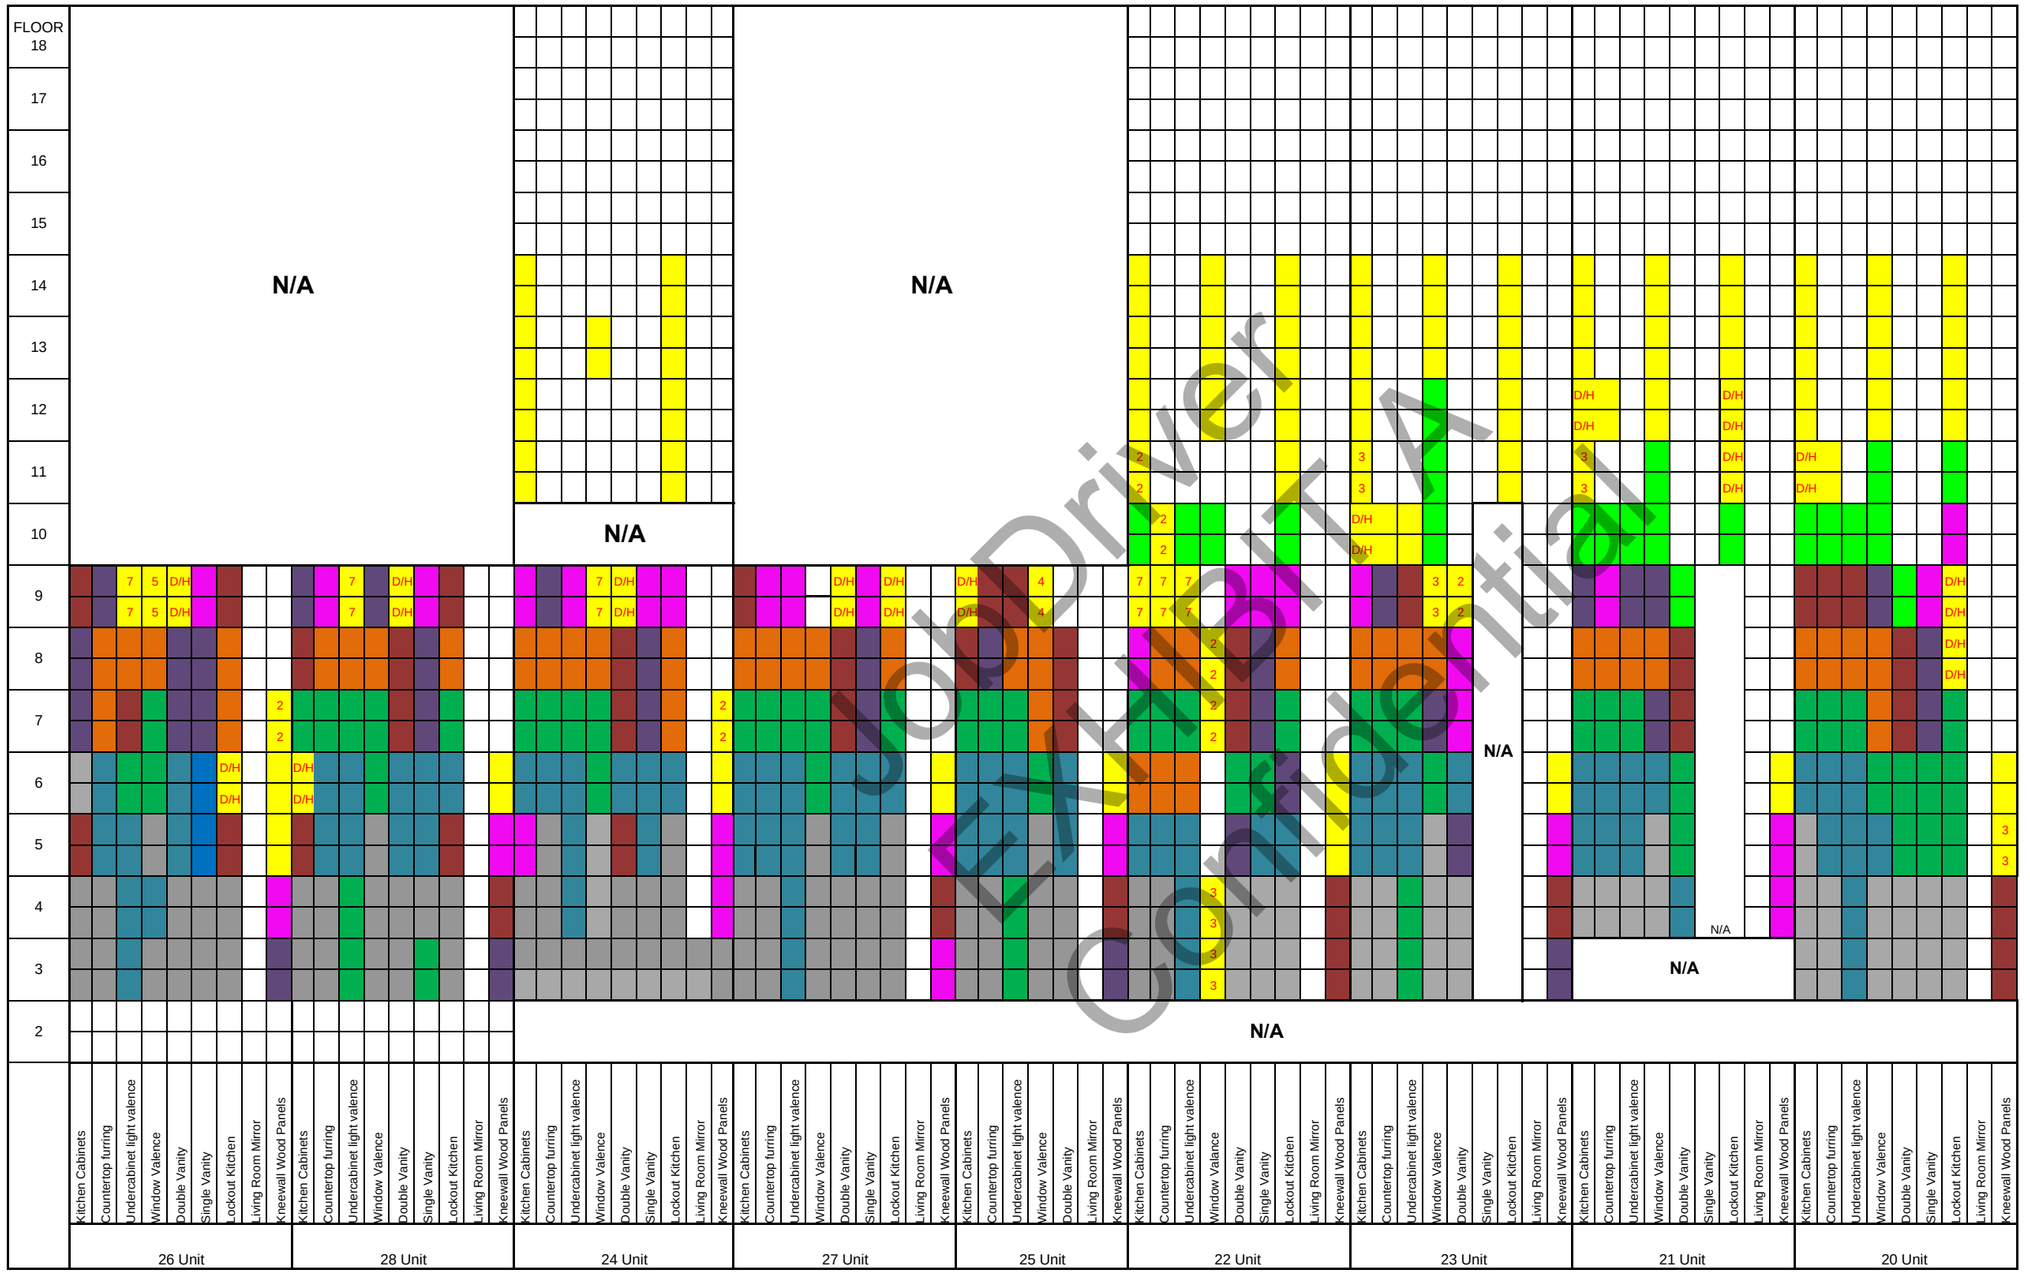

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012

PREMIER MILLWORK PROGRESS CHART

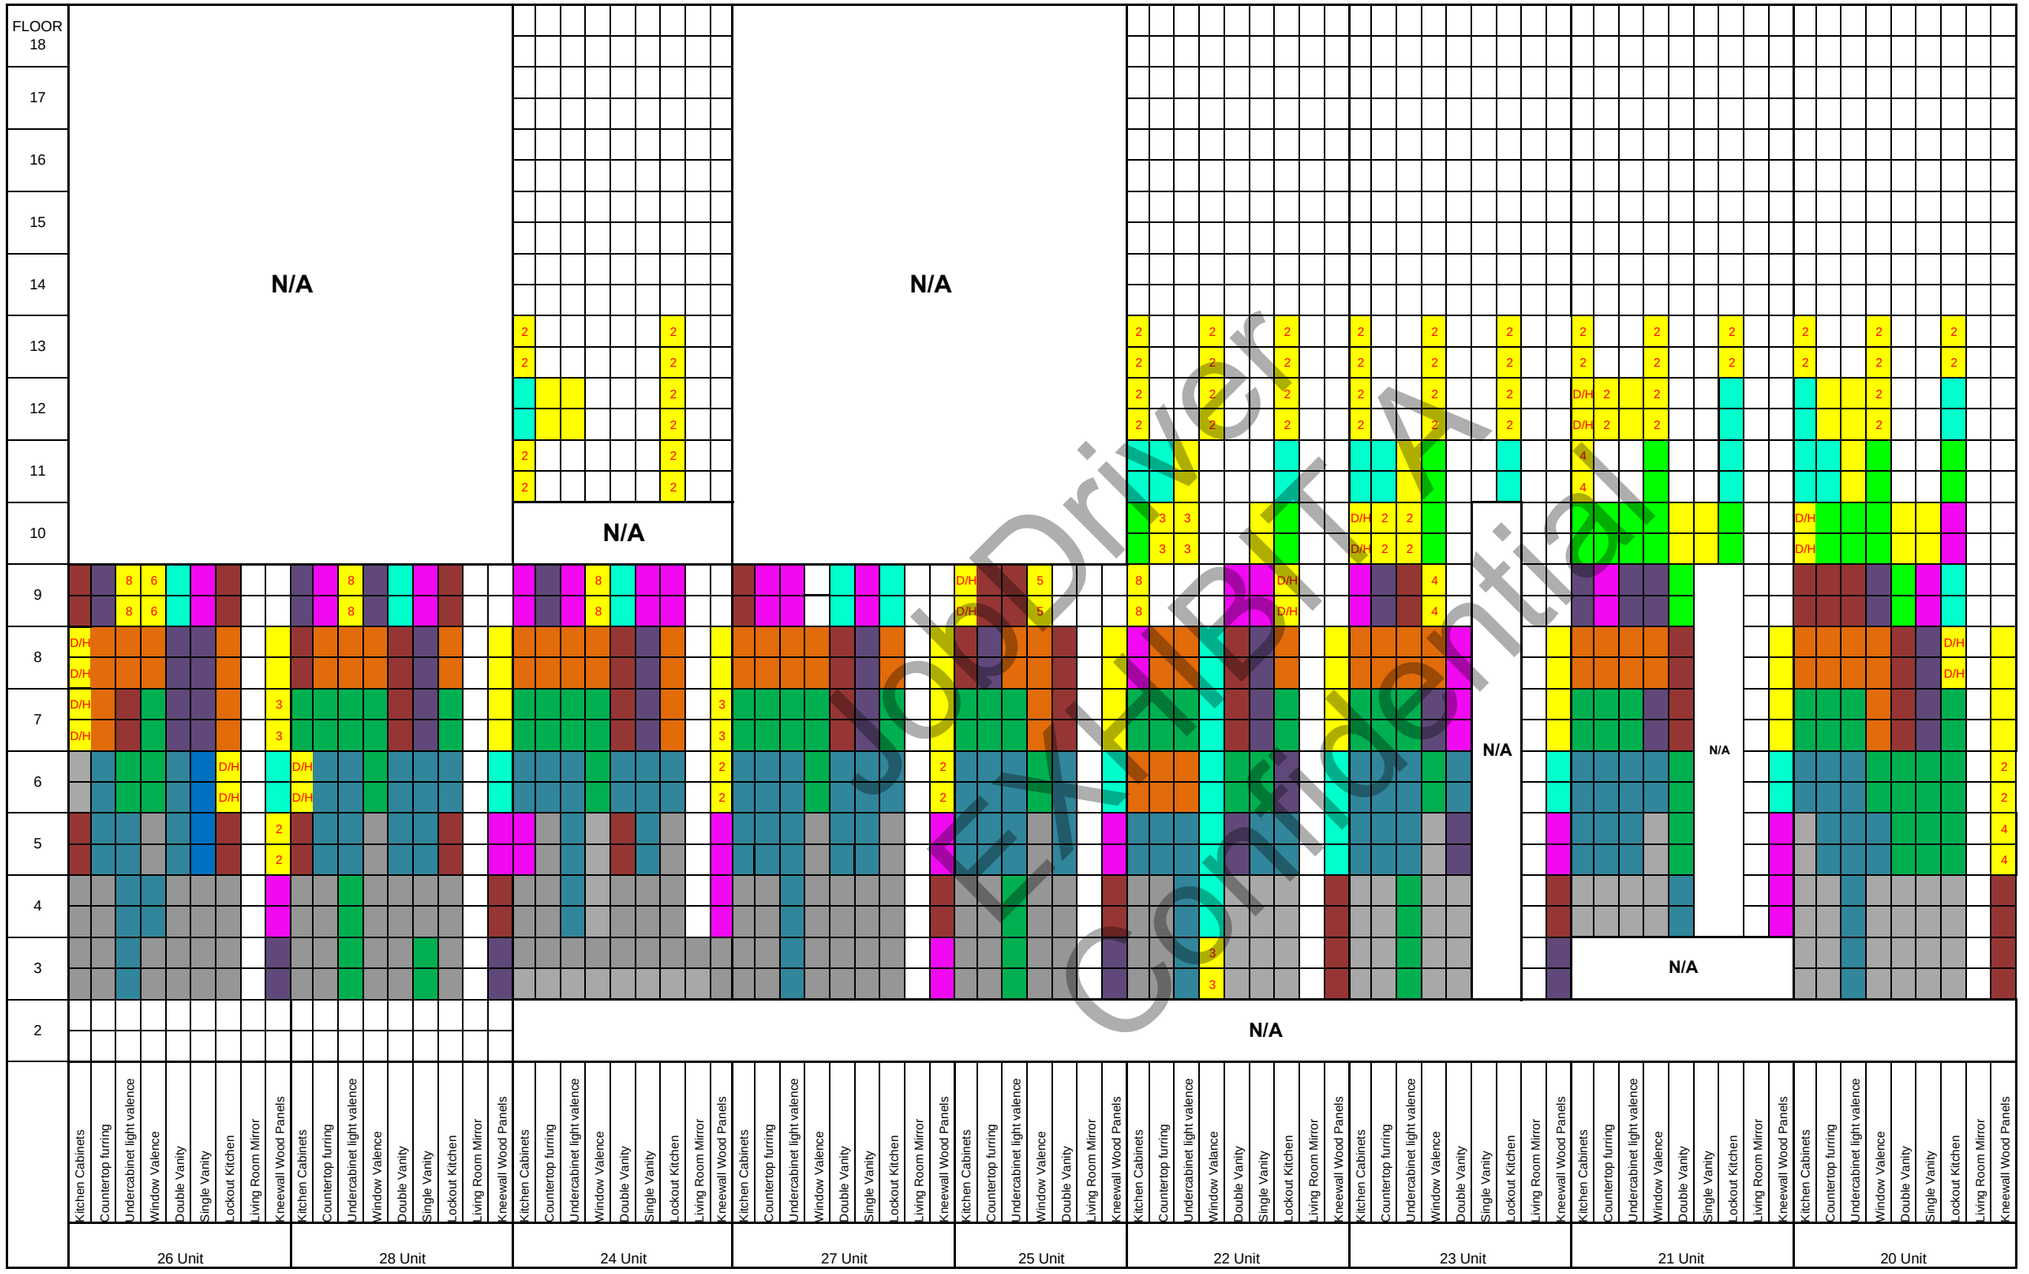

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012

PREMIER MILLWORK PROGRESS CHART

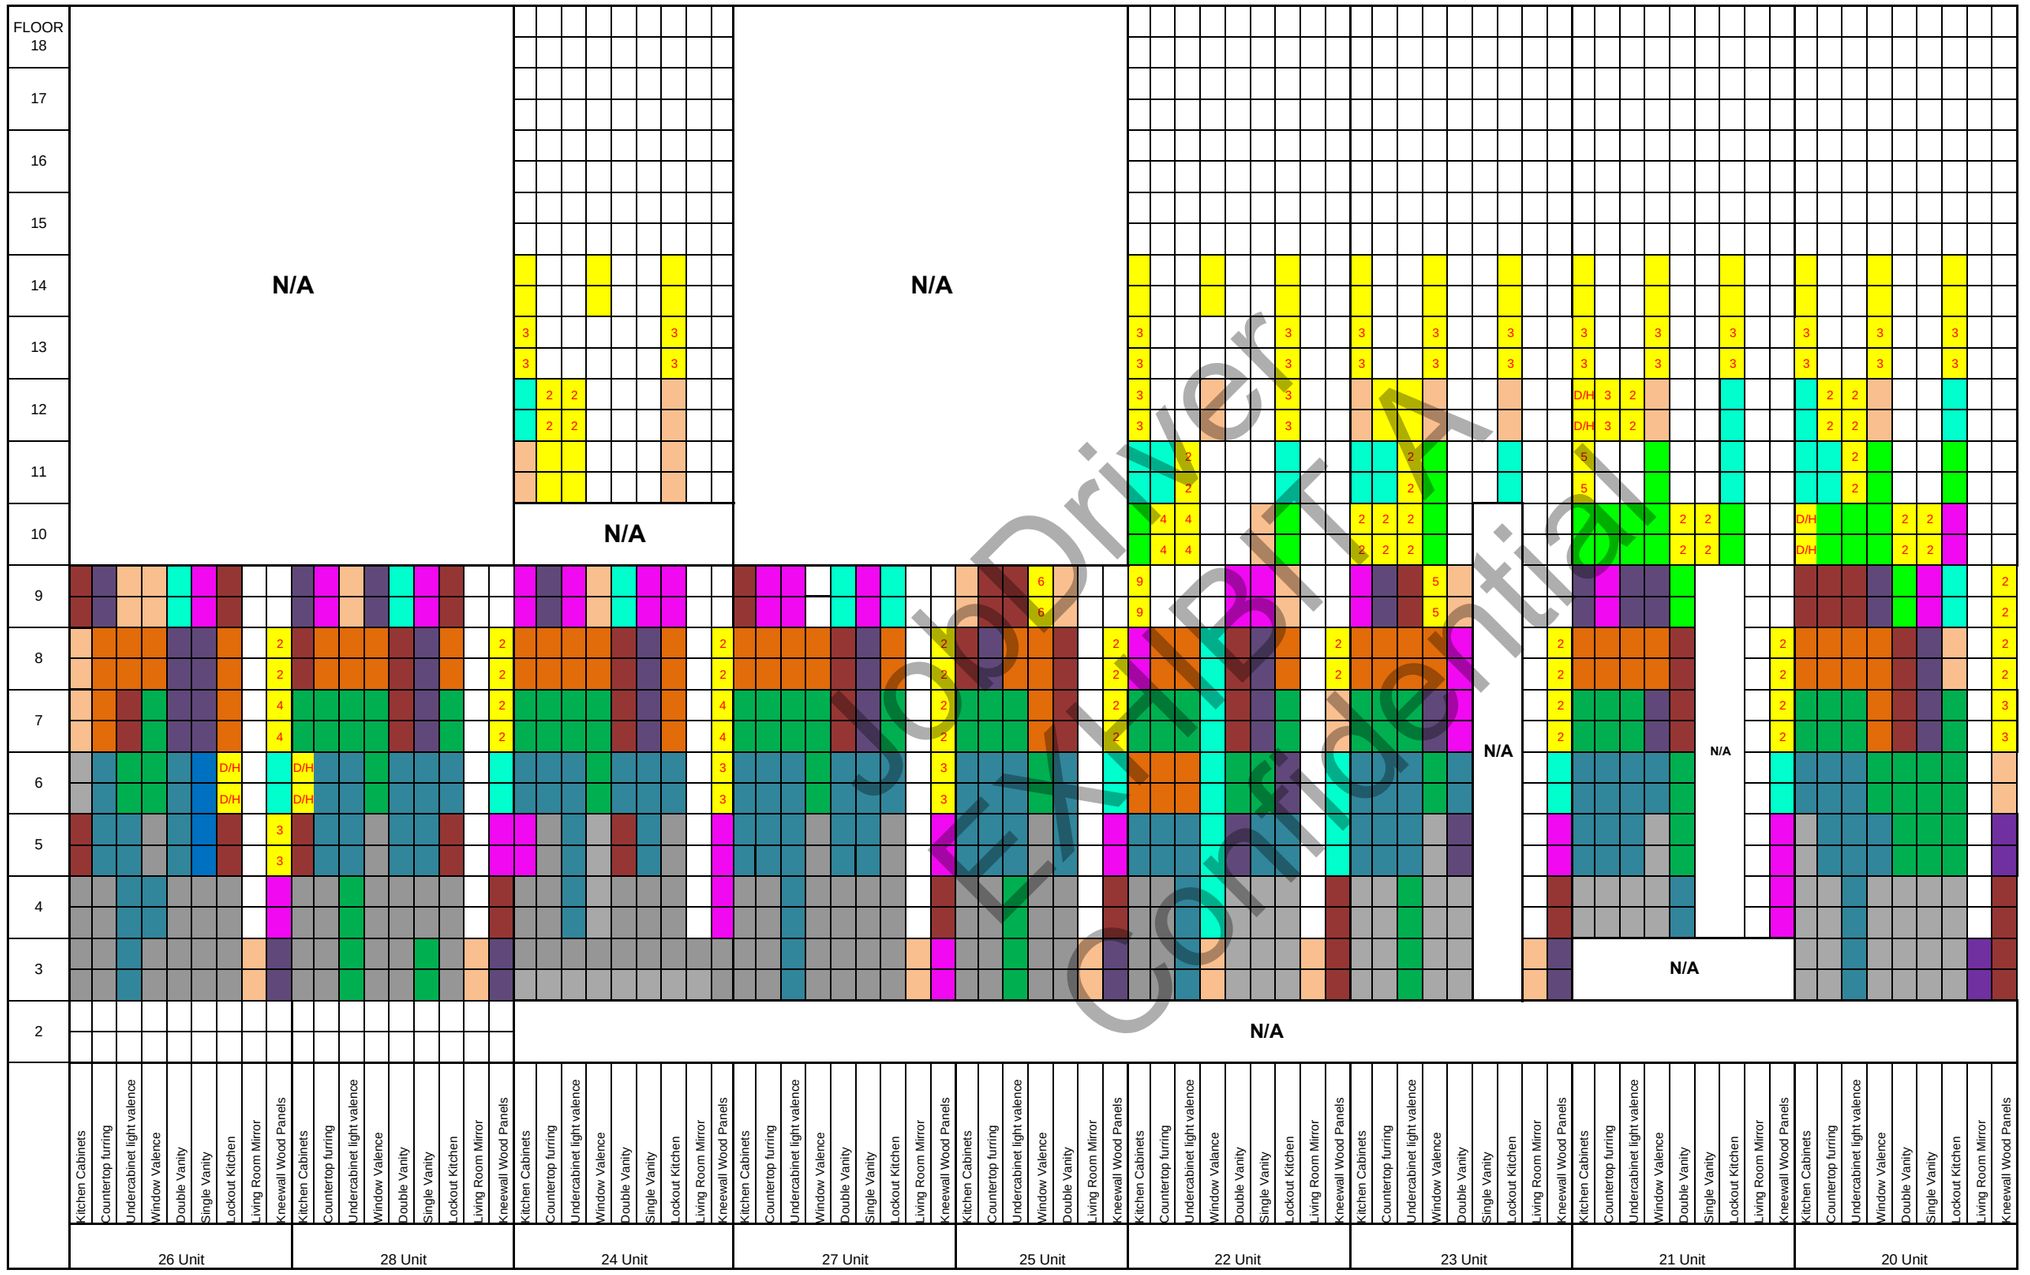

JobDriver
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012

PREMIER MILLWORK PROGRESS CHART

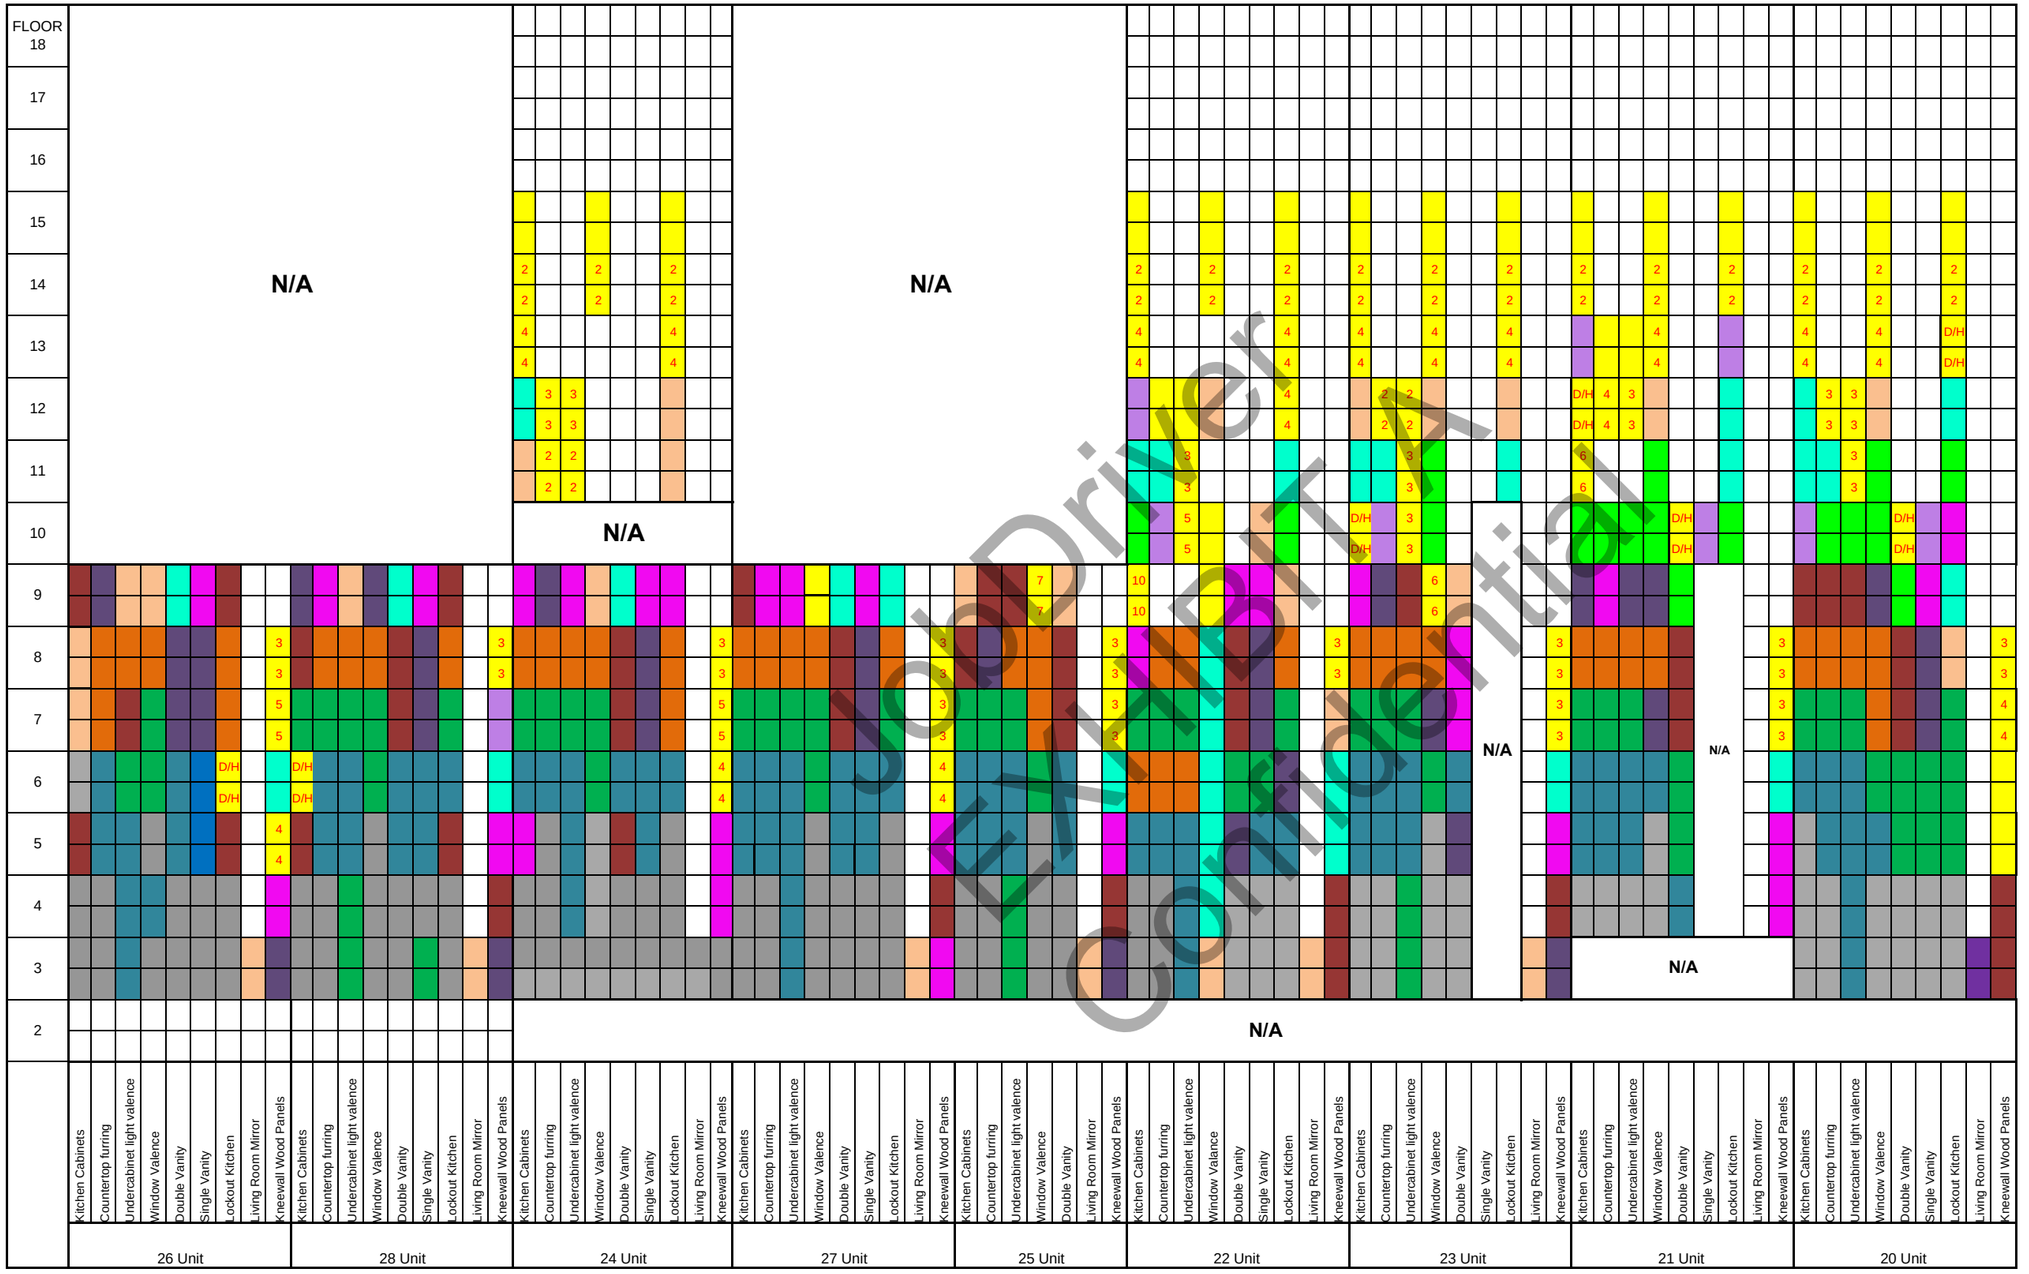

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012

PREMIER MILLWORK PROGRESS CHART

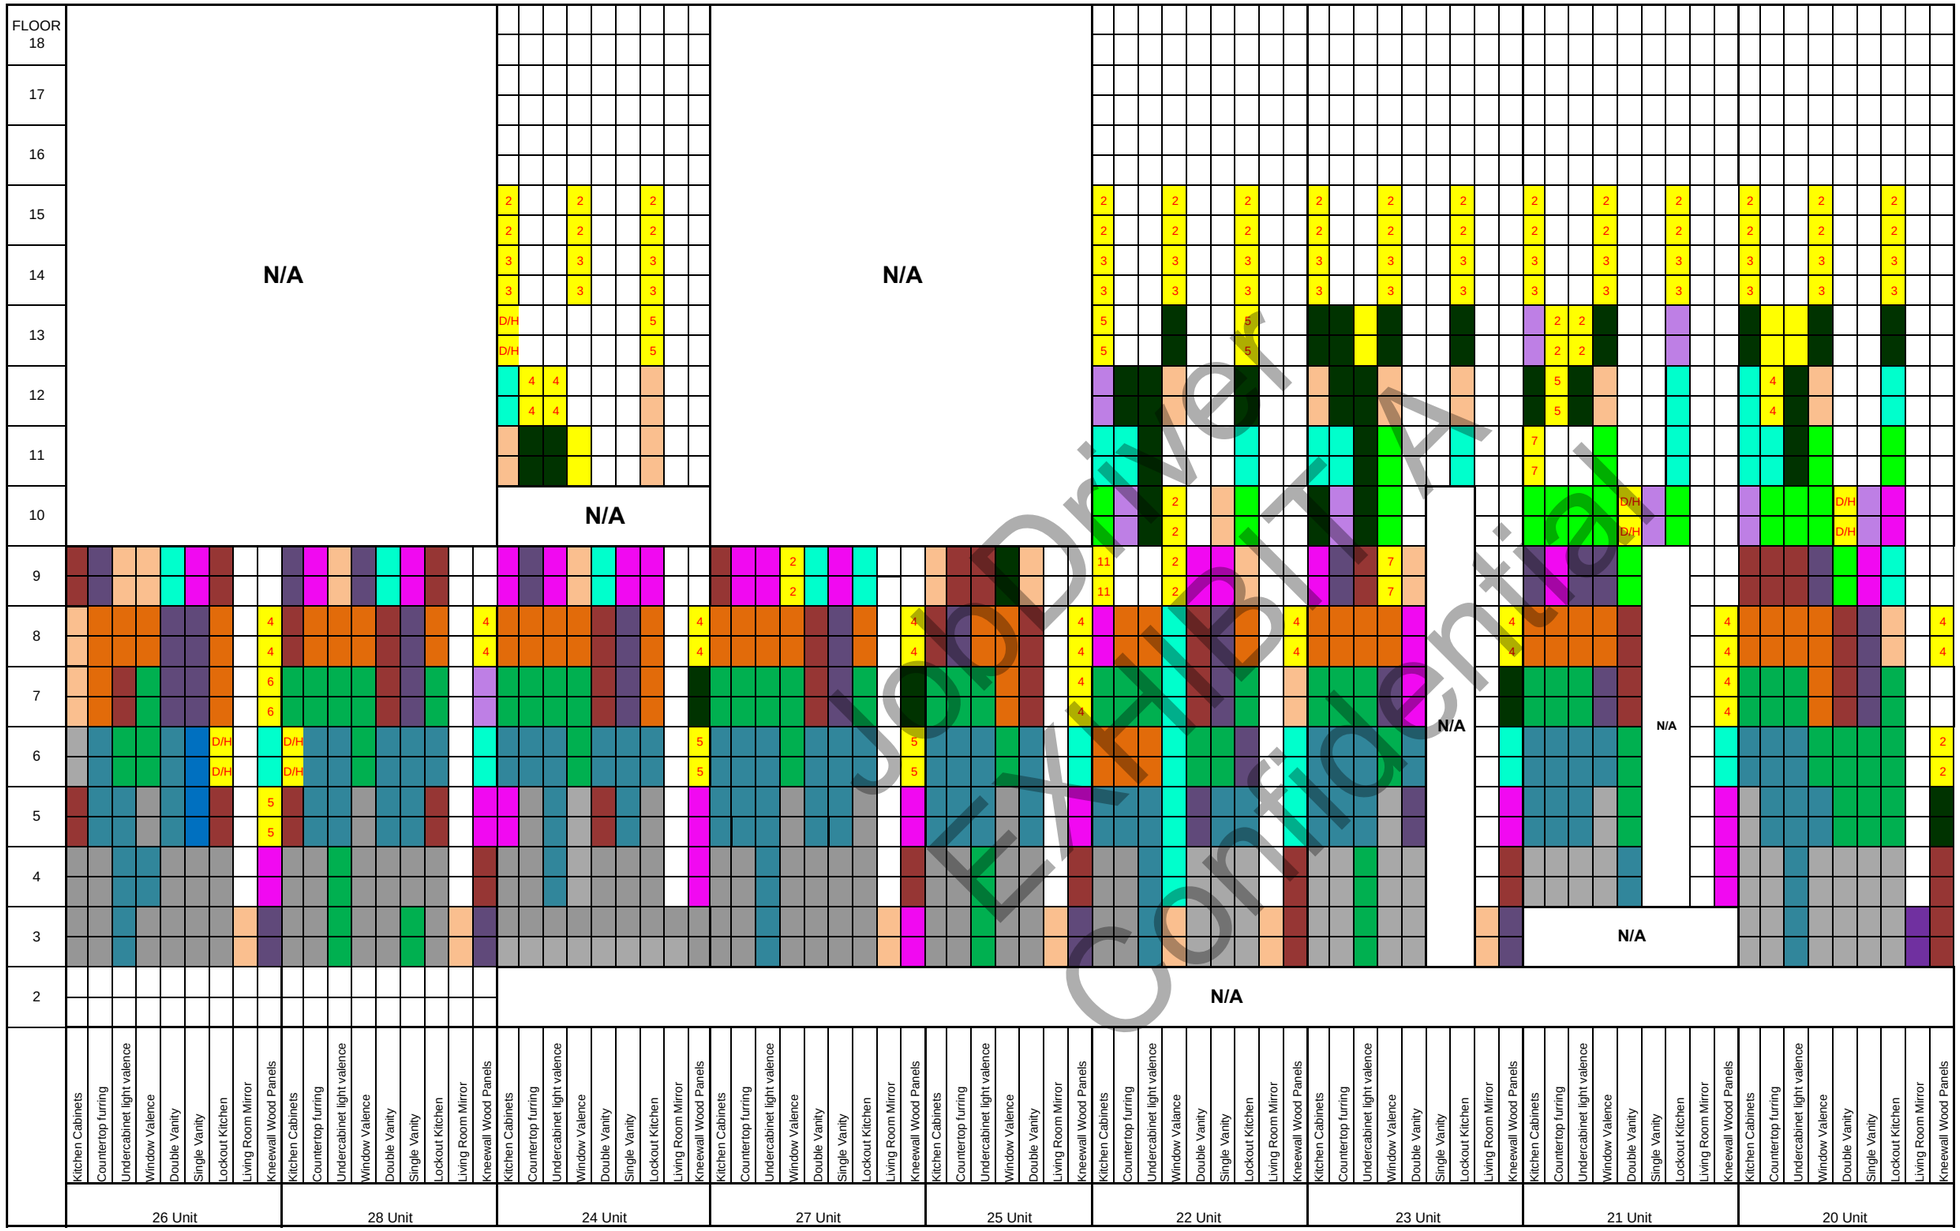

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012

PREMIER MILLWORK PROGRESS CHART

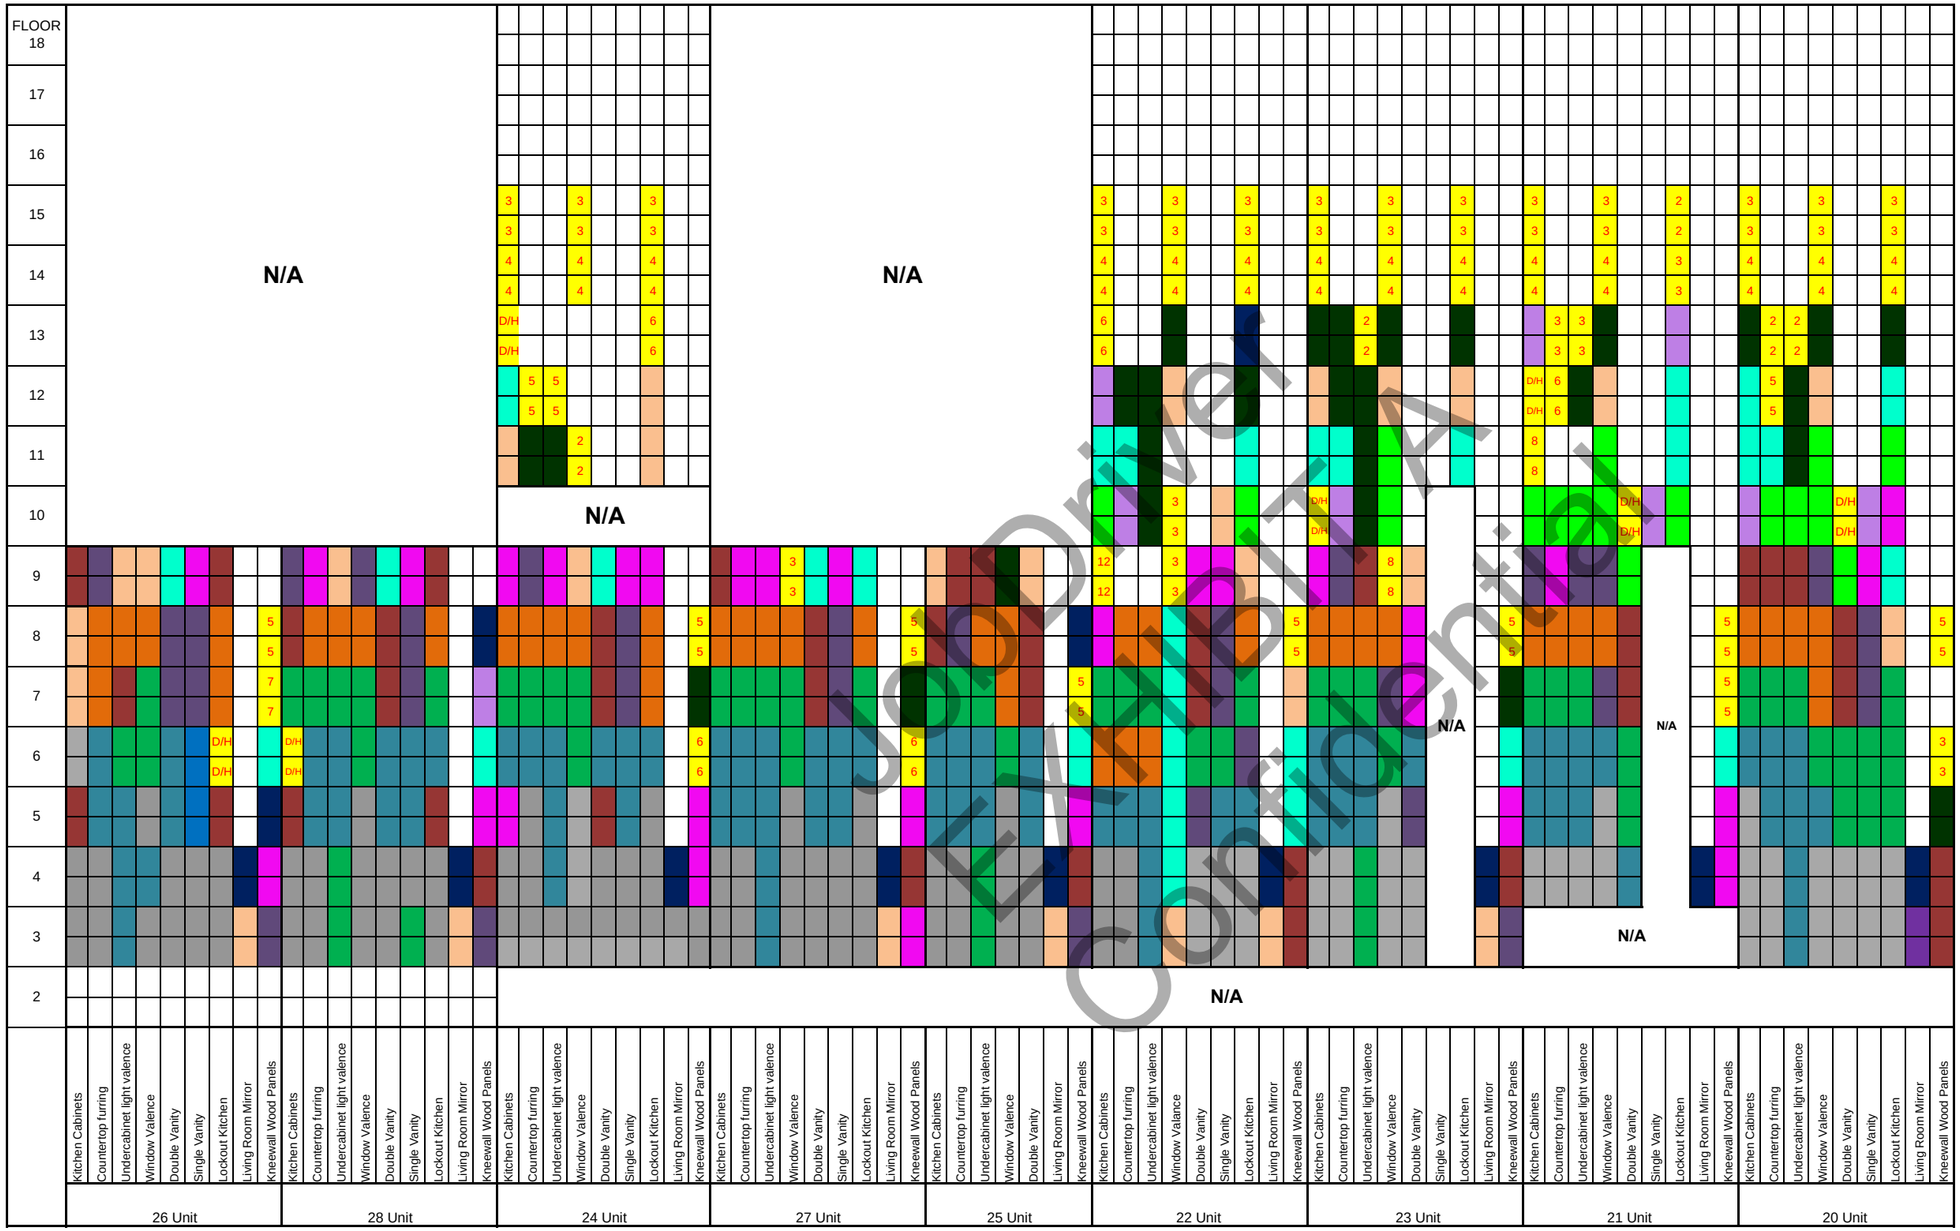

JobDrive EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012

PREMIER MILLWORK PROGRESS CHART

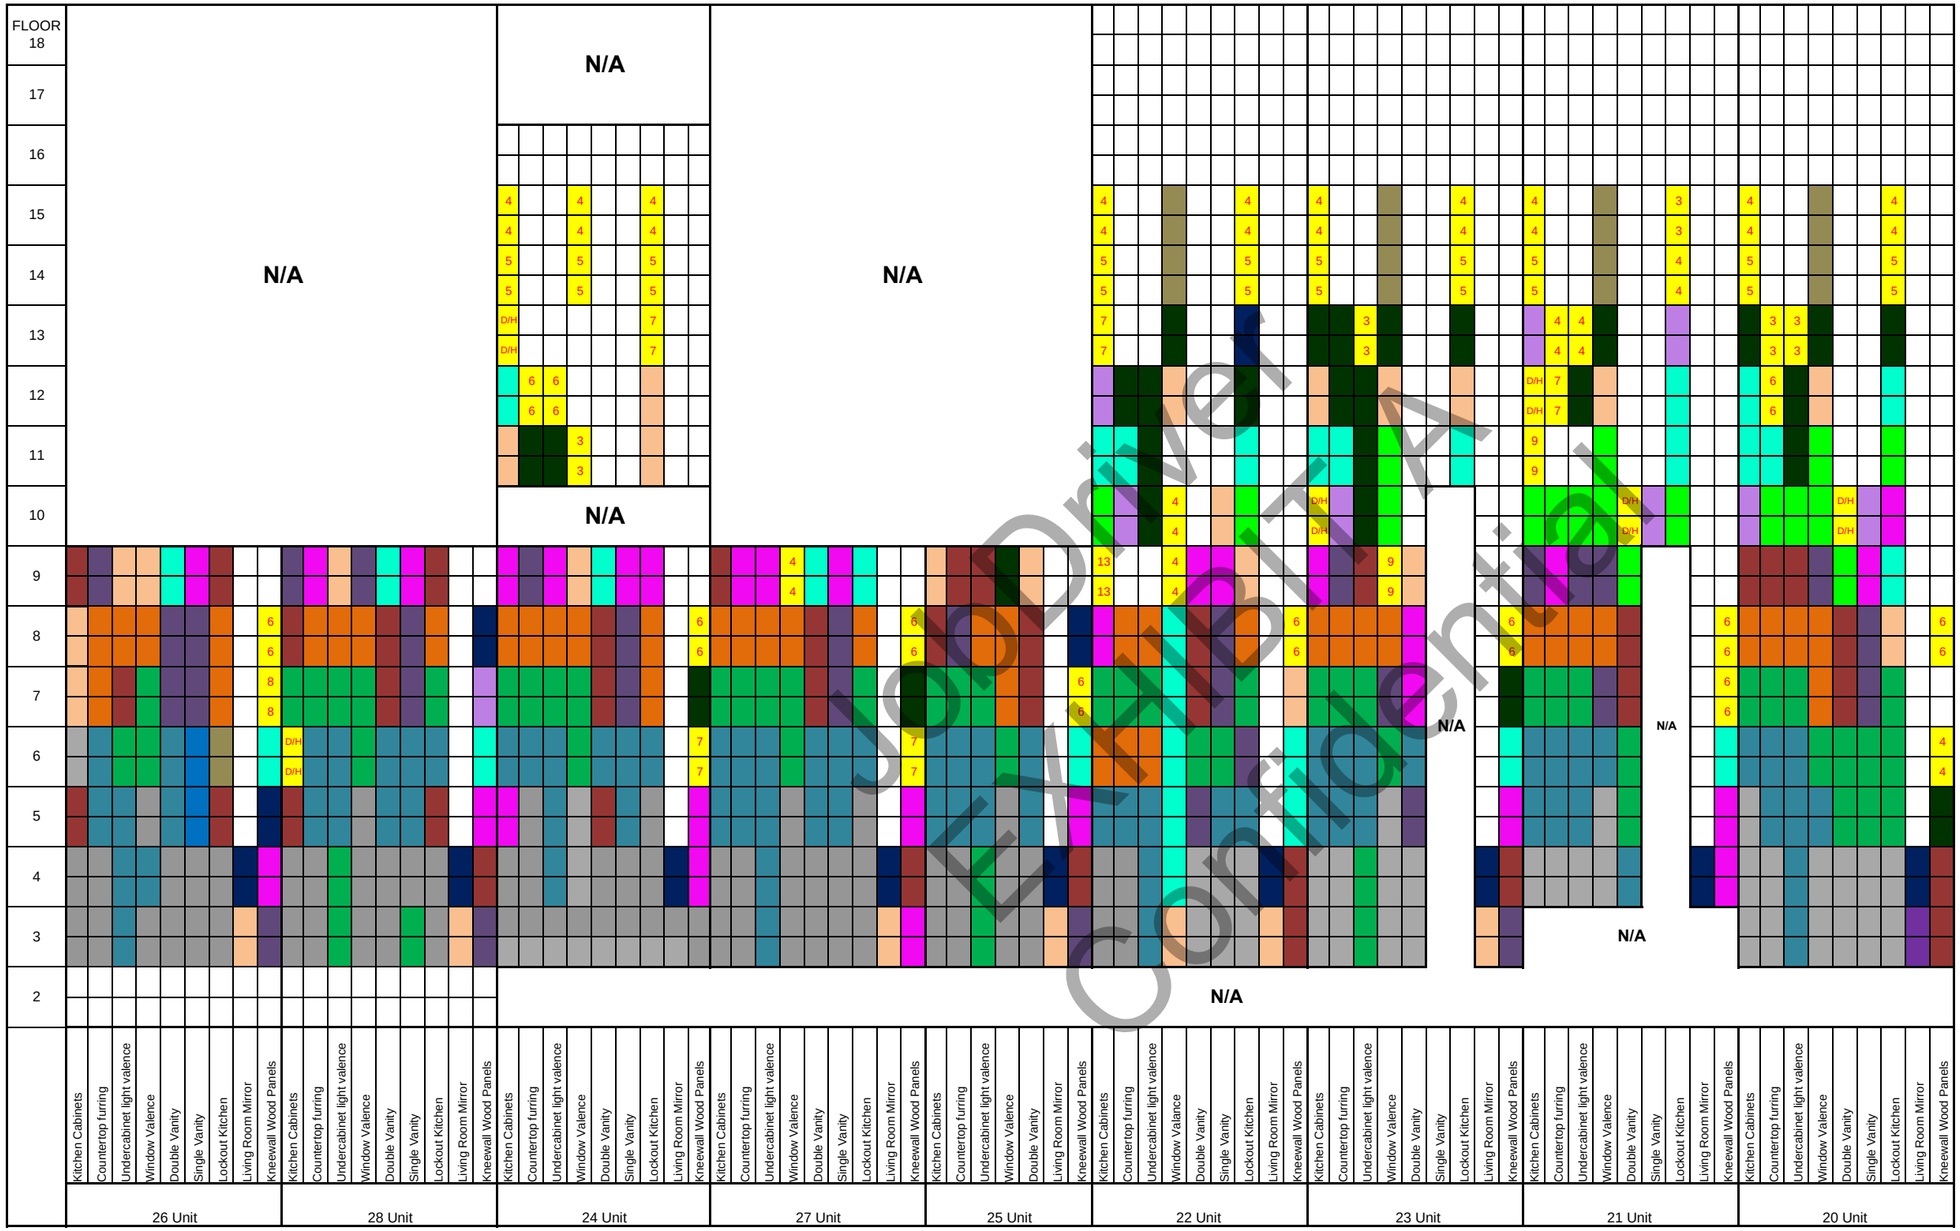

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012

PREMIER MILLWORK PROGRESS CHART

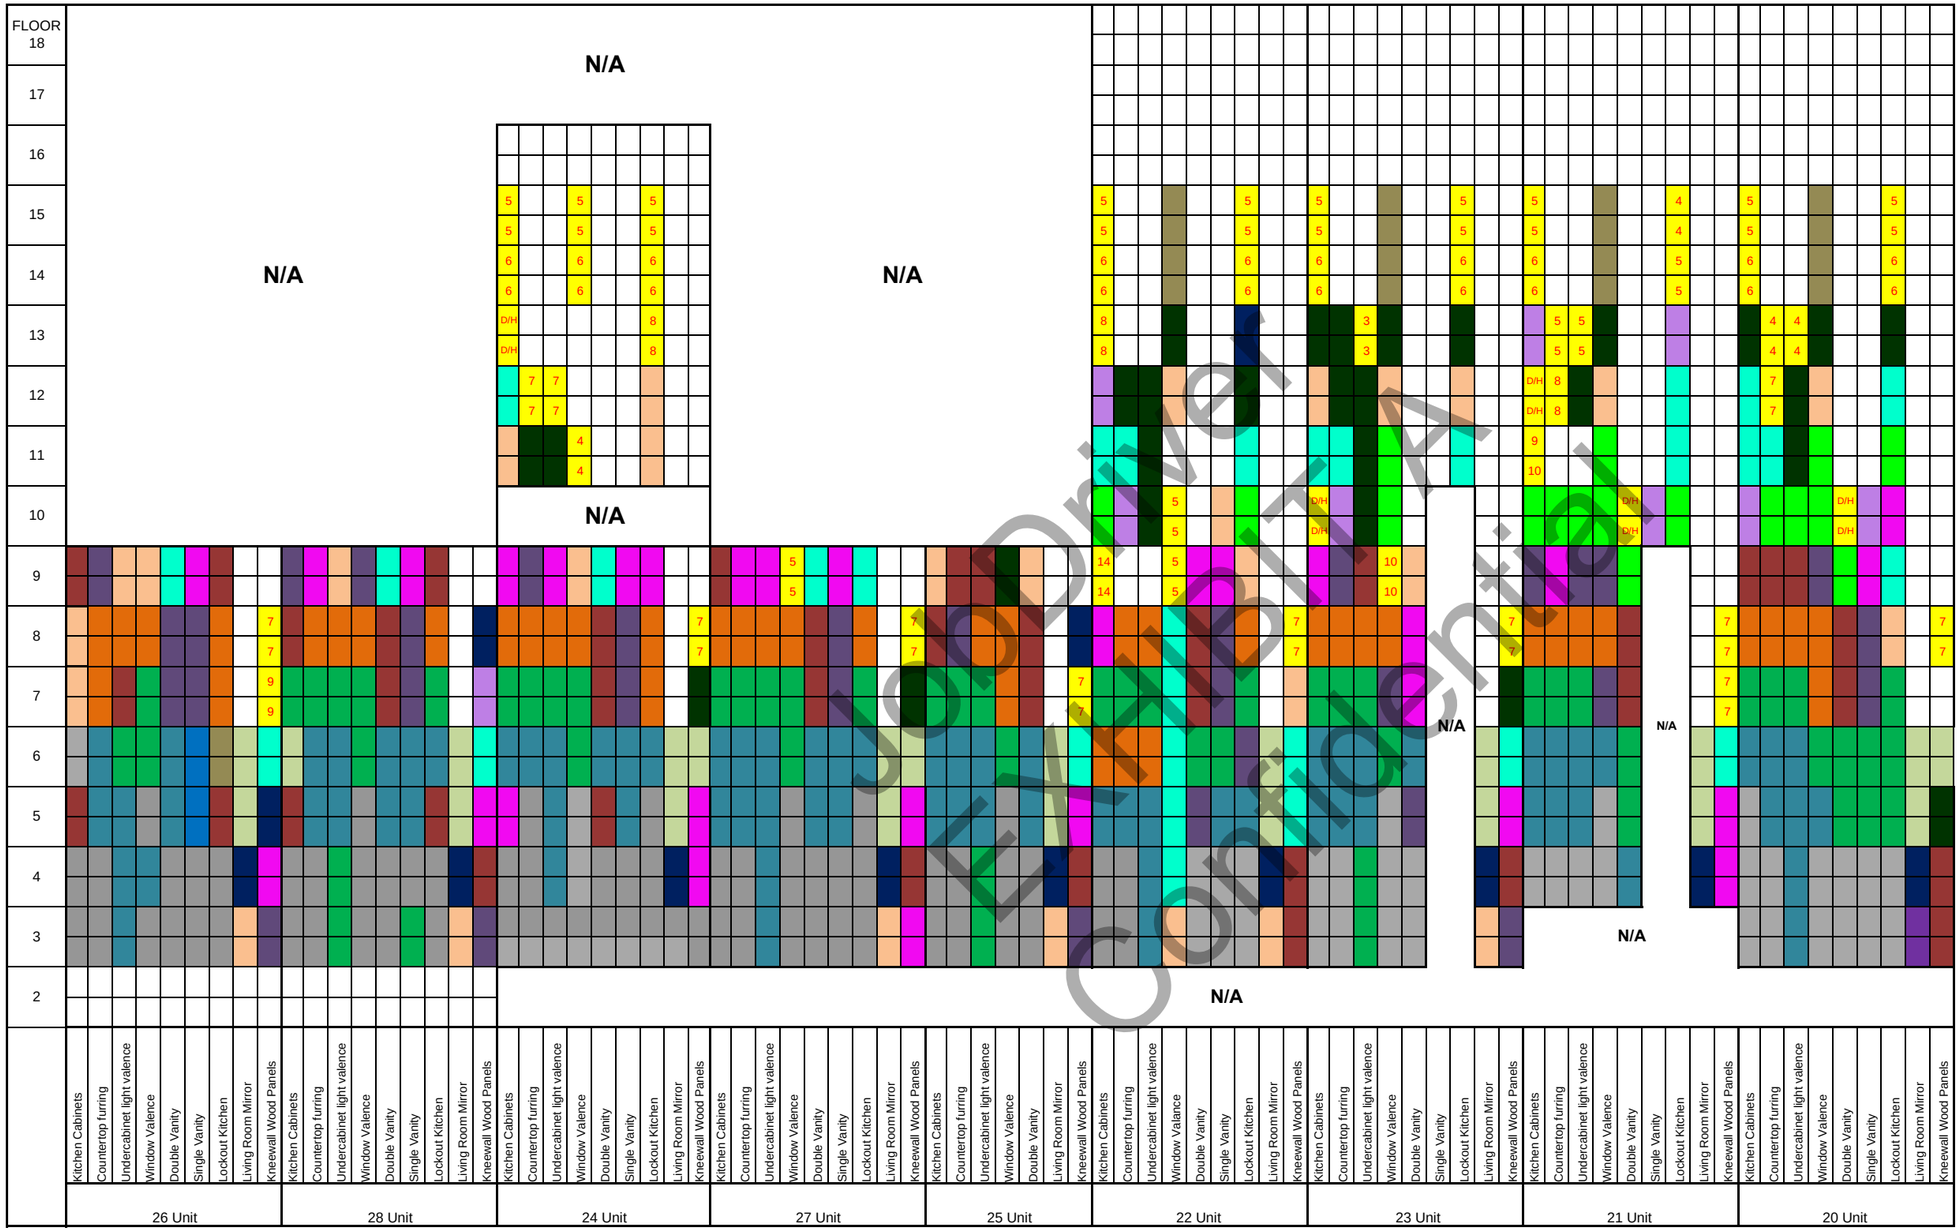

JobDrive EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012

PREMIER MILLWORK PROGRESS CHART

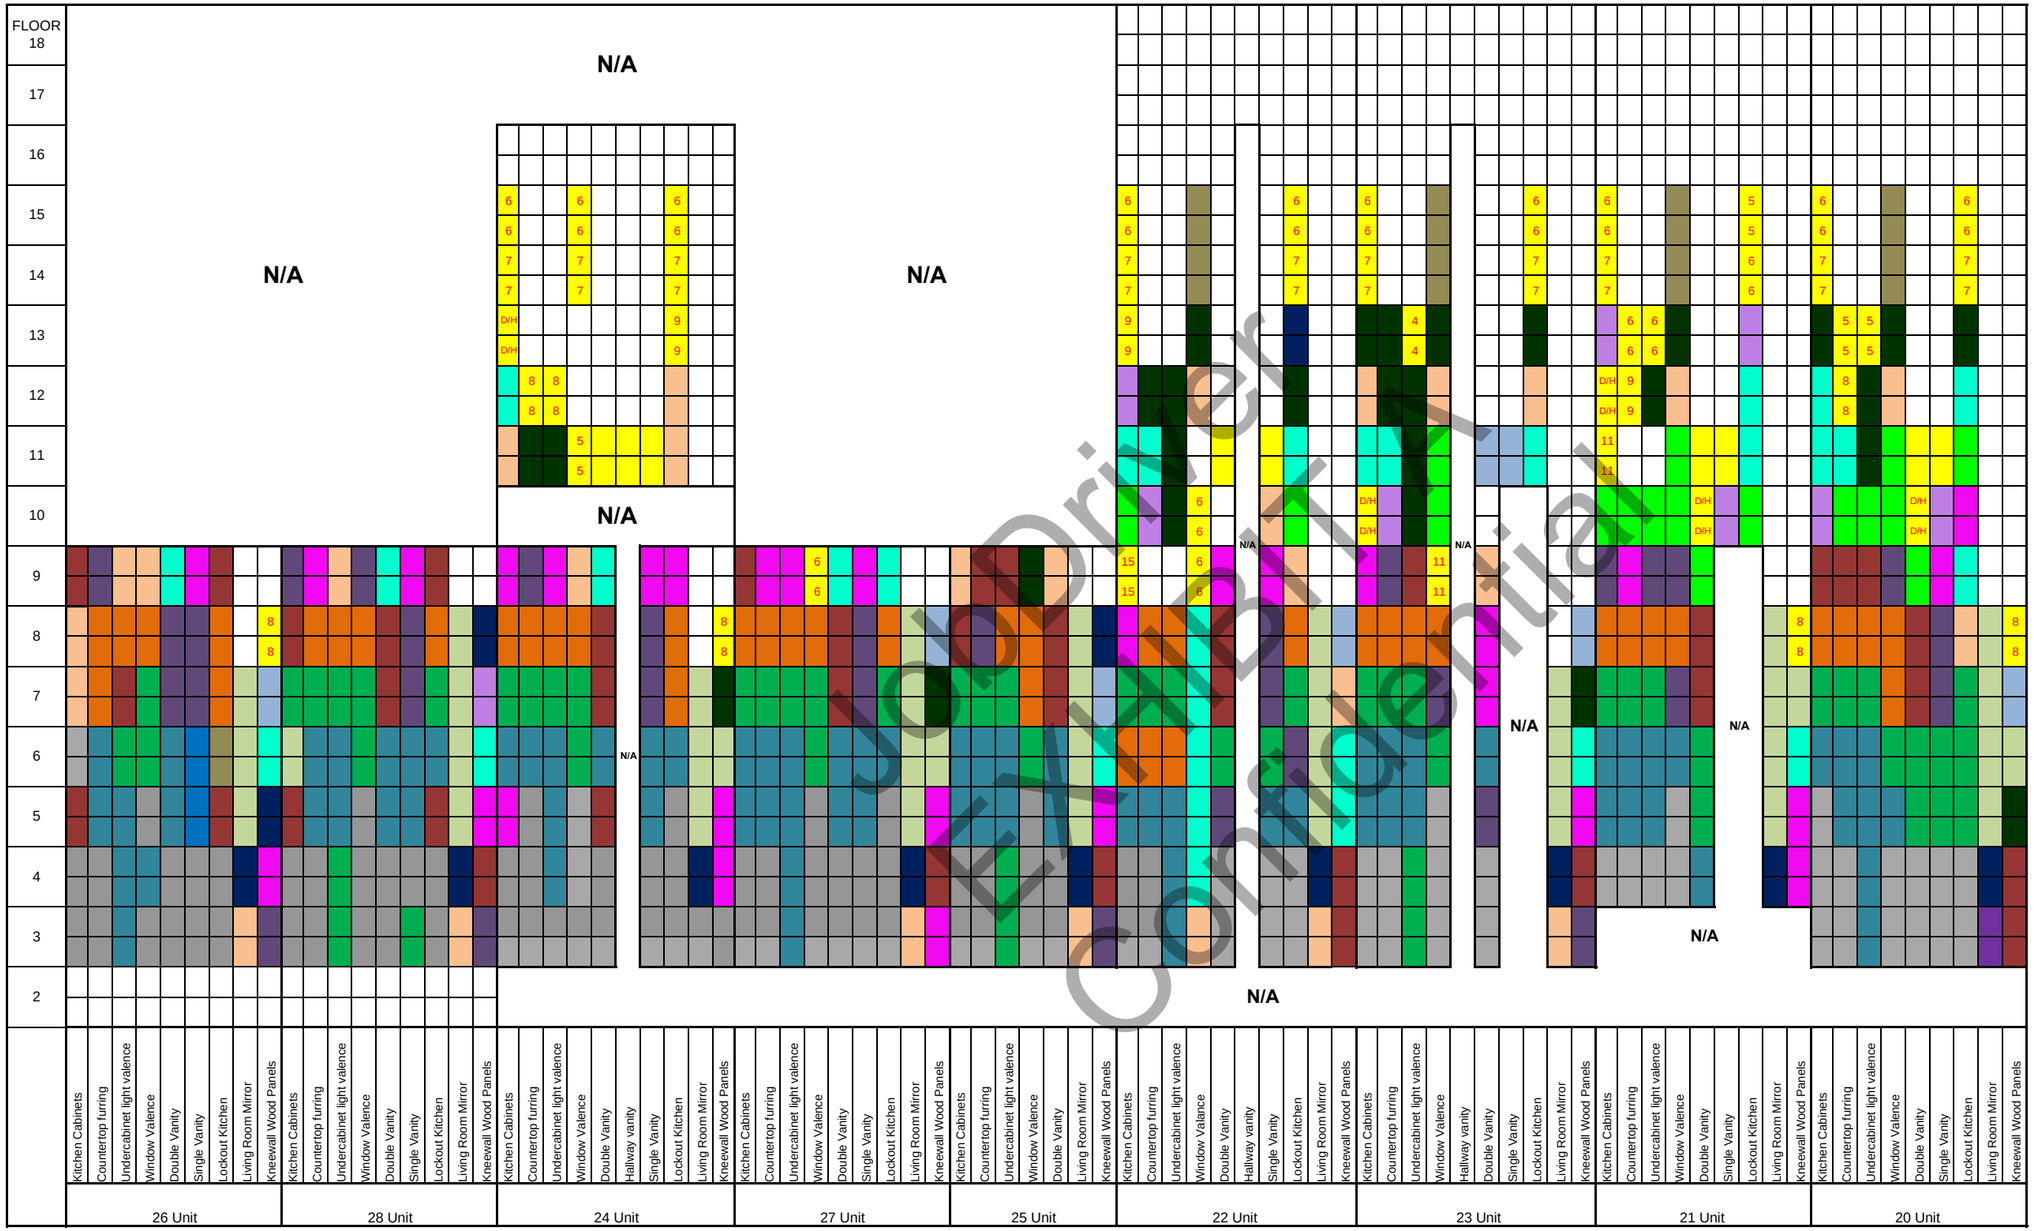

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM

PREMIER MILLWORK PROGRESS CHART

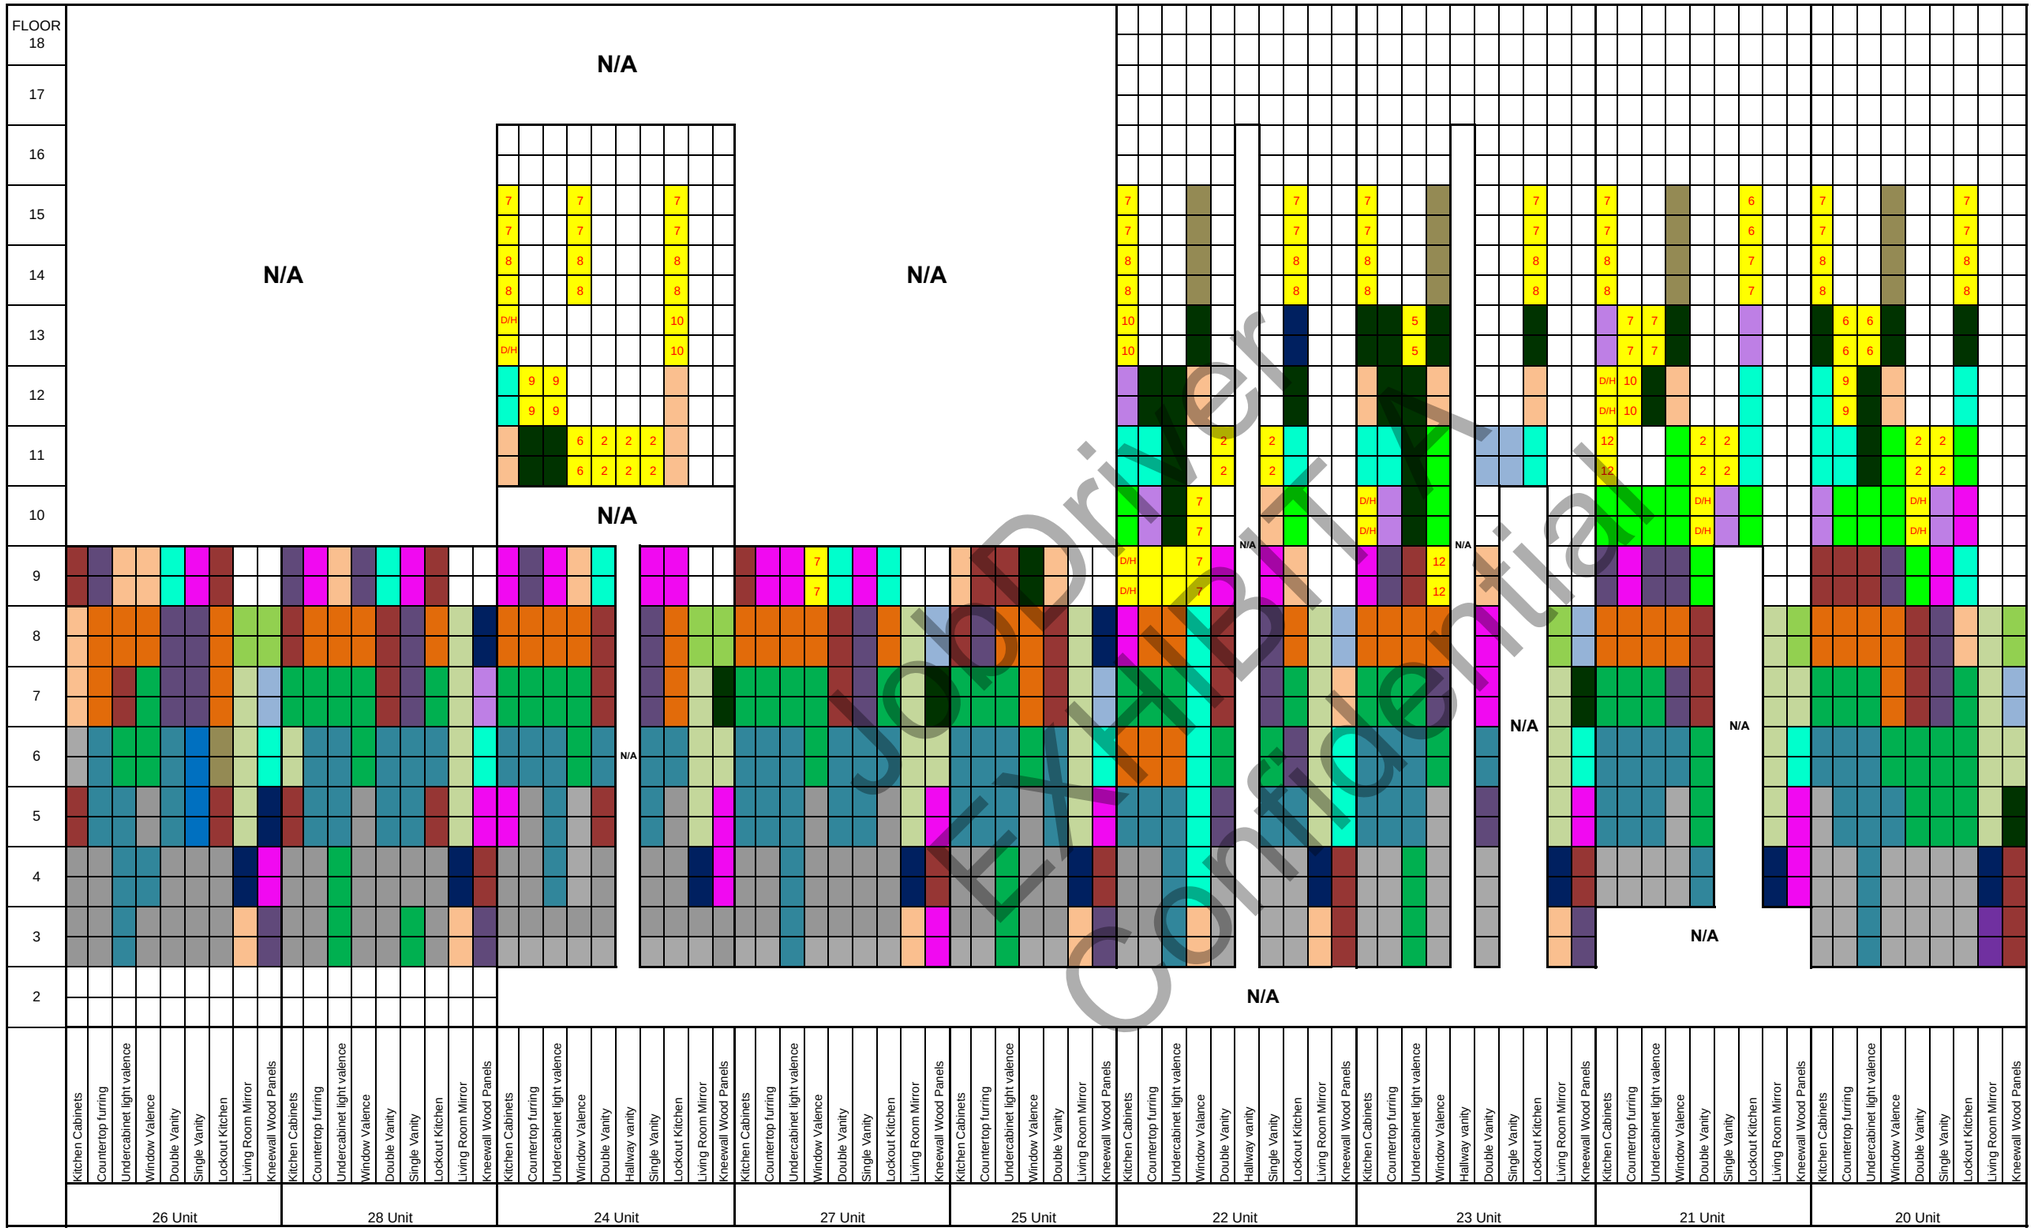

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012

Top Driver EXHIBIT A Confidential

PREMIER MILLWORK PROGRESS CHART

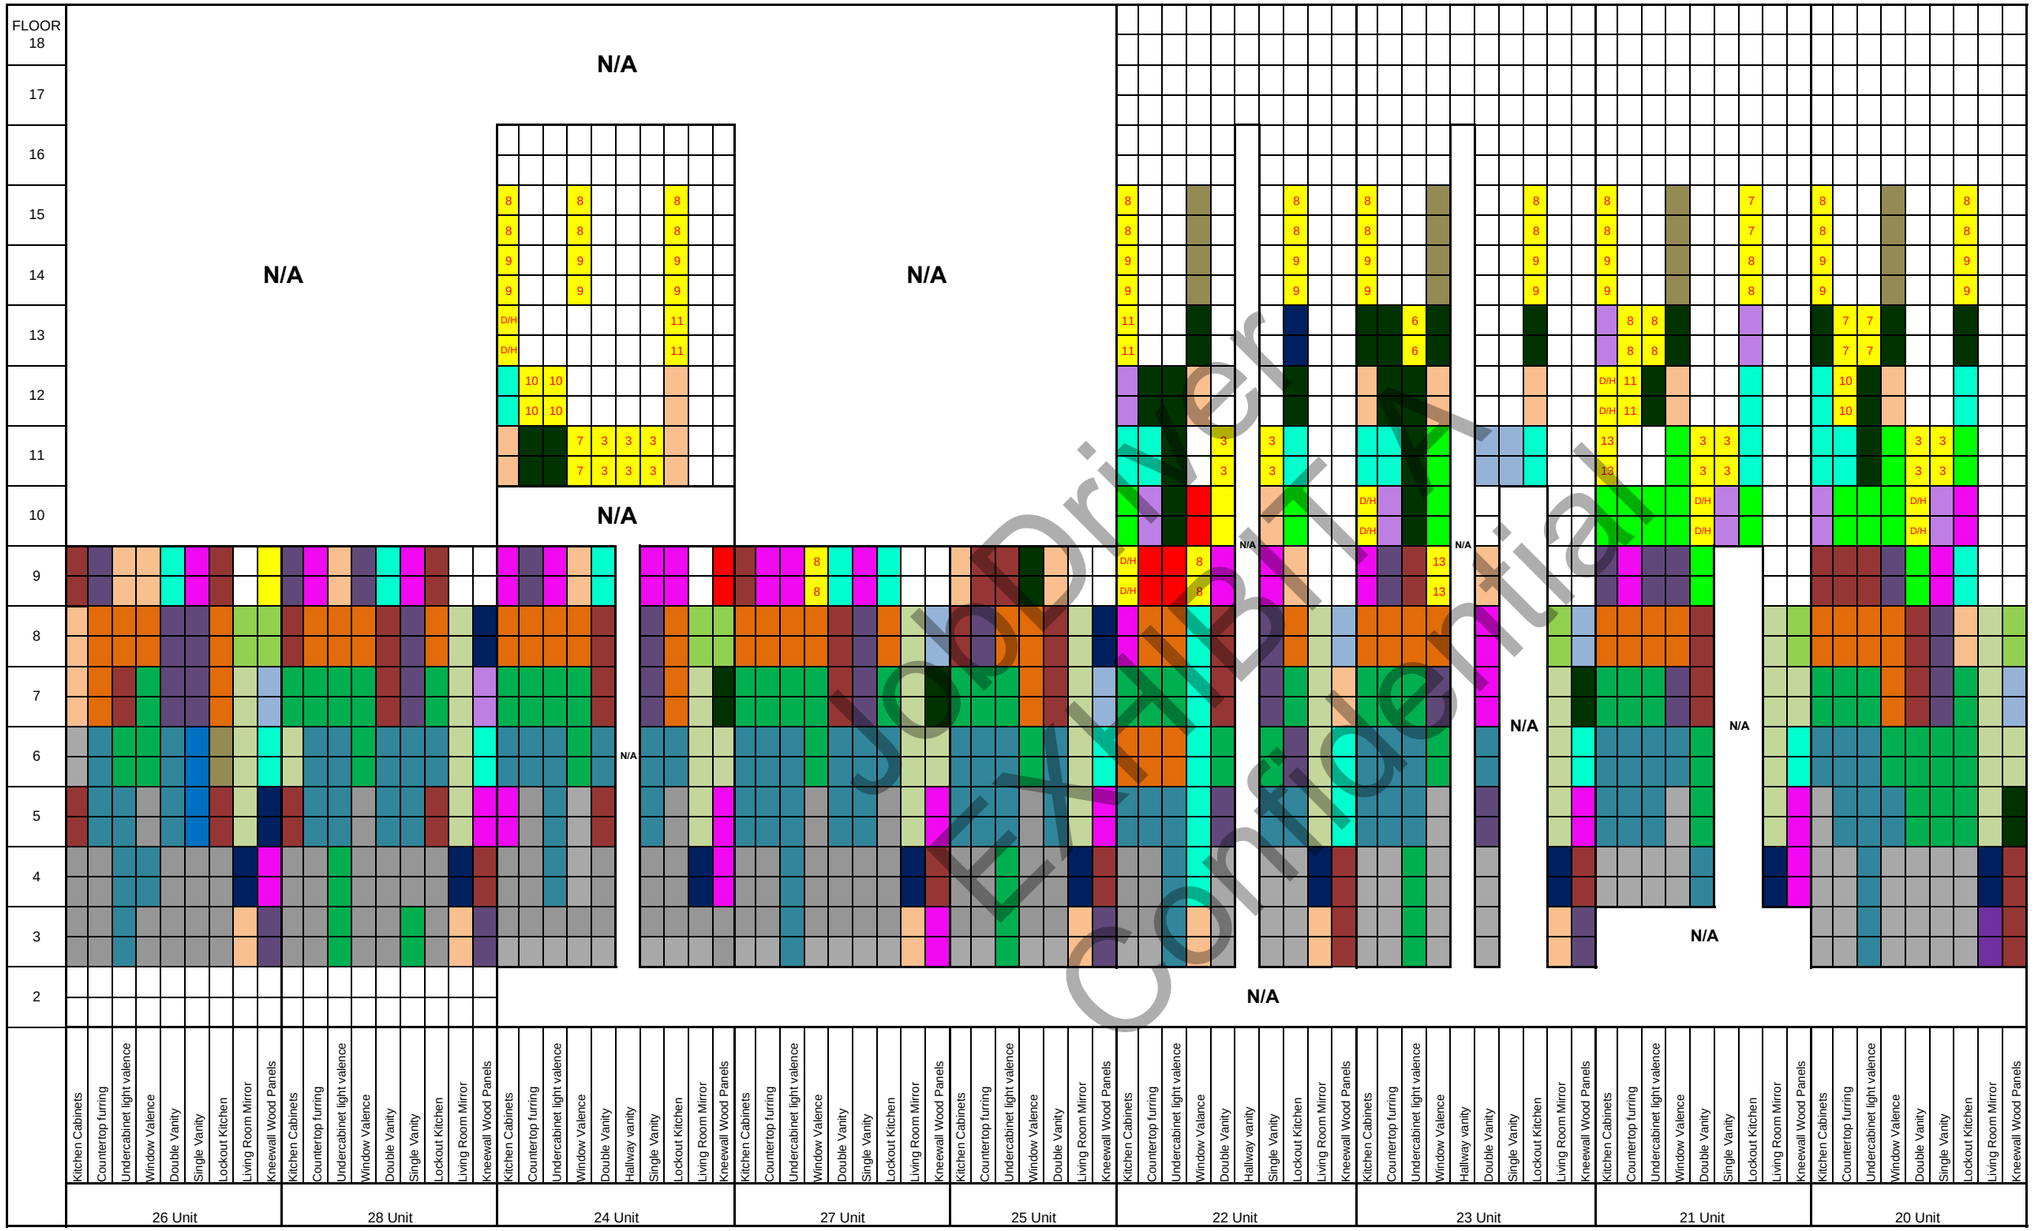

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012

Top Driver
EXHIBIT A
Confidential

PREMIER MILLWORK PROGRESS CHART

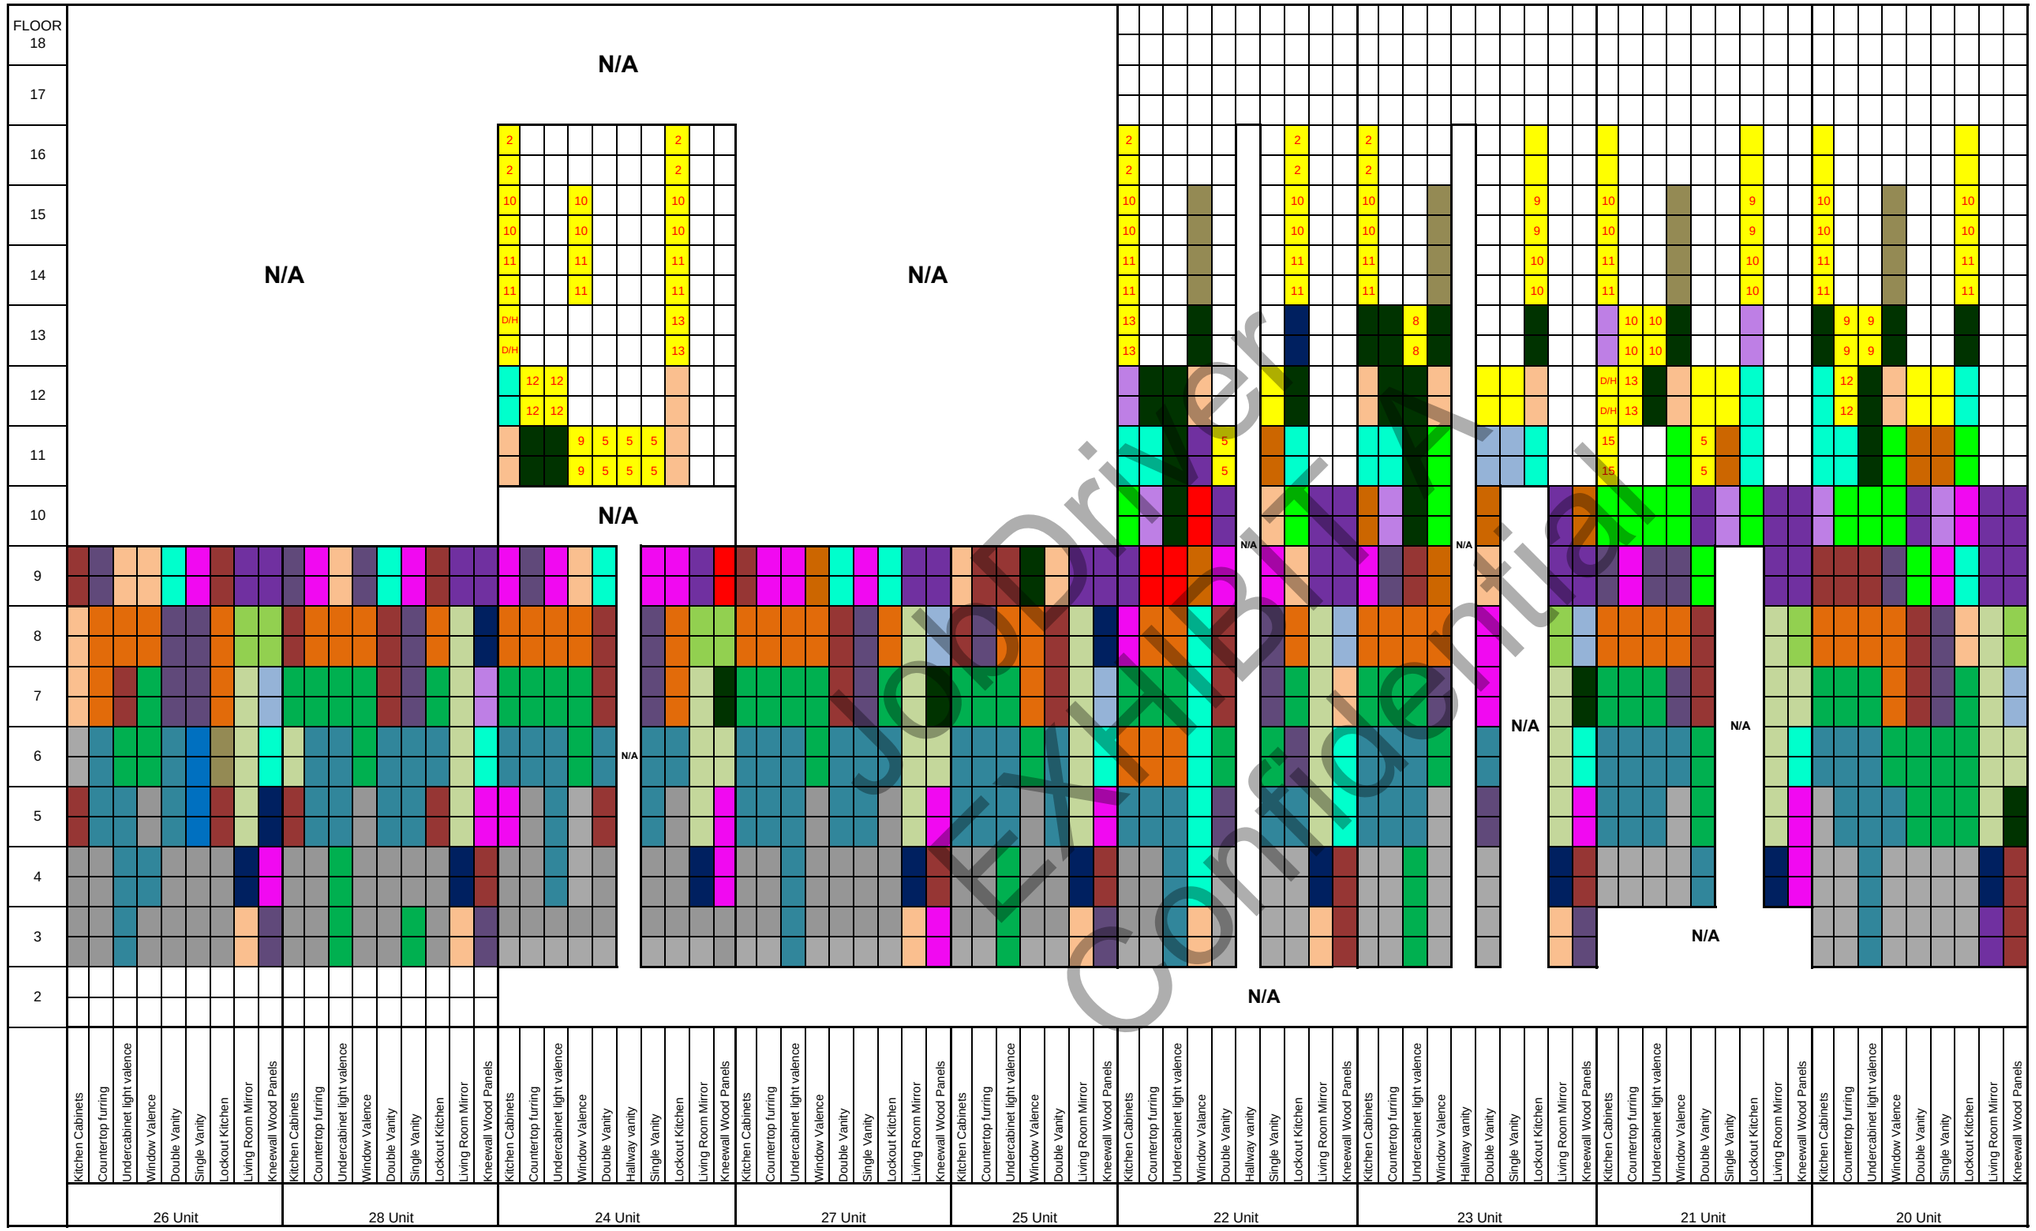

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 5/30/2012

Top Driver EXHIBIT A Confidential

PREMIER MILLWORK PROGRESS CHART

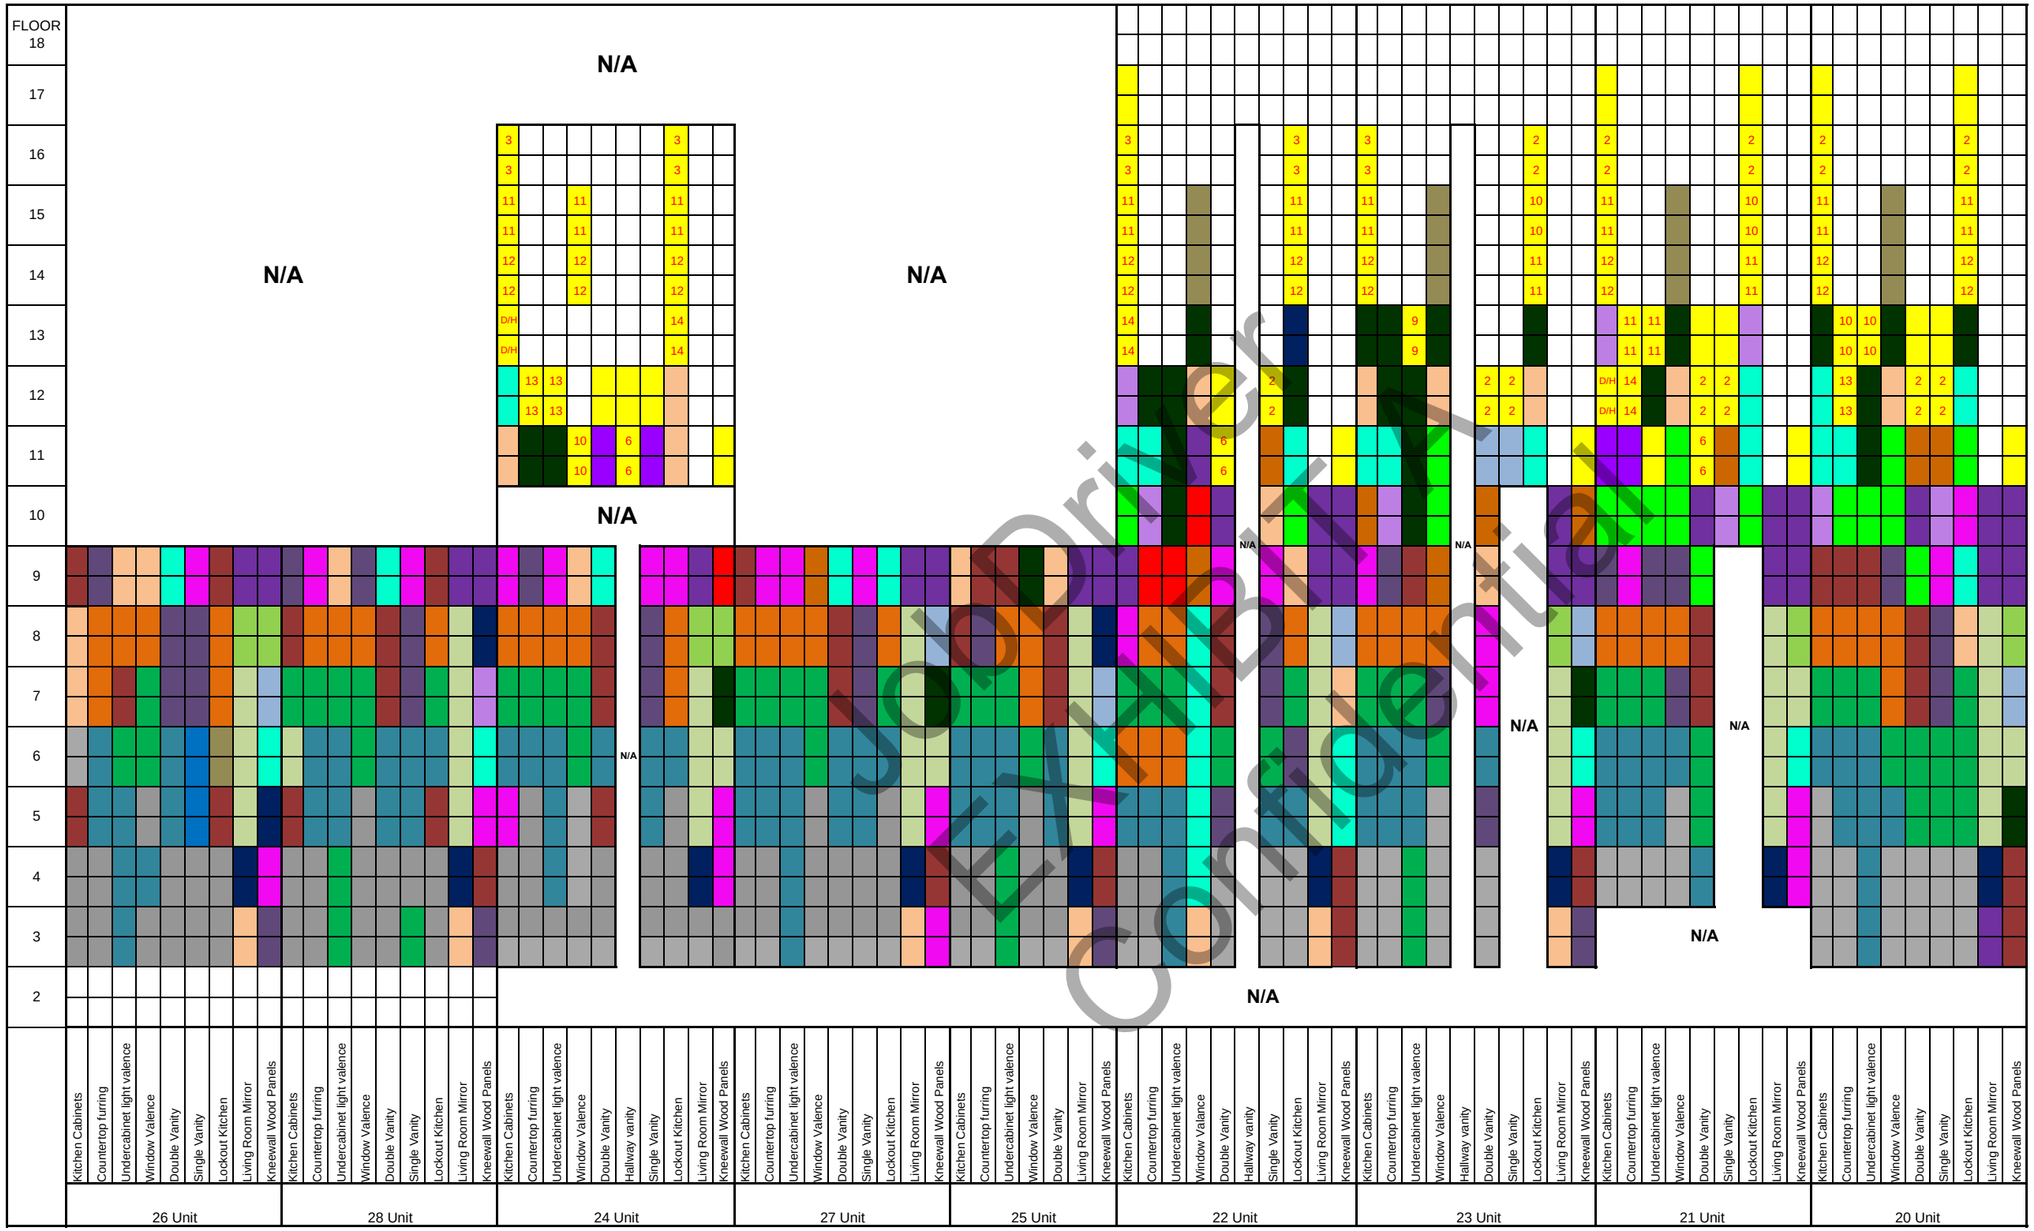

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012

PREMIER MILLWORK PROGRESS CHART

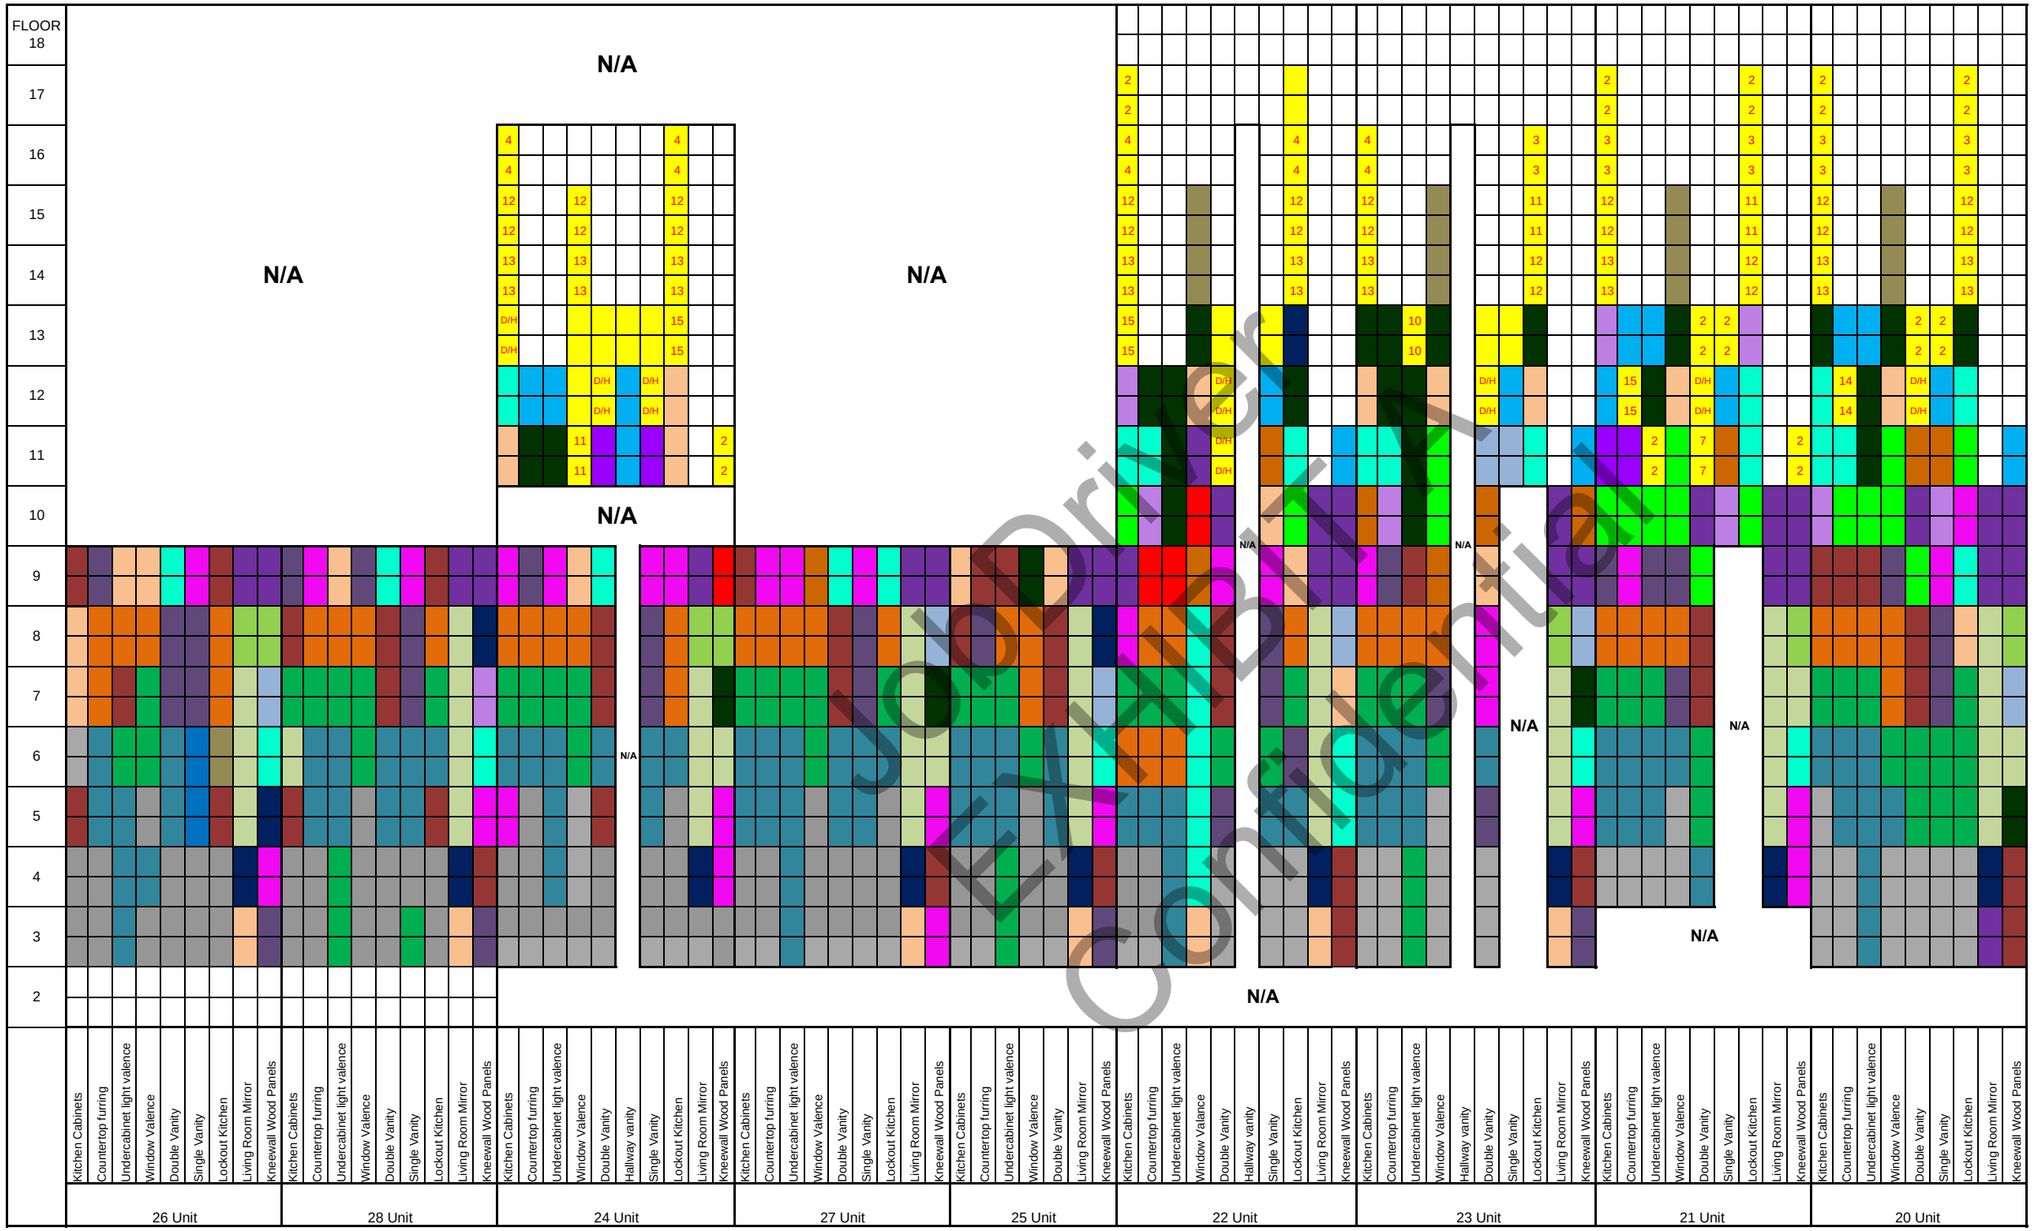

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012

YouDrive EXHIBIT A Confidential

PREMIER MILLWORK PROGRESS CHART

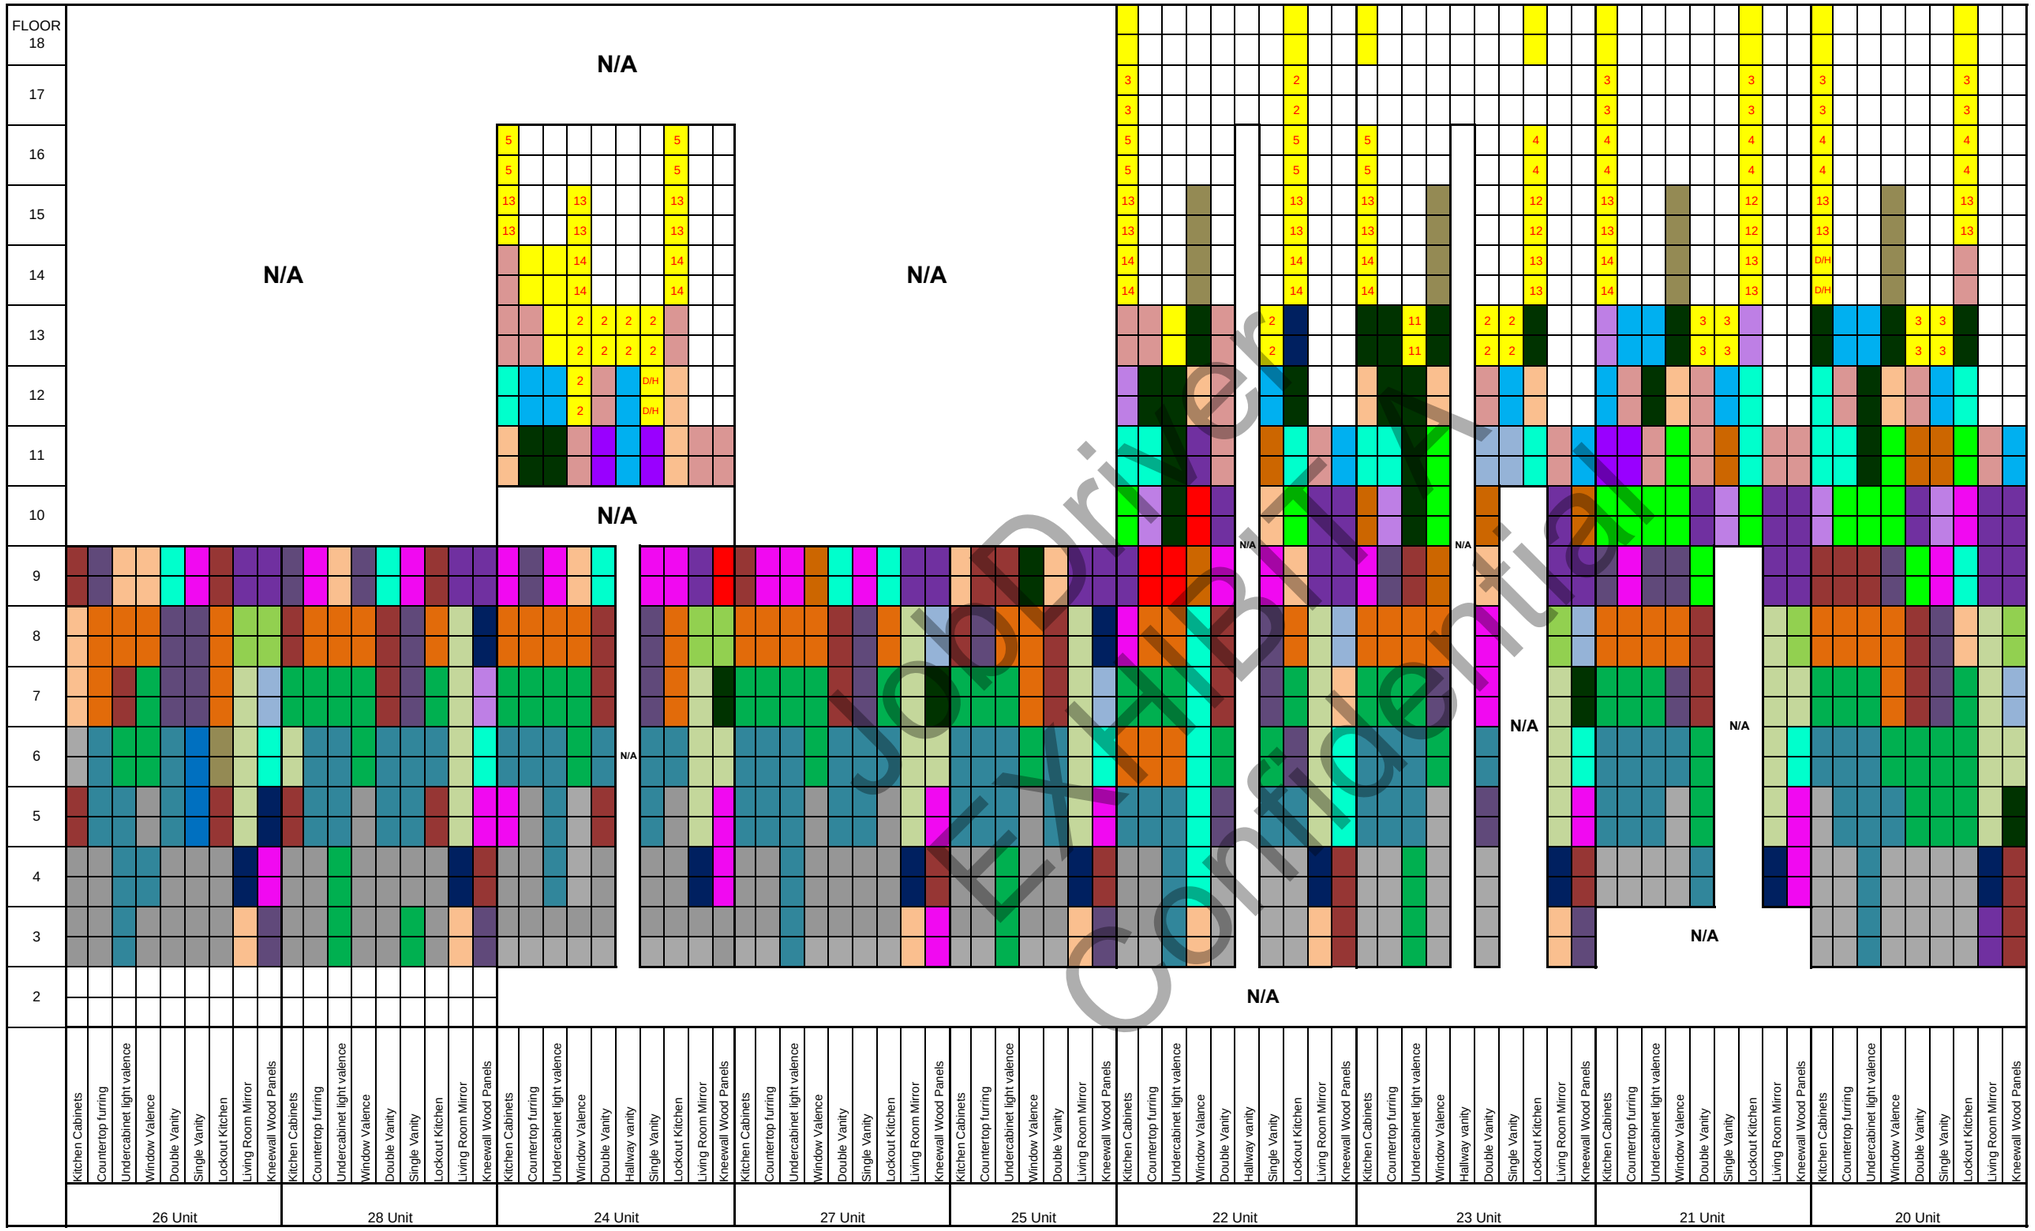

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012

JobDrive EXHIBIT A Confidential

PREMIER MILLWORK PROGRESS CHART

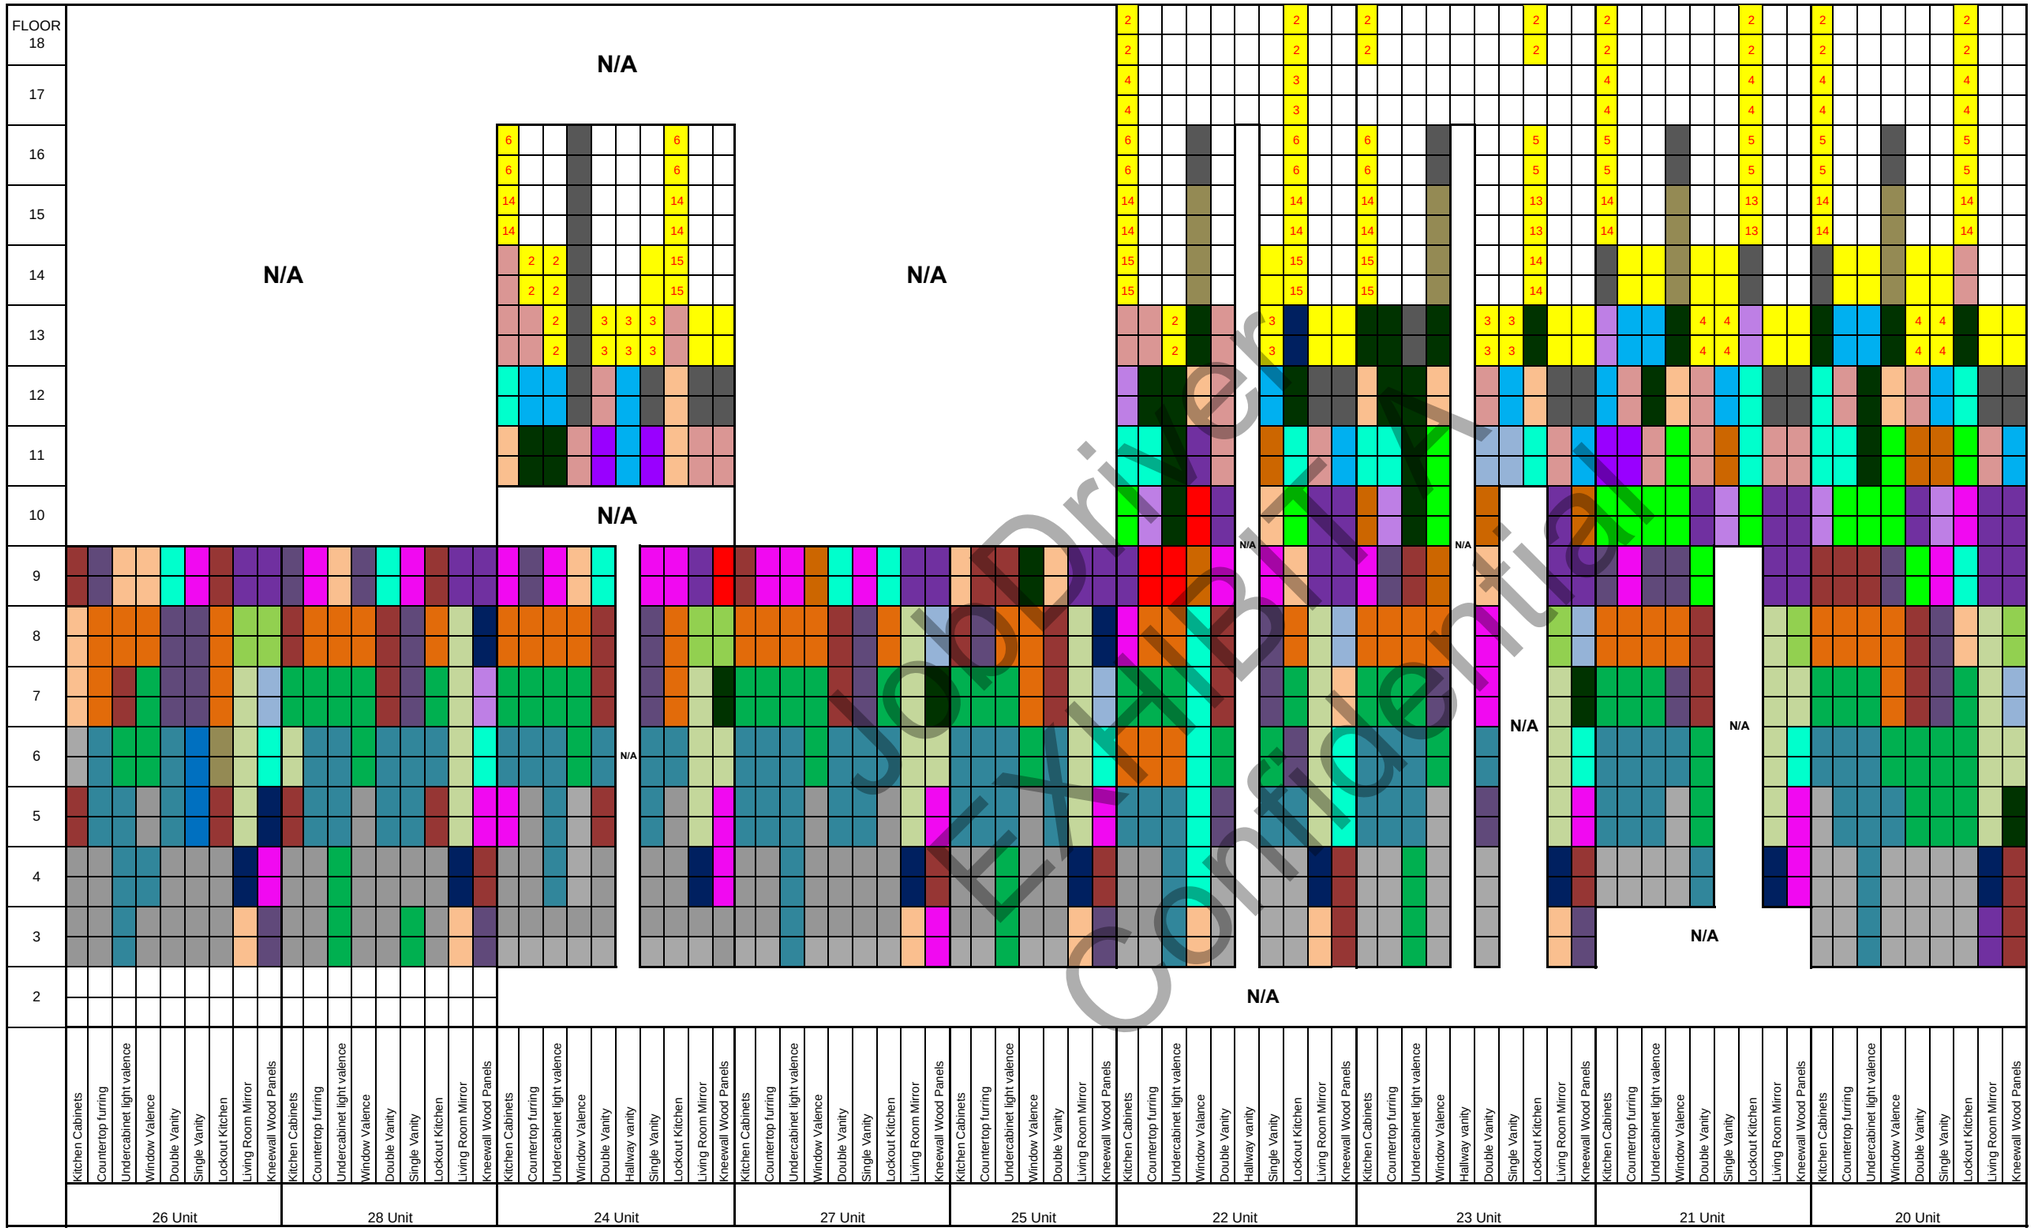

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

YouDrive EXHIBIT A Confidential

PREMIER MILLWORK PROGRESS CHART

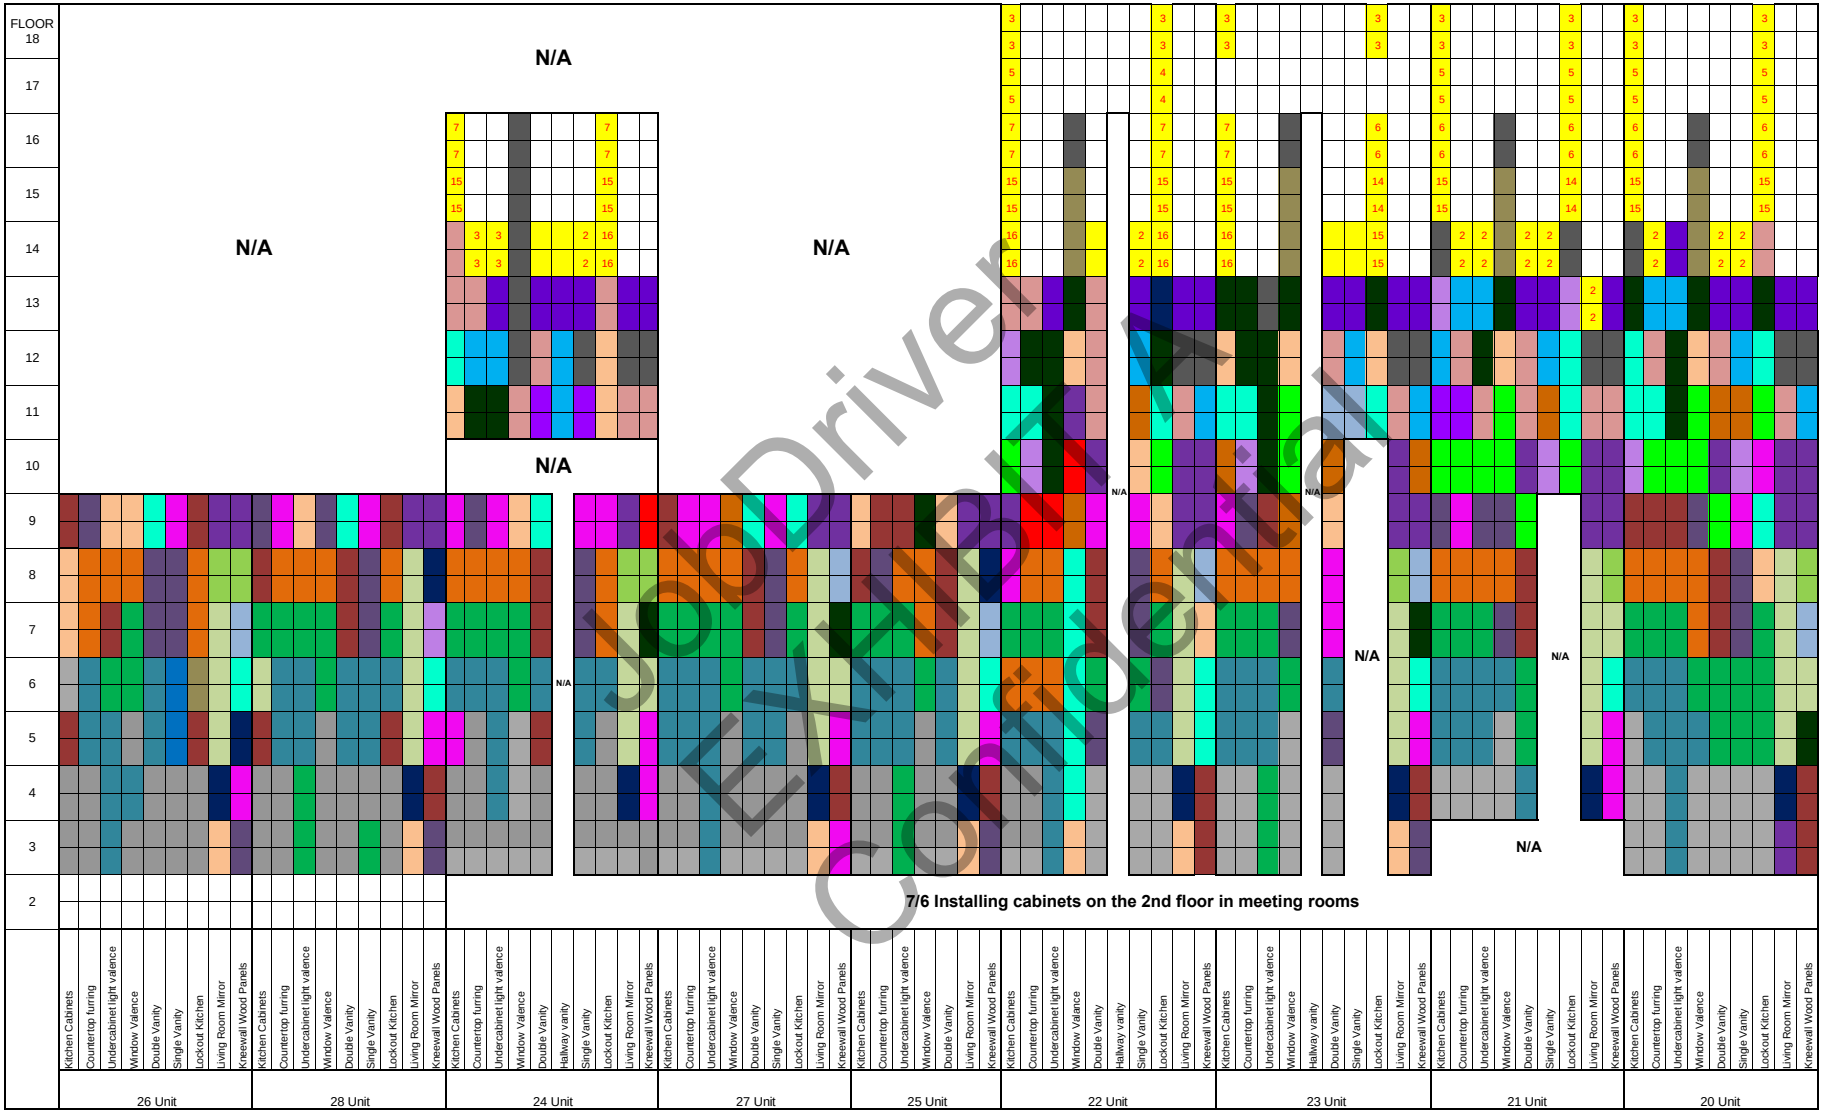

Job Driven
Exhibit A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

PREMIER MILLWORK PROGRESS CHART

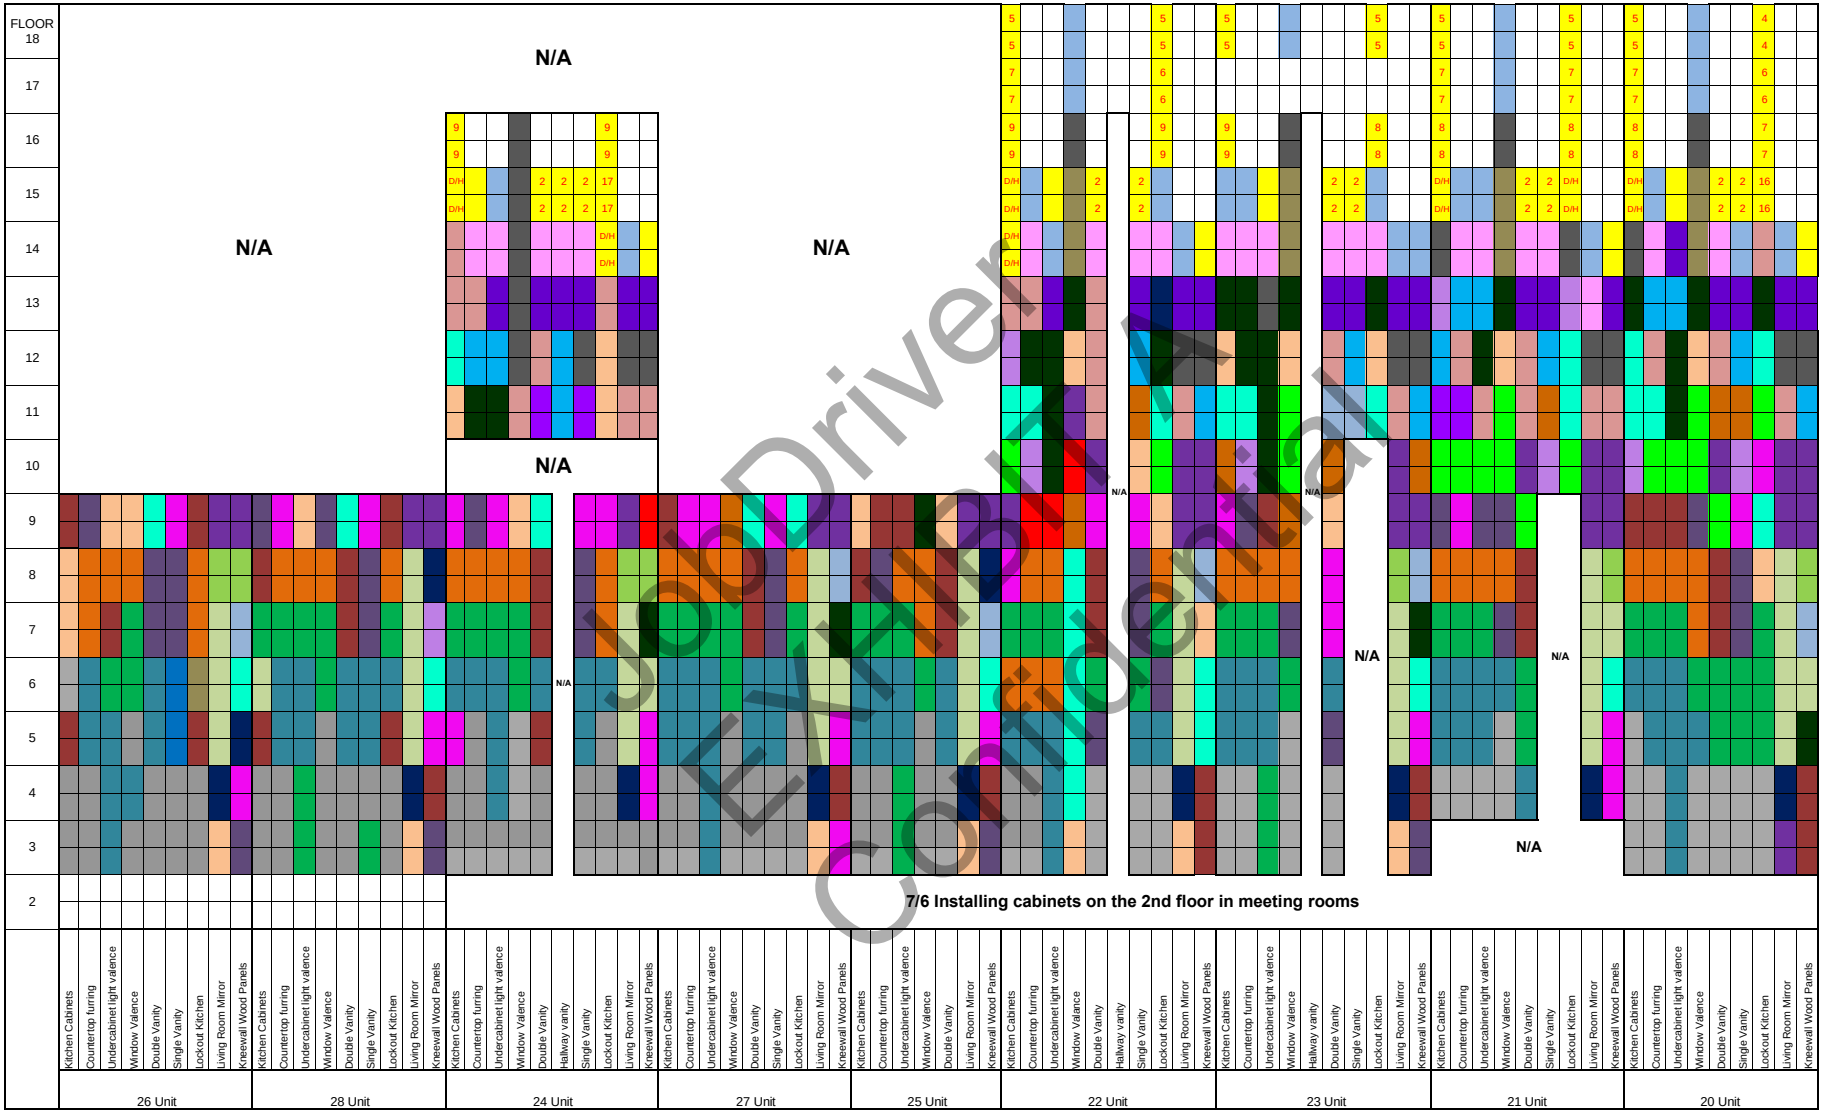

Job Driven
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

PREMIER MILLWORK PROGRESS CHART

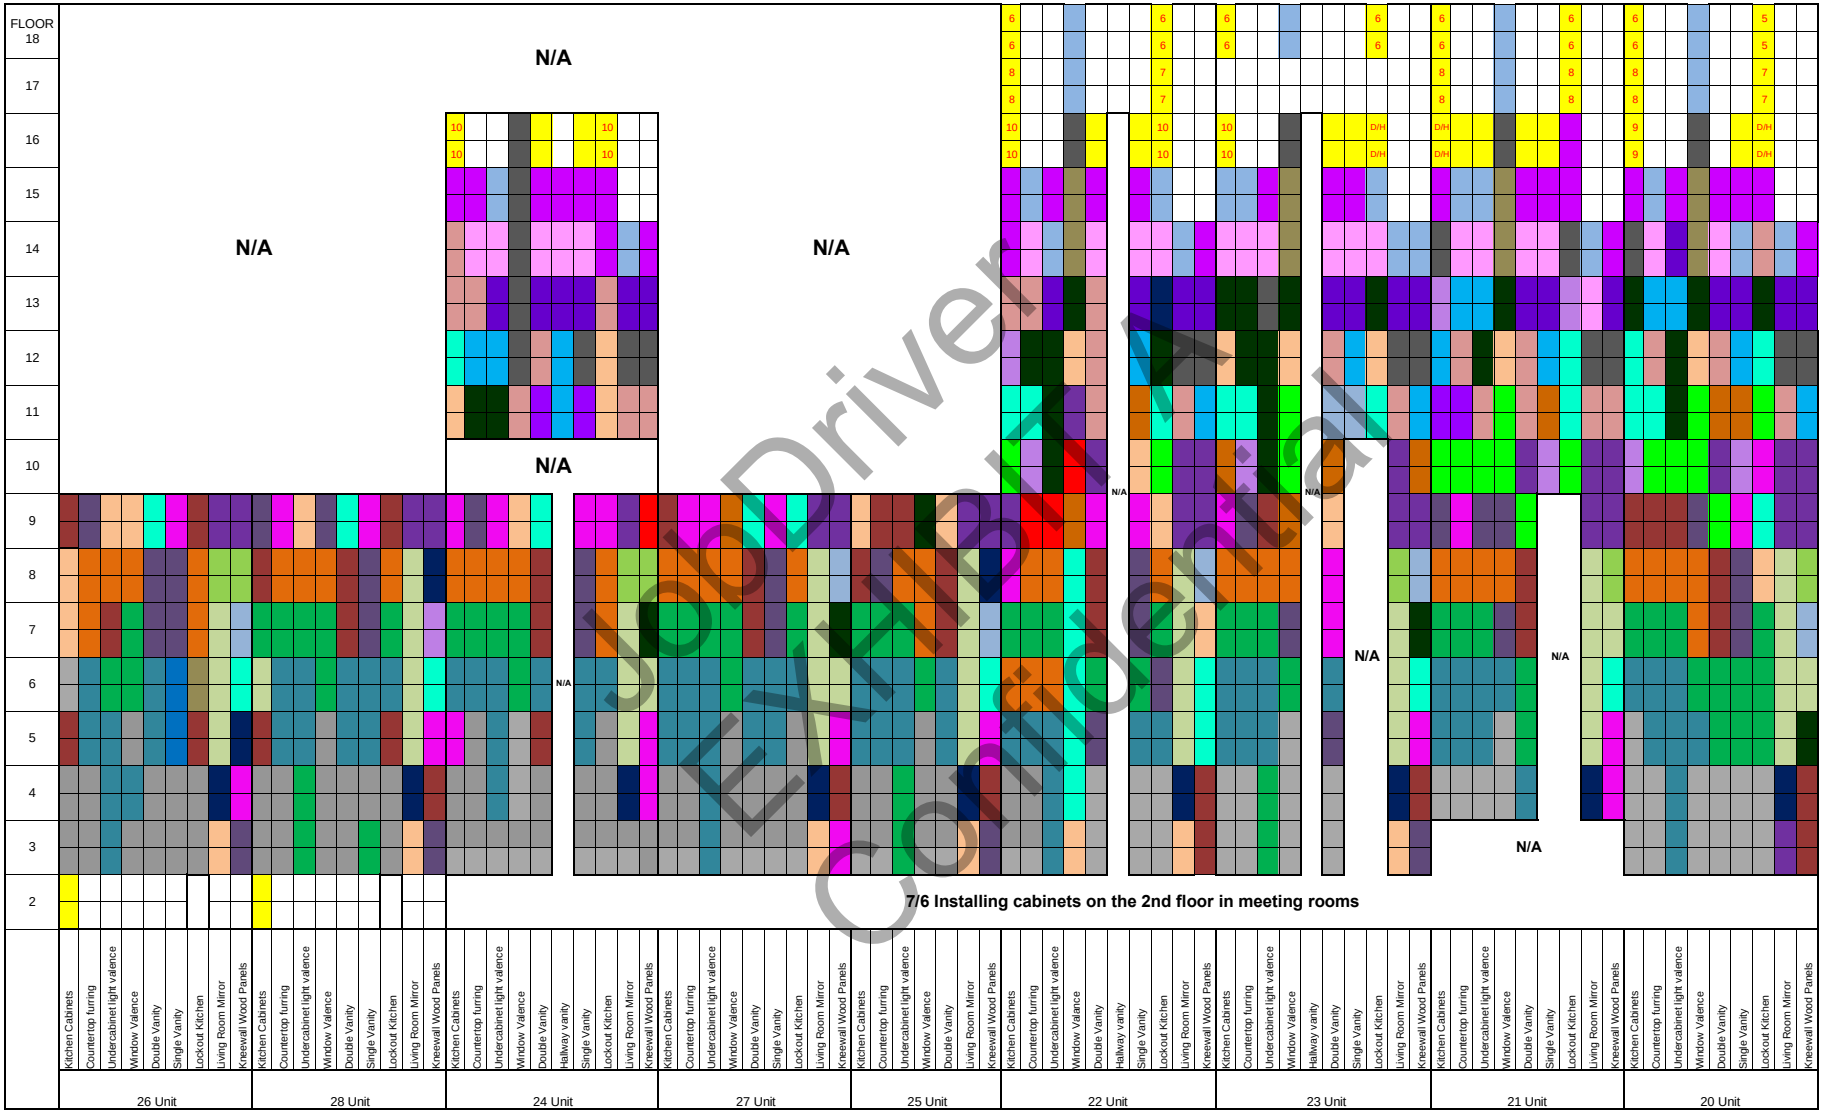

Job Driven
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

PREMIER MILLWORK PROGRESS CHART

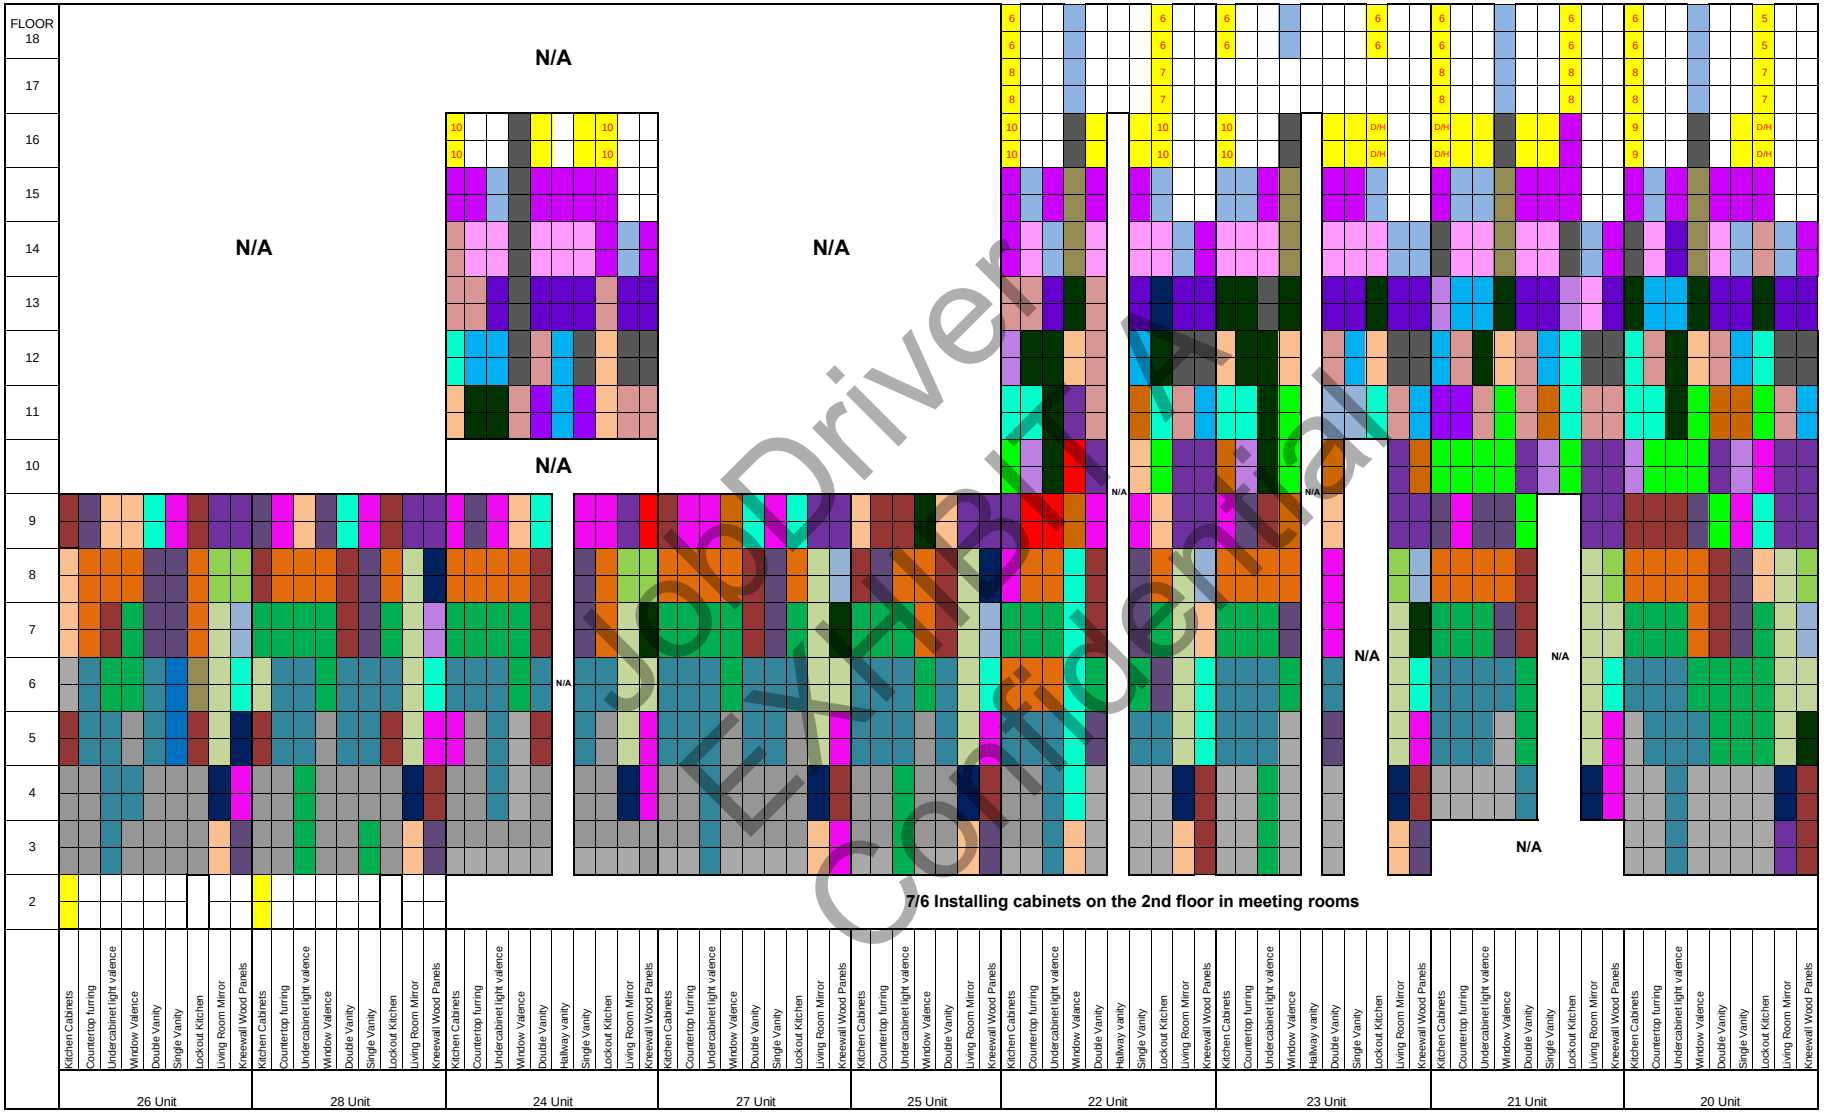

Job Driven
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

PREMIER MILLWORK PROGRESS CHART

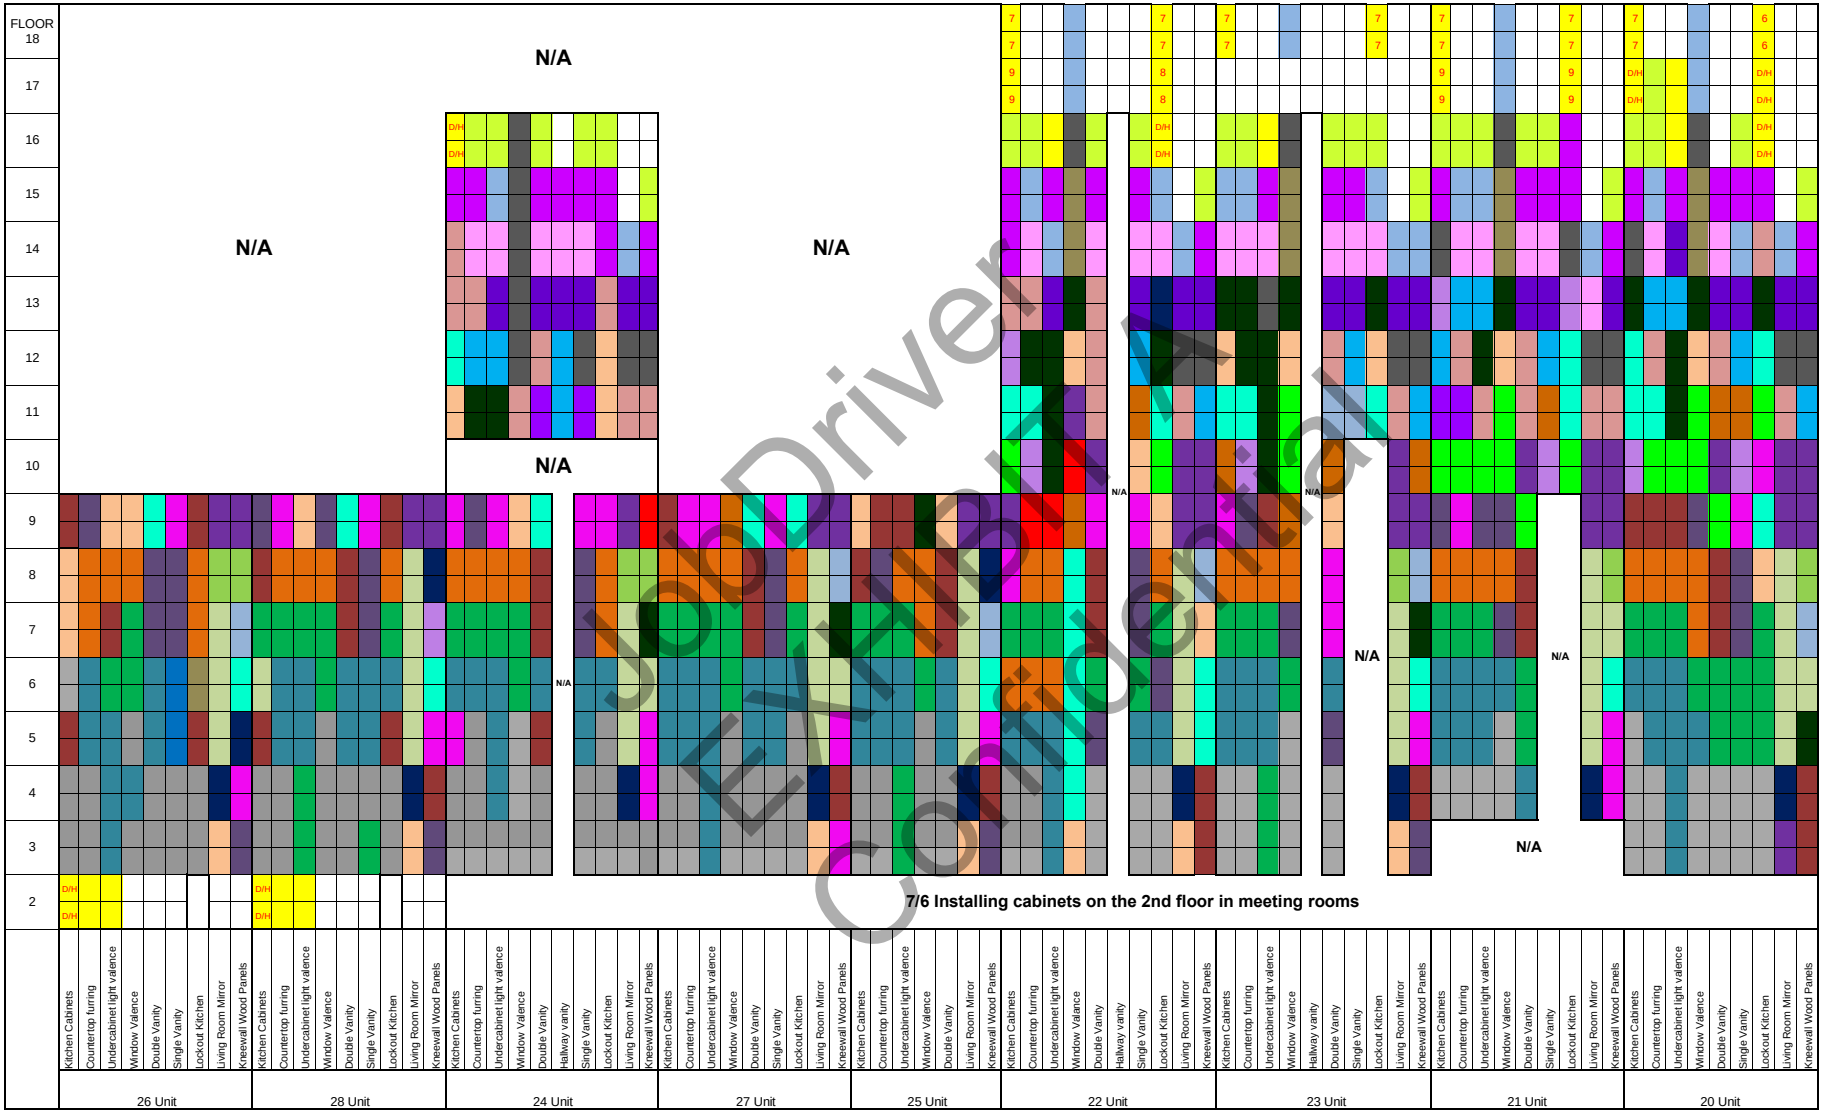

Job Driven
EXHIBIT A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/201
- WORK COMPLETED TO DATE 7/23/201
- WORK COMPLETED TO DATE 7/30/201
- WORK COMPLETED TO DATE 8/6/2012

PREMIER MILLWORK PROGRESS CHART

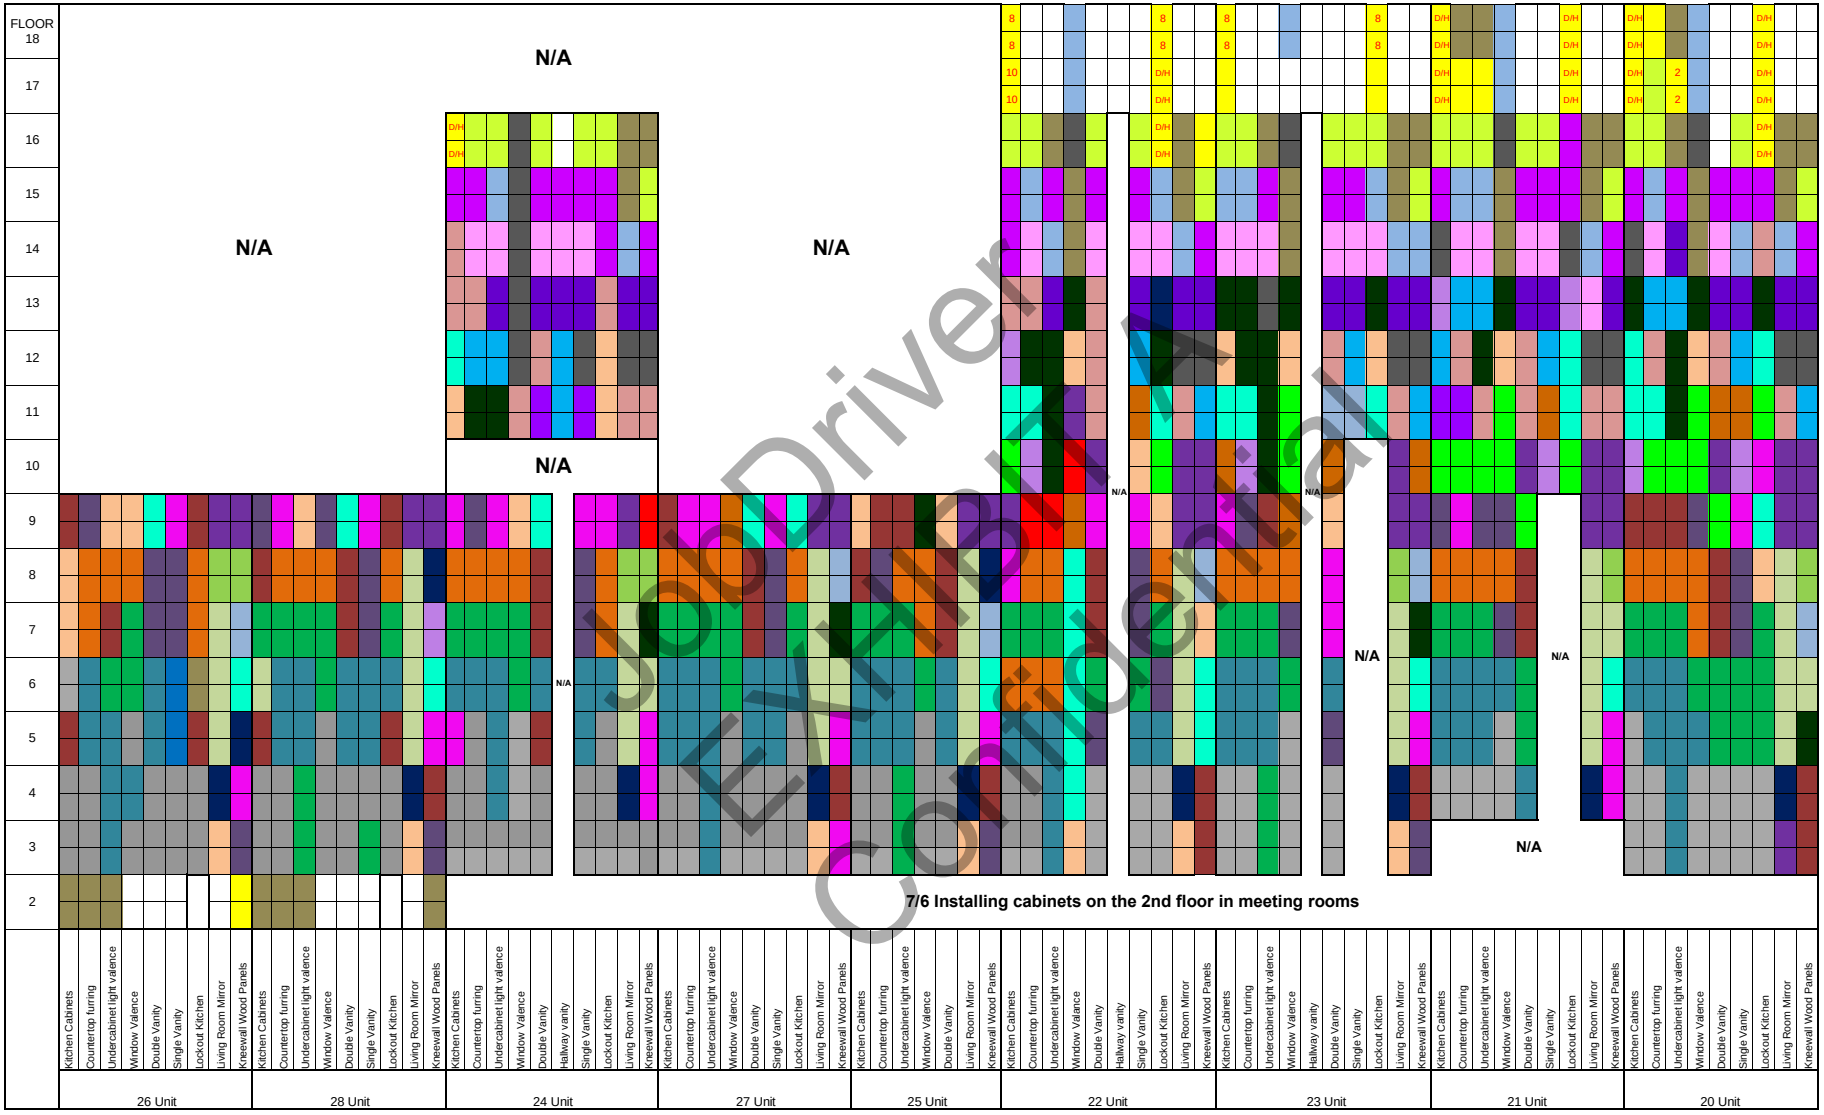

Job Driven
Exhibit A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/201
- WORK COMPLETED TO DATE 7/23/201
- WORK COMPLETED TO DATE 7/30/201
- WORK COMPLETED TO DATE 8/6/2012

PREMIER MILLWORK PROGRESS CHART

Job Driven
Exhibit A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/201
- WORK COMPLETED TO DATE 7/23/201
- WORK COMPLETED TO DATE 7/30/201
- WORK COMPLETED TO DATE 8/6/2012

PREMIER MILLWORK PROGRESS CHART

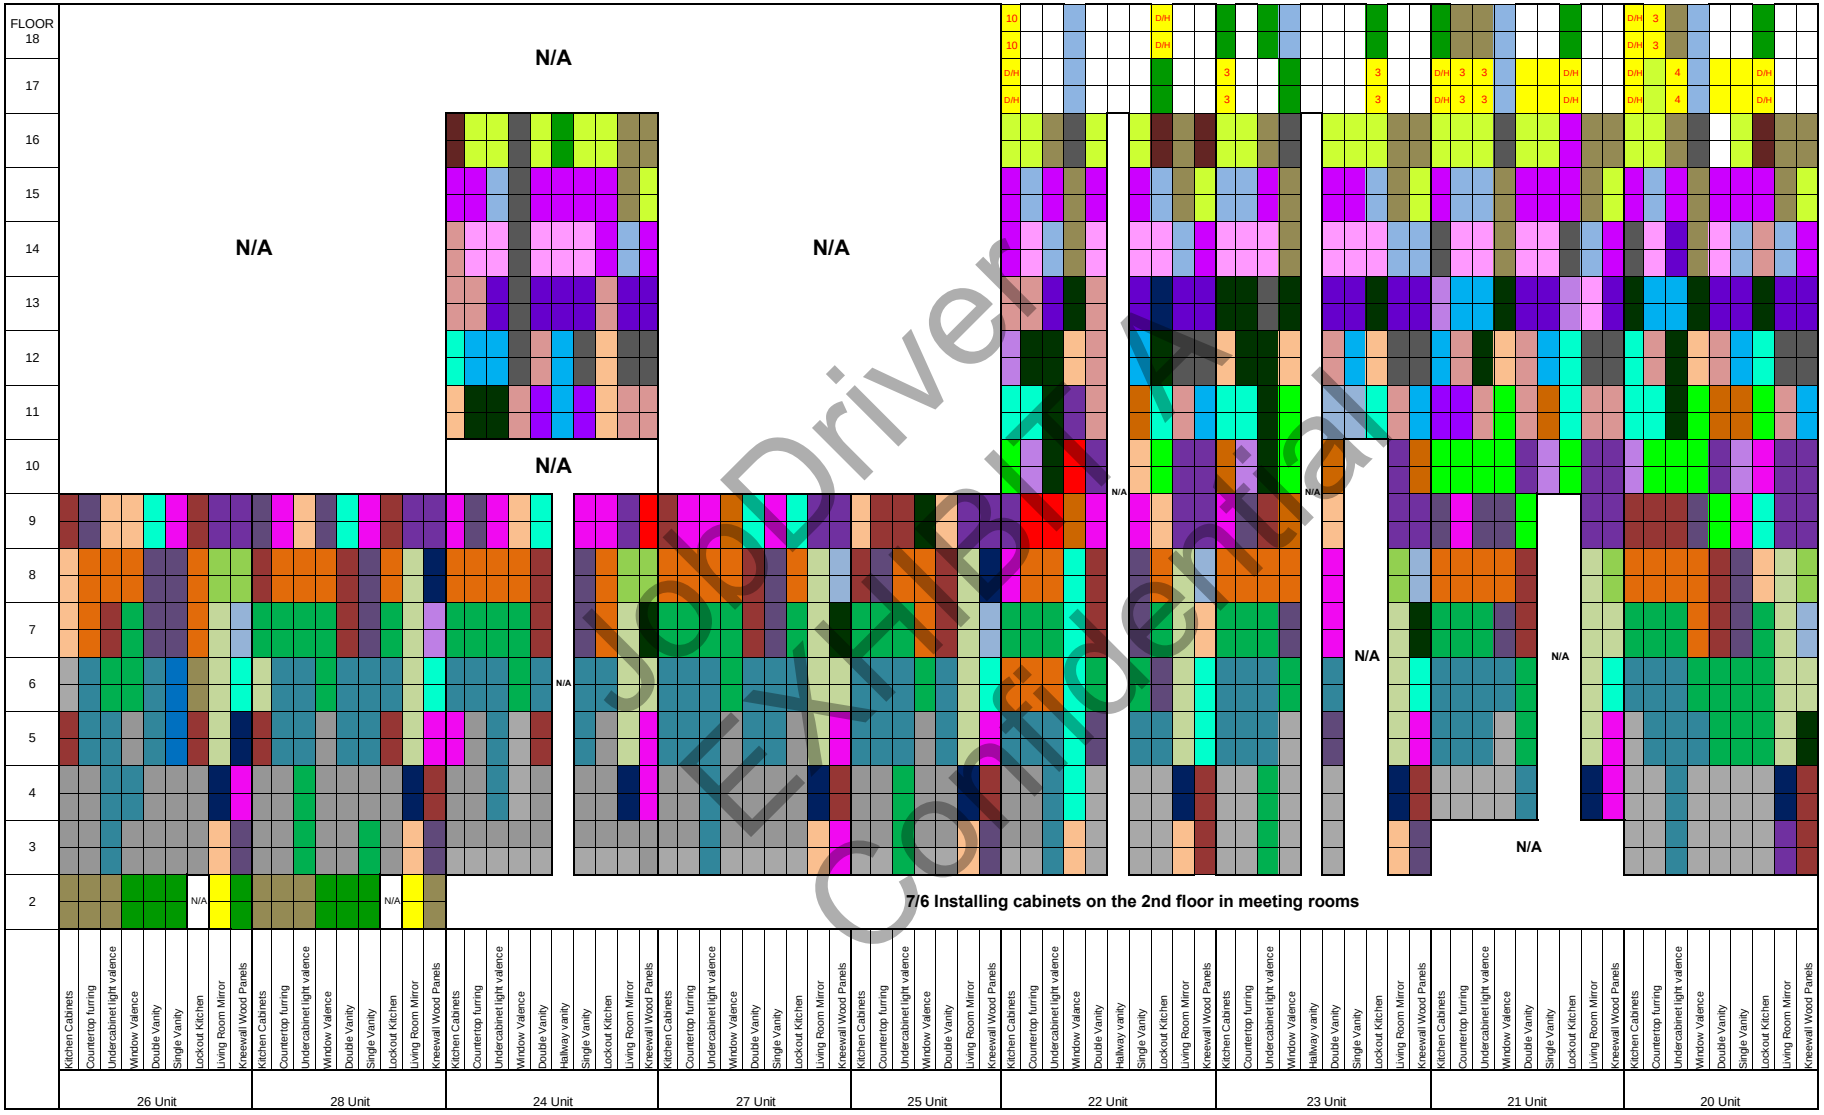

Job Driven
Exhibit A
Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012
- WORK COMPLETED TO DATE 4/23/2012
- WORK COMPLETED TO DATE 4/30/2012
- CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
- WORK COMPLETED TO DATE 5/7/2012
- WORK COMPLETED TO DATE 5/14/2012
- WORK COMPLETED TO DATE 5/21/2012/ Pool Area
- WORK COMPLETED TO DATE 6/11/2012
- WORK COMPLETED TO DATE 5/30/2012
- WORK COMPLETED TO DATE 6/4/2012
- WORK COMPLETED TO DATE 6/18/2012
- WORK COMPLETED TO DATE 6/25/2012
- WORK COMPLETED TO DATE 7/6/2012
- WORK COMPLETED TO DATE 7/9/2012
- WORK COMPLETED TO DATE 7/16/201
- WORK COMPLETED TO DATE 7/23/201
- WORK COMPLETED TO DATE 7/30/201
- WORK COMPLETED TO DATE 8/6/2012

PREMIER MILLWORK PROGRESS CHART

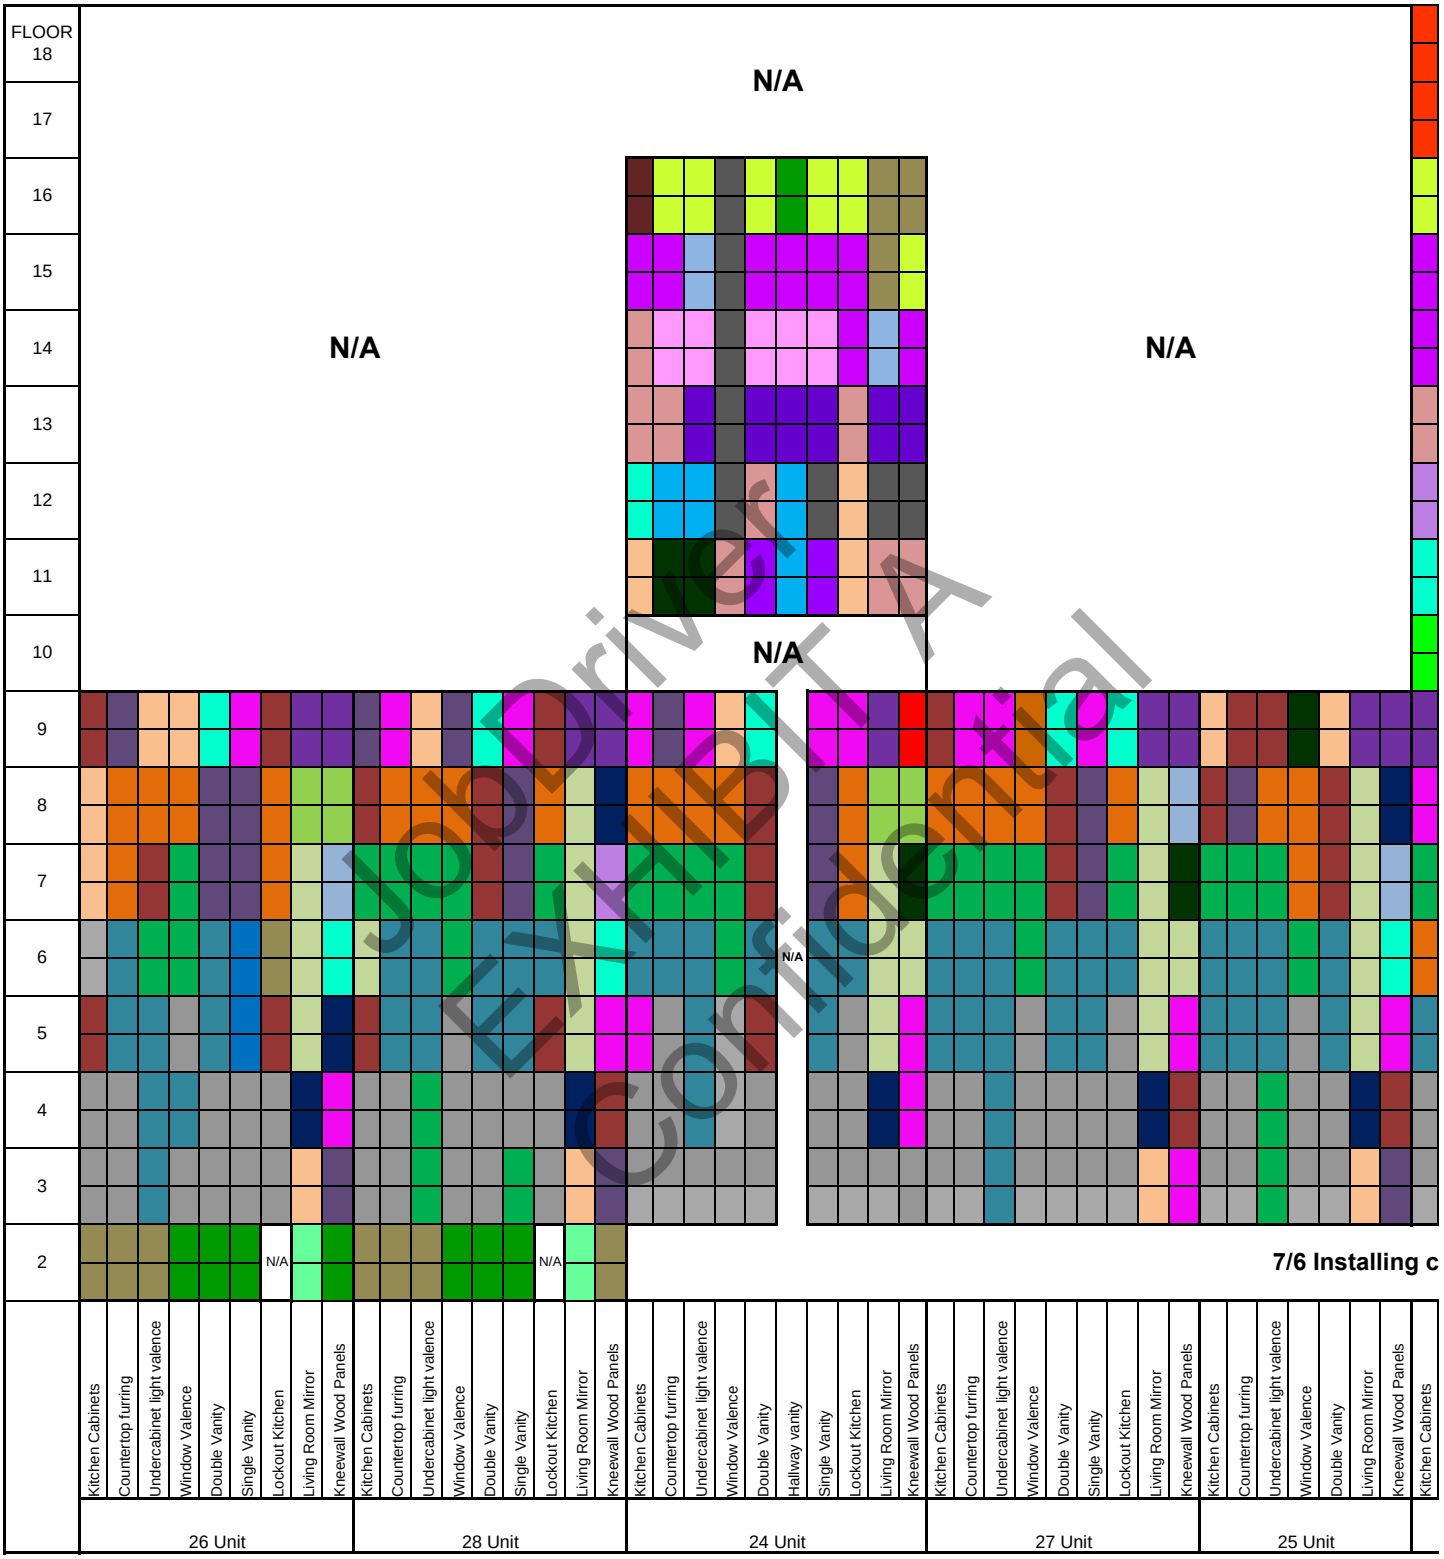

JobDriver EXHIBIT A Confidential

PREMIER PROGRESS CHART

RUN DATE : 5/16/2019

- WORK COMPLETE TO DATE 1/13/12
- AREAS AVAILABLE FOR YOU TO WORK
- # AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES
- WORK COMPLETED TO DATE 1/23/2012
- WORK COMPLETE TO DATE 1/30/12
- WORK COMPLETED 2/6/2012
- D/H DOOR OR HARDWARE MISSING
- WORK COMPLETED 2/13/2012
- WORK COMPLETED 2/20/2012
- WORK COMPLETED TO DATE 2/27/2012
- WORK COMPLETED TO DATE 3/5/2012
- WORK COMPLETE TO DATE 3/12/2012
- WORK COMPLETE TO DATE 3/19/2012
- WORK COMPLETE TO DATE 3/26/2012
- WORK COMPLETED TO DATE 4/2/2012
- WORK COMPLETED TO DATE 4/9/2012
- WORK COMPLETED TO DATE 4/16/2012

PREMIER MILLWORK PROGRESS CHART

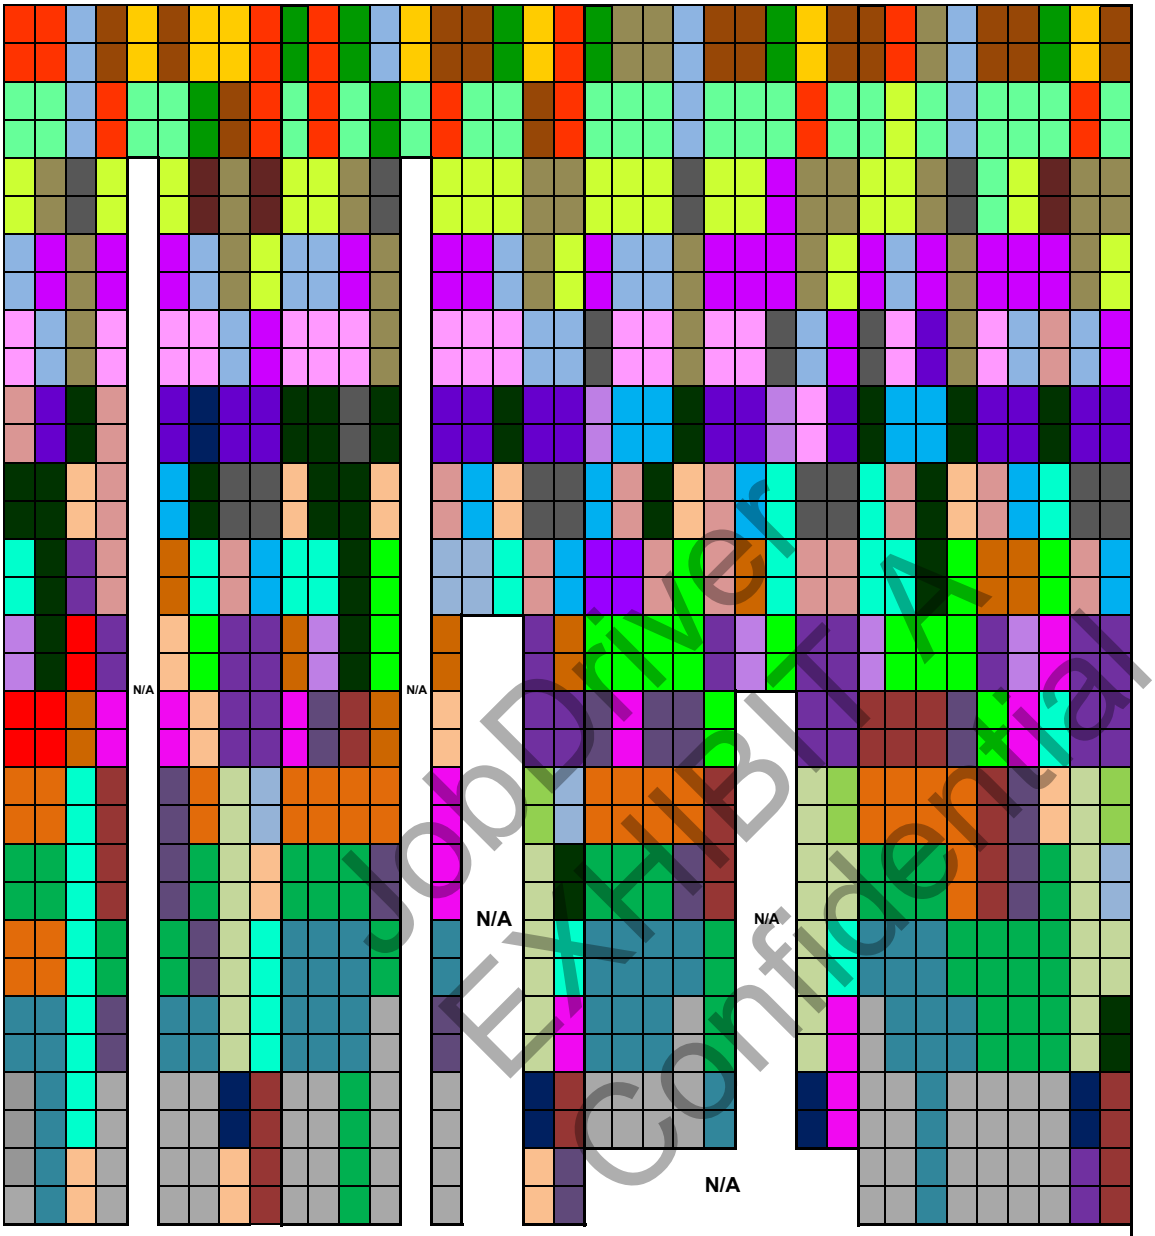

JobDriver EXHIBIT A Confidential

abinets on the 2nd floor in meeting rooms

22 Unit	23 Unit	21 Unit	20 Unit
Countertop furring	Kitchen Cabinets	Kitchen Cabinets	Kitchen Cabinets
Undercabinet light valence	Countertop furring	Countertop furring	Countertop furring
Window Valance	Undercabinet light valence	Undercabinet light valence	Undercabinet light valence
Double Vanity	Window Valence	Window Valence	Window Valence
Hallway vanity	Hallway vanity	Double Vanity	Double Vanity
Single Vanity	Double Vanity	Single Vanity	Single Vanity
Lockout Kitchen	Single Vanity	Lockout Kitchen	Lockout Kitchen
Living Room Mirror	Lockout Kitchen	Living Room Mirror	Living Room Mirror
Kneewall Wood Panels	Living Room Mirror	Kneewall Wood Panels	Kneewall Wood Panels
	Kneewall Wood Panels		

WORK COMPLETED TO DATE 4/23/2012
WORK COMPLETED TO DATE 4/30/2012
CONTINUE WORKING ON THE 1ST FLOOR INSTALLING CABINETS, CEILINGS AND TRIM
WORK COMPLETED TO DATE 5/7/2012
WORK COMPLETED TO DATE 5/14/2012
WORK COMPLETED TO DATE 5/21/2012/ Pool Area
WORK COMPLETED TO DATE 6/11/2012
WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/4/2012
WORK COMPLETED TO DATE 6/18/2012
WORK COMPLETED TO DATE 6/25/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012
WORK COMPLETED TO DATE 7/16/201
WORK COMPLETED TO DATE 7/23/201
WORK COMPLETED TO DATE 7/30/201
WORK COMPLETED TO DATE 8/6/2012

PREMIER MILL WORK PROGRESS CHART

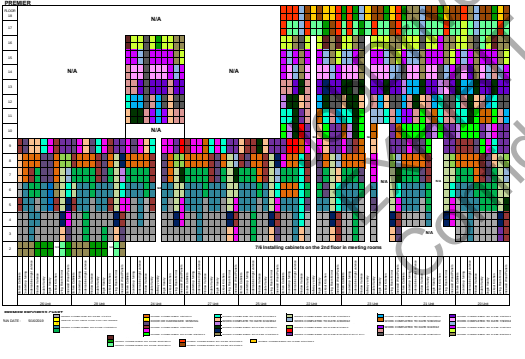

Confidential

BAY MECHANICAL PROGRESS CHART

| FLOOR | | |

BAY MECHANICAL PROGRESS CHART

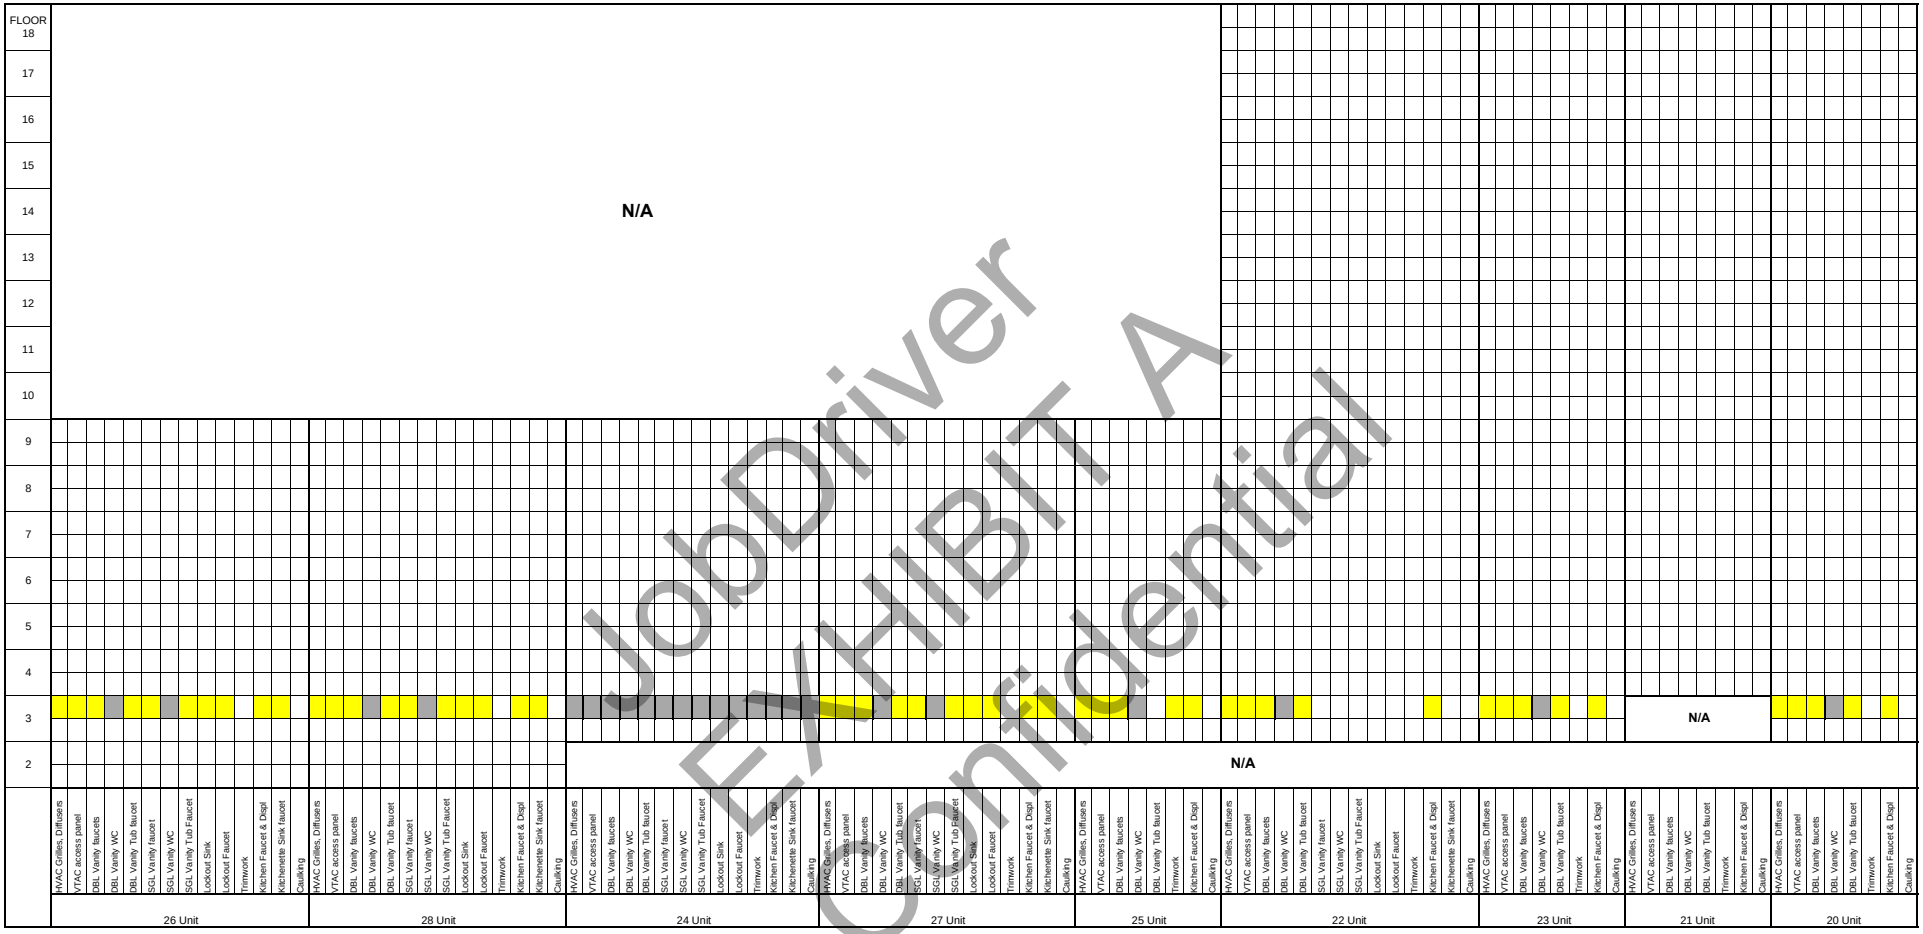

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

RUN DATE : 5/16/2019

WORK COMPLETE TO DATE 1/13/12

AREAS AVAILABLE FOR YOU TO WORK

* AREAS OF WORK AVAILABLE FOR MULTIPLE UPDATES

INCOMPLETE ITEMS

BAY MECHANICAL PROGRESS CHART

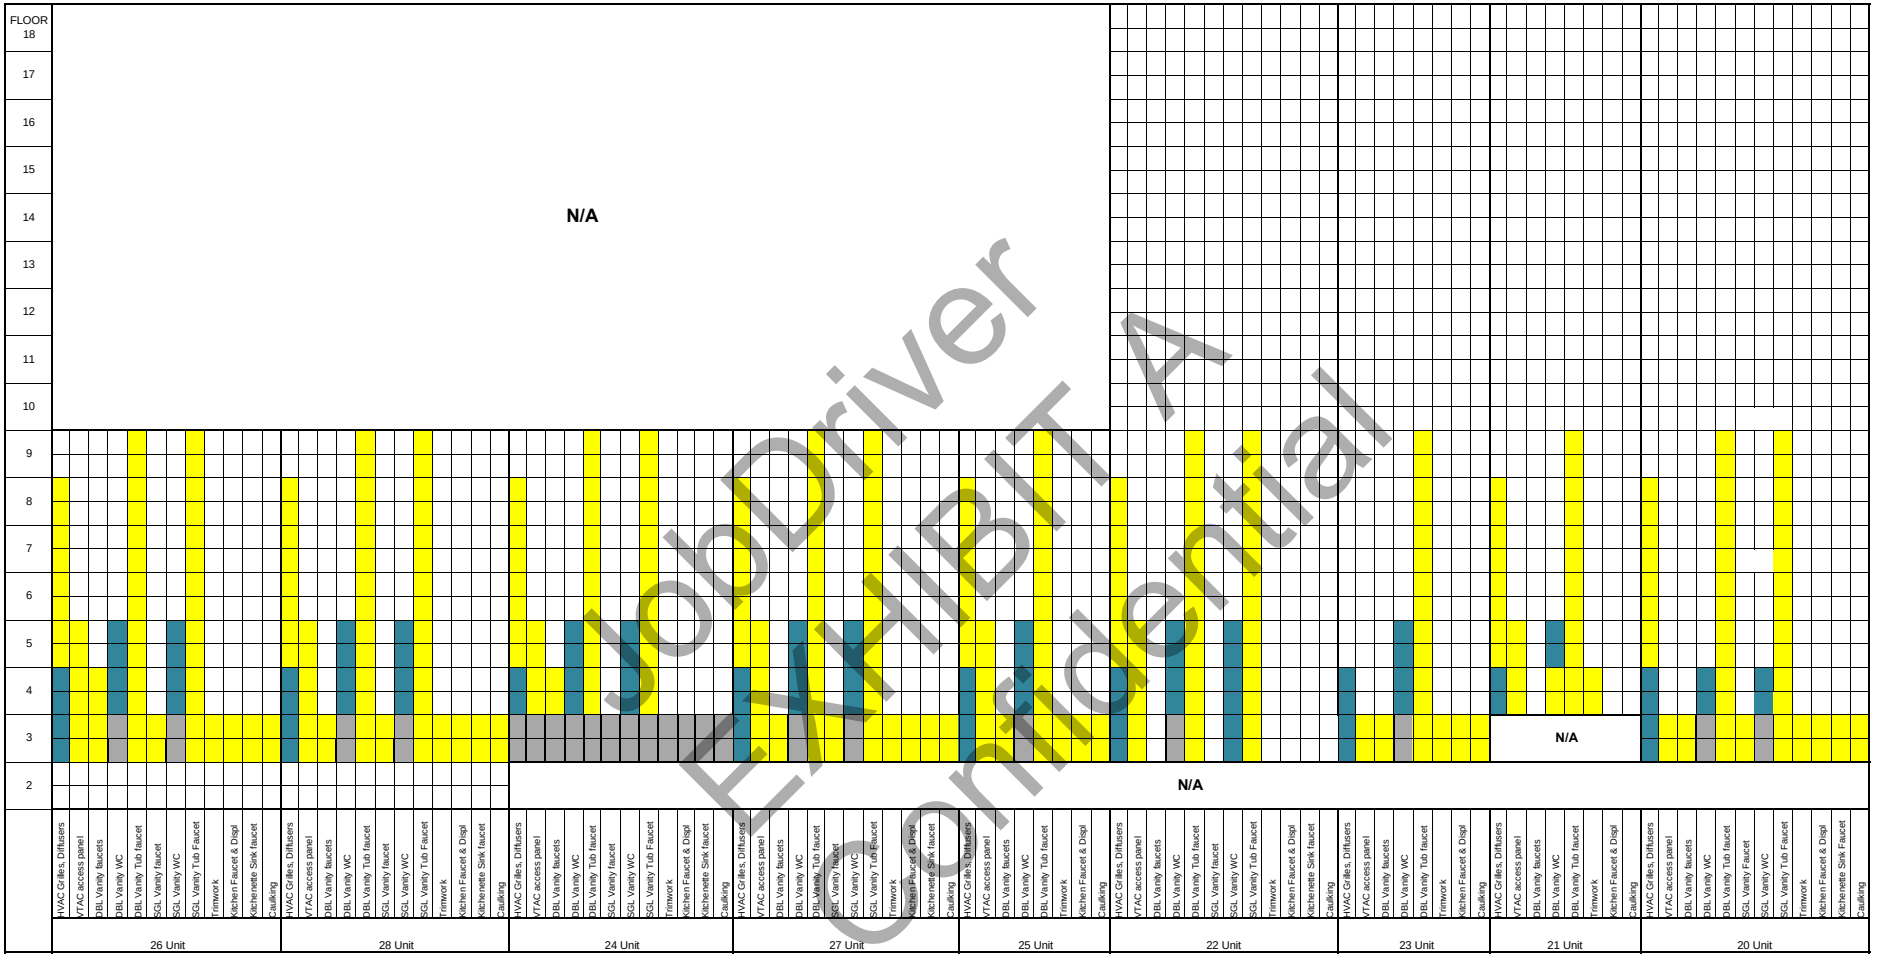

JobDriver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 1/13/2012

Work Completed to Date 1/13/2012
Areas Available For You To Work
Areas if Work Available For Multiple Updates
Work Completed to Date 1/18/2012

INCOMPLETE ITEMS

BAY MECHANICAL PROGRESS CHART

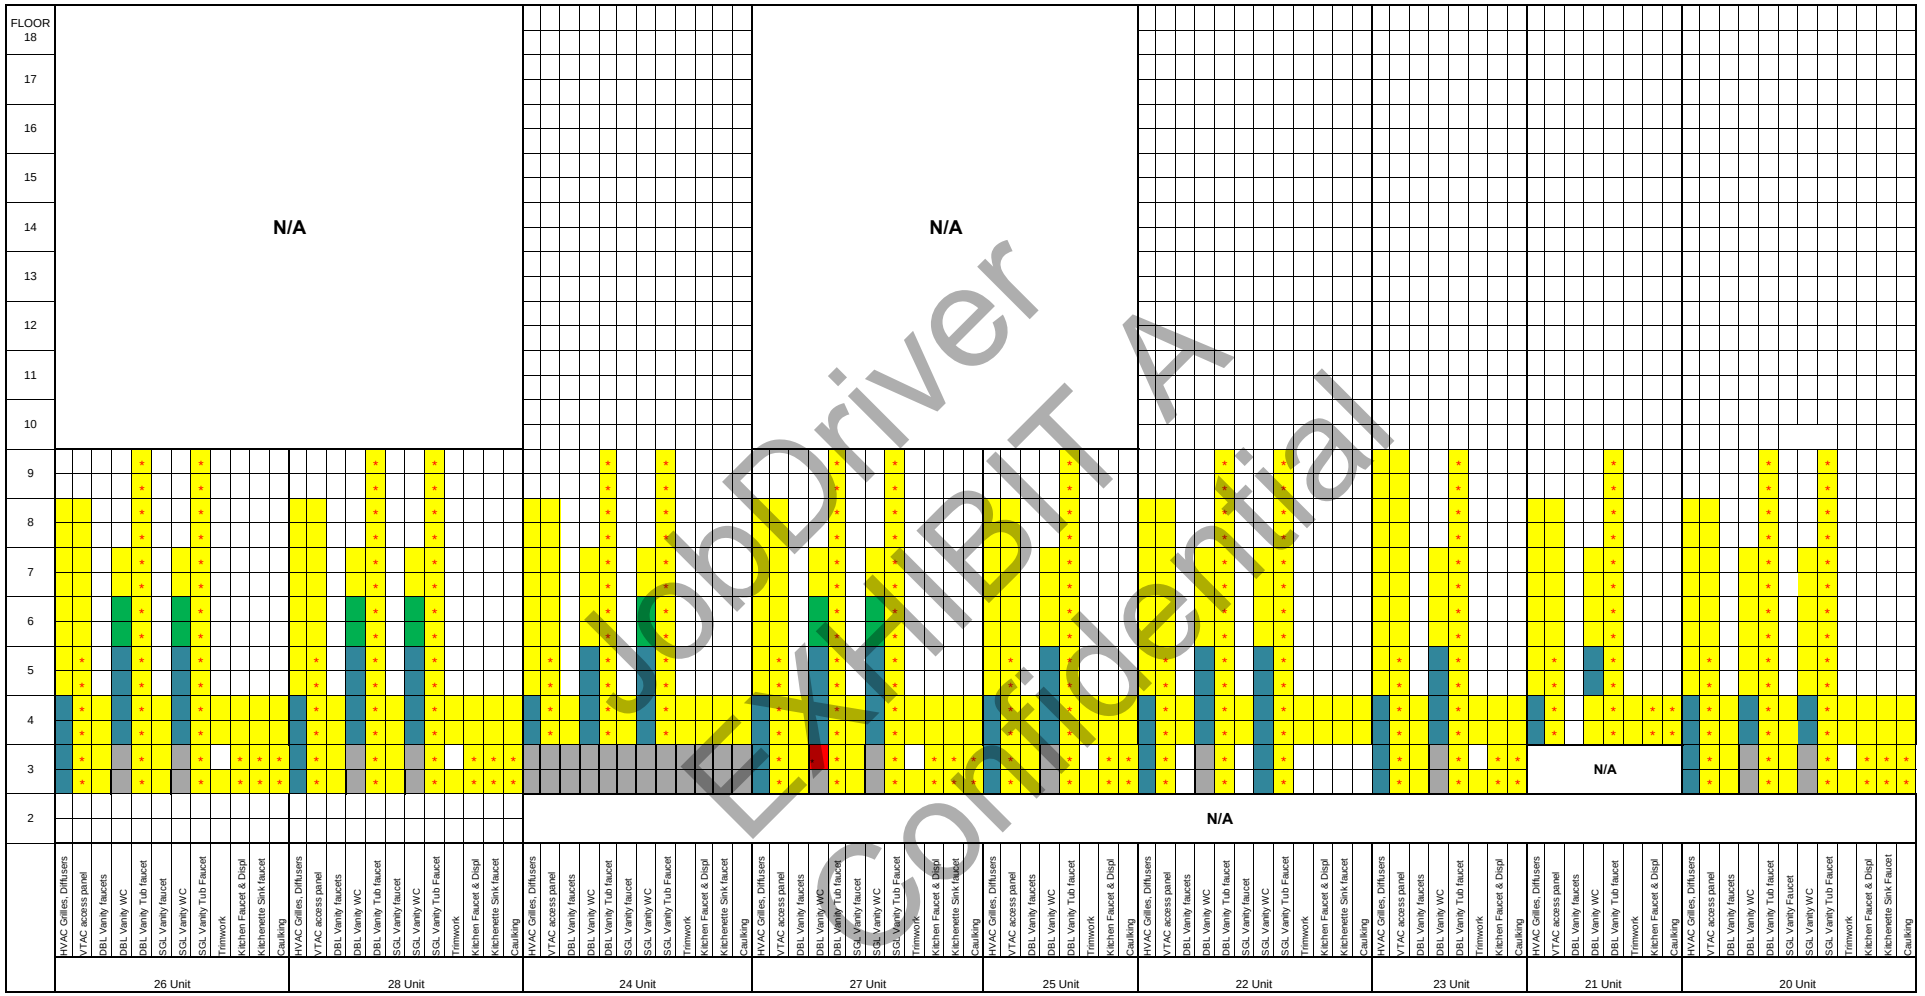

JobDriver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 1/13/2012

Work Completed to Date 1/13/2012
Areas Available For You To Work
Areas if Work Available For Multiple Updates
Work Completed to Date 1/18/2012
WORK COMPLETED TO DATE 1/25/2012

INCOMPLETE ITEMS

ROOM 327 TOILET WATER LINE NEEDS REPAIR

BAY MECHANICAL PROGRESS CHART

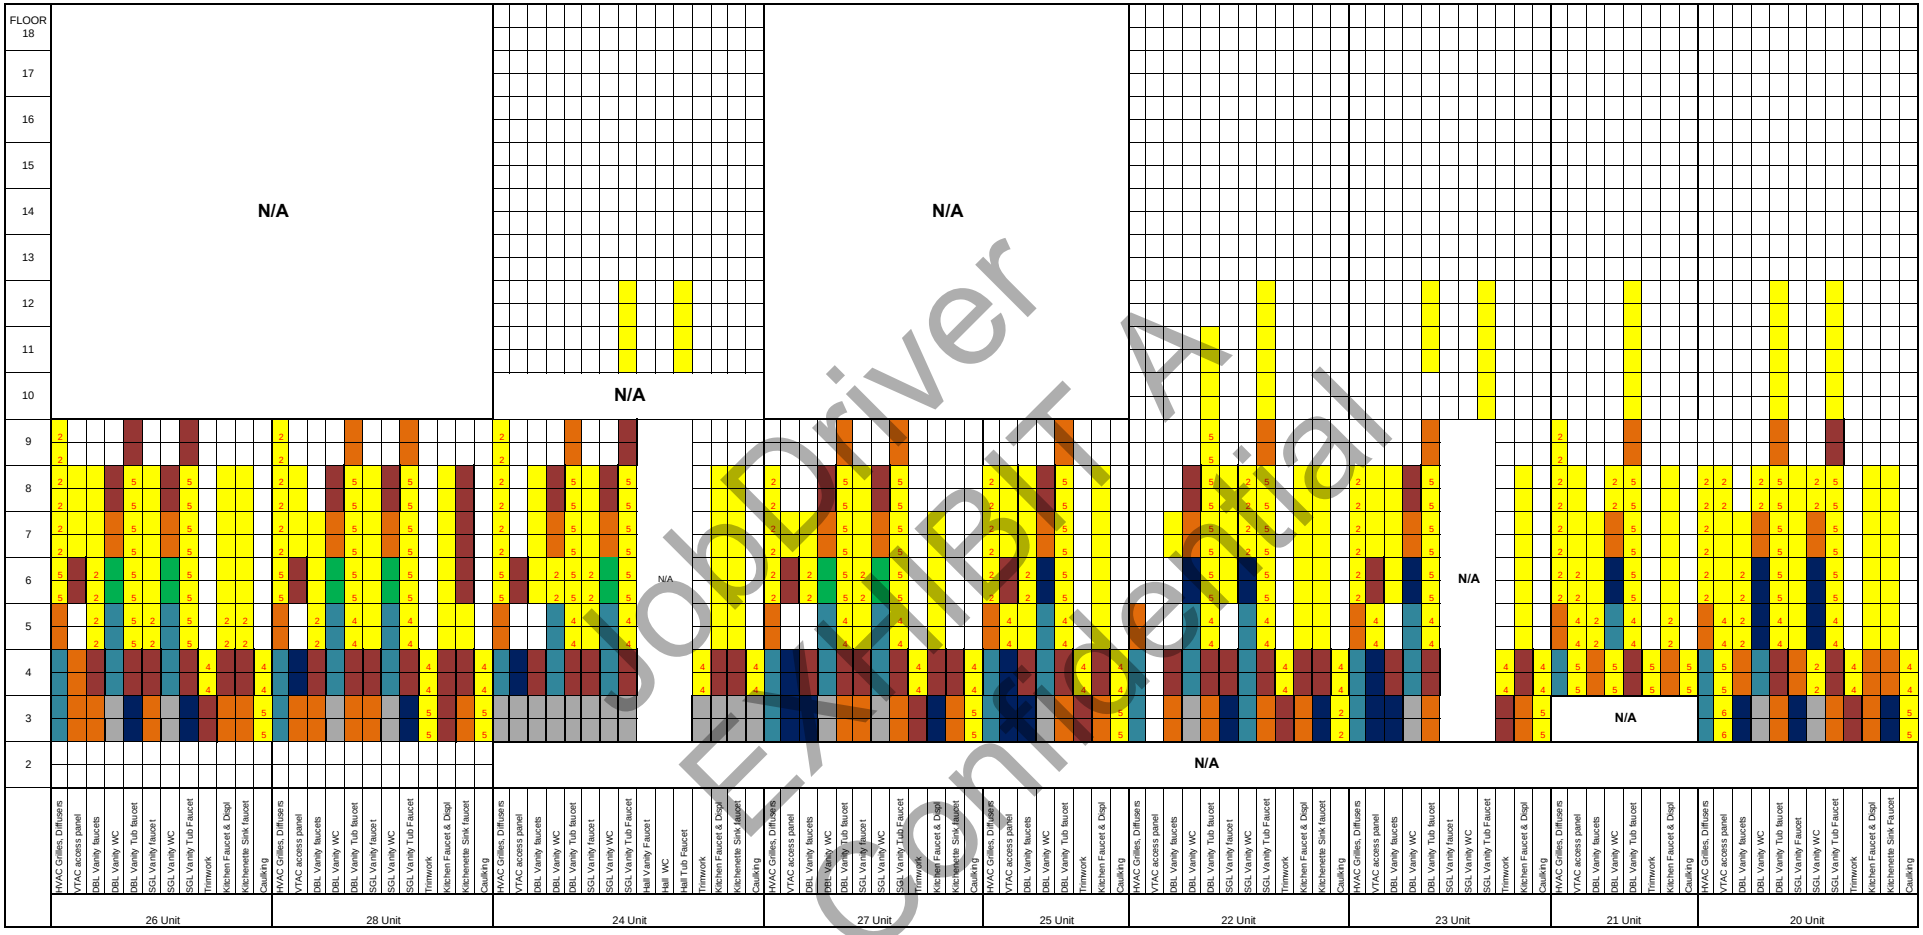

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- S/H SHOWER HEAD MISSING
- WORK COMPLETED TO DATE 2/15/2012

INCOMPLETE ITEMS

! 5TH FLOOR COULD NOT BE WALKED DUE TO PAINTING 2/15/2012

BAY MECHANICAL PROGRESS CHART

FLOOR	26 Unit	28 Unit	24 Unit	27 Unit	25 Unit	22 Unit	23 Unit	21 Unit	20 Unit
18	N/A		N/A						
17									
16									
15									
14									
13									
12									
11									
10									
9									
8									
7									
6									
5									
4									
3								N/A	
2			N/A						

HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink faucet
Caulking

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

Work Completed to Date 1/13/2012
Areas Available For You To Work
of weeks work has been available to install
Work Completed to Date 1/18/2012
WORK COMPLETED TO DATE 1/25/2012
WORK COMPLETED 2/1/2012

INCOMPLETE ITEMS

ROOM 327 TOILET WATER LINE NEEDS REPAIR
REPAIR COMPLETED

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

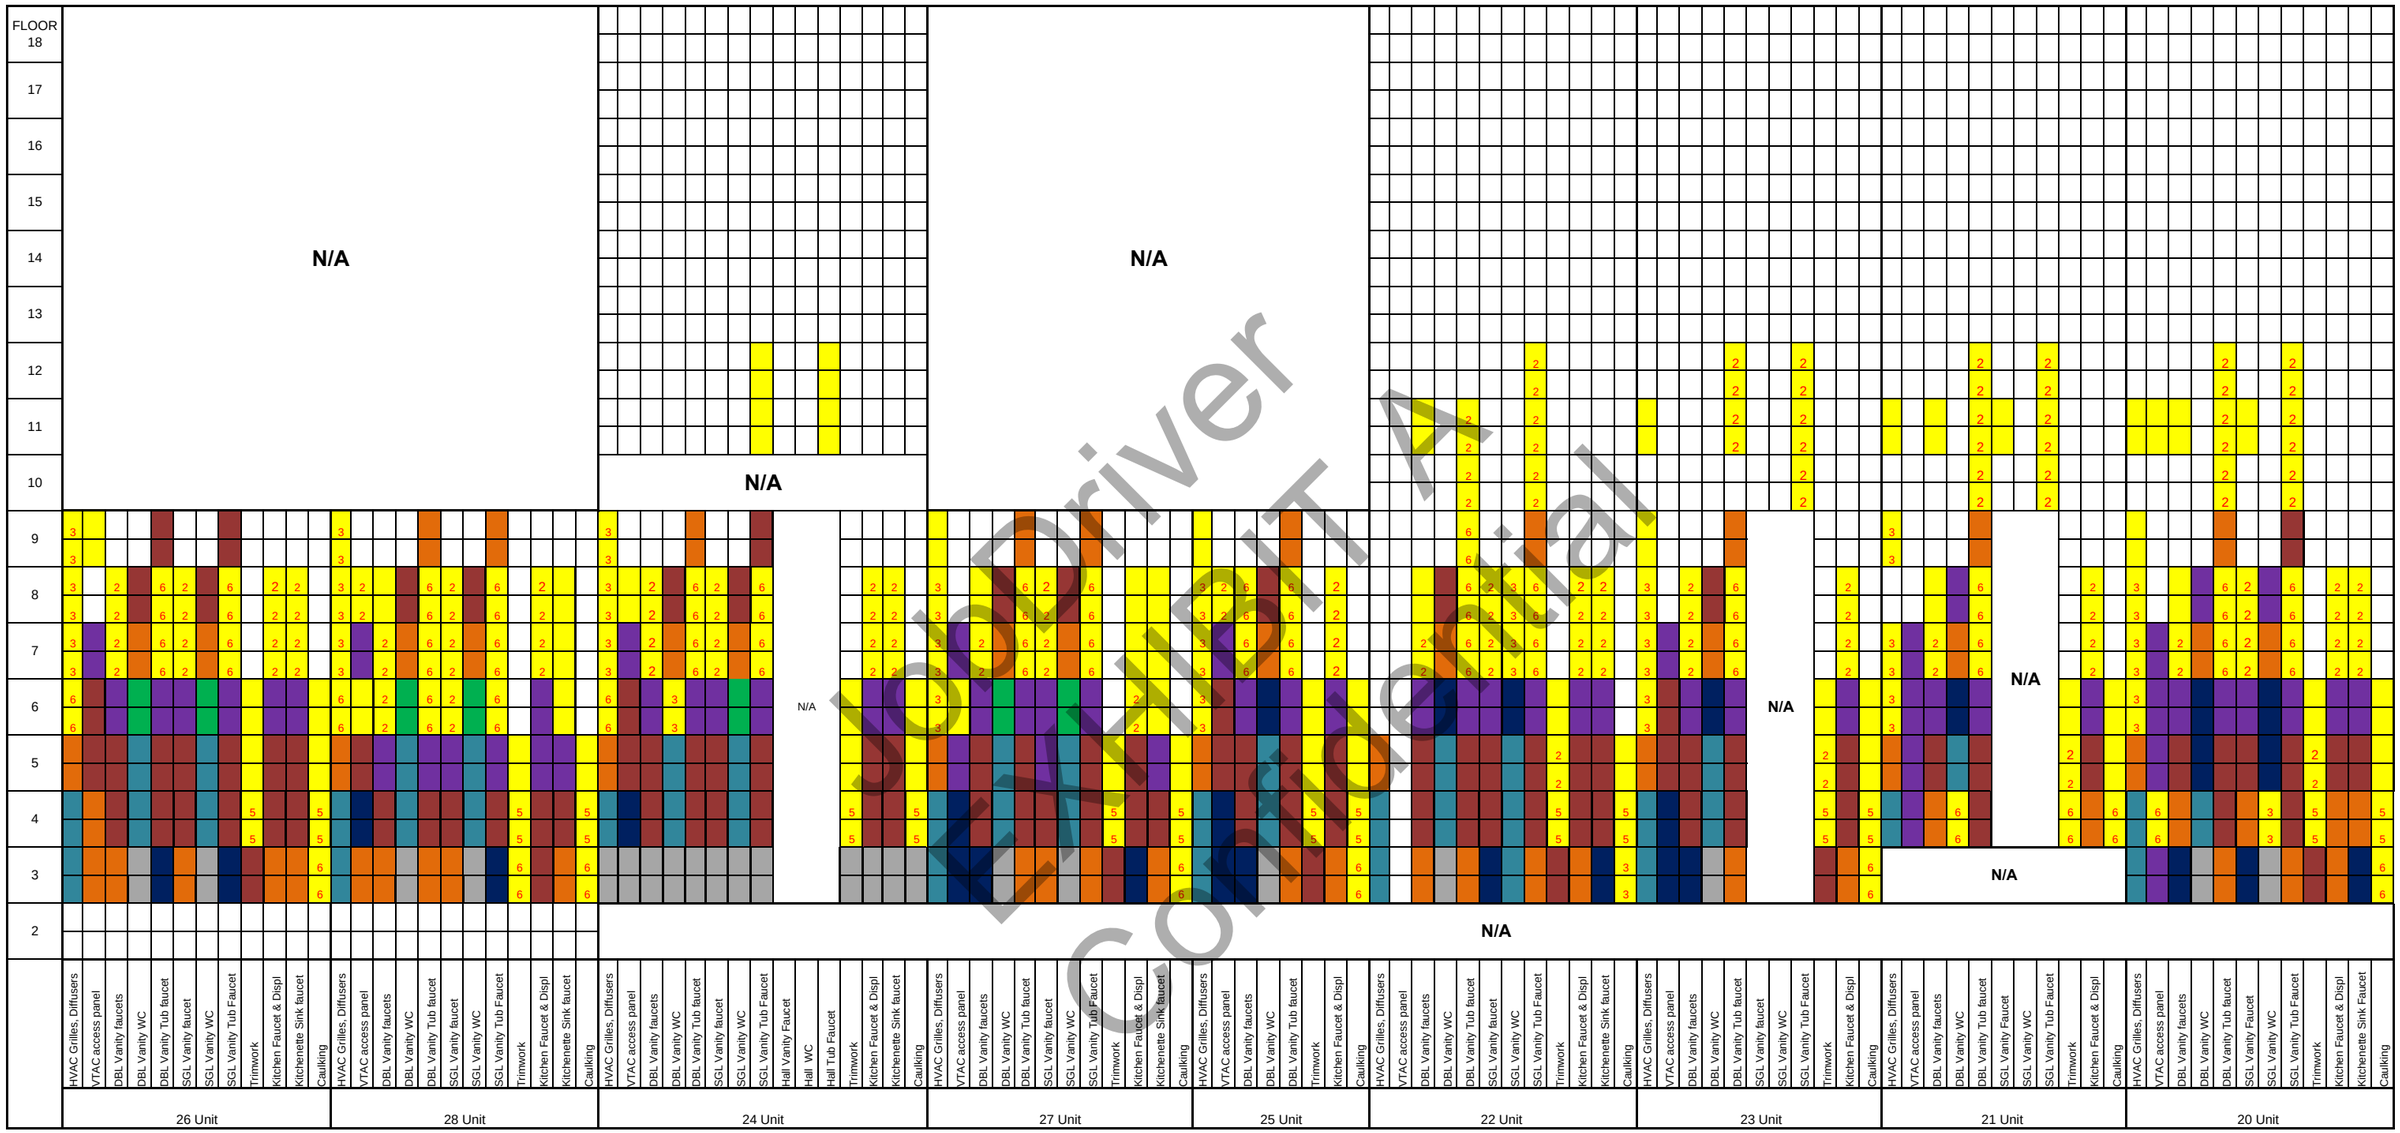

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- S/H SHOWER HEAD MISSING
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012

INCOMPLETE ITEMS

BAY MECHANICAL PROGRESS CHART

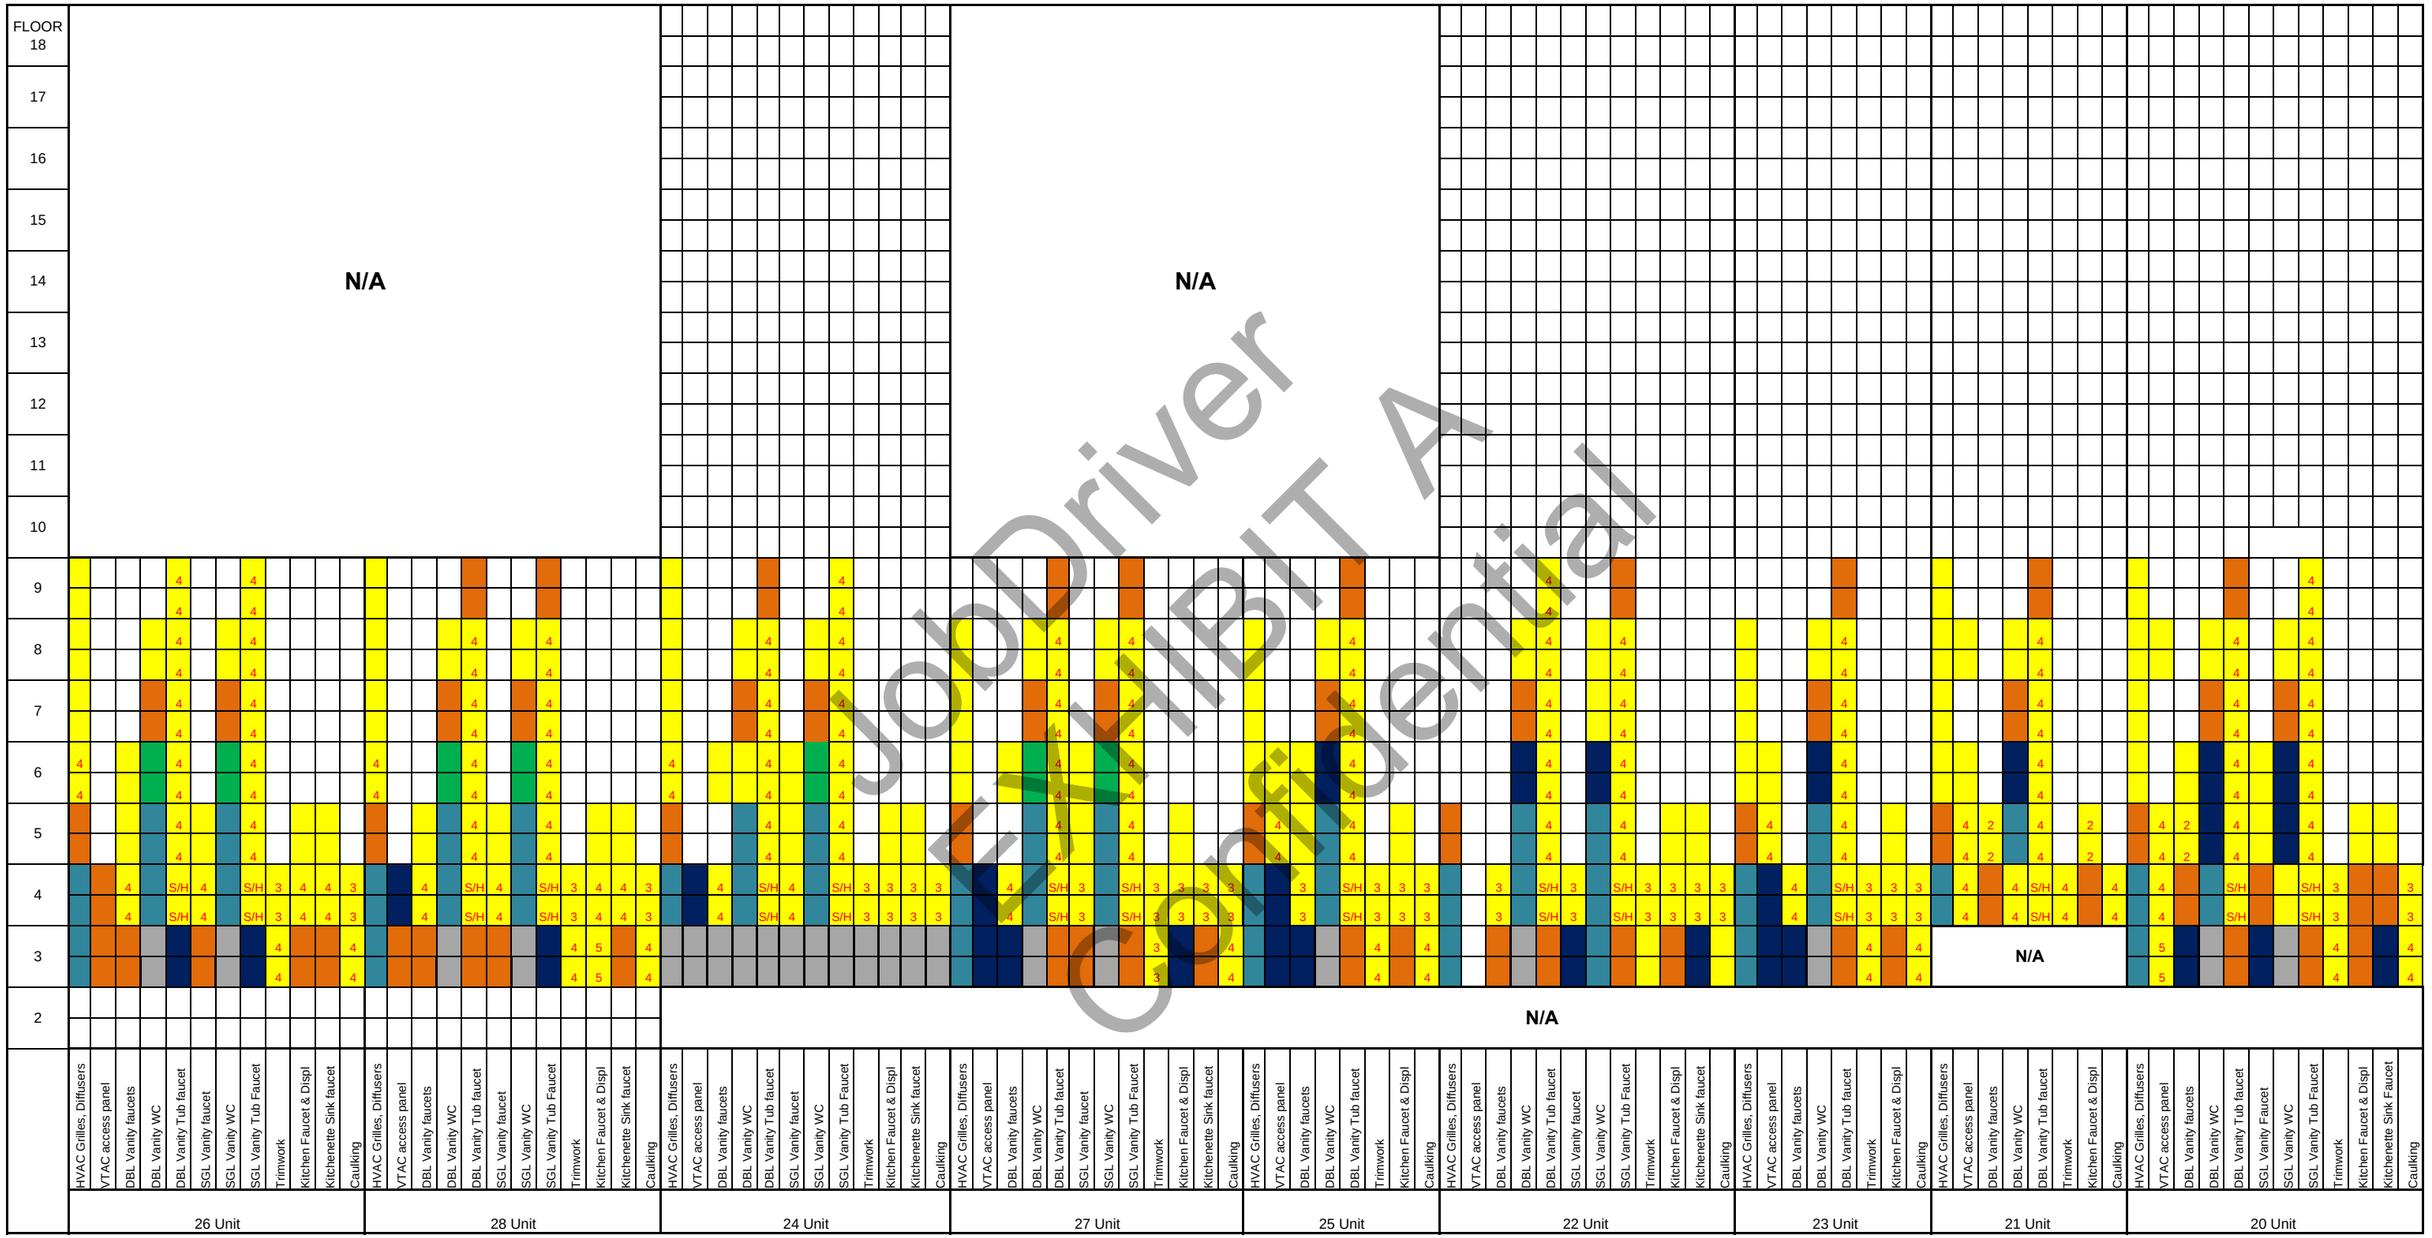

JobDriver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

Work Completed to Date 1/13/2012
Areas Available For You To Work
Areas if Work Available For Multiple Updates
Work Completed to Date 1/18/2012
WORK COMPLETED TO DATE 1/25/2012
WORK COMPLETED TO DATE 2/8/2012
S/H SHOWER HEAD MISSING

INCOMPLETE ITEMS

BAY MECHANICAL PROGRESS CHART

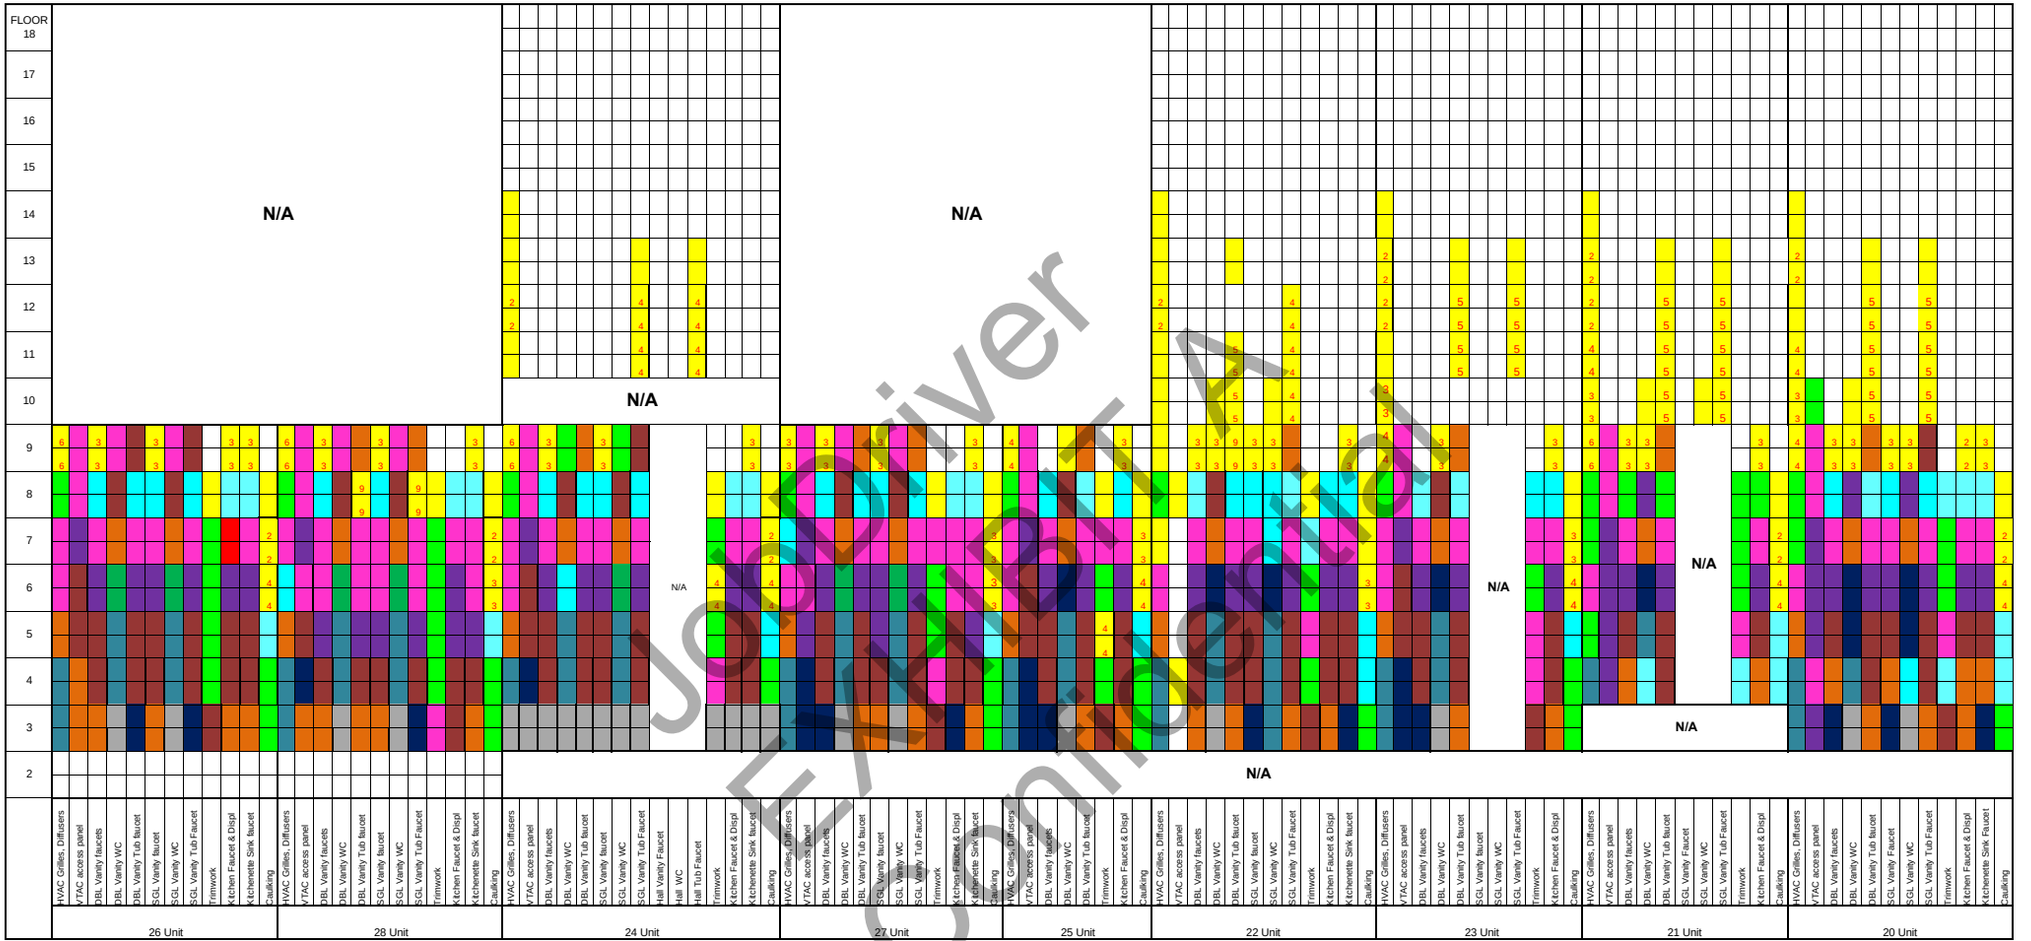

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012

INCOMPLETE ITEMS

- Missing soap dispensor in kitchen in unit 726
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012

Jobdriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

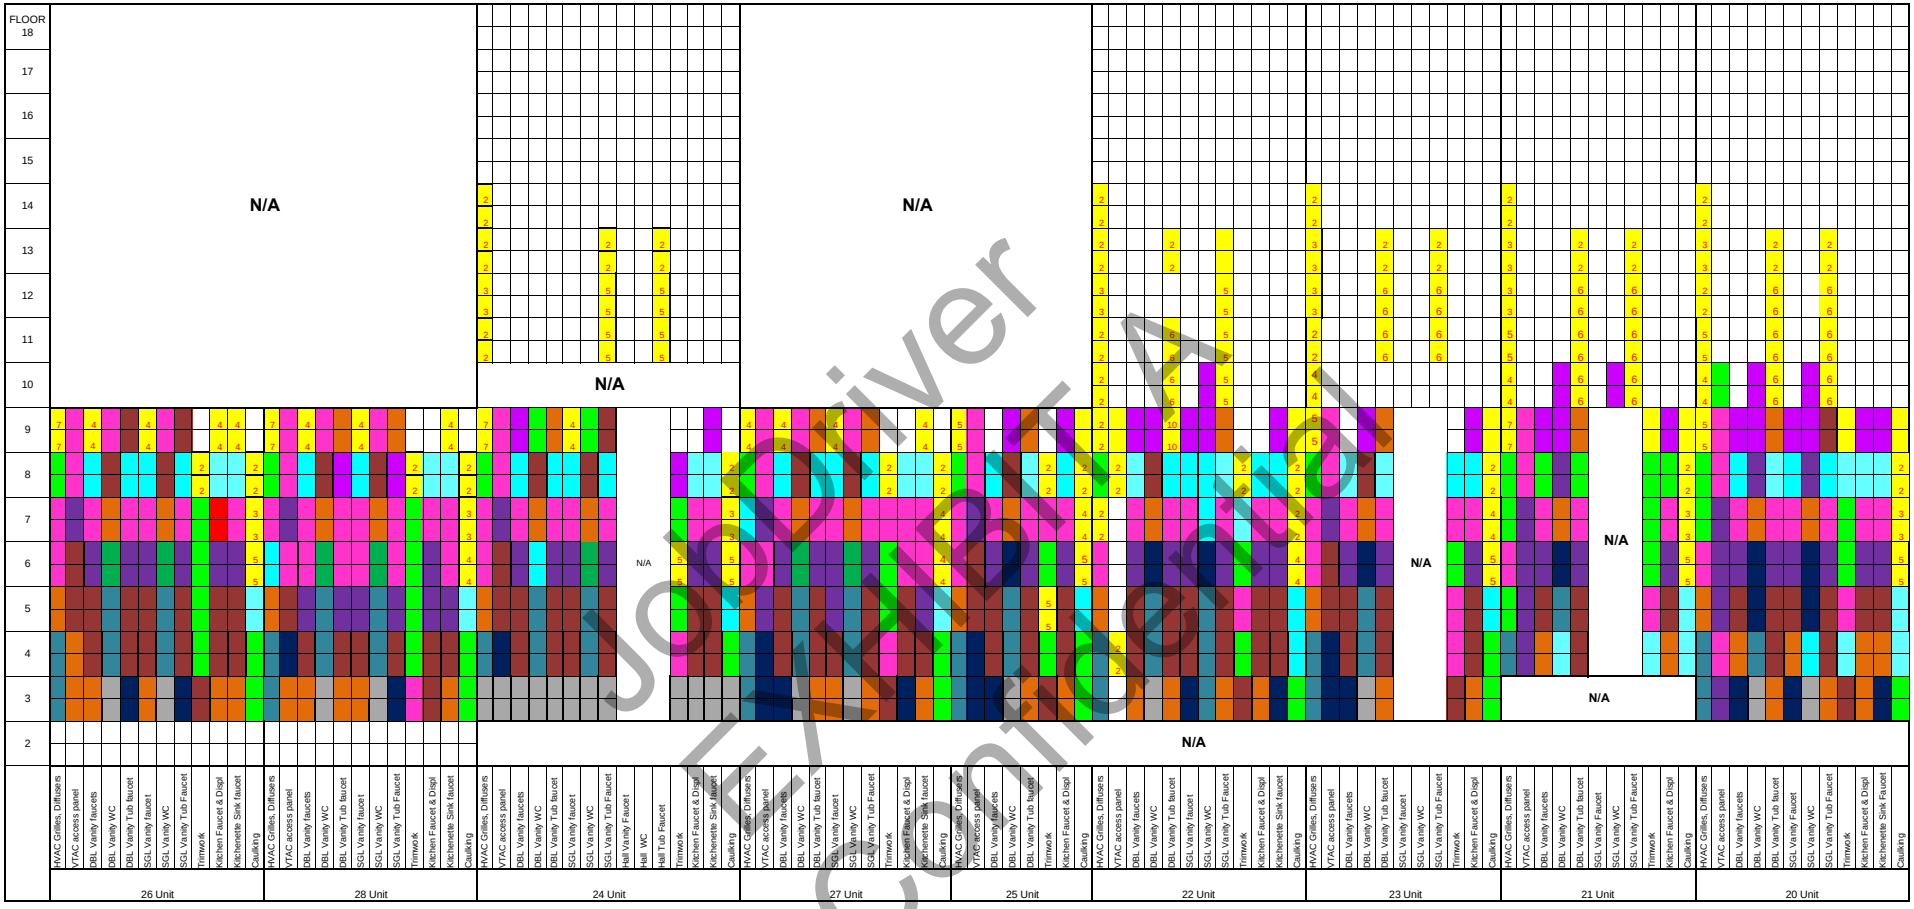

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012

INCOMPLETE ITEMS

- Missing soap dispensor in kitchen in unit 726
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012

JobDriver EXHIBIT A Confidential

BAY MECHANICAL PROGRESS CHART

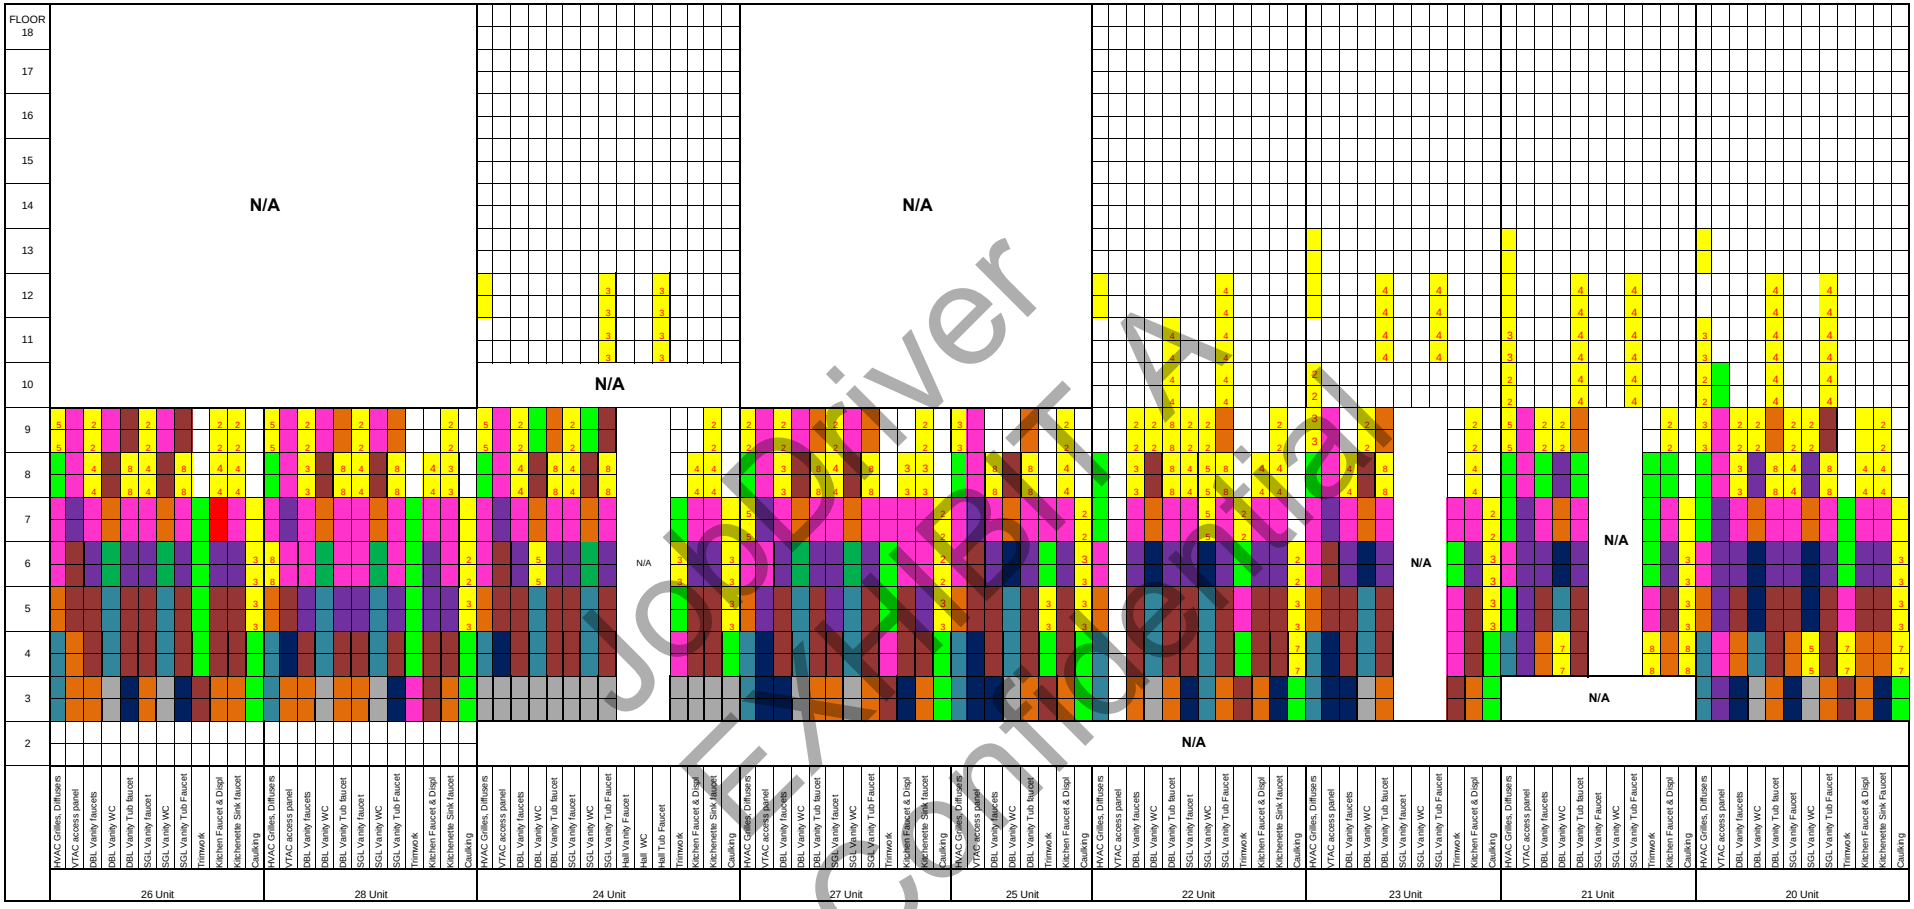

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012

INCOMPLETE ITEMS

- Missing soap dispensor in kitchen in unit 726

JobDriver EXHIBIT A Confidential

BAY MECHANICAL PROGRESS CHART

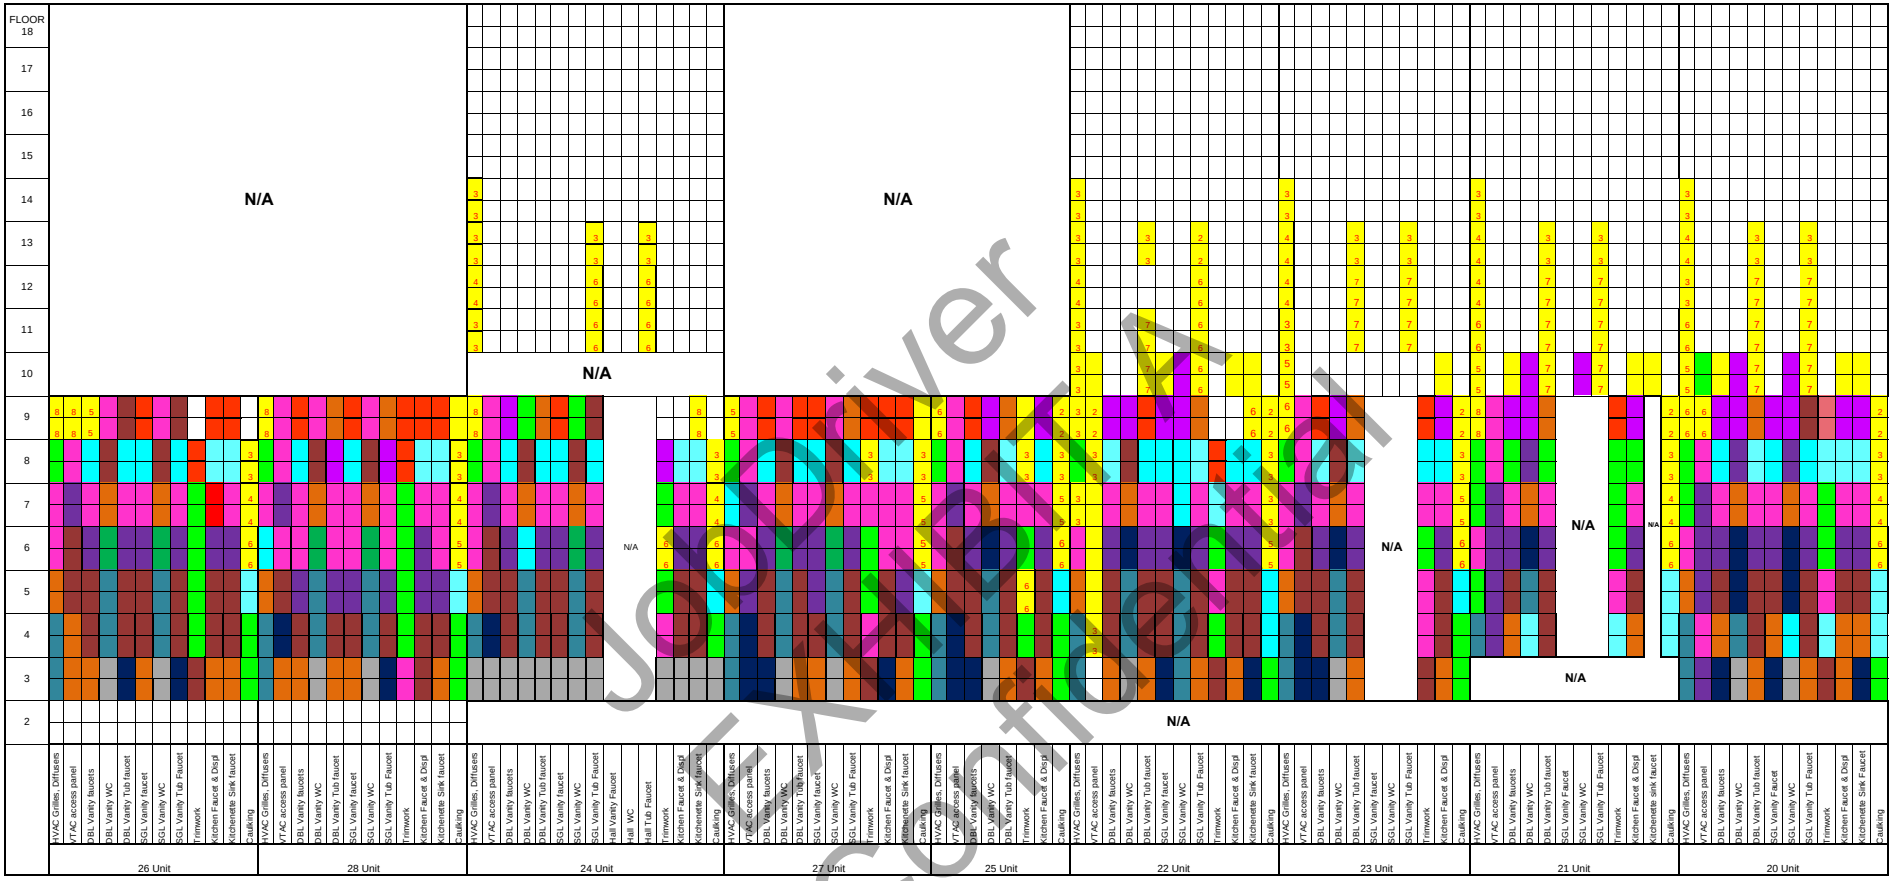

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012

Job Driver
Exhibit A
Confidential

BAY MECHANICAL PROGRESS CHART

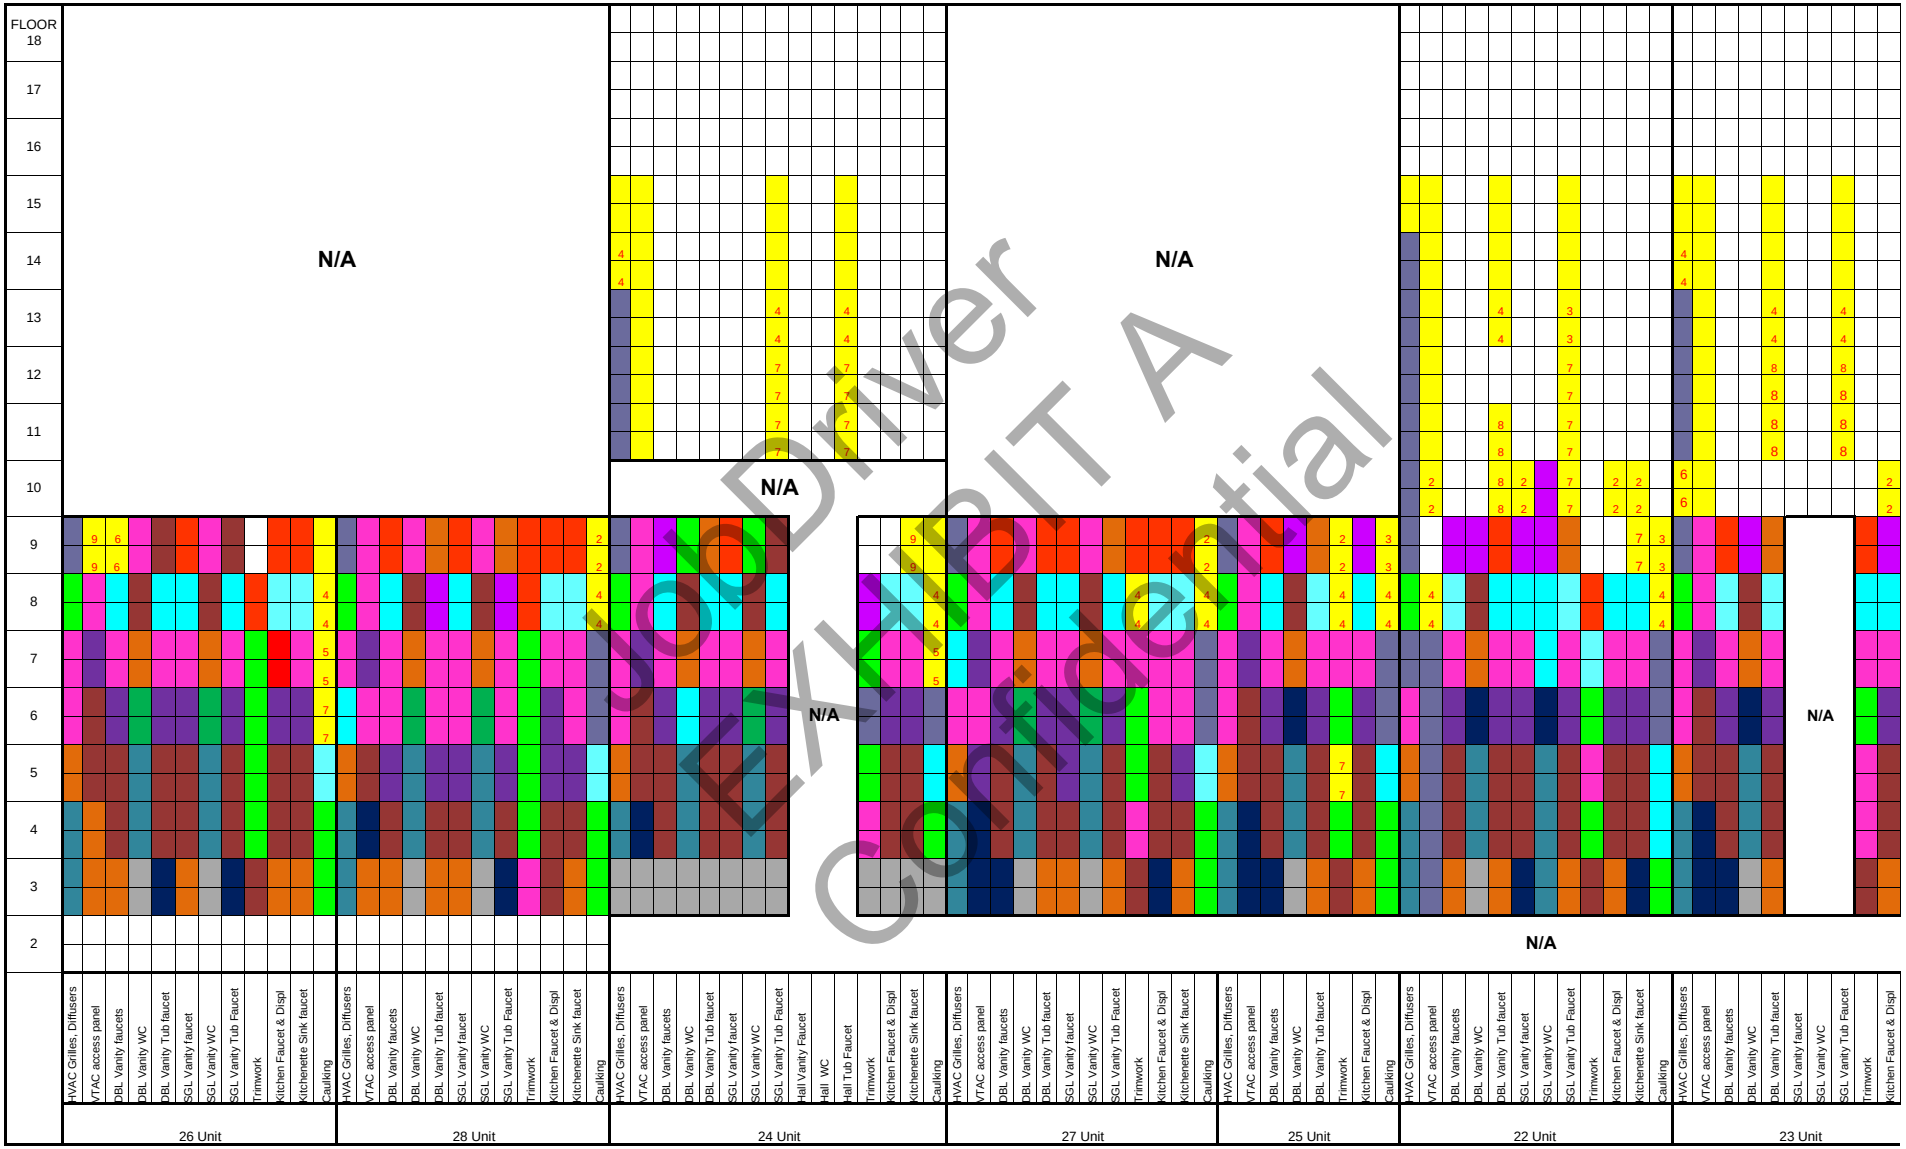

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012

BAY MECHANICAL PROGRESS CHART

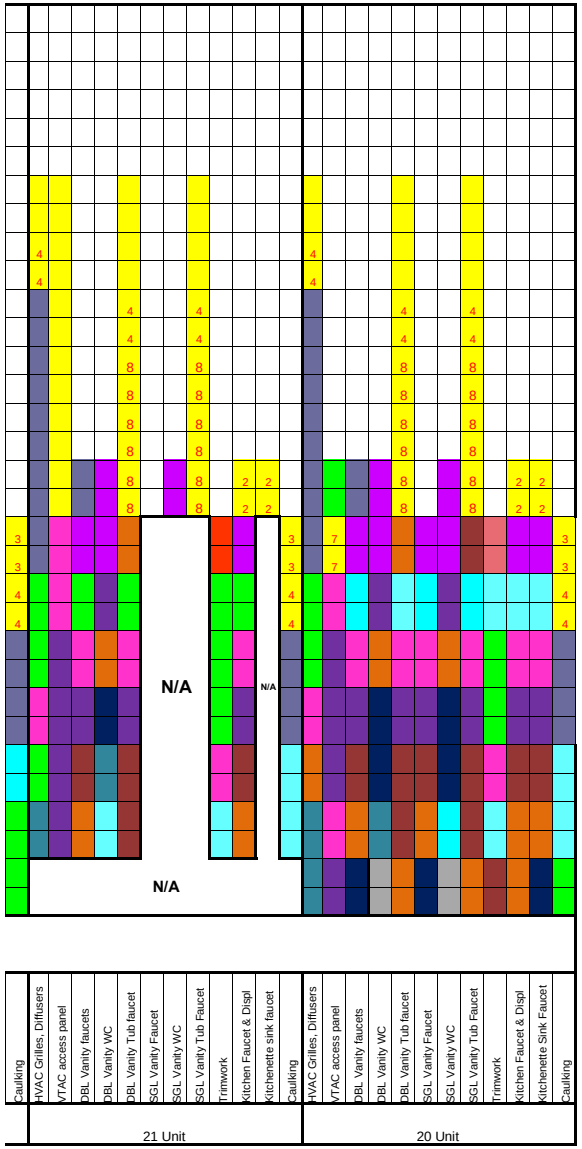

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

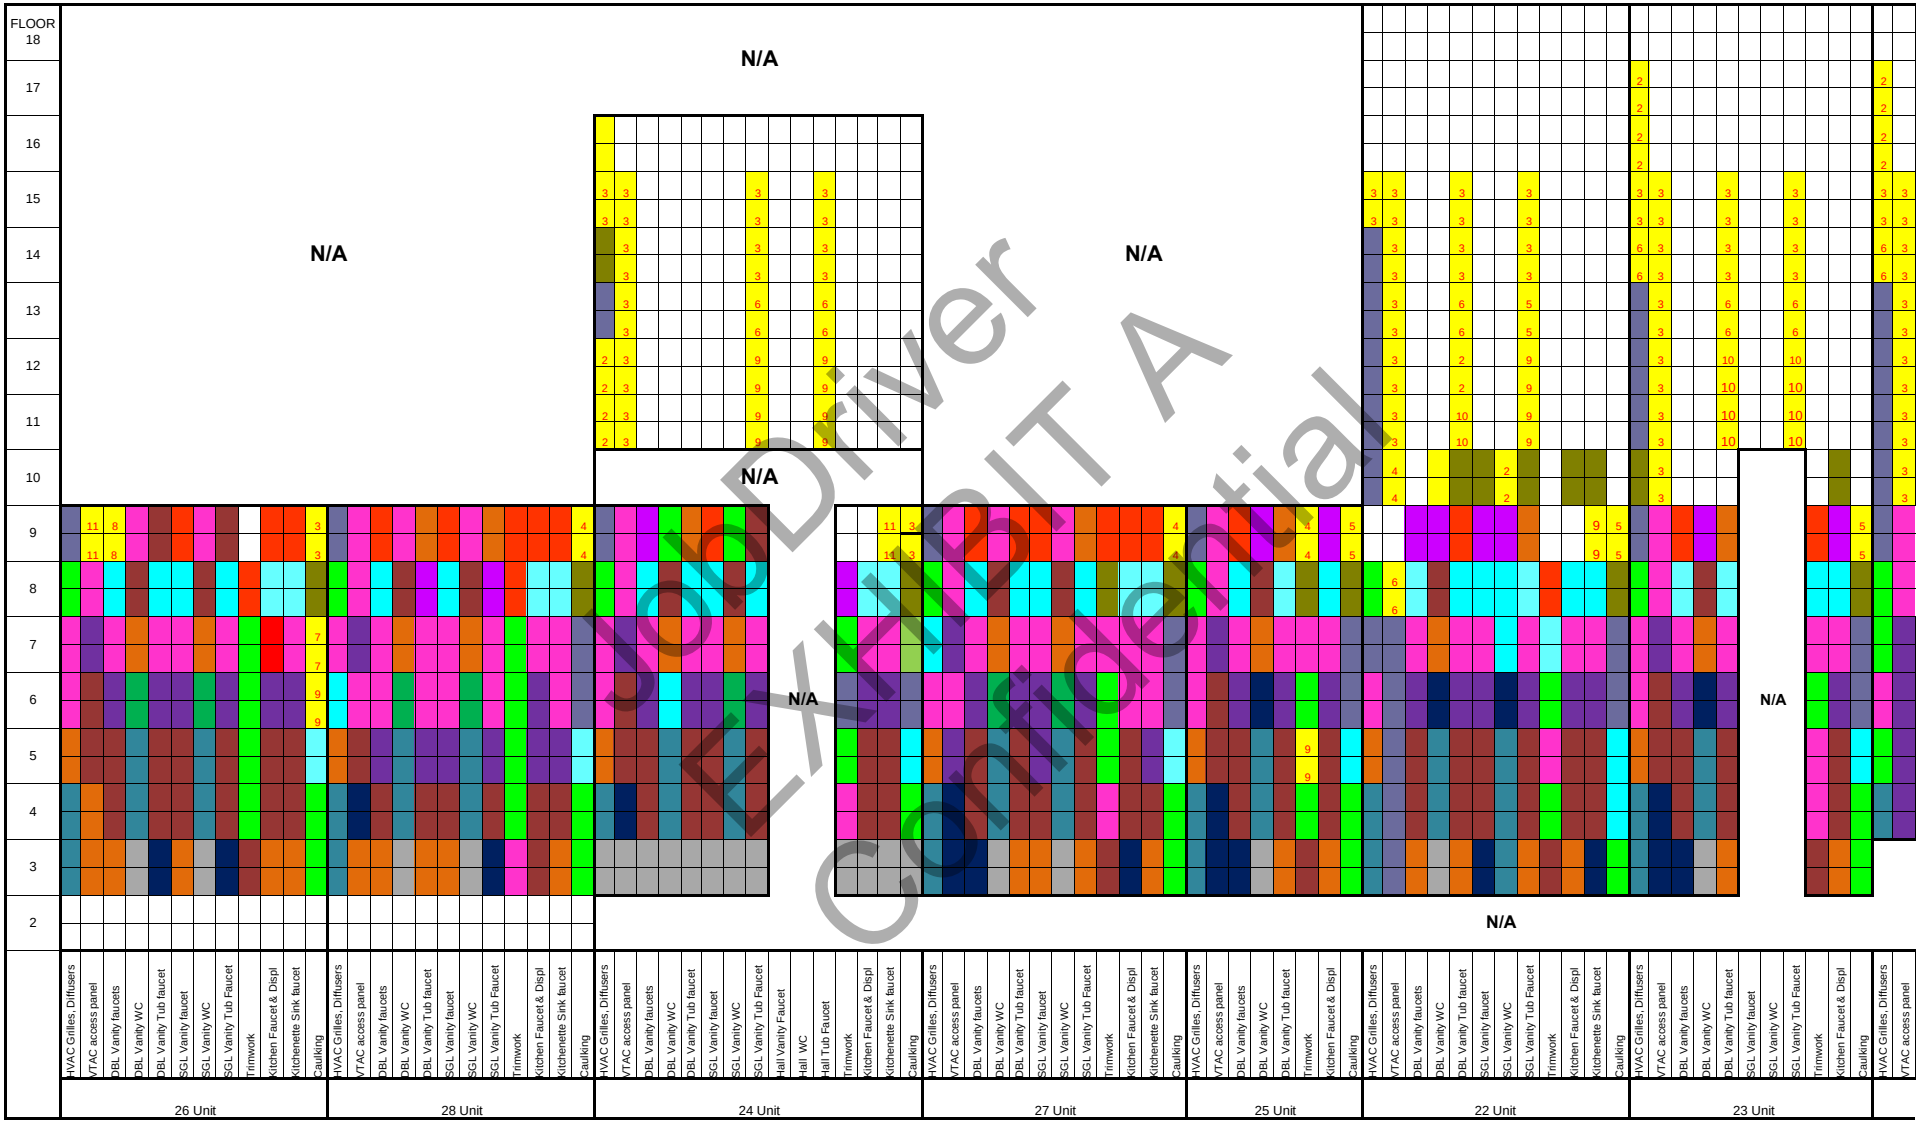

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012

BAY MECHANICAL PROGRESS CHART

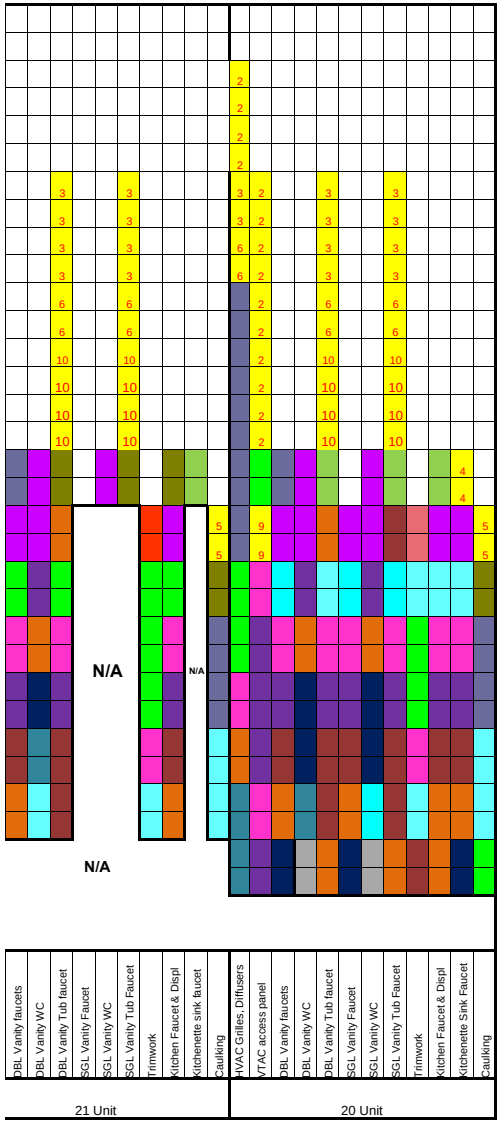

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

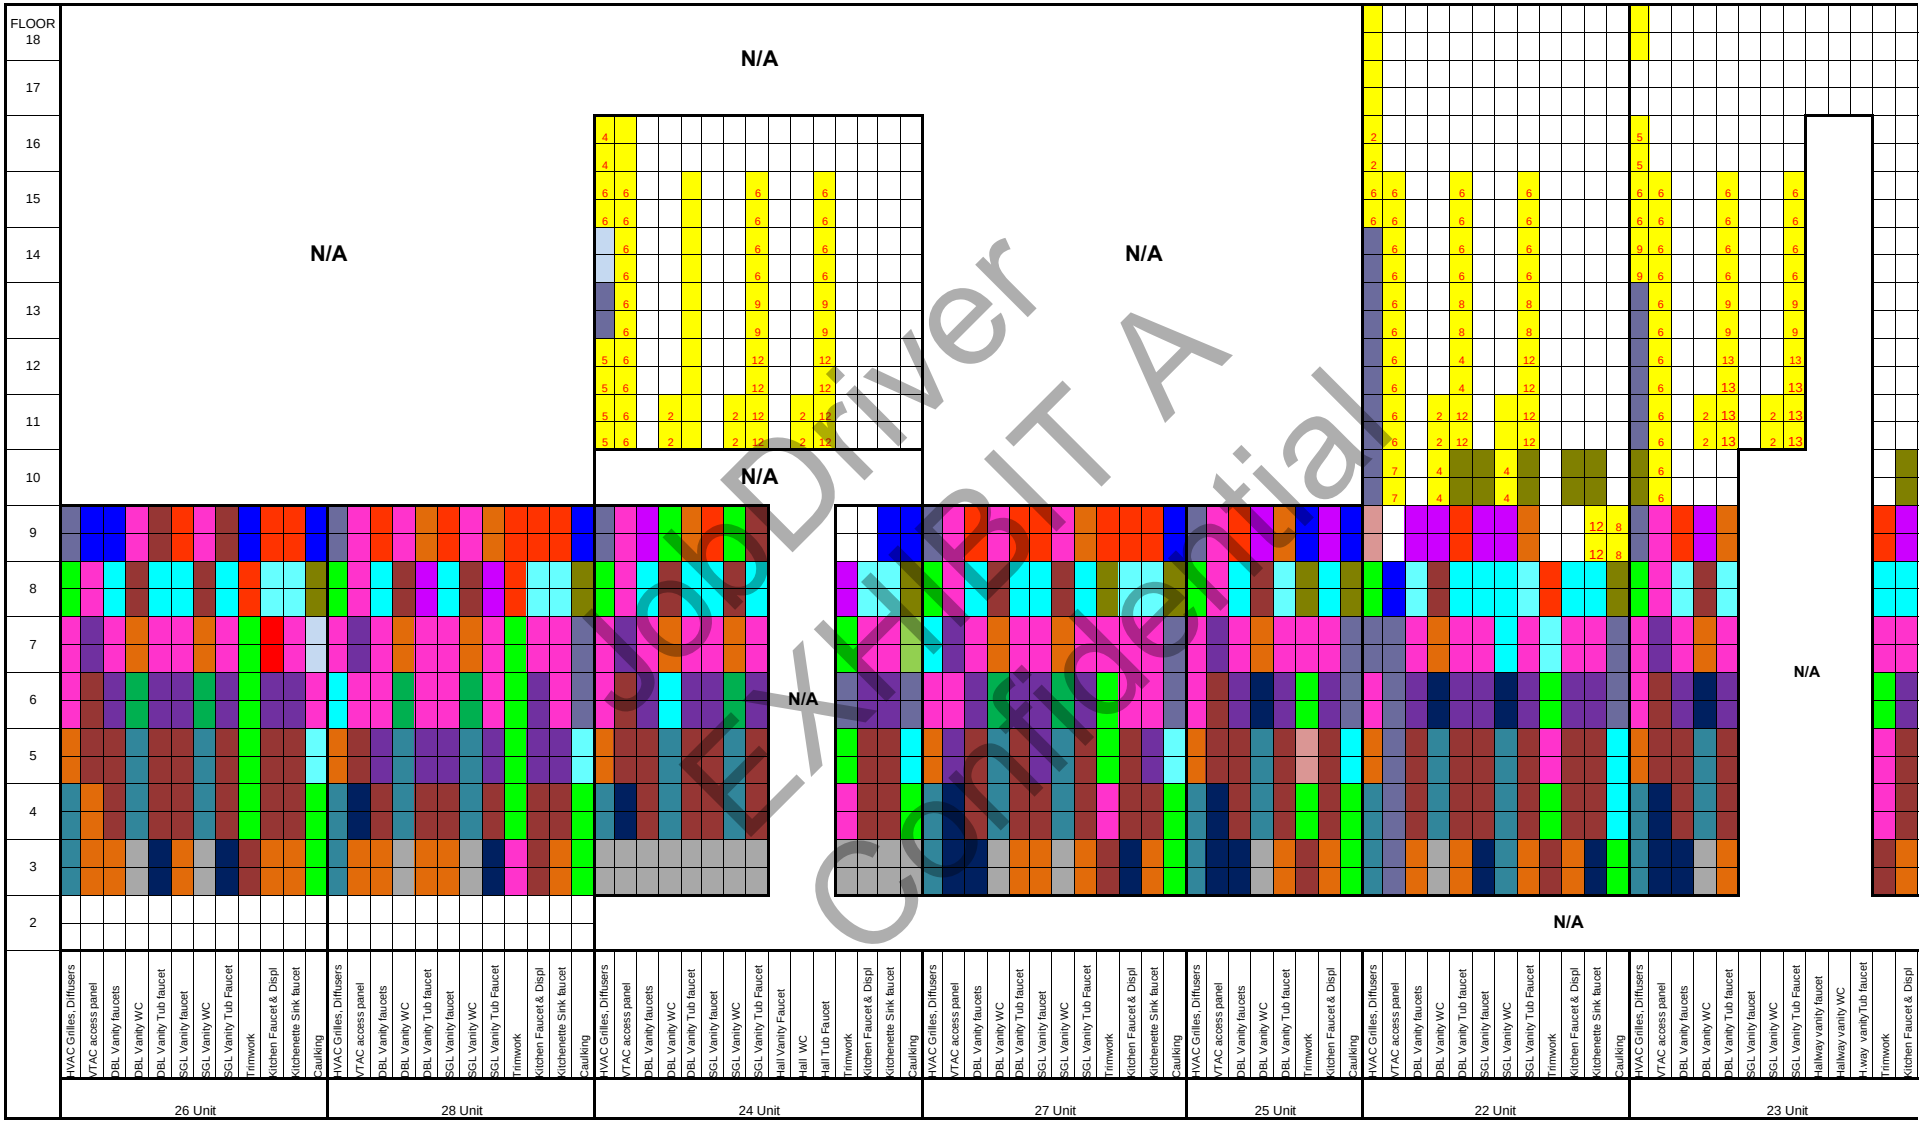

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

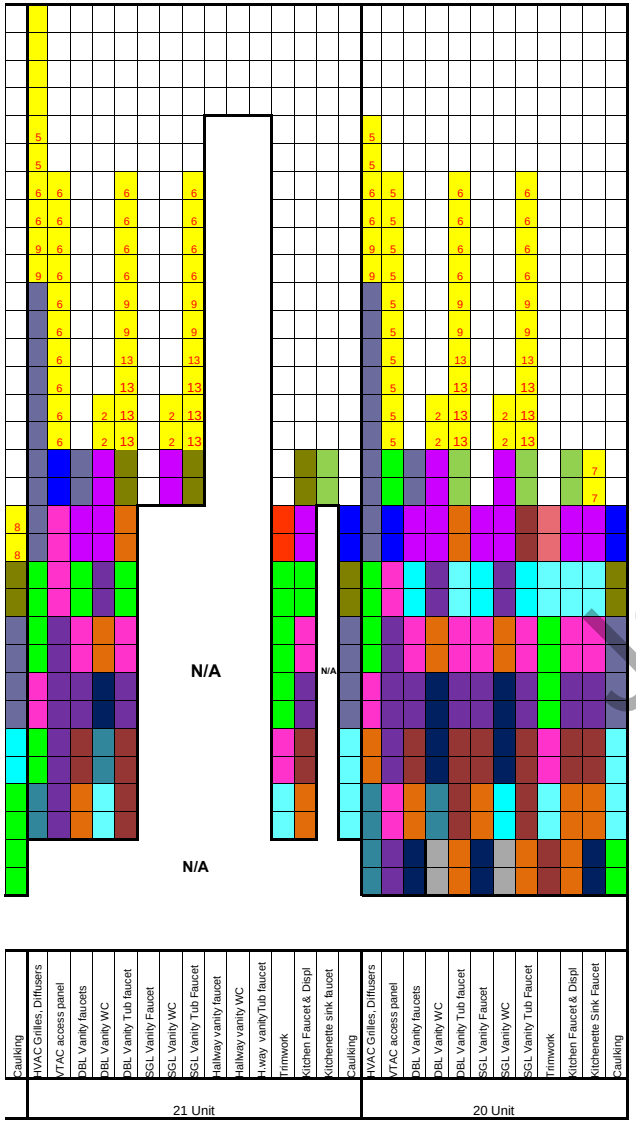

5/2/2012
5/9/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

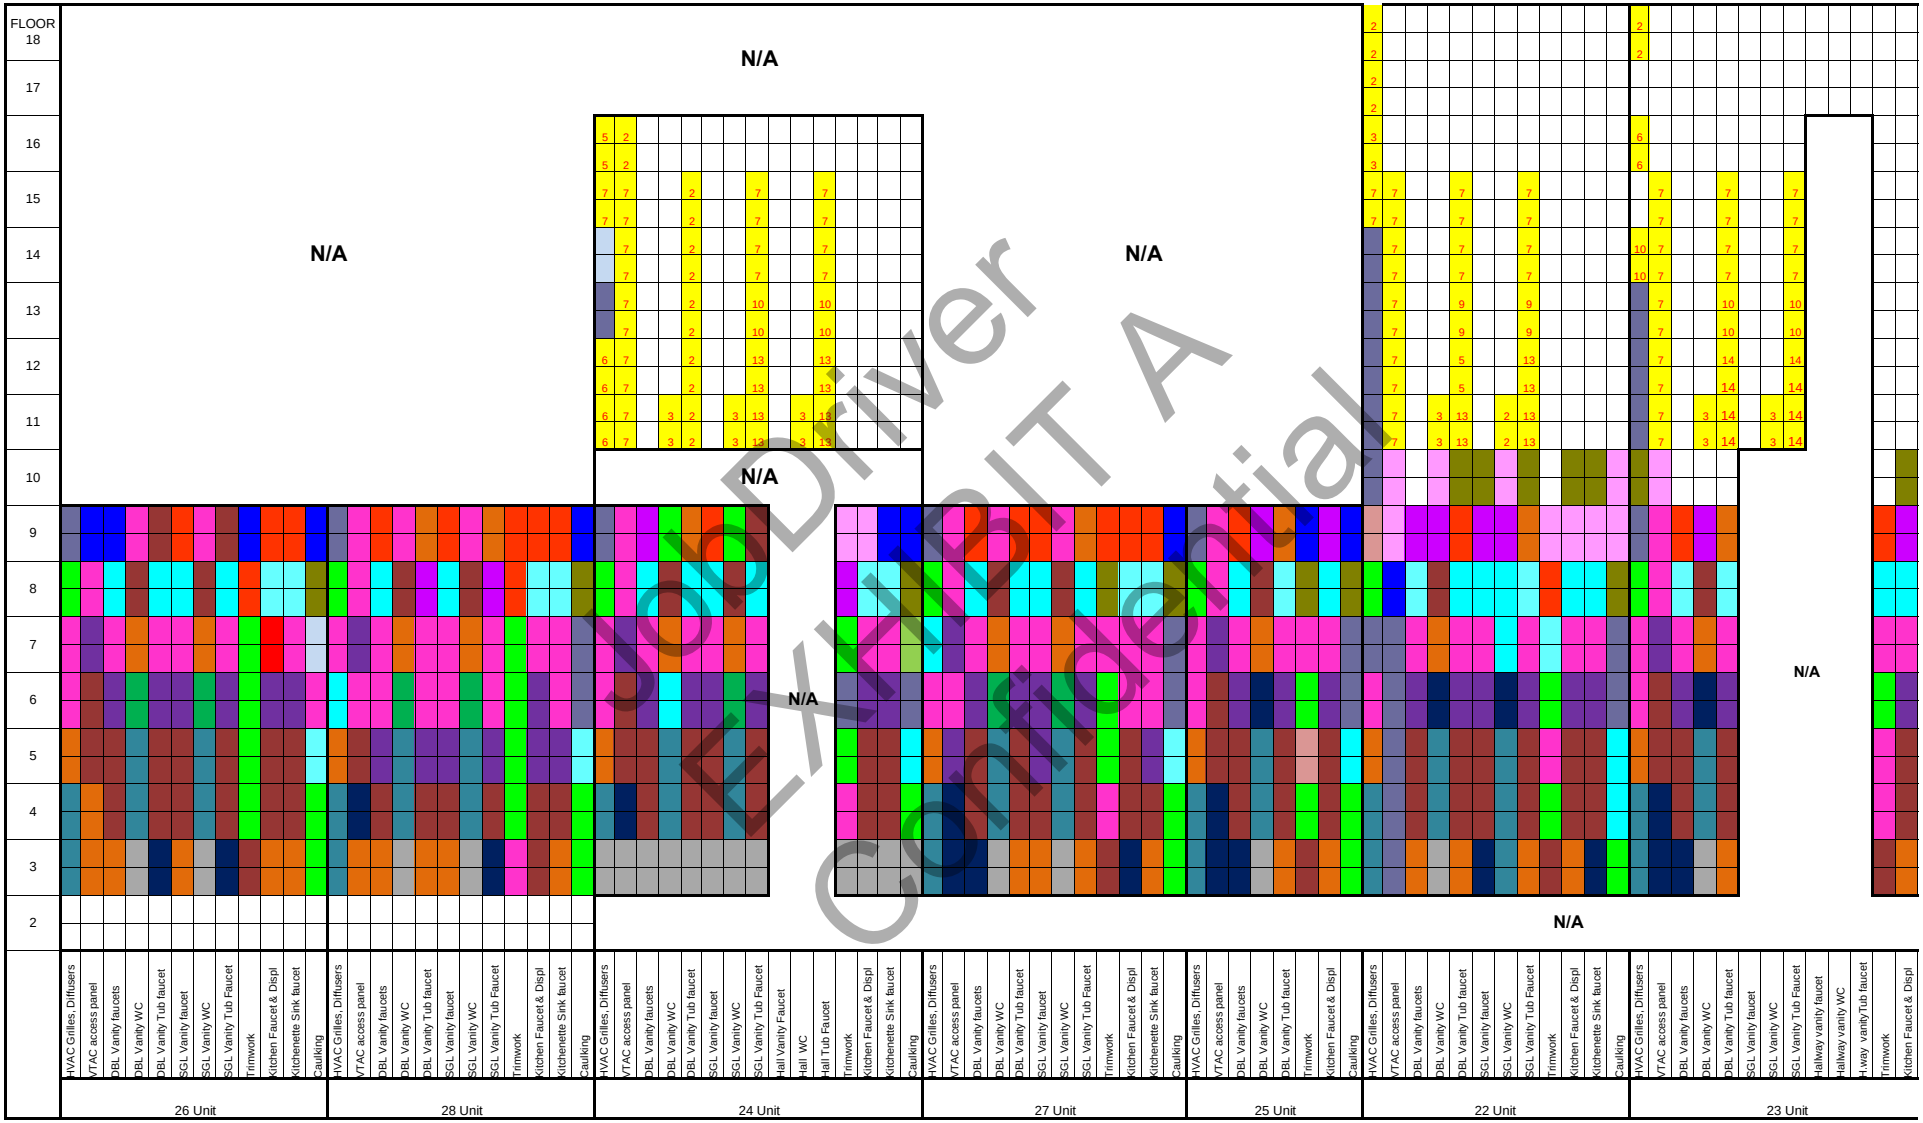

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

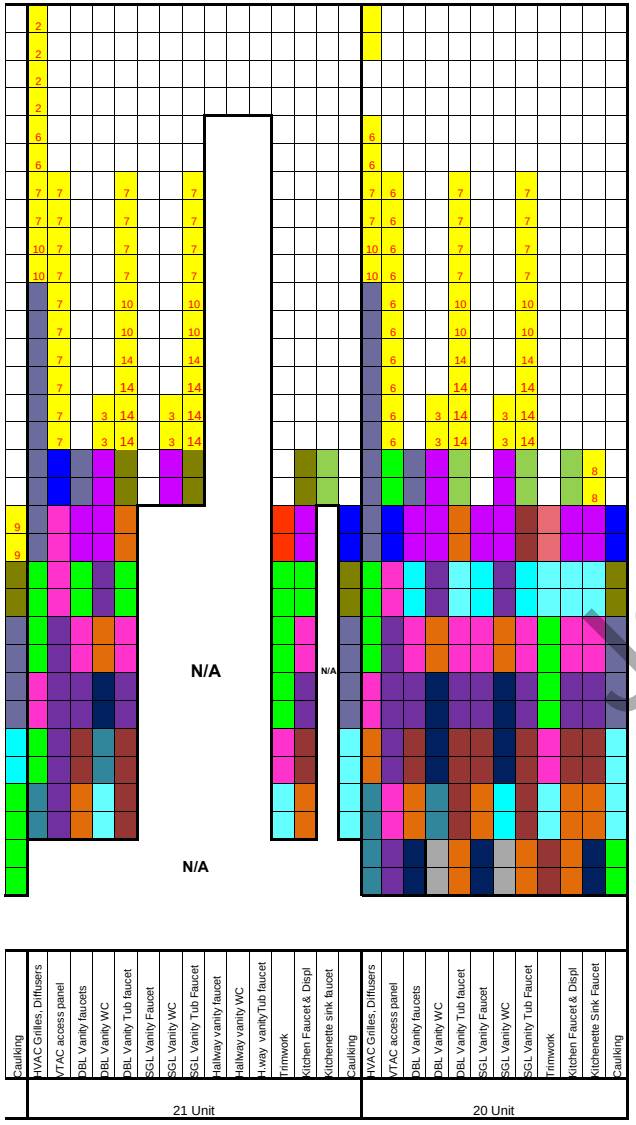

: 5/2/2012
: 5/9/2012
: 5/16/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

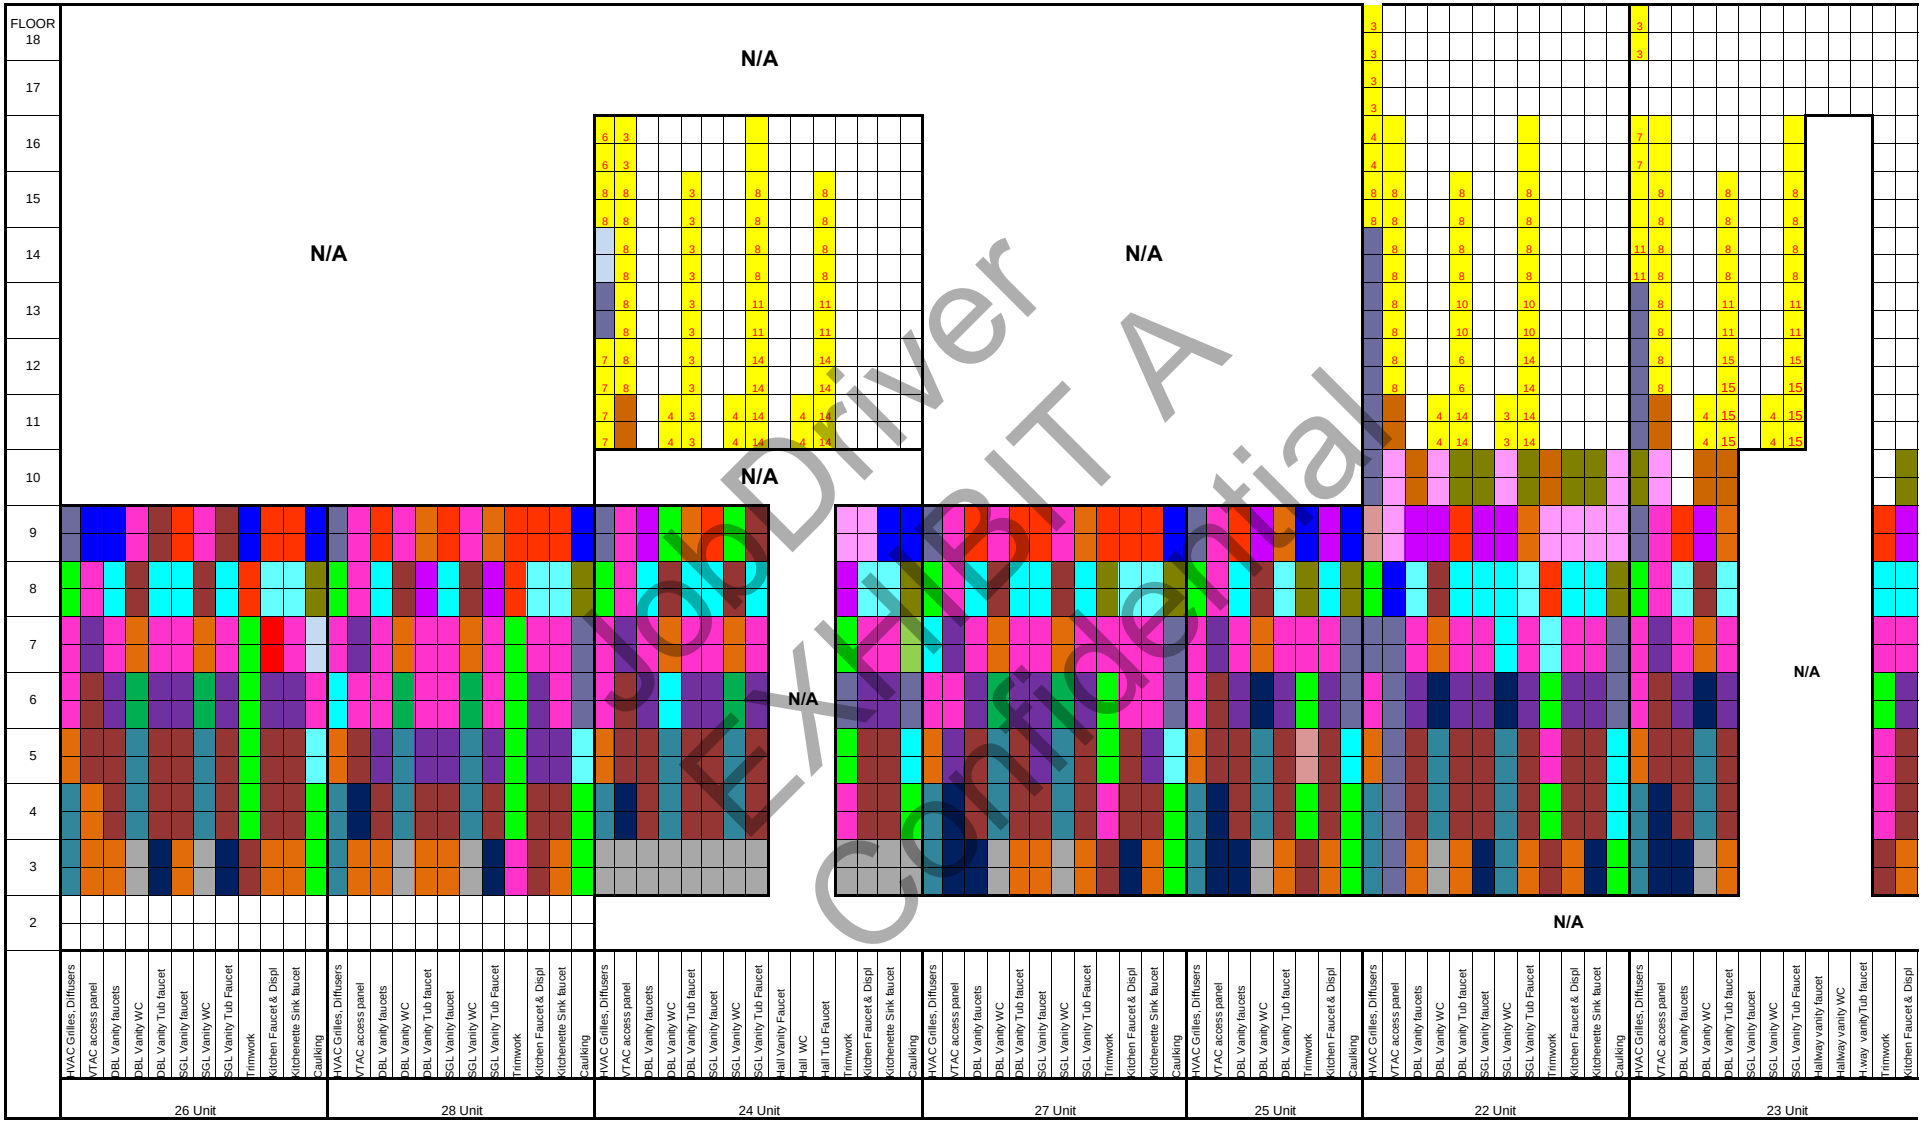

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

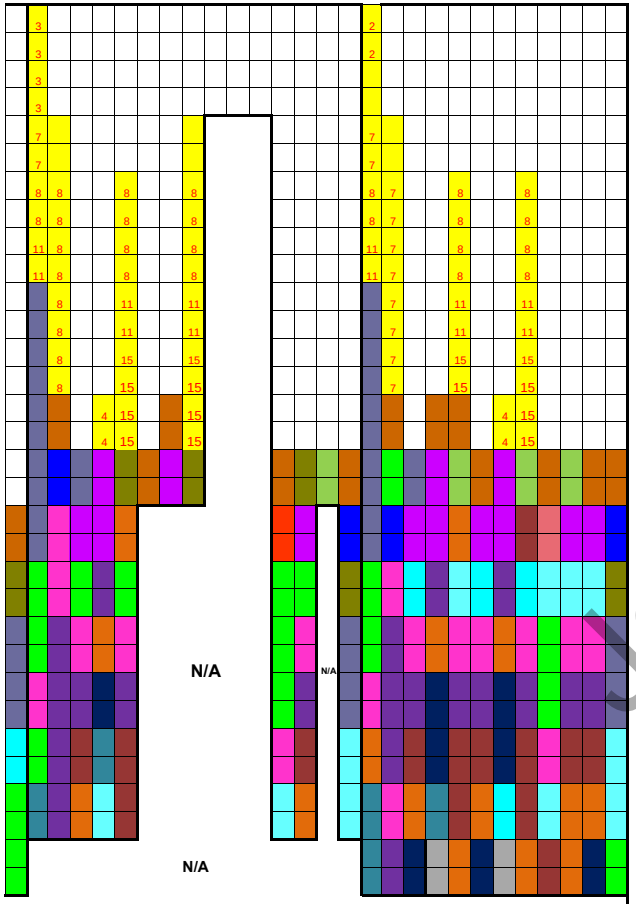

| | | |

BAY MECHANICAL PROGRESS CHART

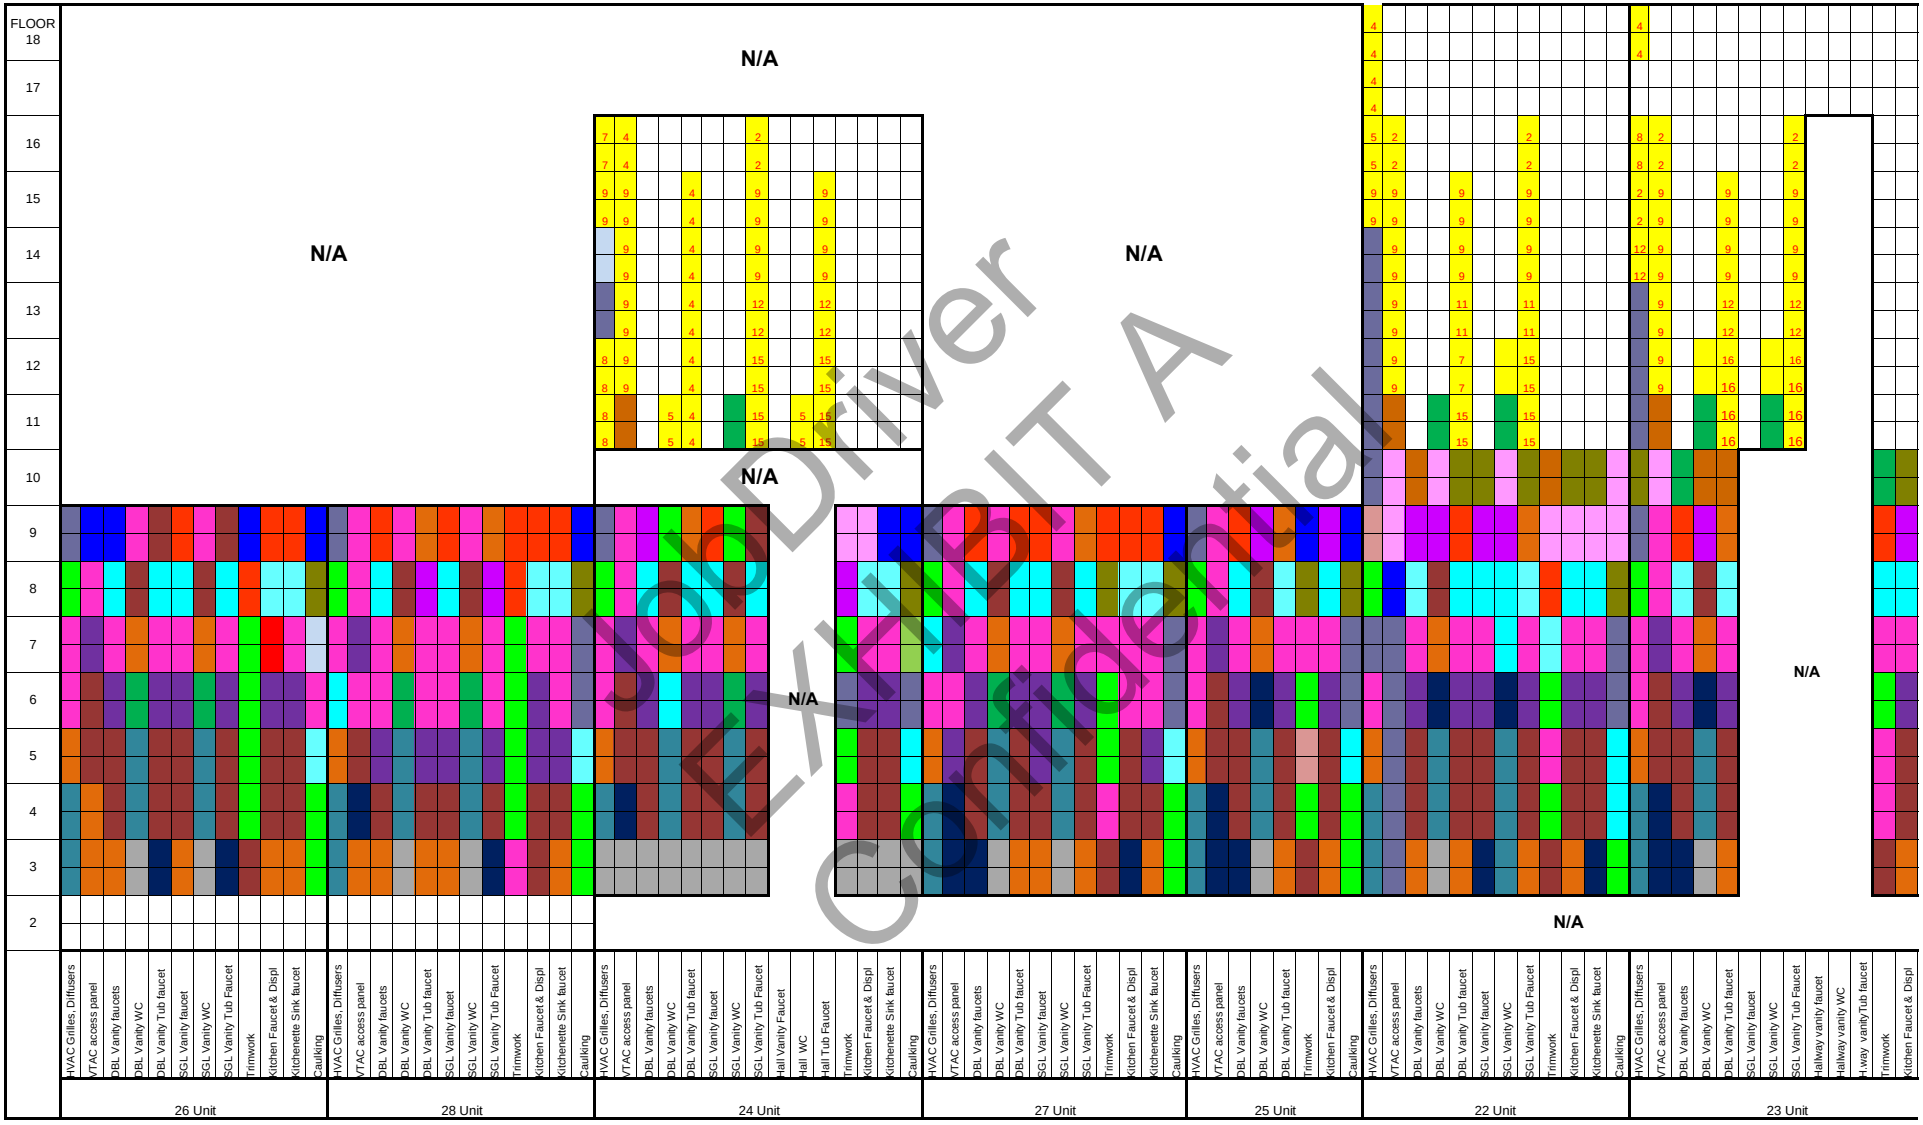

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

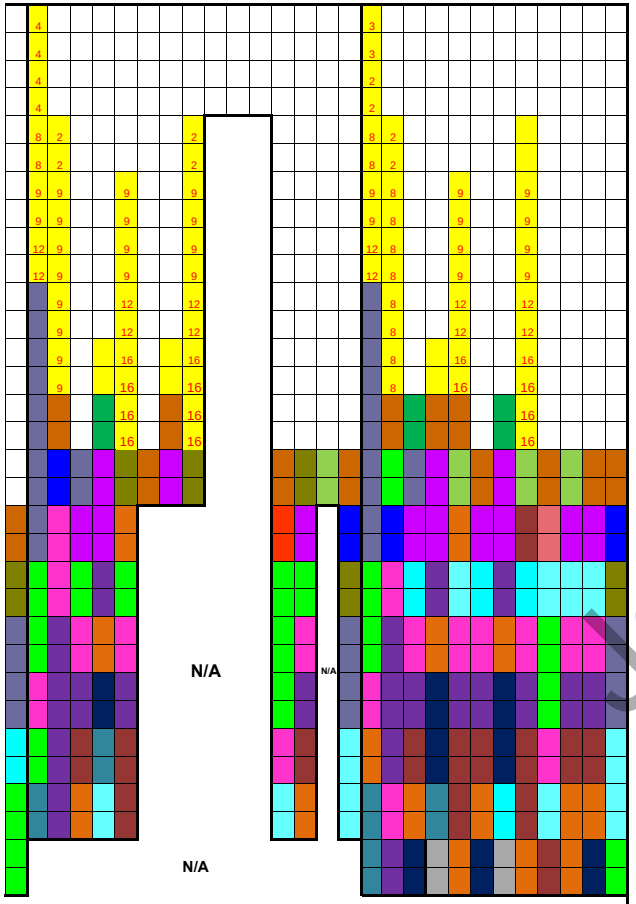

Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit

20 Unit

5/2/2012
5/9/2012
5/16/2012
5/23/2012

WORK COMPLETED TO DATE 5/30/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

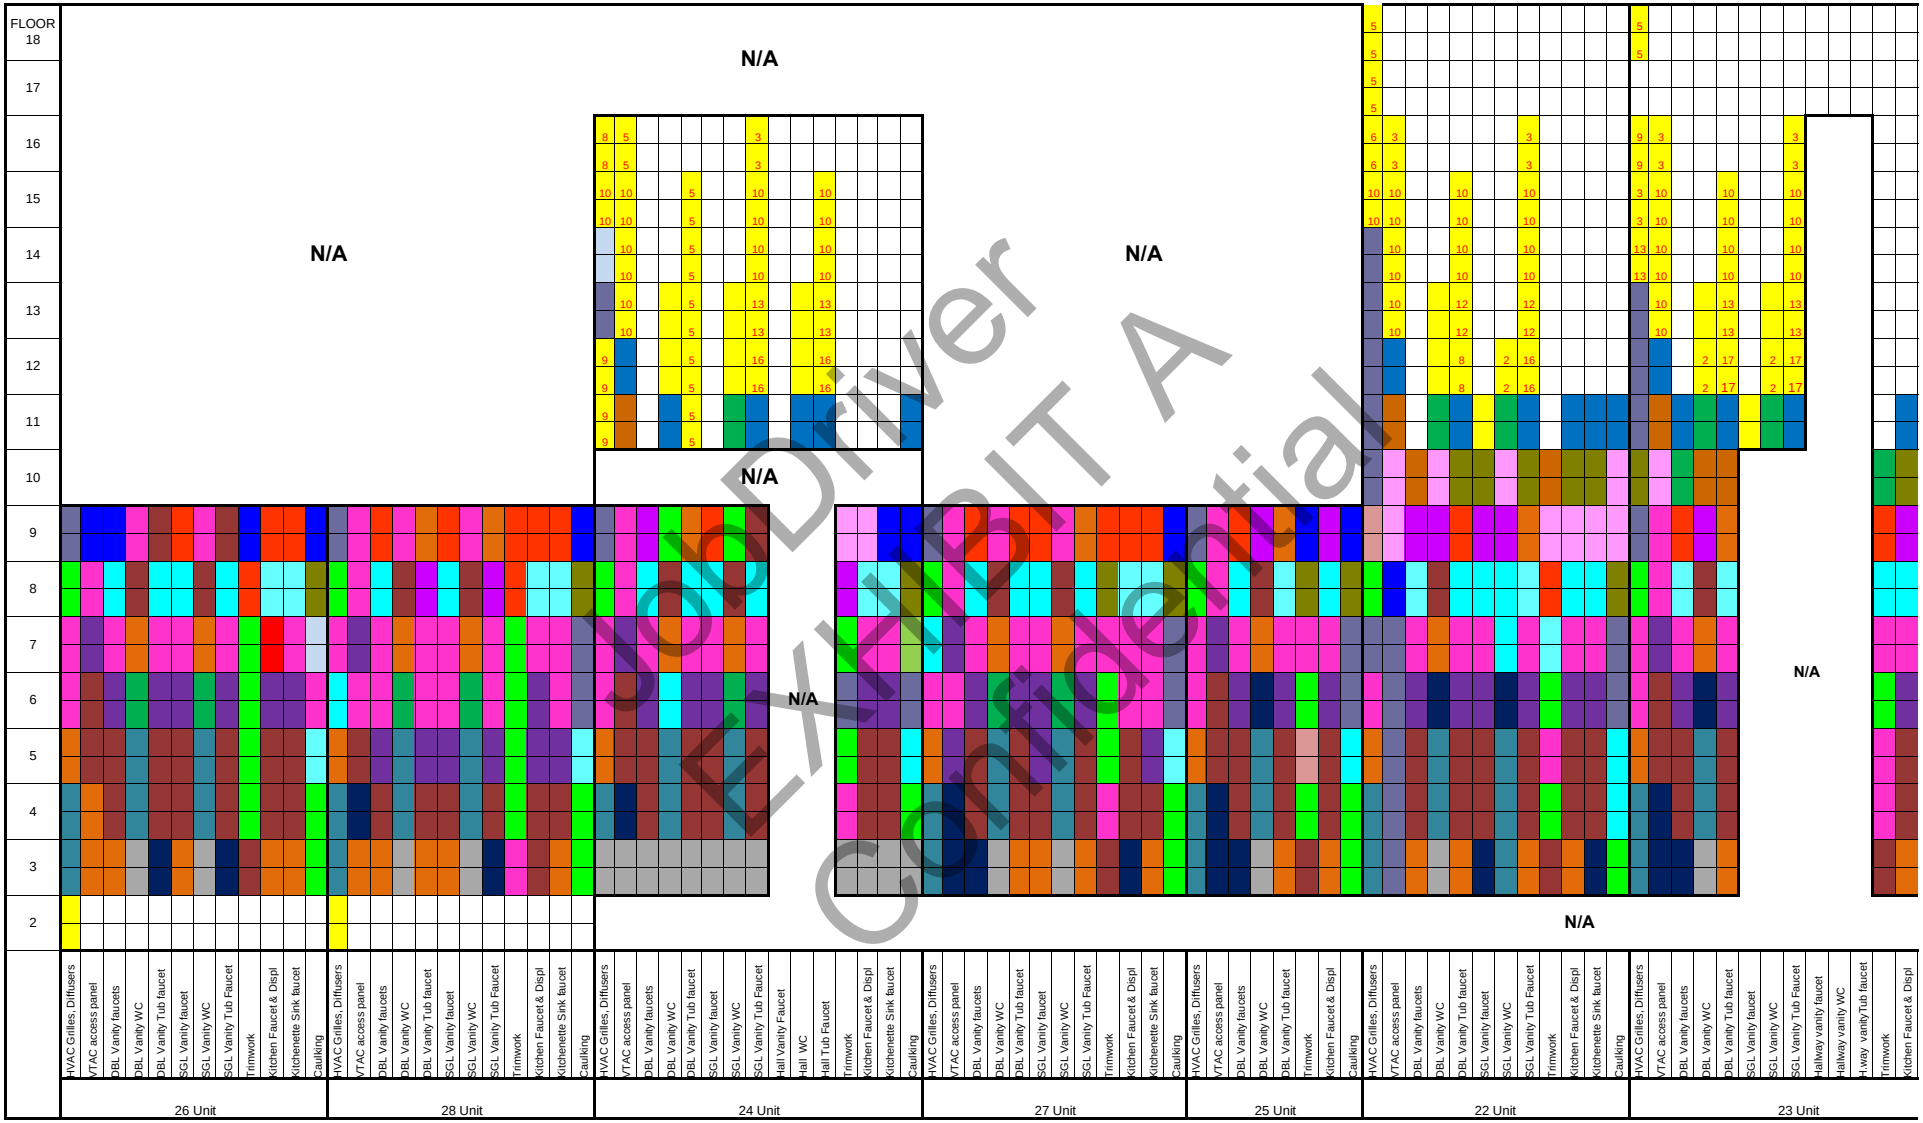

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

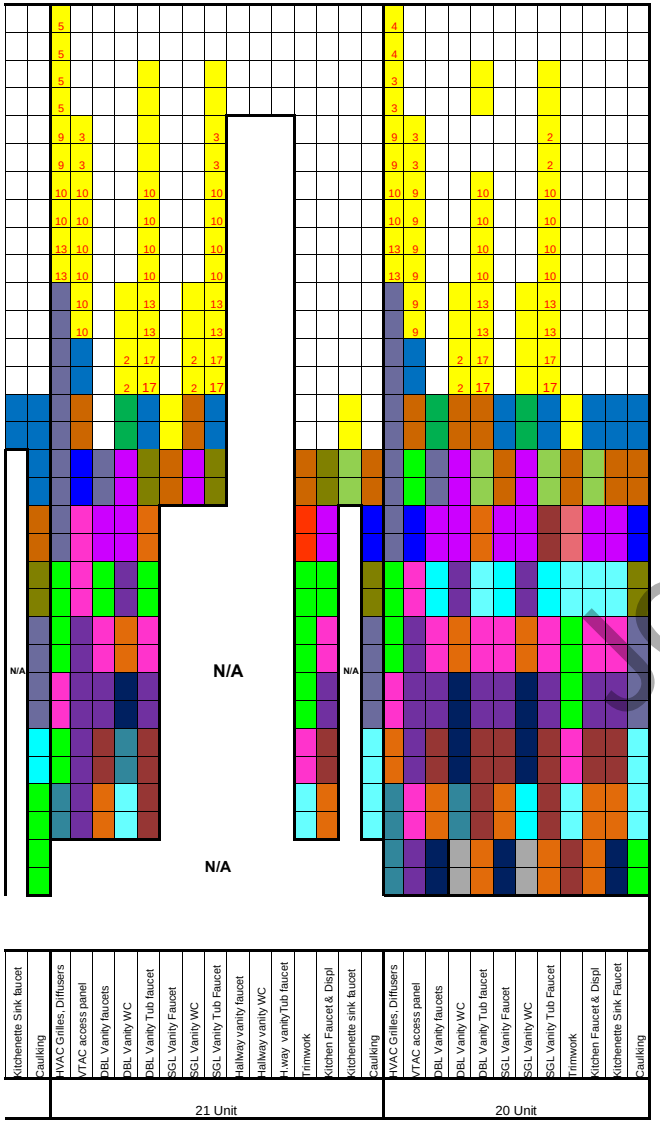

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

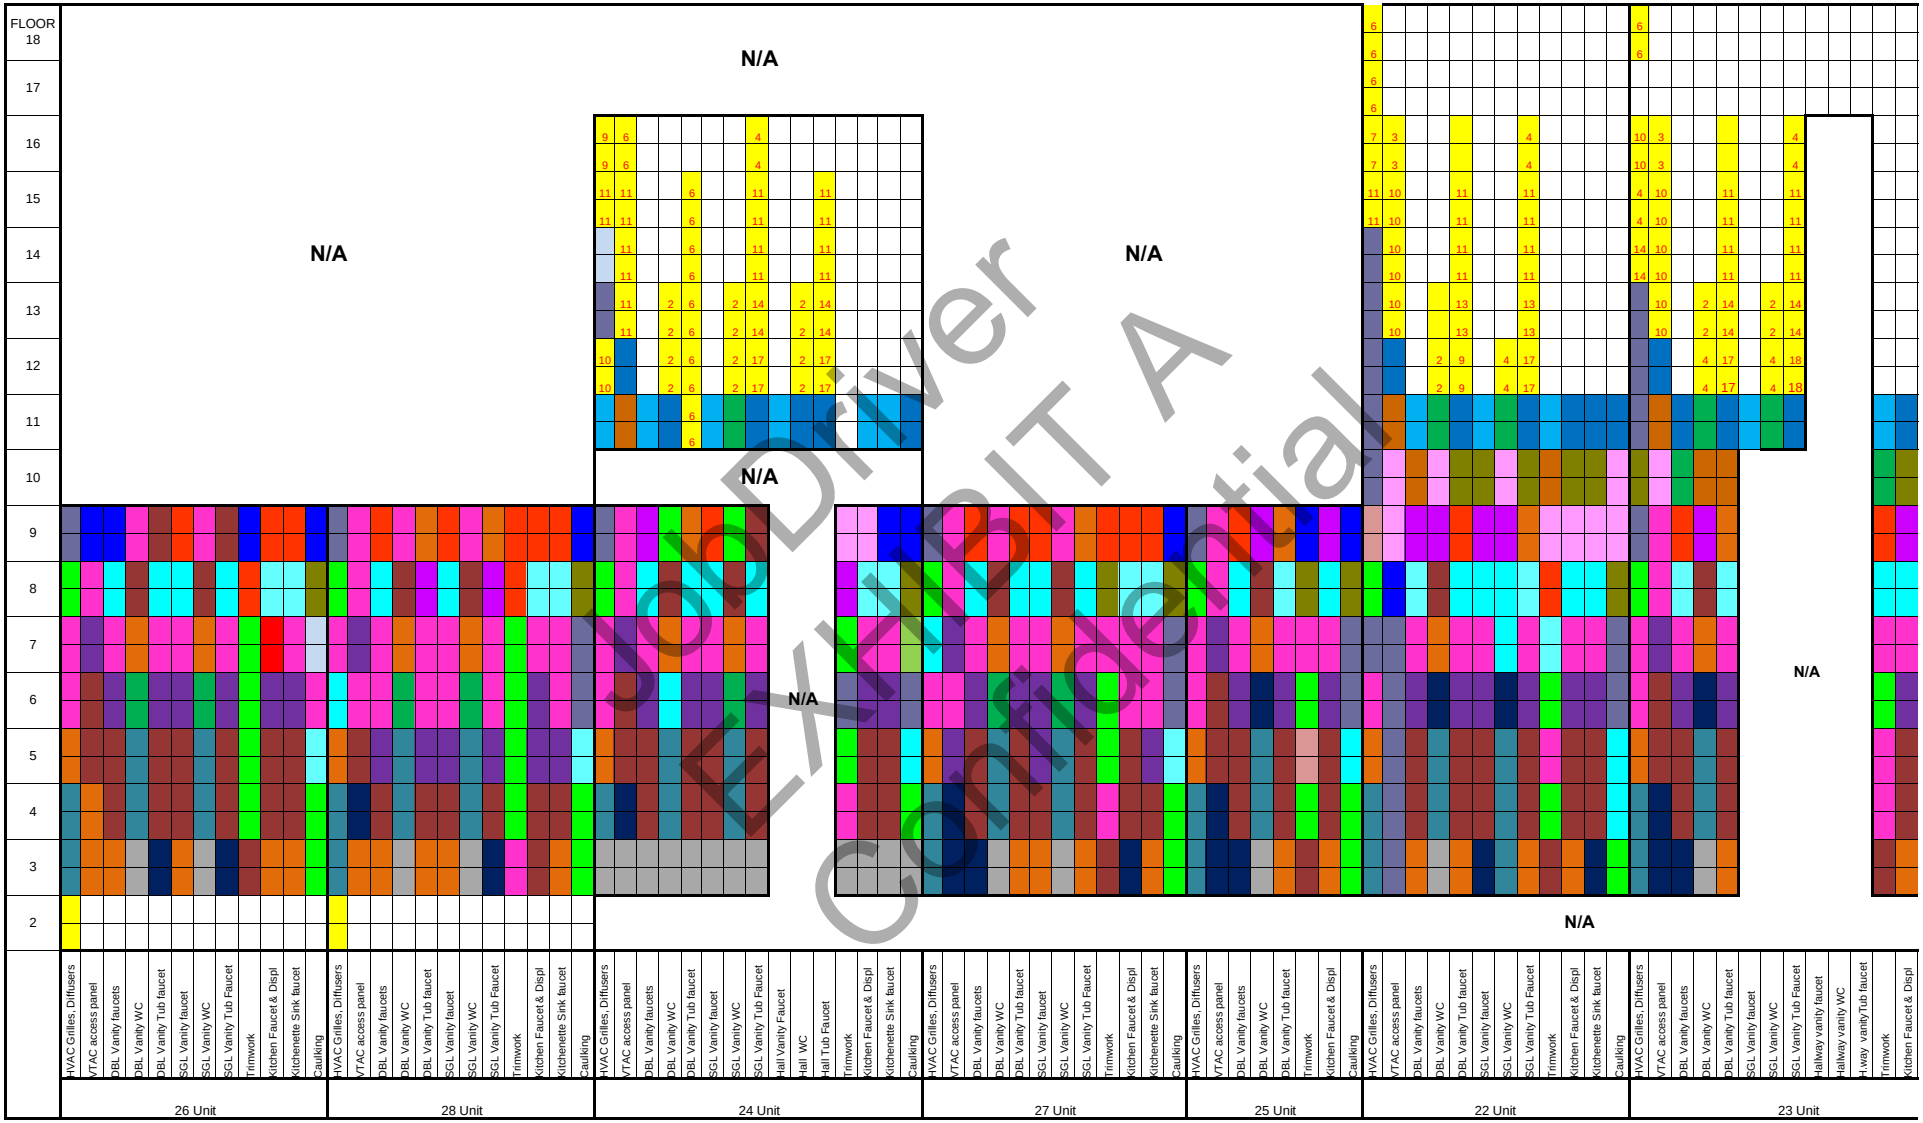

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

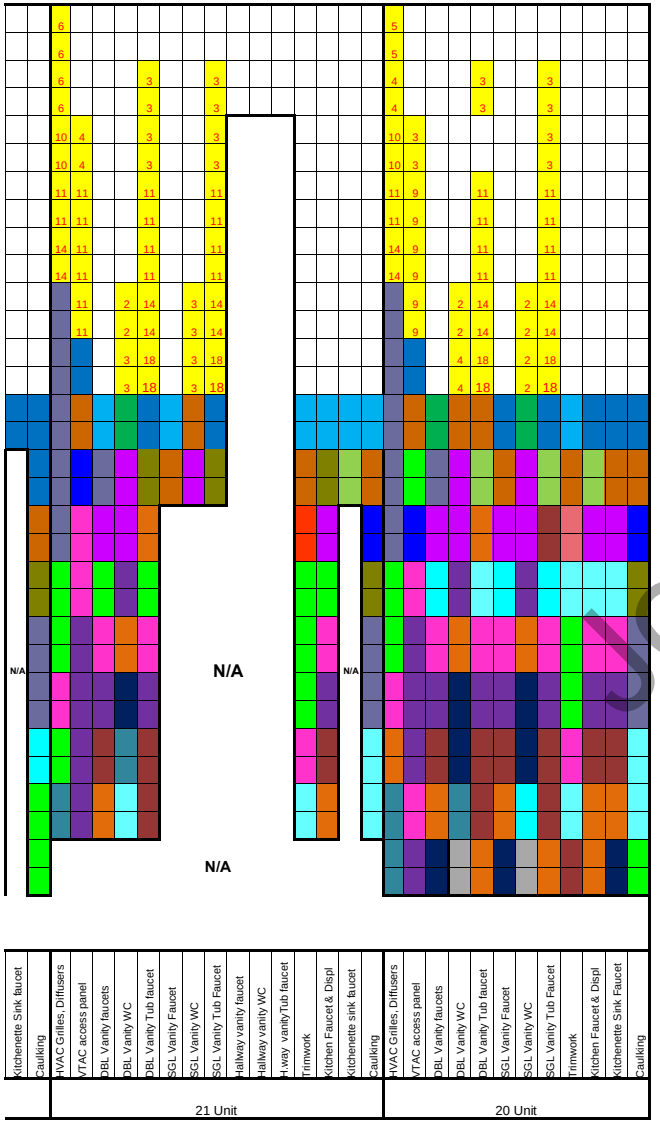

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

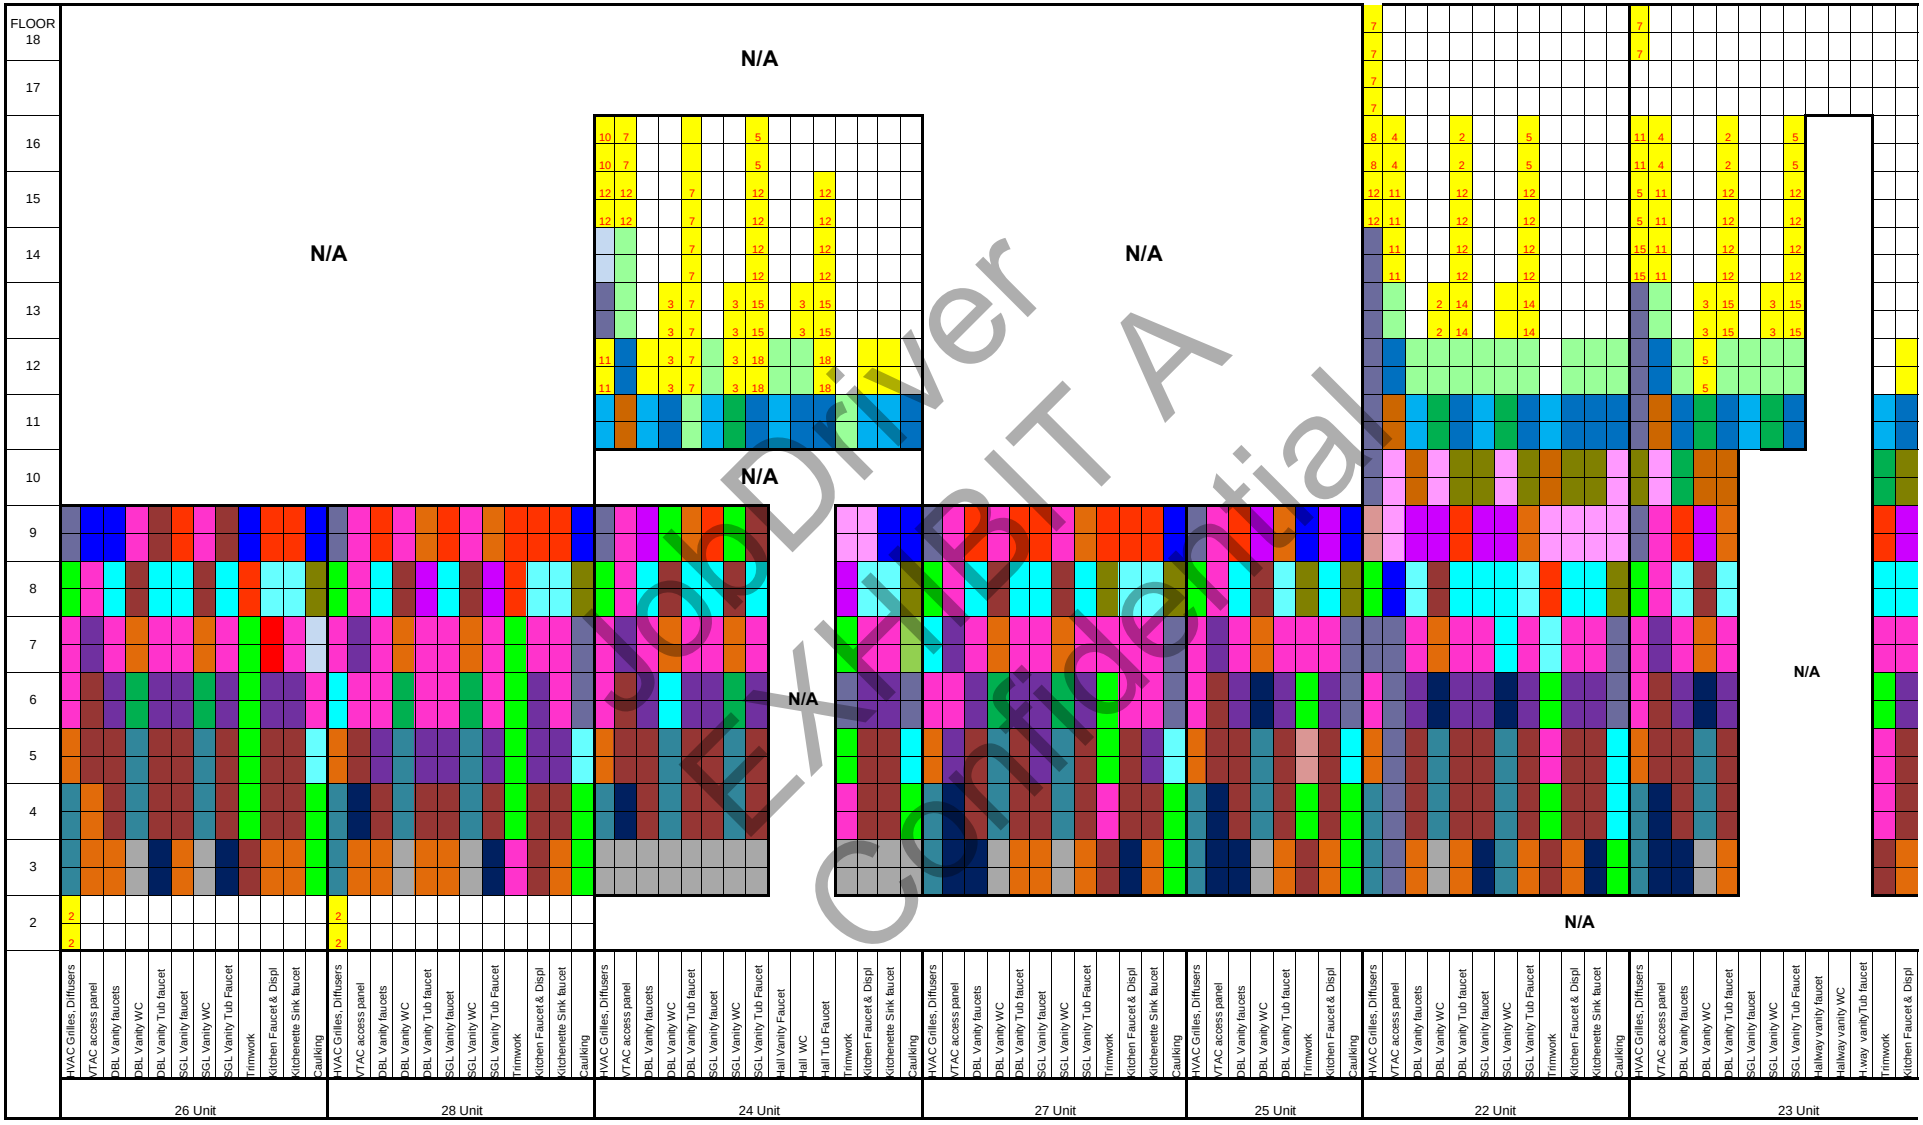

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

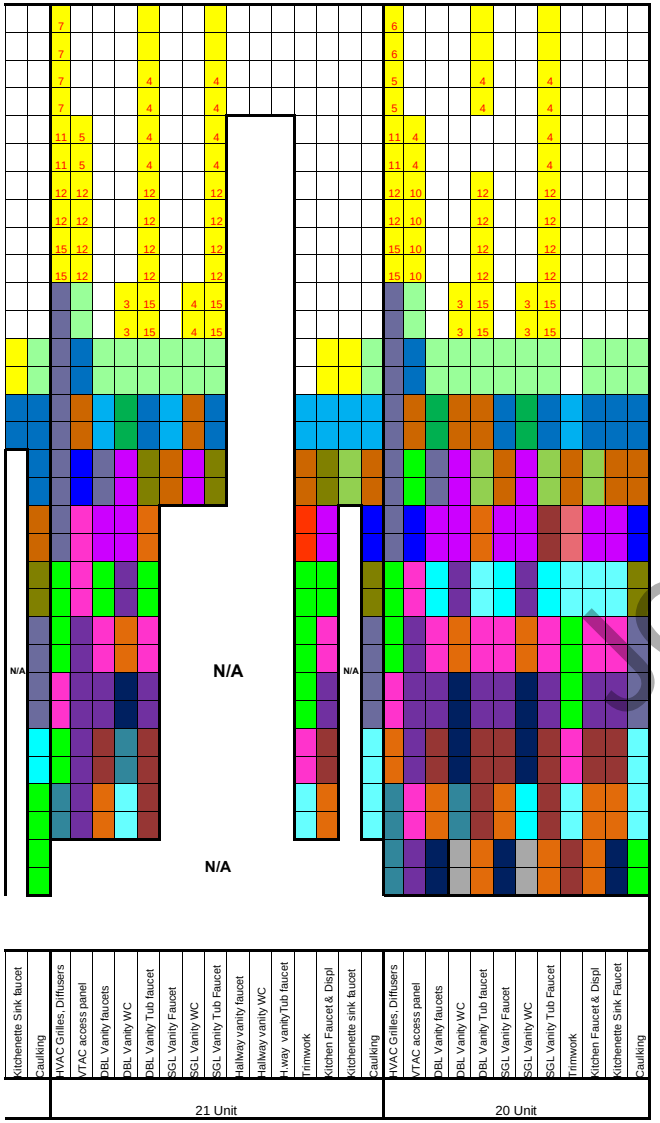

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

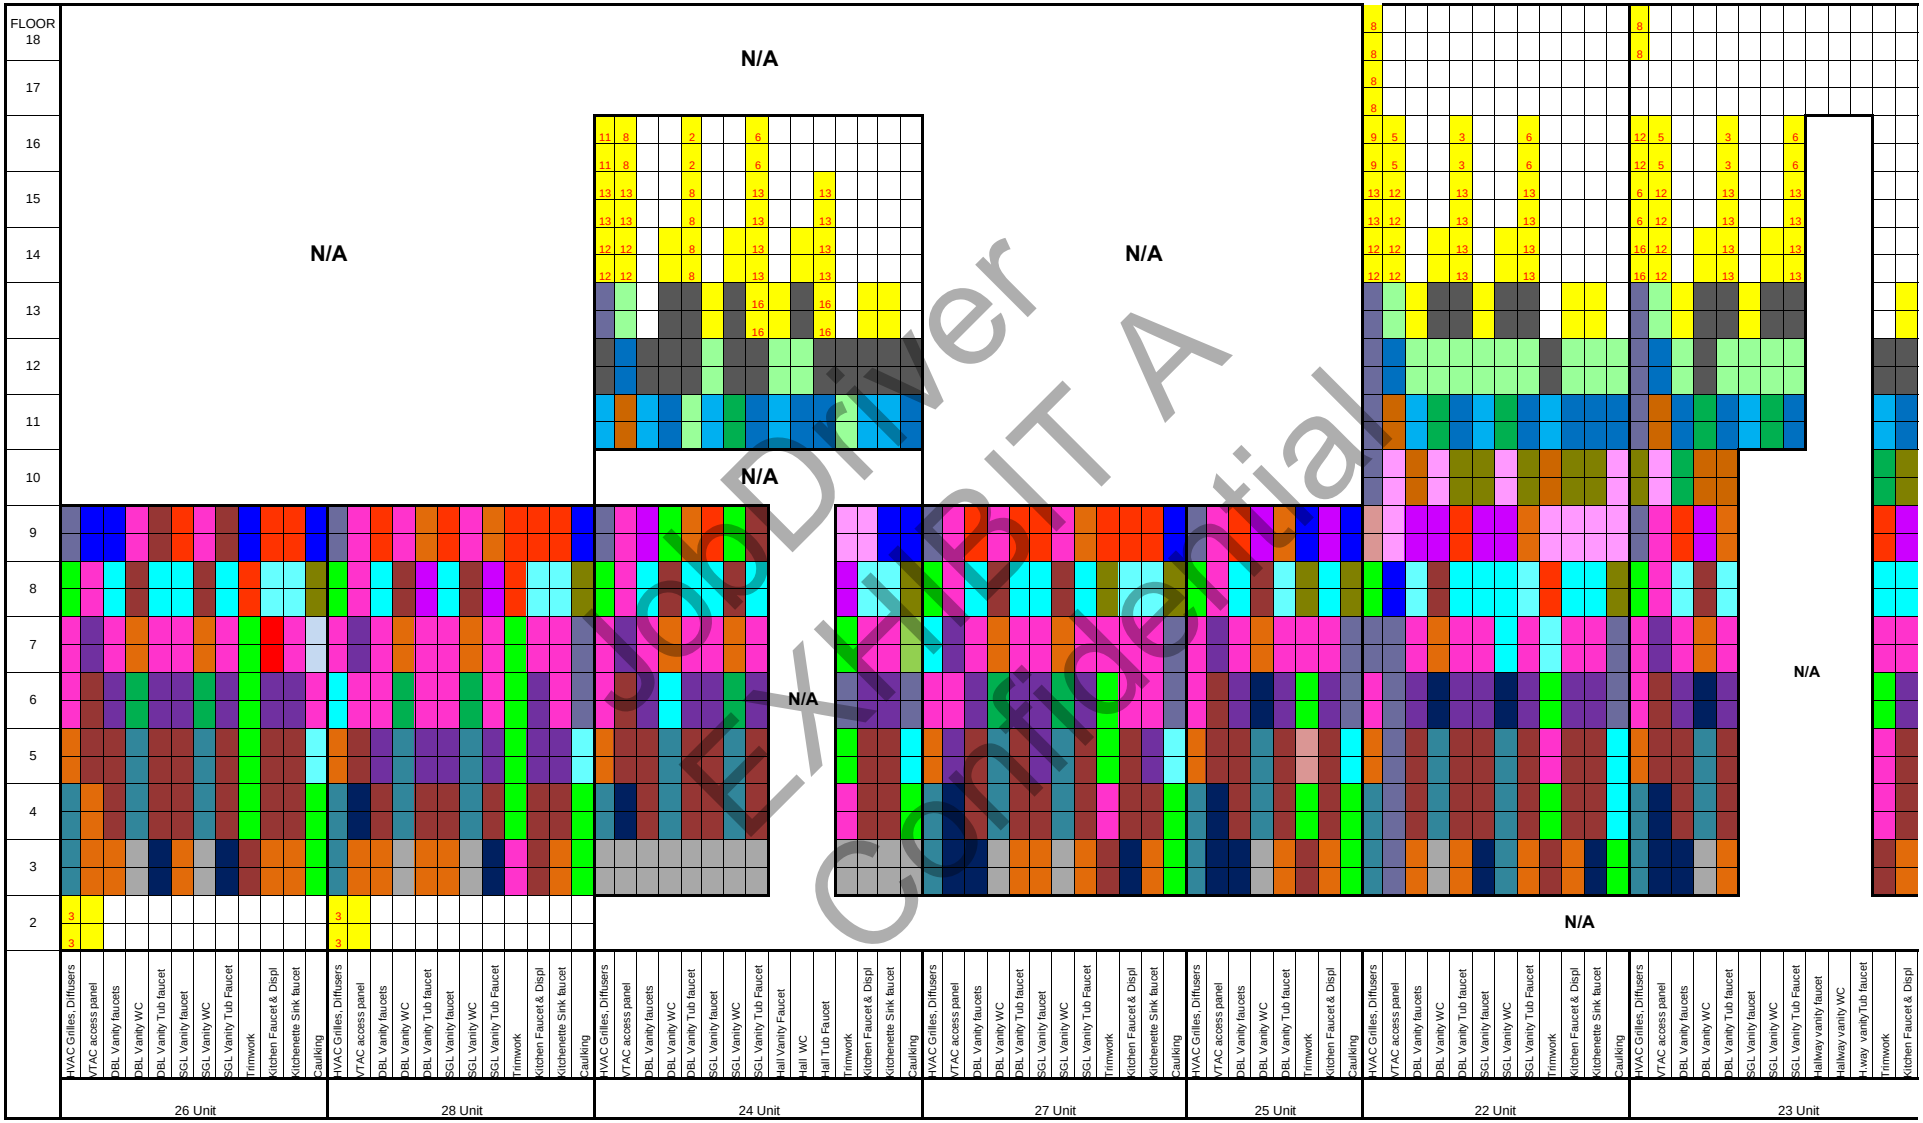

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

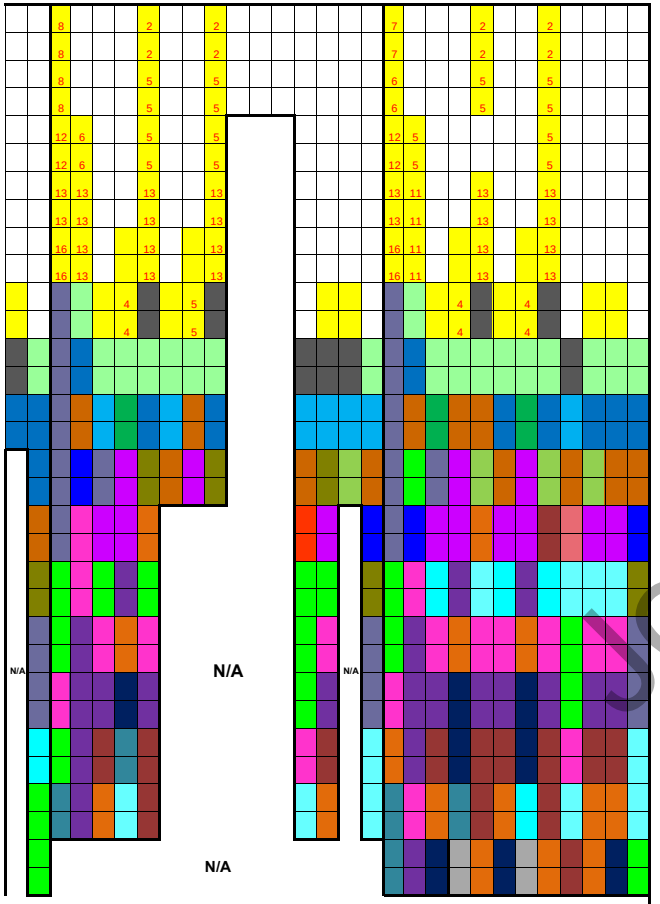

Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit
20 Unit

: 5/2/2012
: 5/9/2012
: 5/16/2012
: 5/23/2012

WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/6/2012
WORK COMPLETED TO DATE 6/13/2012
WORK COMPLETED TO DATE 6/20/2012

WORK COMPLETED TO DATE 6/27/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

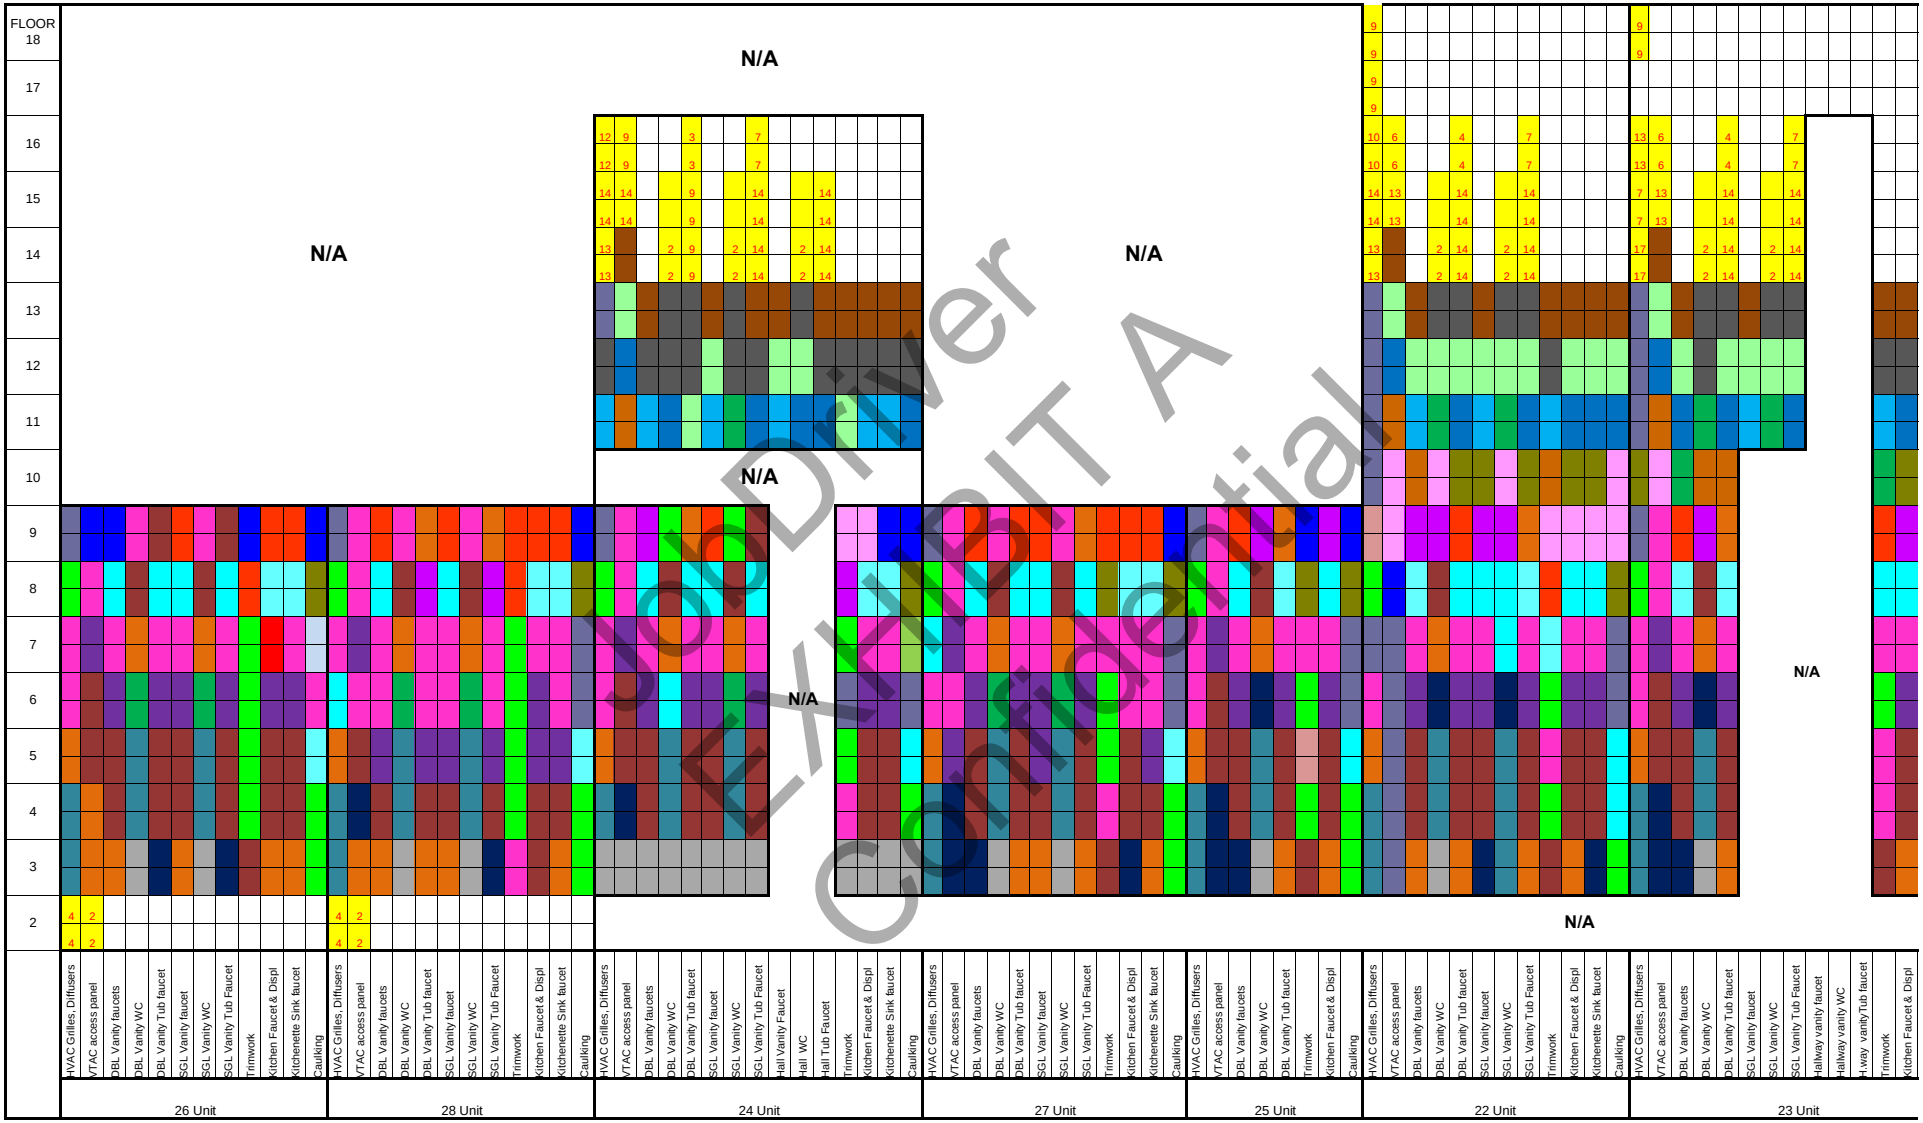

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

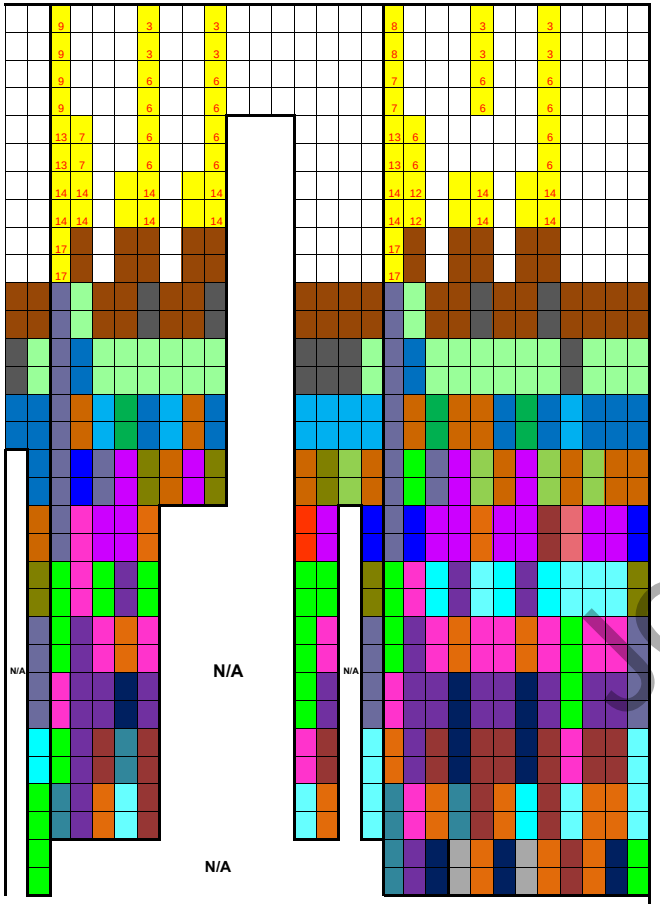

Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit
20 Unit

: 5/2/2012
: 5/9/2012
: 5/16/2012
: 5/23/2012

WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/6/2012
WORK COMPLETED TO DATE 6/13/2012
WORK COMPLETED TO DATE 6/20/2012
WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/6/2012
WORK COMPLETED TO DATE 7/9/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

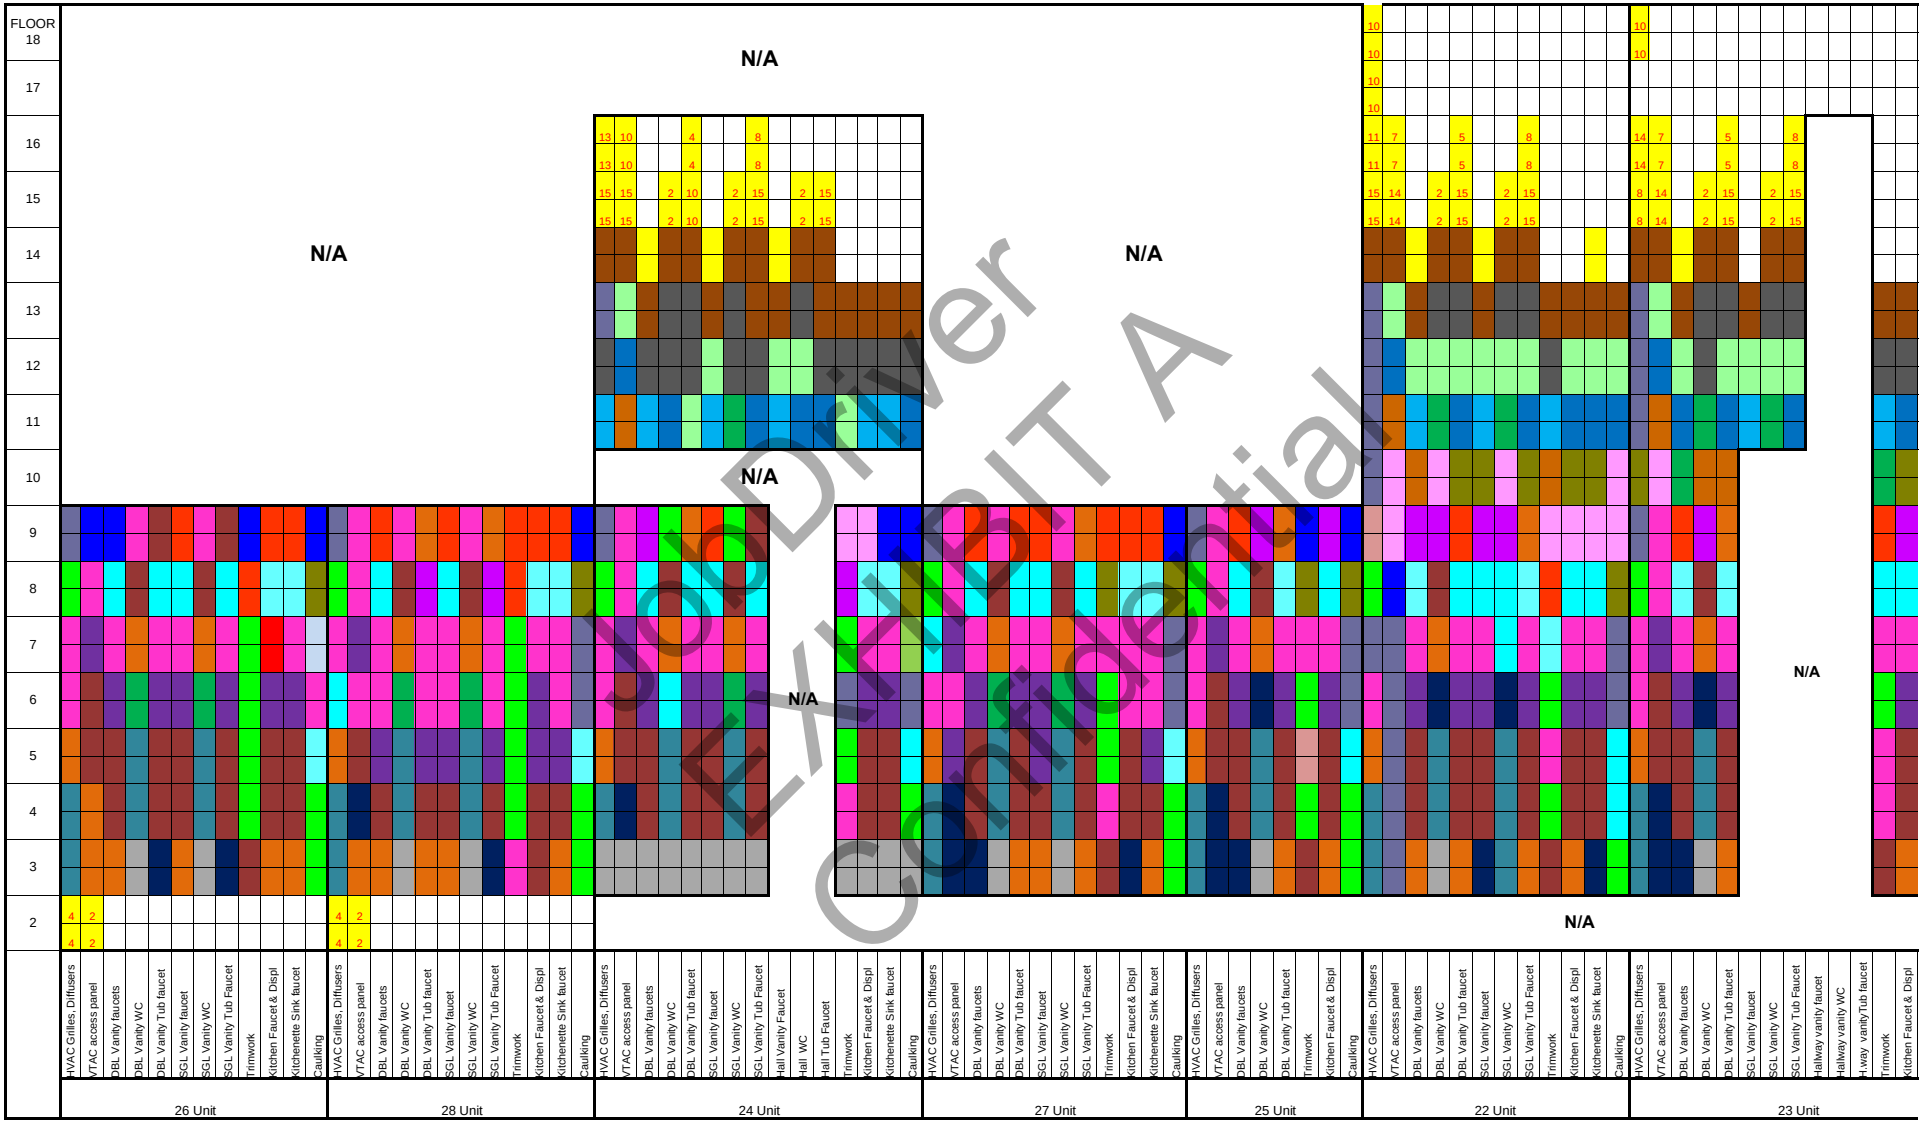

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

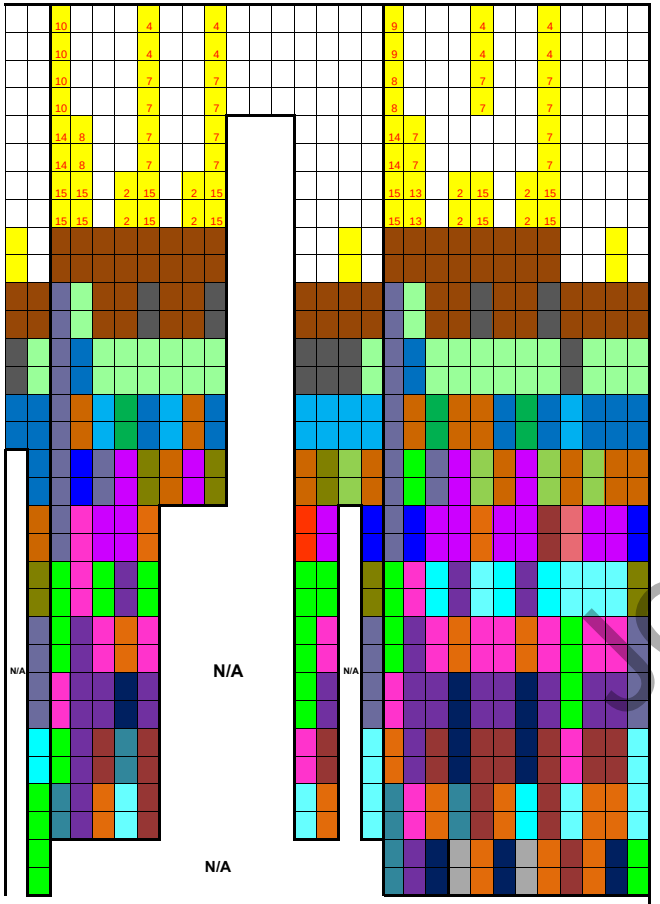

Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit
20 Unit

: 5/2/2012
: 5/9/2012
: 5/16/2012
: 5/23/2012

WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/6/2012
WORK COMPLETED TO DATE 6/13/2012
WORK COMPLETED TO DATE 6/20/2012
WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/4/2012
WORK COMPLETED TO DATE 7/11/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

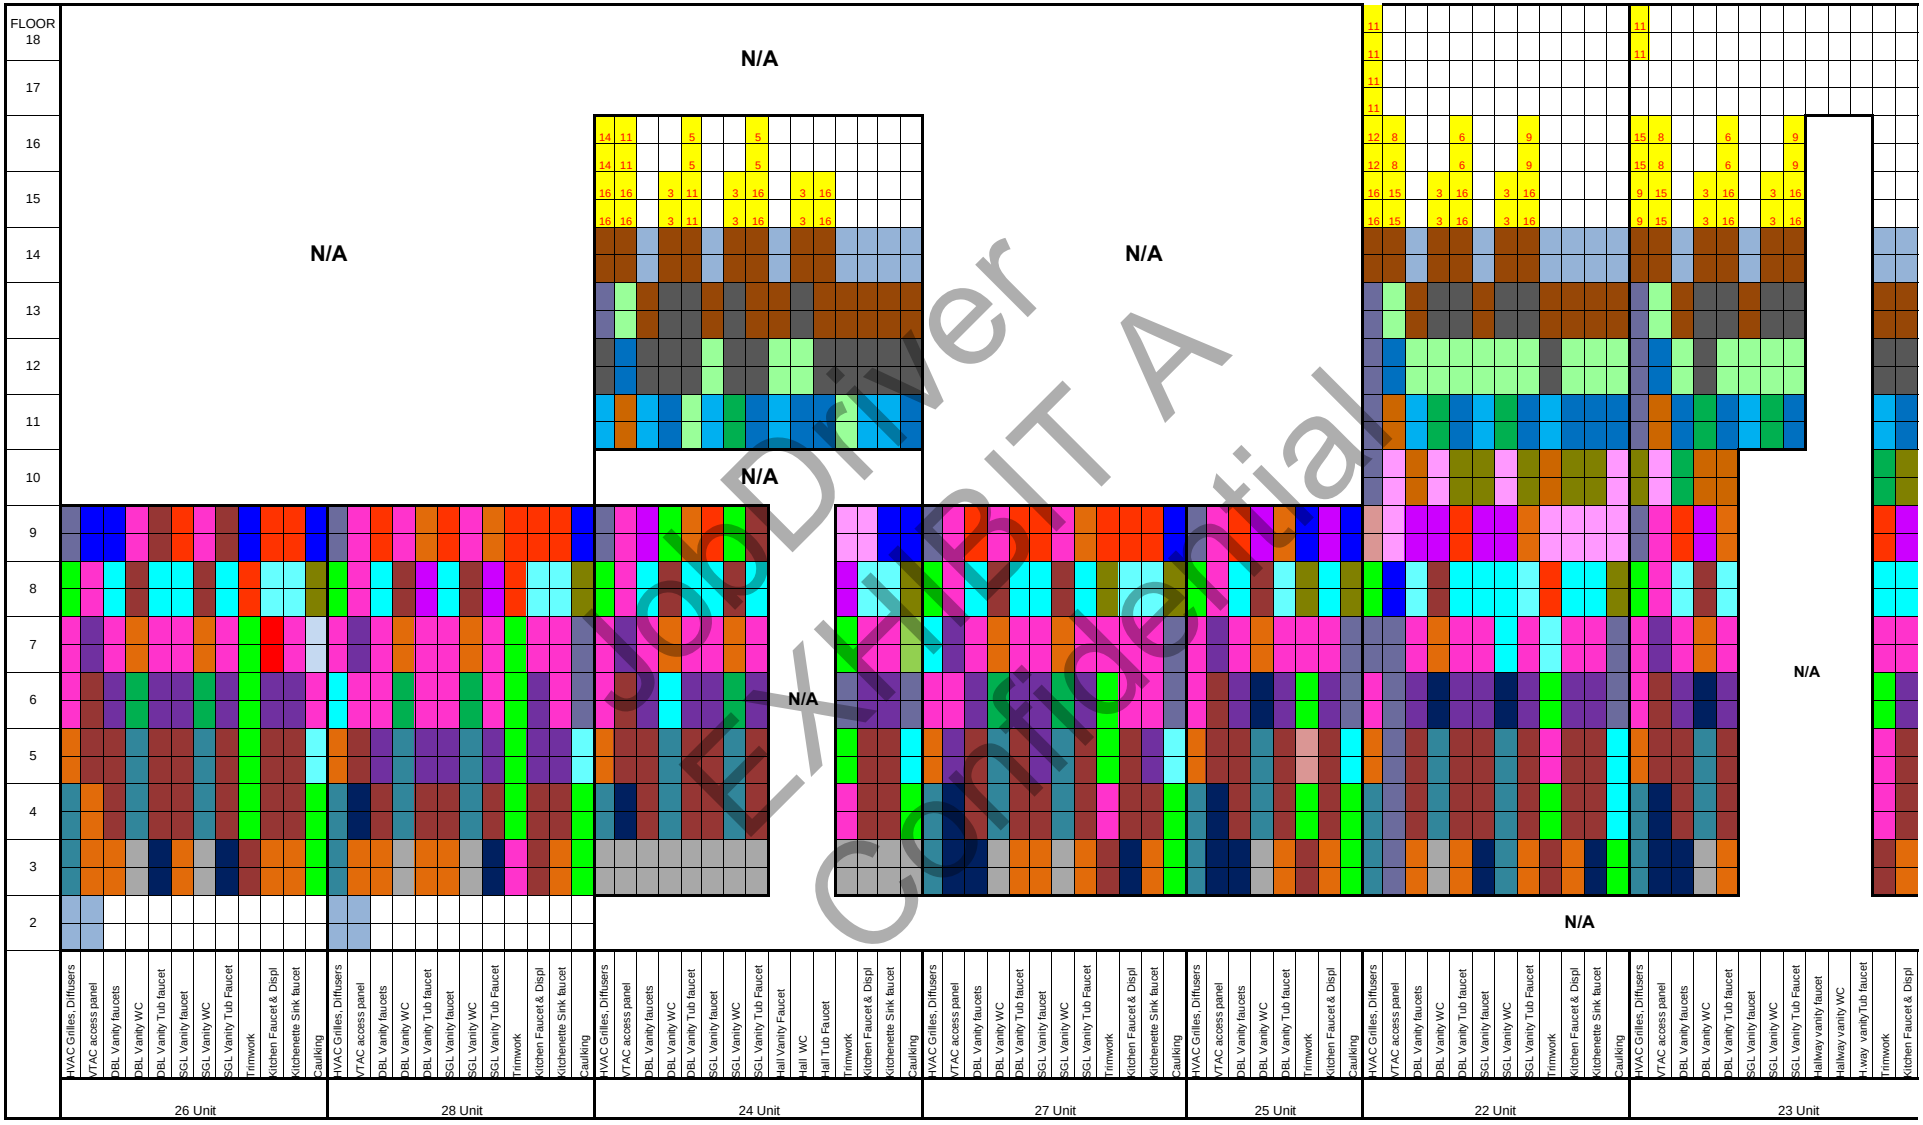

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

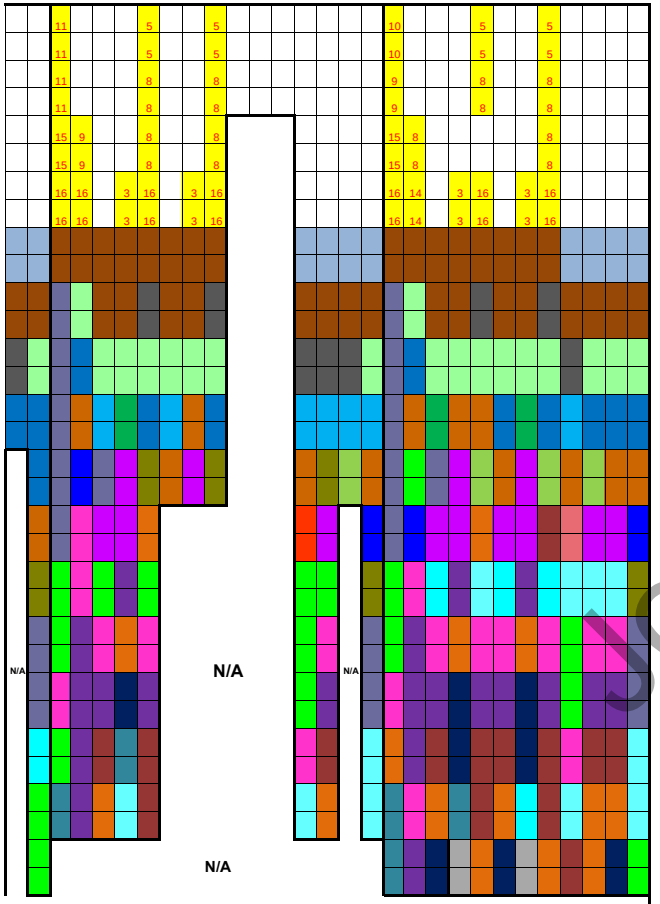

Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit
20 Unit

: 5/2/2012
: 5/9/2012
: 5/16/2012
: 5/23/2012

WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/6/2012
WORK COMPLETED TO DATE 6/13/2012
WORK COMPLETED TO DATE 6/20/2012
WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/4/2012
WORK COMPLETED TO DATE 7/11/2012
WORK COMPLETED TO DATE 7/18/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

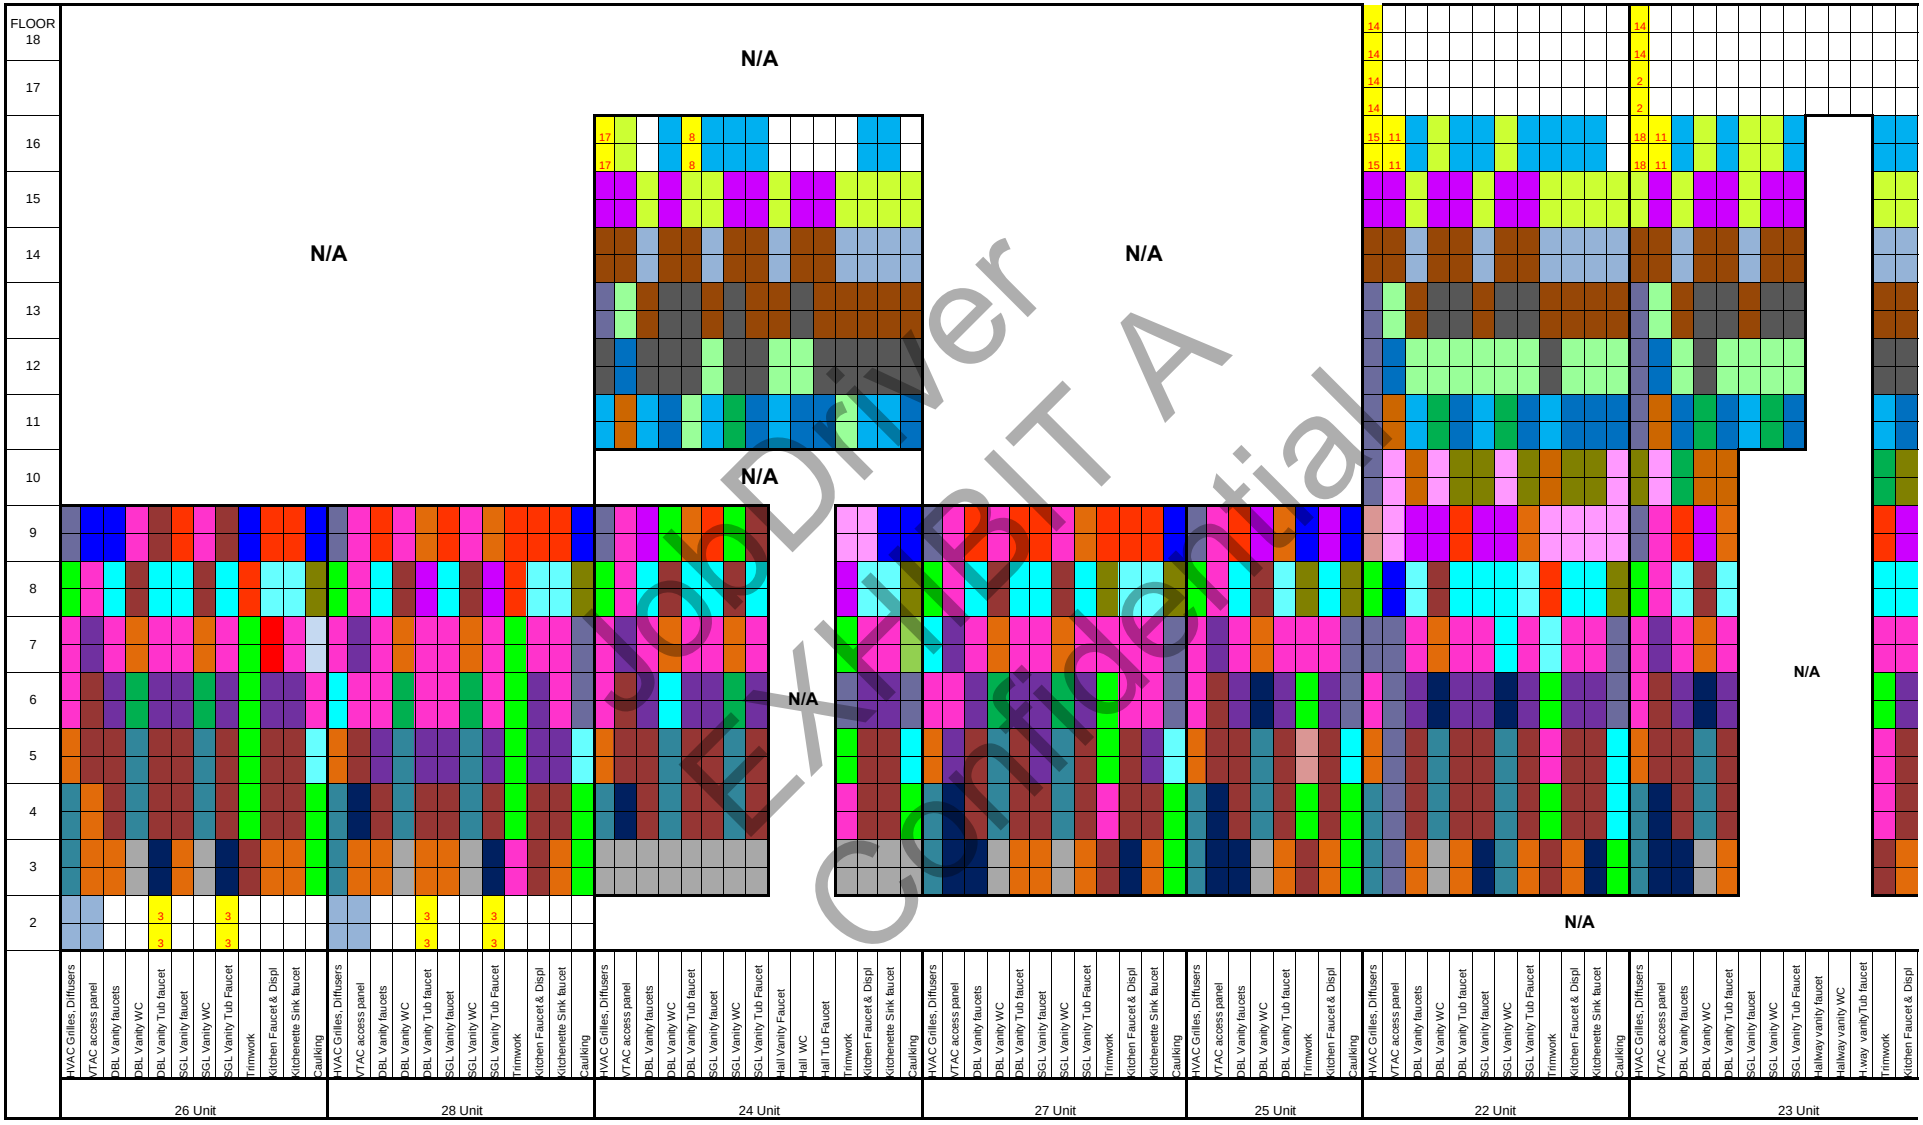

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

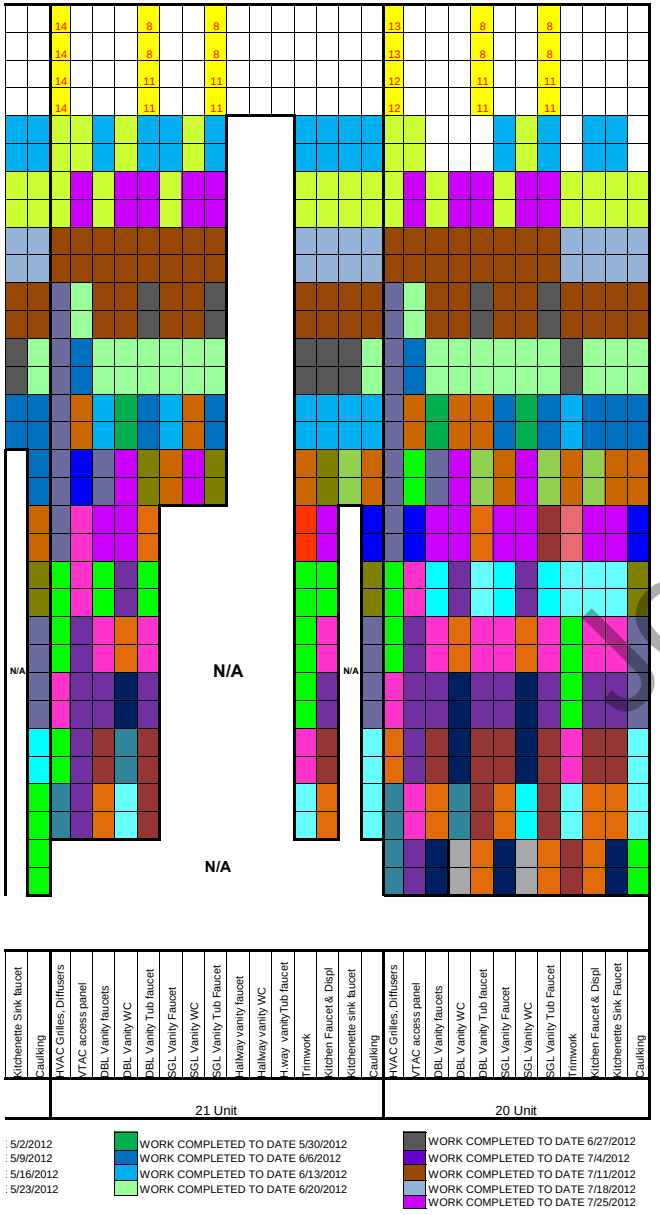

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

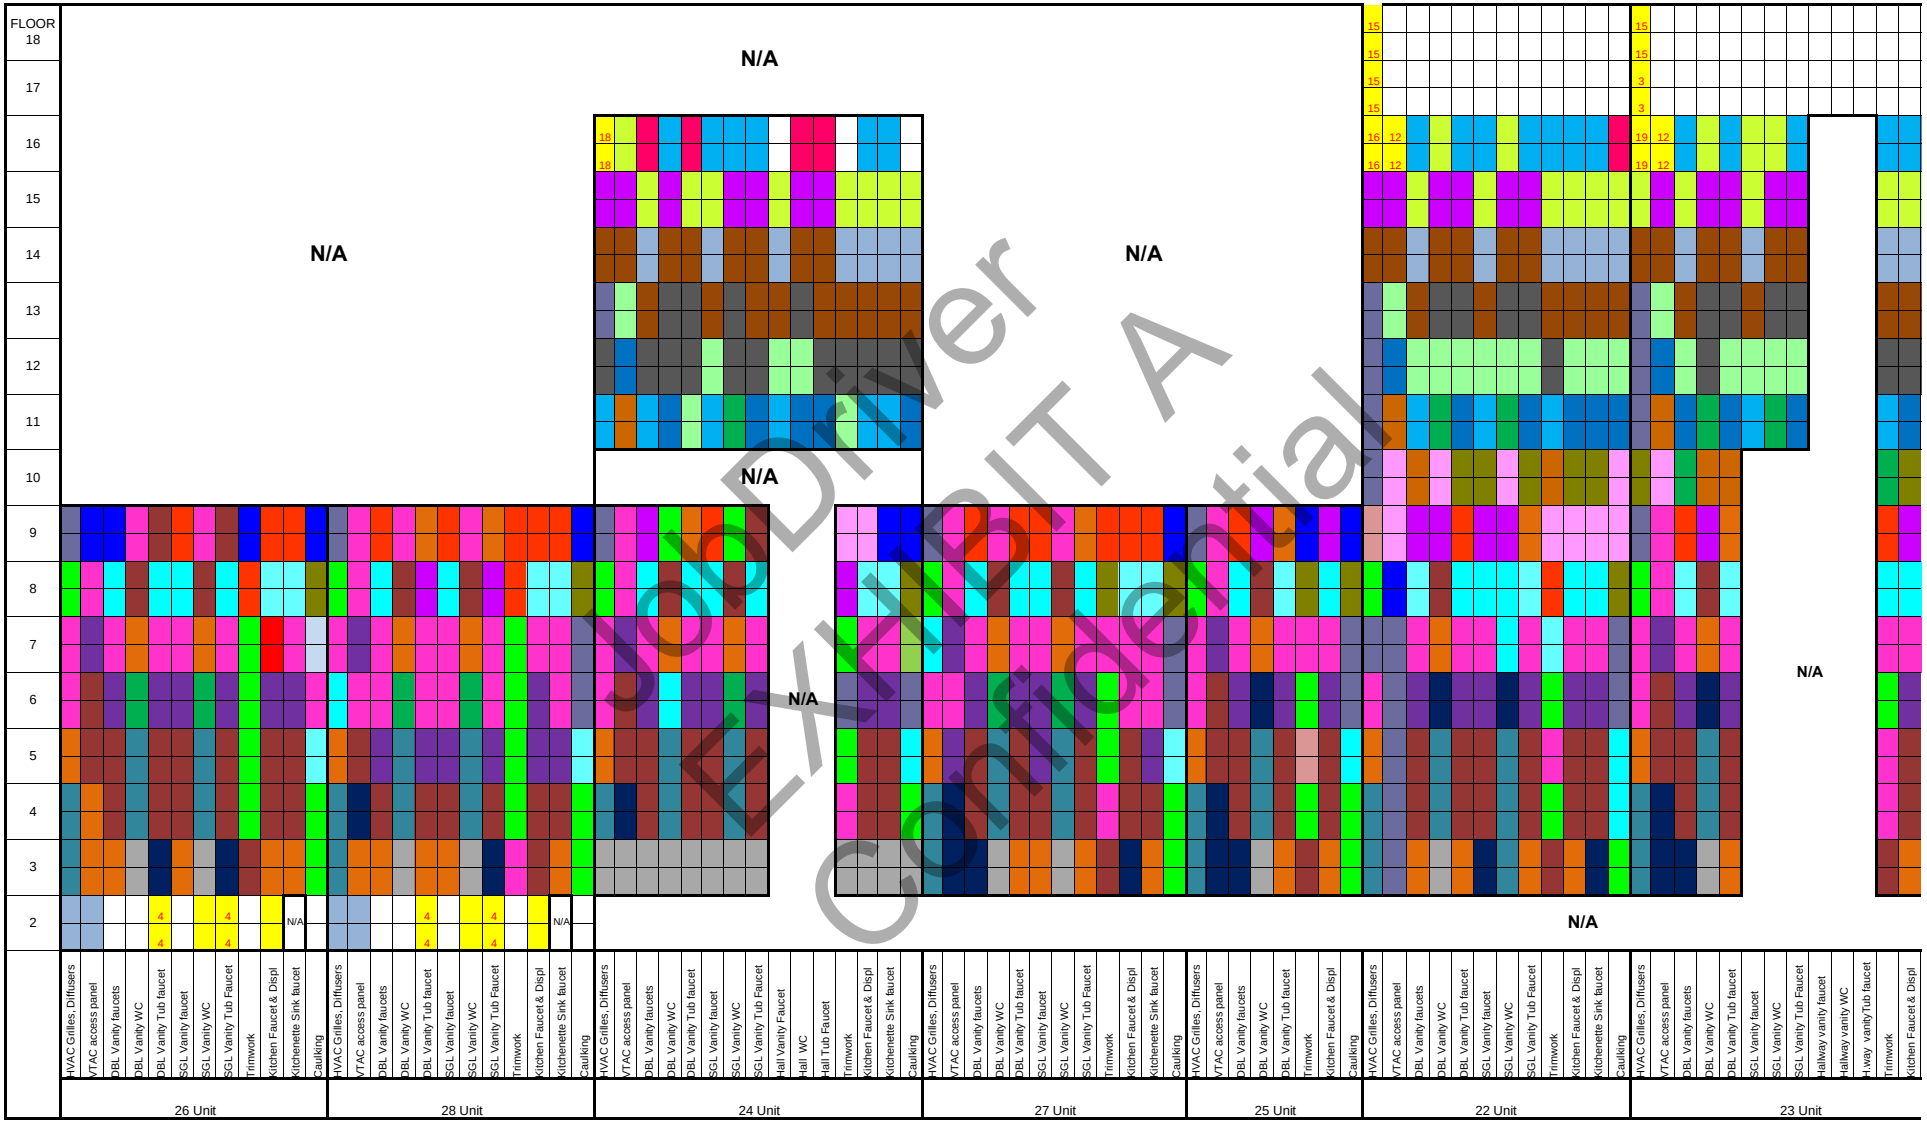

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE
- WORK COMPLETED TO DATE

BAY MECHANICAL PROGRESS CHART

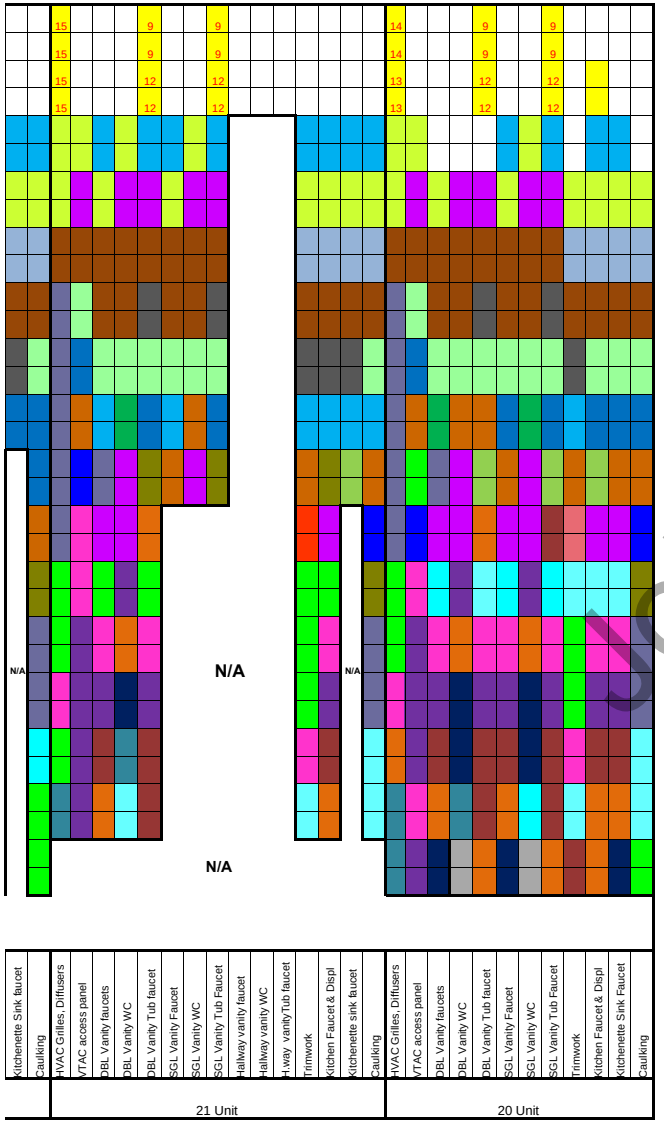

Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Hallway vanity faucet
Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit

20 Unit

: 5/2/2012
: 5/9/2012
: 5/16/2012
: 5/23/2012

WORK COMPLETED TO DATE 5/30/2012
WORK COMPLETED TO DATE 6/6/2012
WORK COMPLETED TO DATE 6/13/2012
WORK COMPLETED TO DATE 6/20/2012

WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/4/2012
WORK COMPLETED TO DATE 7/11/2012
WORK COMPLETED TO DATE 7/18/2012
WORK COMPLETED TO DATE 7/25/2012

WORK COMPLETED TO DATE 8/1/2012
WORK COMPLETED TO DATE 8/8/2012
WORK COMPLETED TO DATE 8/15/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

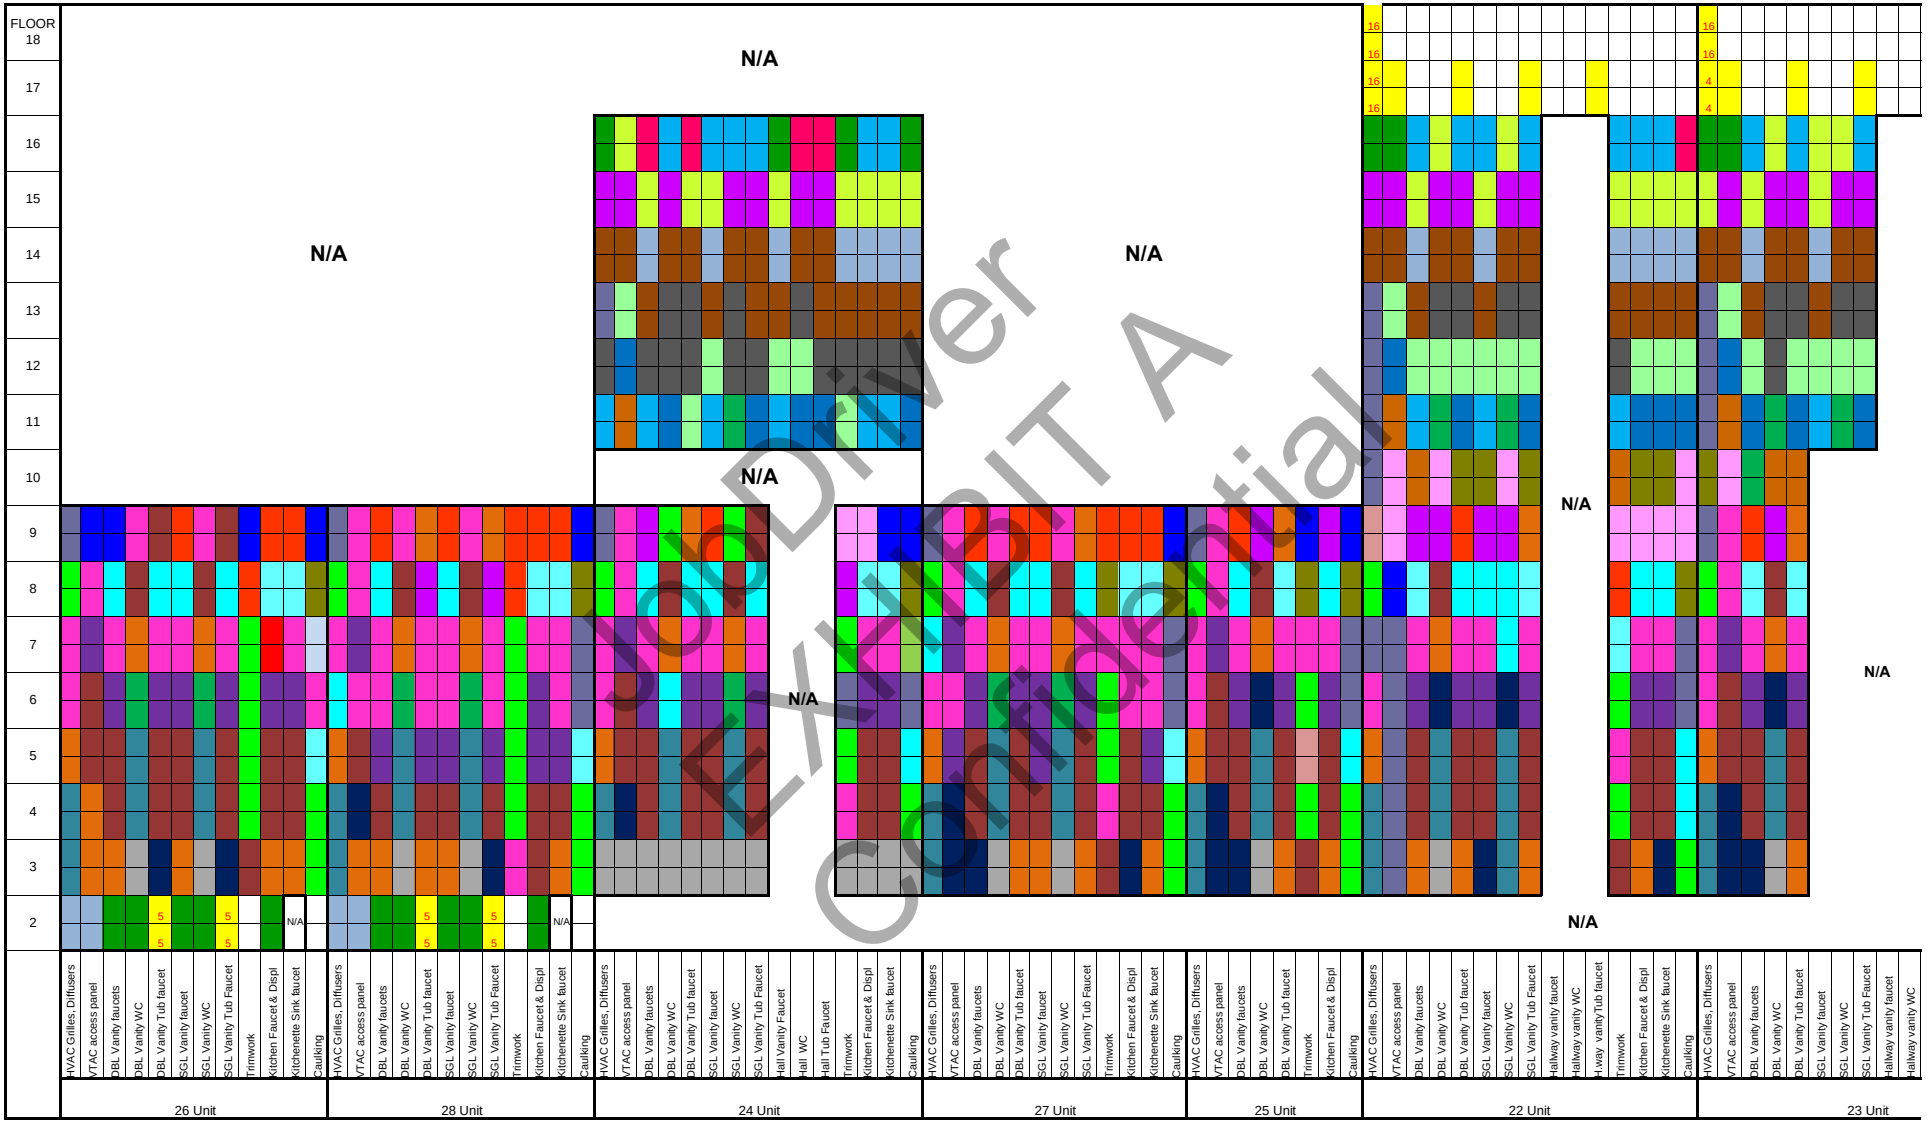

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMPLET
- WORK COMPLET
- WORK COMPLET
- WORK COMPLET

BAY MECHANICAL PROGRESS CHART

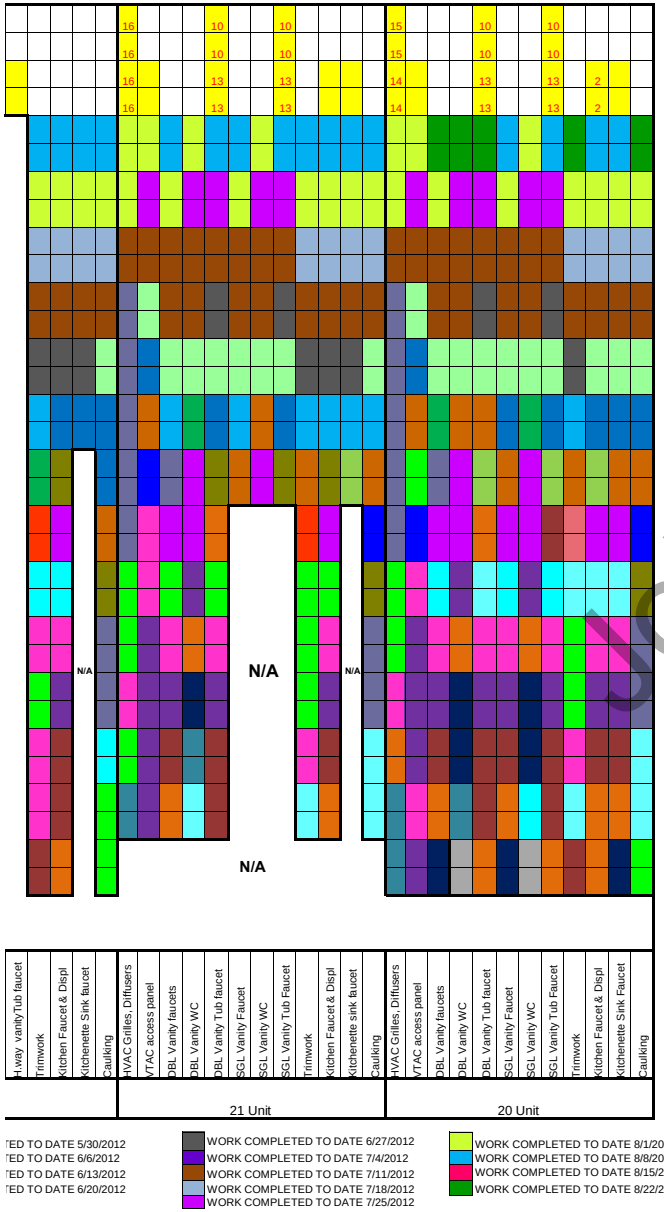

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMP
- WORK COMP
- WORK COMP
- WORK COMP

BAY MECHANICAL PROGRESS CHART

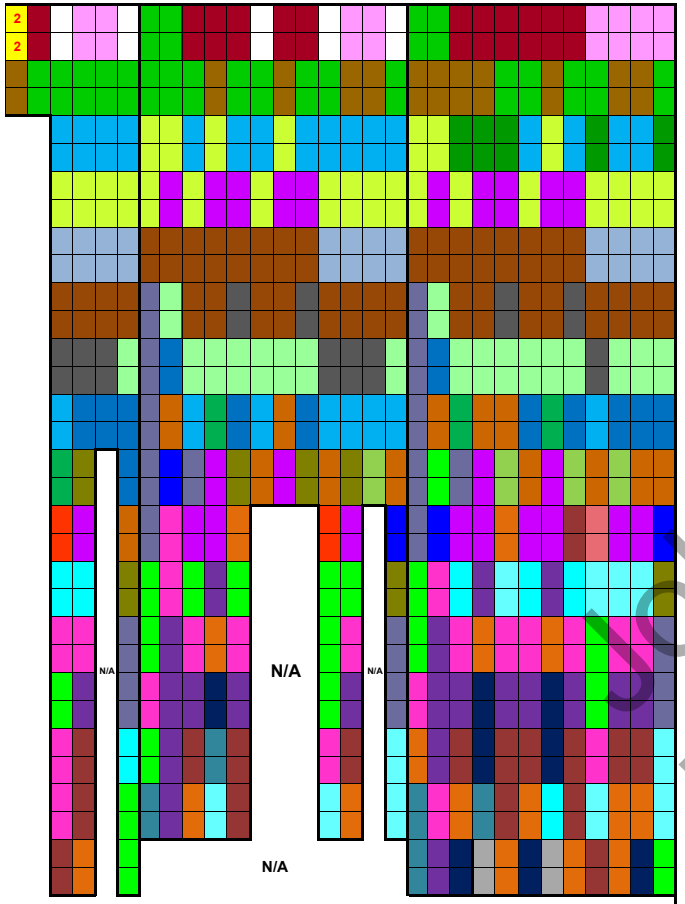

Hallway vanity WC
H.way vanityTub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit

20 Unit

PLETED TO DATE 5/30/2012
PLETED TO DATE 6/6/2012
PLETED TO DATE 6/13/2012
PLETED TO DATE 6/20/2012

WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/4/2012
WORK COMPLETED TO DATE 7/11/2012
WORK COMPLETED TO DATE 7/18/2012
WORK COMPLETED TO DATE 7/25/2012

WORK COMPLETED TO DATE 8/1/2012
WORK COMPLETED TO DATE 8/8/2012
WORK COMPLETED TO DATE 8/15/2012
WORK COMPLETED TO DATE 8/22/2012
WORK COMPLETED TO DATE 8/29/2012

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

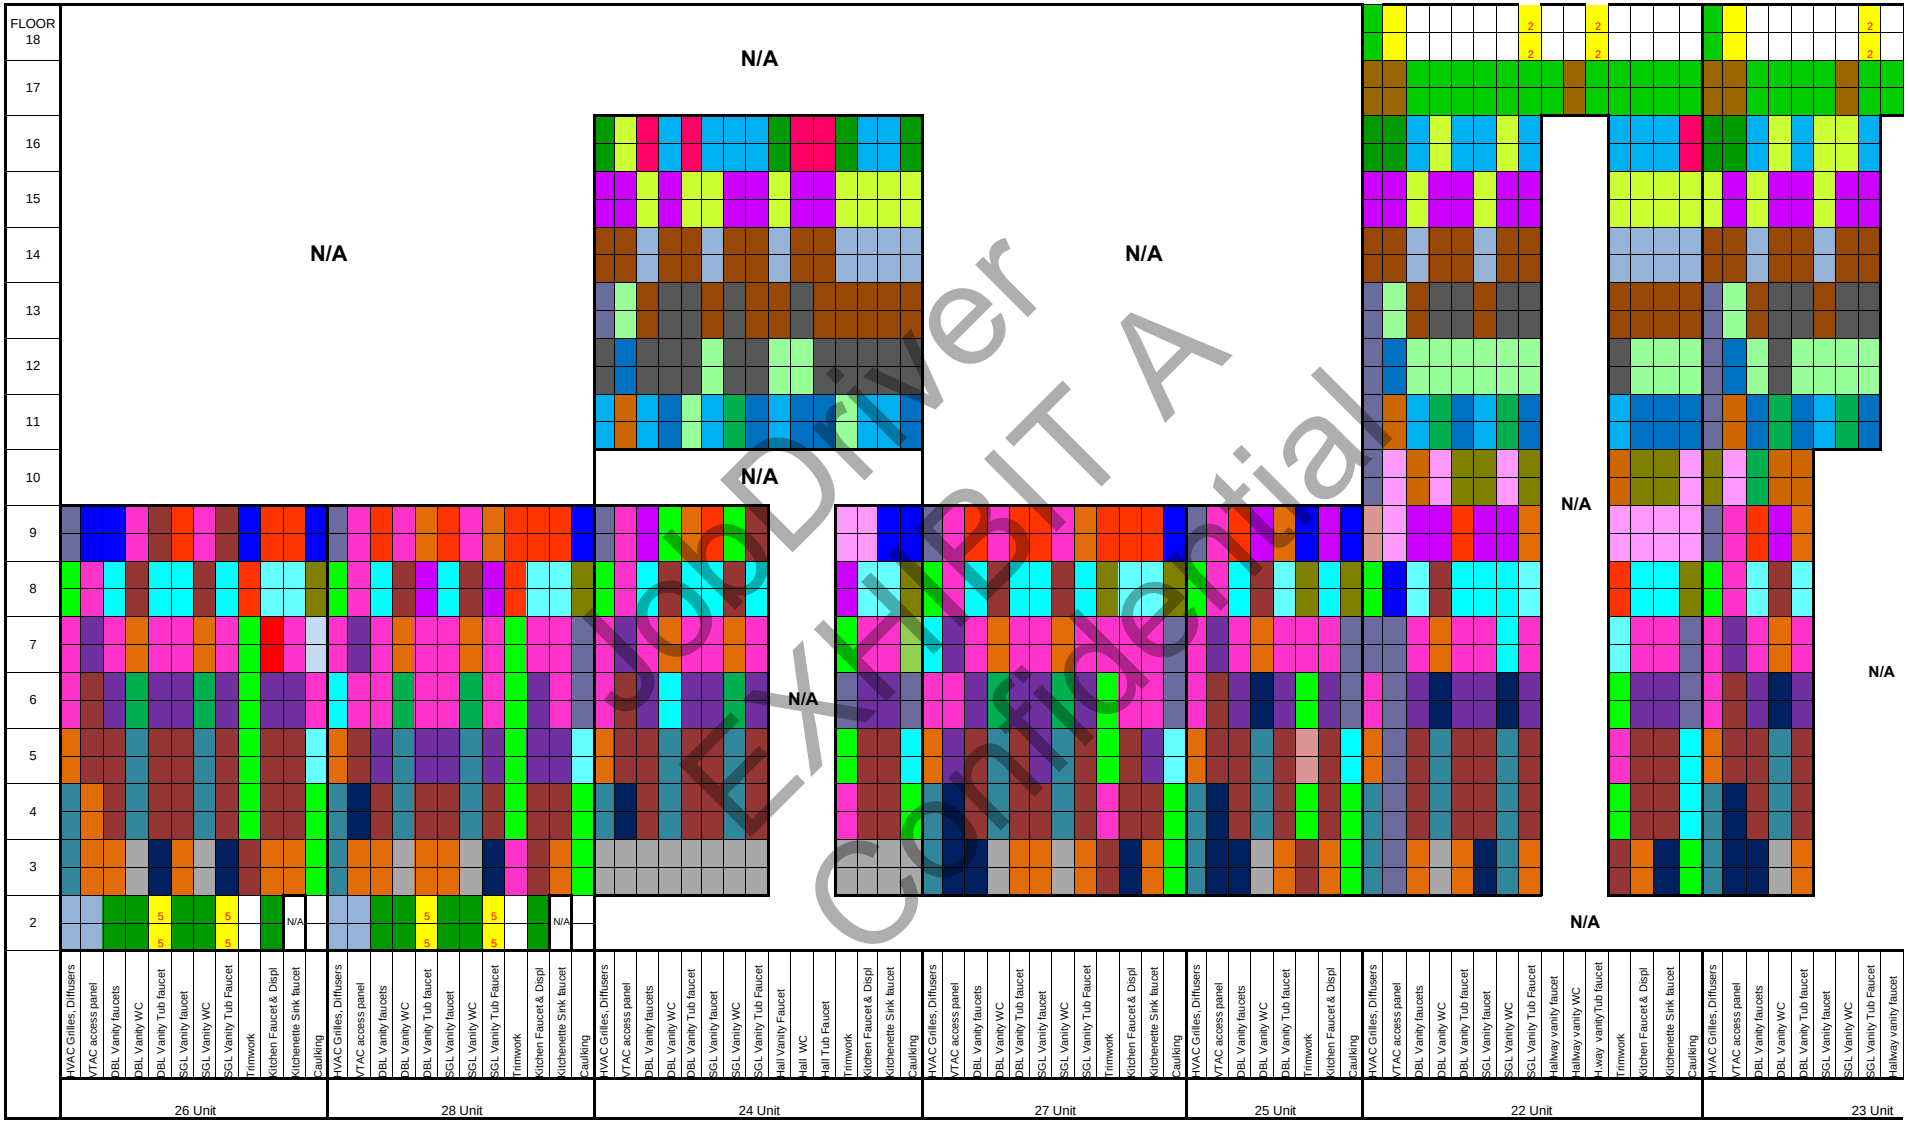

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMP
- WORK COMP
- WORK COMP
- WORK COMP

BAY MECHANICAL PROGRESS CHART

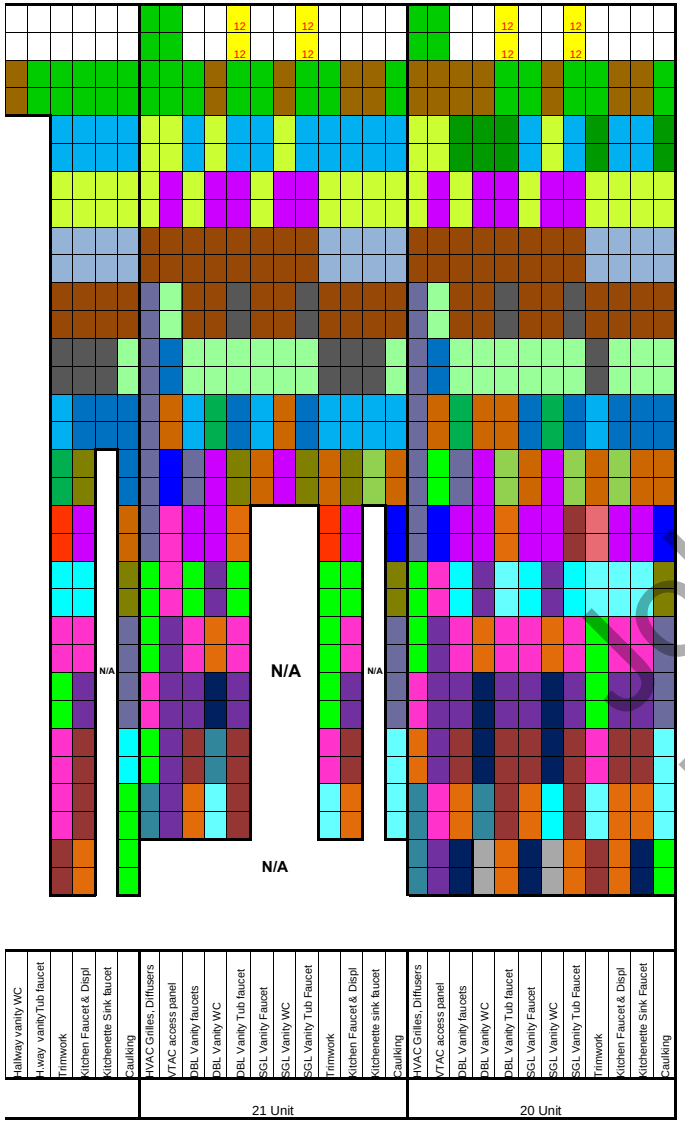

JobDriver
EXHIBIT A
Confidential

BAY MECHANICAL PROGRESS CHART

Job Driver
EXHIBIT A
Confidential

Bay Mechanical Progress Chart

RUN DATE : 2/1/2012

- Work Completed to Date 1/13/2012
- Areas Available For You To Work
- # Areas if Work Available For Multiple Updates
- Work Completed to Date 1/18/2012
- WORK COMPLETED TO DATE 1/25/2012
- WORK COMPLETED TO DATE 2/1/2012
- WORK COMPLETED TO DATE 2/8/2012
- WORK COMPLETED TO DATE 2/15/2012
- WORK COMPLETED TO DATE 2/22/2012
- WORK COMPLETED TO DATE 2/29/2012
- WORK COMPLETED TO DATE 3/7/2012
- WORK COMPLETED TO DATE 3/14/2012
- WORK COMPLETED TO DATE 3/21/2012
- WORK COMPLETEED TO DATE 3/28/2012
- WORK COMPLETED TO DATE 4/4/2012
- WORK COMPLETED TO DATE 4/11/2012
- WORK COMPLETED TO DATE 4/20/2012
- WORK COMPLETED TO DATE 4/25/2012
- WORK COMPLETED TO DATE 5/2/2012
- WORK COMPLETED TO DATE 5/9/2012
- WORK COMPLETED TO DATE 5/16/2012
- WORK COMPLETED TO DATE 5/23/2012
- WORK COMP
- WORK COMP
- WORK COMP
- WORK COMP

BAY MECHANICAL PROGRESS CHART

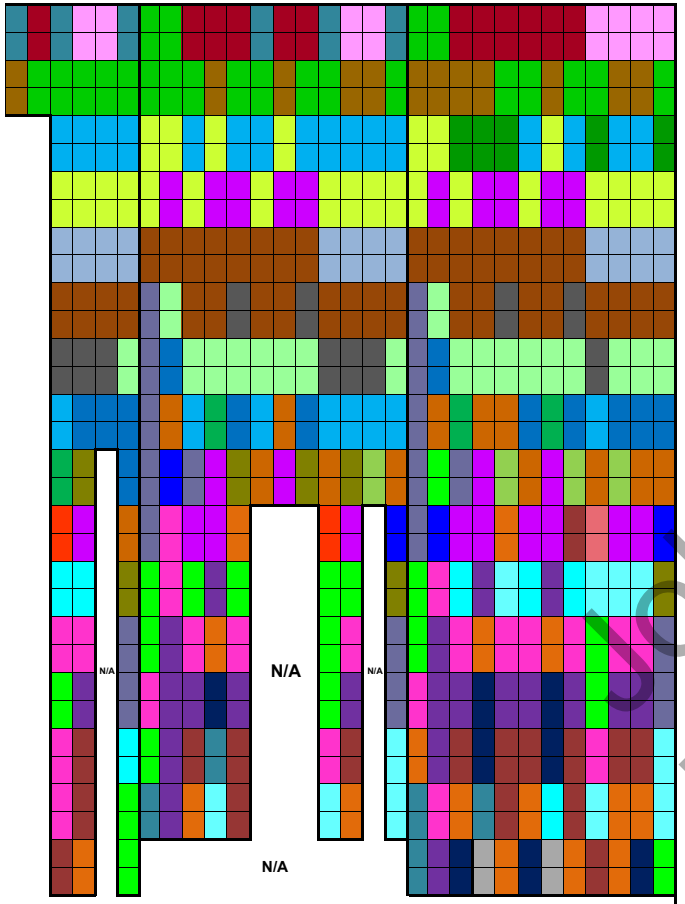

Hallway vanity WC
H.way vanity Tub faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette sink faucet
Caulking
HVAC Grilles, Diffusers
VTAC access panel
DBL Vanity faucets
DBL Vanity WC
DBL Vanity Tub faucet
SGL Vanity Faucet
SGL Vanity WC
SGL Vanity Tub Faucet
Trimwork
Kitchen Faucet & Displ
Kitchenette Sink Faucet
Caulking

21 Unit

20 Unit

PLETED TO DATE 5/30/2012
PLETED TO DATE 6/6/2012
PLETED TO DATE 6/13/2012
PLETED TO DATE 6/20/2012

WORK COMPLETED TO DATE 6/27/2012
WORK COMPLETED TO DATE 7/4/2012
WORK COMPLETED TO DATE 7/11/2012
WORK COMPLETED TO DATE 7/18/2012
WORK COMPLETED TO DATE 7/25/2012

WORK COMPLETED TO DATE 8/1/2012
WORK COMPLETED TO DATE 8/8/2012
WORK COMPLETED TO DATE 8/15/2012
WORK COMPLETED TO DATE 8/22/2012
WORK COMPLETED TO DATE 8/29/2012

JobDriver
EXHIBIT A
Confidential
